#### Sarah Hamman

From: Luis Garcia <l.garcia@crcmail.com>
Sent: Tuesday, December 10, 2019 8:04 AM

To: Sarah Hamman
Cc: Luis Garcia
Subject: Supporting Docs

Attachments: Scope Table of Contents.pdf; Officer's Club .docx; Justice Center.docx; 4H Activity

Center.docx; Building 15 Hewitt.docx; Change Order 22,220.00.pdf; CHANGE ORDER -

JIMBOS ROOF.pdf

Importance: High

Hi Sarah,

I sent you the actual copy of the scope of work that we walked. I realized the table of contents wasn't attached. I am with my corporate team this week and plan on coming to Victoria next week to go over our findings and put this behind us. I am available any day, as I think it is important to discuss in person. I just want to be spot on when we close this out. I have attached a few buildings that I scrubbed, the others I'm reconciling and will have ready soon.

#### Luis Garcia

National Project Coordinator



L: 13725 S Mur-Len Road, Olathe, KS 66062

# Victoria County Officers Club Building #14 on Virtus Progress Report

Summary for invoices for details- Scope \$41,923.64 Previously billed \$26.318.64 Balance owed \$15605.00

Scope- Roof replacement items 1929-1937

No interior work assigned to Virtus Group



# Victoria County

ID	Building # and Name	Address	Comments	
013-001	#1 Old Jail	206 Constitution	Turn over to county	
002-001	#2 Old Courthouse	101 N. Bridge	Turn over to county	
002-001	#3 Old Courthouse Tunnel	1	Turn over to county	
001-001	#4 New Courthouse	115 N. Bridge	Turn over to county	
014-001	#5 Old Fire Station	209 W. Forrest	Turn over to county	
012-001	#6 PCT 1 Machine Storage	2000 FM 1686	Turn over to county	
009-001	#7 PCT 3 Machine Storage	133 Aloe Field	Turn over to county	
009-004	#8 PCT 3 Radio Tower	133 Aloe Field	Turn over to county	
009-002	#9 PCT 3 Mechanic Shop	133 Aloe Field	Turn over to county	
009-003	#10 Service Center Cover	133 Aloe Field	Turn over to county	
018-004	#11 PCT 2 Truck Storage	3323 Nursery	Turn over to county	
002-007	#12 Park Metal Storage	500 Fordyce Rd.	Turn over to county	
022-002	#13 Park Comfort Station	500 Fordyce Rd.	Turn over to county	

004-001	#14 New Jail	101 N. Glass	Complete
020-008	#15 Airplane Hangar (code upgrade)	133 N. Hangar Dr.	Complete
020-014	#16 Airplane Hangar (FBO)	437 S. Hangar Dr.	Complete
020-013	#17 Airplane Hangar B	305 S. Hangar Dr.	Complete
020-015	#18 Airplane Hangar C	207 Storehouse Drive	To be demoed
019-001	#19 PCT 4 Truck Storage	155 Corpus Christi	To be demoed
015-001	#20 PCT 4 Building	155 Corpus Christi	To be demoed
020-011	#21 Airplane Hangar (T-Hangar Units)	348 N. Hangar Dr.	Complete
020-010	#22 Aircraft Storage (T-Hangar Units)	388 N. Hangar Dr.	Complete
007-001	#23 Office Elections & JP 3	111 N. Glass	Turn over to county
020-004 020-006	#24 Airport Terminal 2 Storage Buildings Code Upgrade	609 Foster	To be demoed
020-003	#25 Airport Maintenance w/ Generator	41 Hangar	Complete:
003-001	#26 SWB Building Bridge St. Annex	204 N. Bridge	Turn over to county
024-001	#27 Extension Service	528 Waco Circle	Complete
026-001	#28 Juvenile Detention Center	97 Foster Field	Turn over to county
027-002	#29 Modular Building Highway Patrol	ND	Turn over to county
010-001	#30 Health Department	2805 Navarro	Complain
016-001	#31 4-H Activity Center	259 Bachelor Drive	

020-005	#32 Fire Marshal Office TSA	25 & 27 Hangar Dr.	Complete
006-001	#33 Officers Club	333 Bachelor Dr.	Did roof only. Decking repair and New Vents
023-001	#34 Victoria Well Service	169 Aviation Dr.	Turn over to county
029-001	#35 COMAT Building Code Upgrade	442 Foster Dr.	Complete AC installs with AARF. * fans.
028-001	#36 Animal Shetter	102 Perimeter	Turn over to county
027-001	#37 Weigh Station HWY 59 N. Scales		Turn over to county
005-001	#38 Storehouse 103 S. Glass		Turn over to county
020-007	907 #39 AARFF Fire 121 N. Hangar Station		Complete Fan Change order fence
020-009	#40 Hangar	390 N. Hangar Dr.	Turn over to county
020-012	#41 Control Tower/ 348 Bachelor Dr. Airport		Soffit panels in this length are custom waiting for material.
012-002	#42 PCT 1 Pole Barn Storage	16043 FM 1686	Turn over to county
008-001	#43 Hartman JP 1	**************************************	Turn over to county
008-002	#44 Hartman Building	901 E. Pecan	Turn over to county
017-001	#45 JP 4 Building	2604 E. Mockingbird	Turn over to county
017-999	JP 4 Wood Fence		Water and Charles
	#46 JP2 Building	4407 Lilac	Turn over to county
015-001	#47 PCT4 New Barn	226 Beck Rd.	Turn over to county
015-002	#48 P4 Storage Building	226 Beck Rd.	Turn over to county
Unsch	#49 Old Outreach School	131 Galvaston	To be demoed

031-001 #50 Celebration Church Code Upgrade		358 Foster Field	Complete	
Unsch	#51 Sky Restaurant	236 Foster Field	Complete	
035-001	#52 Fisher Stevens	43 Storehouse	Completed Roof, but wall has to be addressed	
033-001	#53 Reliant Field Services	112 Corpus Christi	Complete	
030-001	#54 Townsend Remodeling	470 Foster Field	Complete	
	#55	339 Foster Field	Turn over to county	
025-001	01 #56 LDS Builders 396		Complete	
034-001	#57 Straight Arrow Archery Roof	60 Storehouse	Complete	
032-001	#58 Dorm 1 Celebration Church	292 Foster Field	Complete	
Unsch	#59 Fire Marshall's Storage	354 Hangar	Boarded 2 windows up	
Unsch	#60 Vacant Building Code Upgrade	479 Waco Circle	Complete	
Unsch	#61 Old Golden Crescent	568 Waco Circle	To be demoed	
Unsch	#62 Texas Mile Warehouse	131 Hangar	Complete	
Unsch	#63 Condemned Warehouse H&H Door	158 Hangar	To be demoed	
Unsch	#64 Civil Air Patrol	381 Hangar	To be demoed	
Unsch	#65 Old Brig	153 Corpus Christi	To be demoed	
	#66 Old Dorm 2 Building Code Upgrade	294 Foster Field	To be demoed	

# Victoria County 4H Activity Center Building #31 on Virtus Progress Report

Summary for invoices for details- Previously billed \$5,238.23 Balance owed \$1903.48

Ext/South Elevation item 1830

Interior womens items 1831-1851

Hallway items 1852-1860



8380 Warren Parkway – Suite 700 Frisco, TX 75034

4/3/18

Ms. Joyce Dean
Director of Administrative Services
County of Victoria
115 N. Bridge, Room 213
Victoria, Texas 77904

RE:

Airport Maintenance - INS ID 020-002

609 Foster Field Rd

## **PROPOSAL**

#### Roof Repair - Coating (Option 1):

Clean existing roof and apply 2 coats Gaco Silicone coating to upper and lower flat roofs and roof penetrations.

\$34,200

#### Roof Repair - Overlay TPO (Option 2)

Install 68 SQ of 1" Poly-ISO board and 60mil TPO roof membrane over existing Built-up Roof on Upper roof field. Install new edge metal and accessories.

\$35,750

Install 65 SQ of 1" Poly-ISO board and 60mil TPO roof membrane over existing Built-up Roof on Lower roof field. Install new edge metal and accessories.

\$34,100

Respectfully submitted, Shawn Jernigan 214-551-1606

Corporate Office: 13725 S. Mur-Len Rd, Olathe, KS 66062

# Victoria County 133 Airplane Hangar Building #15 on Virtus Progress Report

Summary for invoices for details- Previously billed \$75,522.10 Balance due \$29,187.37

Items 542-618

Items 660-665

Items 676-679

Items 688-718

### Victoria County Justice Center Building #14 on Virtus Progress Report

Summary for invoices for details-Previously Billed \$25,089.11 Balance \$9310.40 for deprec

Patrol office-items 388-401

Conf room items 402-417

Valdez office items 418-431

Classroom items 432-445

Capt Canfield's office items 446-460

Jones' office items 461-474

Restroom items 475-490

Chief Deputy Boyd's office items 491-503

Sheriff O'Connor's office items 504-515

Courts items 516-517

Records Room items 518-530

Dispatcher's office items 531-537





Change order for removing the windows on the east and west sides of the FBO Building and replace with R panel sheets and fiberglass side lights.

\$22,220.00

Victoria	County	Representative	

Date



# Victoria County

ID	an and appear	Building # and Name	Address	Comments
013-001	No	#1 Old Jail	206 Constitution	
002-001	NO	#2 Old Courthouse	101 N. Bridge	
002-001	NO	#3 Old Courthouse Tunnel		
001-001	•	#4 New Courthouse	115 N. Bridge	Still Waiting on approval from Kelly for additional \$7263.01
014-001	***************************************	#5 Old Fire Station	209 W. Forrest	- 1
012-001	No	#6 PCT 1 Machine Storage	2000 FM 1686	
009-001	NO	#7 PCT 3 Machine Storage	133 Aloe Field	-14-
009-004	MO	#8 PCT 3 Radio Tower	133 Aloe Field	
009-002	No	#9 PCT 3 Mechanic Shop	133 Aloe Field	
009-003	NO	#10 Service Center Cover	133 Aloe Field	
018-004	NO	#11 PCT 2 Truck Storage	3323 Nursery	
002-007	NO	#12 Park Metal Storage	500 Fordyce Rd.	
022-002	NO	#13 Park Comfort Station	500 Fordyce Rd.	

004-001 404,	#14 New Jail	101 N. Glass	(Int france)
020-008	#15 Airplane Hangar		542- 618 660-665
463	(code upgrade)		676-679 688-718
020-014	#16 Airplane Hangar (FBO)	437 S. Hangar Dr.	725-750 755-886 751-753 886-951
020-013	#17 Airplane Hangar B	305 S. Hangar Dr.	
020-015	#18 Airplane Hangar C	207 Storehouse Drive	To be demoed
019-001	#19 PCT 4 Truck Storage	155 Corpus Christi	To be demoed
015-001	#20 PCT 4 Building	155 Corpus Christi	To be demoed
020-011 465	#21 Airplane Hangar (T-Hangar Units)	348 N. Hangar Dr.	1205-1219
020-010	#22 Aircraft Storage (T-Hangar Units)	388 N. Hangar Dr.	1225-1230
007-001	#23 Office Elections & JP 3	111 N. Glass	
020-004 020-006	#24 Airport Terminal 2 Storage Buildings Code Upgrade	609 Foster	To be demoed to
020-003 405	#25 Airport Maintenance w/ Generator	41 Hangar	1292-1410
003-001	#26 SWB Building Bridge St. Annex	204 N. Bridge	
024-001	#27 Extension Service	528 Waco Circle	Change order???
026-001	#28 Juvenile Detention Center	97 Foster Field	
027-002	#29 Modular Building Highway Patrol	ND	
010-001 NO	#30 Health Department	2805 Navarro	Complete
016-001	#31 4-H Activity Center	259 Bachelor Drive	1830-1860

Caloret Which Roof? Pire Station

020-005	40,5	#32 Fire Marshal Office TSA	25 & 27 Hangar Dr.	1863-1926
006-001	Tres	#33 Officers Club	333 Bachelor Dr.	1929-1937 Rof DO
023-001	NO	#34 Victoria Well Service	169 Aviation Dr.	
029-001	ues	#35 COMAT Building Code Upgrade	442 Foster Dr.	2148-2164 RUCIF - VAL X2
028-001	NO	#36 Animal Shelter	102 Perimeter	
027-001	NO	#37 Weigh Station Scales	HWY 59 N.	
005-001	NO	#38 Storehouse	103 S. Glass	
020-007	UCS	#39 AARFF Fire Station	121 N. Hangar	2564-2567 2569
020-009	NO	#40 Hangar	390 N. Hangar Dr.	
020-012	425	#41 Control Tower/ Airport	348 Bachelor Dr.	
012-002	No	#42 PCT 1 Pole Barn Storage	16043 FM 1686	
008-001	ND	#43 Hartman JP 1		
008-002	NO	#44 Hartman Building	901 E. Pecan	
017-001	NO	#45 JP 4 Building	2604 E. Mockingbird	
017-999	yes	JP 4 Wood Fence		Wood Fence
	No	#46 JP2 Building	4407 Lilac	
015-001	No	#47 PCT4 New Barn	226 Beck Rd.	
015-002	No	#48 P4 Storage Building	226 Beck Rd.	
Unsch	NO	#49 Old Outreach School	131 Galvaston	To be demoed
031-001		#50 Celebration Church Code Upgrade	358 Foster Field	2641-2670 2671-2677???
Unsch	_	#51 Sky Restaurant	236 Foster Field	Complete
		SI	ppenent	

	•			
			Structure not	Troed UP 1
035-001	yes	#52 Fisher Stevens	43 Storehouse	2754-2759
033-001	425	#53 Reliant Field V	112 Corpus Christi	2780-2787 CONNICTOR
030-001	465	#54 Townsend Remodeling	470 Foster Field	2792-2797
	No	#55	339 Foster Field	
025-001	yes	#56 LDS Builders	396 Foster Field	2817-2838 2839-2846???
034-001		#57 Straight Arrow Archery Roof	60 Storehouse	Change order
032-001	413	#58 Dorm 1 Celebration Church	292 Foster Field	2869-2873
Unsch	ND	#59 Fire Marshall's Storage	354 Hangar	Board up window
Unsch	yes	#60 Vacant Building Code Upgrade	479 Waco Circle	2882-2897
Unsch	No	#61 Old Golden Crescent	568 Waco Circle	To be demoed
Unsch	443	#62 Texas Mile Warehouse	131 Hangar & Panel Roof Jacks, Awain	2923-2937
Unsch	fence	#63 Condemned Warehouse H&H Door	158 Hangar	To be demoed
Unsch	Dem	#64 Civil Air Patrol	381 Hangar	To be demoed L
Unsch	Demo	#65 Old Brig	153 Corpus Christi	To be demoed $\checkmark$
	Den	#66 Old Dorm 2 Building Code Upgrade	294 Foster Field	To be demoed /



Provide Detens on invaces
Supplicaprec

						_		
	ID	<b>Building Description</b>		oject Value	Previously Invoiced	N	Net Invoice Due	
	004-001	Victoria County Justice Center	\$	34,399.51	(25,089.11)	\$	· 9,310.40 Defre	
	006-001	Officers Club	\$	65,918.82	(26,318.64)	)\$	39,600.18	
M	016-001	4-H Activity Center	\$	7,141.71	(5,238.23)	\$	1,903.48 Def	
X	020-001	Airport Terminal	\$	18,898.45	0.00		(18898.95)	
	020-002	Maintenance/Fire Station	\$	56,187.58	0.00	\$	56,187.58 - need full des	
)	020-005	Fire Marshall/TSA Office	\$	13,030.46	(9,377.07)	\$	3,653.39 Defle	
The state of	020-007	ARFF Fire Station	\$	28,774.33	0.00		28,774.33	
	020-008	133 Airplane Hangar	\$	104,709.47	(75,522.10)	-	29,187.37 Suppl. / De pro	
	020-010	388 Airplane Hangar	\$	162,958.15	0.00		162,958.15 Backyp	
	020-011	348 Airplane Hangar(Small T)	\$	18,828.81	(13,730.72)		5,098.09 Depre.	
	020-012	Airport Control Tower	\$	37,258.62	0.00		37,258.62	
	020-013	305 Airplane Hangar	\$	16,080.56	(11,867.30)	-	4,213.26 Depreciation	
	020-014	437 Airplane Hangar	\$	145,909.42	(79,543.00)		66,366.42	
	029-001	U Of H Storage Building (Leased)	\$	37,121.70	0.00		37,121.70	
	024-001	Extension Office		107,341.93	(47,798.42)		59,543.51 SUPP/DED-	
	030-001	VRS Building (Leased)	\$	16,440.45	(5,667.63)		10,772.82 need know	
	034-001	Straight Arrow	\$	3,096.12	0.00		3,096.12 Back	
	035-001	Fisher Stevens Warehouse	\$		ON UPDATED!		E 47 1.NJ	
	Unsch	479 Waco Rd Ros Detrus	\$	44,769.53	send to Key	- 64	44,769.53	
	Unsch	H&H Door		45,178.42	(11,365.87)		33,812.55	
		Sky Restaurant Supple	\$	69,153.70	(37,658.52)		31,495.18	
	Unsch	Texas Mile Warehouse	\$	19,799.84	0.00		19,799.84 Octal In	
	CHANGE	ORDERS -					11	
Q	020-002	Maintenance/Fire Station	\$	34,200.00		\$	34,200.00 Charel	
Par	024-001	Extension (Replace Door unit)				\$	and the same	
0	024-001	Extension Building Windows	\$1	31,548.00	(31,548.00)	- \$	- crex	
ole	024-001	Extenion Building - Blinds C.O					•	
-	020-013	Hangar B - Change Order	\$	<b>∠</b> 68,686.00	(68,686.00)	1\$	, -	
	• 029-008	133 Hangar		68,686.00				
	029-008	FBO - Window Change Order	\$	22,220.00				
	029-008	FBO - TPO layover CO						
	029-008	FBO - Beam Change Order	\$	<b>√</b> 5,100.00	\$ (5,100.00)	\$	. =	
Ner	006-001	Officers Club - Decking C.O.						
- 4					(800 E31 00)	ċ		
8		Building Demolition	\$	800,531.00	(800,531.00)	>	-	

**Net Total Payment Due** 

\$

852,078.05

# Virtus

# **Virtus Group**

8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

Client:

Victoria County Texas

Property:

As shown on Schedule of Locations

Victoria, TX 77901

Operator:

A.FARNSW

Estimator:

Andy Farnsworth

Position:

Project Consultant/ Mgr.

Company:

Virtus Group

**Business:** 

8380 Warren Parkway, Suite 700

Frisco, TX 75034

Type of Estimate:

Hurricane

Date Entered:

10/1/2017

Date Assigned:

Cellular: (501) 247-4815

com

a.farnsworth@thevirtusteam.

E-mail:

Price List:

TXVC8X\_OCT17

Labor Efficiency:

Restoration/Service/Remodel

Estimate:

**VICTORYCOSUB** 

THIS ESTIMATE IS PRELIMINARY ONLY AND SUBJECT TO REVISION AND APPROVAL BY TEXAS ASSOCIATION OF COUNTIES RISK MANAGEMENT POOL.





> VICTORYCOSUB Building 1- Old Jail Ground level



**Homeland Security** 

Height: 8' 8"

482.74 SF Walls 672.74 SF Walls & Ceiling 21.11 SY Flooring 55.67 LF Ceil. Perimeter 190.00 SF Ceiling 190.00 SF Floor 55.67 LF Floor Perimeter

Window Window Door Window 3' X 6' 2 1/16" 3' X 6' 2 1/16" 3' X 6' 8" 3' X 6' 2 1/16" Opens into Exterior
Opens into Exterior
Opens into COPY\_ROOM
Opens into Exterior

REPLACE DESCRIPTION QTY RESET REMOVE TAX TOTAL 1. Carpet 218.50 SF 0.00 2.32 0.00 506.92 15 % waste added for Carpet. 0.00 0.42 0.00 79.80 2. Carpet pad 190.00 SF 3. Tackless strip - per LF 55.67 LF 0.00 0.37 0.00 20.60 4. Cove base molding - rubber or 55.67 LF 0.00 1.37 0.00 76.27 vinyl, 4" high 5. Contents - move out then reset -1.00 EA 0.00 84.56 0.00 84.56 Extra large room 6. Final cleaning - construction -190.00 SF 0.00 0.11 0.00 20.90 Commercial

Totals: Homeland Security

789.05

0.00

FOR THIS
COPY

E- These
ARE NOT
County - In

ACTICO

12/13/2017

Page: 2

**VICTORYCOSUB** 



					eight: 8' 8"	
562.33	SF Walls		286.76 S	F Ceiling		
849.09	SF Walls & Ce	iling	286.76 S	F Floor		
31.86	SY Flooring		64.84 L	F Floor Perime	eter	
64.84	LF Ceil. Perim	eter				
3' X (	5' 8"		Opens into HOMEL	AND_SEC		
4' 4 1/16" X 8' 8 1/16"			Opens into HALLWAY_2			
1'49	/16" X 8' 8 1/1	6"	Opens into HALLWA	AY_2		
3' X	5' 8"		Opens into OFFICE_	_1		
3' X	6' 8"		Opens into JOES_OI	FFICE		
3' X	6' 2 1/16"		<b>Opens into Exterior</b>			
3' X	6' 8"		<b>Opens into Exterior</b>			
3' X	6' 2 1/16"	/	Opens into Exterior			
QTY	RESET	REMOVE	REPLACE	TAX	TOTAL	
	849.09 31.86 64.84 3' X ( 4' 4 1 1' 4 9 3' X ( 3' X ( 3' X (	849.09 SF Walls & Ce 31.86 SY Flooring 64.84 LF Ceil. Perime  3' X 6' 8"  4' 4 1/16" X 8' 8 1/16  1' 4 9/16" X 8' 8 1/16  3' X 6' 8"  3' X 6' 8"  3' X 6' 8"  3' X 6' 2 1/16"  QTY RESET	849.09 SF Walls & Ceiling 31.86 SY Flooring 64.84 LF Ceil. Perimeter  3' X 6' 8" 4' 4 1/16" X 8' 8 1/16" 1' 4 9/16" X 8' 8 1/16" 3' X 6' 8" 3' X 6' 8" 3' X 6' 2 1/16"  QTY RESET REMOVE	849.09 SF Walls & Ceiling 31.86 SY Flooring 64.84 LF Ceil. Perimeter  3' X 6' 8" 4' 4 1/16" X 8' 8 1/16" 1' 4 9/16" X 8' 8 1/16" 3' X 6' 8" Opens into HALLW 3' X 6' 8" Opens into OFFICE 3' X 6' 8" Opens into Exterior 3' X 6' 2 1/16" Opens into Exterior	286.76 SF Floor   31.86 SY Flooring   64.84 LF Floor Perime   64.84 LF Ceil. Perimeter   64.84 LF Floor Perime   64.84 LF Ceil. Perimeter   64.84 LF Floor Perime   64.84 LF	


DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
7. Suspended ceiling system - 2' x 4'	286.76 SF		0.00	2.24	0.00	642.34
Detach & Reset Fluorescent - acoustic grid fixture - four tube, 2'x 4'	4.00 EA	60.04	0.00	0.00	0.00	240.16
9. Carpet	329.78 SF		0.00	2.32	0.00	765.09
15 % waste added for Carpet.		/				
10. Carpet pad	286.76 SF	/	0.00	0.42	0.00	120.44
11. Tackless strip - per LF	64.84 LF		0.00	0.37	0.00	23.99
12. Cove base molding - rubber or vinyl, 4" high	64.84 LF		0.00	1.37	0.00	88.83
13. Contents - move out then reset - Extra large room	1.00 EA		0.00	84.56	0.00	84.56
14. Final cleaning - construction - Commercial	286.76 SF		0.00	0.11	0.00	31.54
Teals Com Boom					0.00	1 006 05

Totals: Copy Room 0.00 1,996.95





11' 6" 3' 1' 7"	oe's Office				H	leight: 8' 8'	
-6.9°	517.60	SF Walls		222.41	SF Ceiling		
Joe's Office	740.02	SF Walls & Co	eiling	222.41	SF Floor		
5 5 5 5 5 5 5 5 5 5 5 5 5 5 5 5 5 5 5	24.71	SY Flooring		59.69 1	LF Floor Perim	eter	
50 28 43 5 5 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	59.69	LF Ceil. Perim	eter				
Door	3' X	3' X 6' 8"		Opens into COPY_ROOM			
Door	2' 6"	2' 6" X 6' 8"		Opens into CLOSET_1			
Door	2' 8 1	2' 8 1/16" X 6' 8"		Opens into TOILET	_1		
Window	3' X	3' X 6' 2 1/16"		Opens into Exterior			
Window	3' X	6' 2 1/16"		Opens into Exterior			
Window	3' X	6' 2 1/16"		Opens into Exterior			
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL	
15. Carpet	255.77 SF	1	0.00	2.32	0.00	593.39	
15 % waste added for Carpet.							
16. Carpet pad	222.41 SF		0.00	0.42	0.00	93.41	
7. Tackless strip - per LF	59.69 LF		0.00	0.37	0.00	22.09	
18. Cove base molding - rubber or vinyl, 4" high	59.69 LF		0.00	1.37	0.00	81.78	
19. Contents - move out then reset - Extra large room	1.00 EA		0.00	84.56	0.00	84.56	
20. Final cleaning - construction - Commercial	222.41 SF		0.00	0.11	0.00	24.47	
Totals: Joe's Office		1			0.00	899.70	



Closet 1

98.37 SF Walls 106.30 SF Walls & Ceiling 0.88 SY Flooring 11.34 LF Ceil. Perimeter

alls 7.93 SF Ceiling
alls & Ceiling 7.93 SF Floor
coring 11.34 LF Floor Perimeter

Height: 8' 8"

Door 2' 6" X 6' 8" Opens into JOES\_OFFICE


DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
21. Carpet	9.12 SF		0.00	2.32	0.00	21.16
15 % waste added for Carpet.						
2. Carpet pad	7.93 SF		0.00	0.42	0.00	3.33



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### **CONTINUED - Closet 1**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
23. Tackless strip - per LF	11.34 LF		0.00	0.37	0.00	4.20
24. Cove base molding - rubber or vinyl, 4" high	11.34 LF		0.00	1.37	0.00	15.54
25. Final cleaning - construction - Commercial	7.93 SF		0.00	0.11	0.00	0.87
Totals: Closet 1					0.00	45.10



Toilet 1 Height: 8' 8"

239.83 SF Walls 285.12 SF Walls & Ceiling 5.03 SY Flooring

45.29 SF Floor 27.66 LF Floor Perimeter

45.29 SF Ceiling

27.66 LF Ceil. Perimeter

Door Door 2' 8 1/16" X 6' 8" 2' 8 1/16" X 6' 8"

Opens into OFFICE\_1
Opens into JOES\_OFFICE

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
26. Final cleaning - construction - Commercial	45.29 SF		0.00	0.11	0.00	4.98
Totals: Toilet 1					0.00	4.98



Office 1 Height: 8' 8"

608.35 SF Walls
233.17 SF Ceiling
841.52 SF Walls & Ceiling
25.91 SY Flooring
70.15 LF Ceil. Perimeter

Door 3' X 6' 8"

Window 3' X 6' 2 1/16"

Window 3' X 6' 2 1/16"

Door 2' 8 1/16" X 6' 8"

Door 2' 6" X 6' 8"

Opens into COPY\_ROOM
Opens into Exterior
Opens into Exterior
Opens into TOILET\_1
Opens into CLOSET\_2

 DESCRIPTION
 QTY
 RESET
 REMOVE
 REPLACE
 TAX
 TOTAL


 7. Carpet
 268.15 SF
 0.00
 2.32
 0.00
 622.11





#### **CONTINUED - Office 1**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
15 % waste added for Carp						
28. Carpet pad	233.17 SF		0.00	0.42	0.00	97.93
29. Tackless strip - per LF	70.15 LF		0.00	0.37	0.00	25.96
30. Cove base molding - rubber or vinyl, 4" high	70.15 LF		0.00	1.37	0.00	96.11
31. Contents - move out then reset - Extra large room	1.00 EA		0.00	84.56	0.00	84.56
32. Final cleaning - construction - Commercial	233.17 SF		0.00	0.11	0.00	25.65
Totals: Office 1					0.00	952.32




Closet 2 Height: 8' 8"

98.37 SF Walls 106.30 SF Walls & Ceiling 0.88 SY Flooring 11.34 LF Ceil, Perimeter 7.93 SF Ceiling7.93 SF Floor11.34 LF Floor Perimeter

2' 6" X 6' 8" Opens into OFFICE\_1 Door QTY REMOVE REPLACE TAX TOTAL DESCRIPTION RESET 2.32 9.12 SF 0.00 0.00 21.16 33. Carpet 15 % waste added for Carpet. 7.93 SF 0.00 0.42 0.00 3.33 34. Carpet pad 35. Tackless strip - per LF 11.34 LF 0.00 0.37 0.00 4.20 0.00 1.37 0.00 15.54 36. Cove base molding - rubber or 11.34 LF vinyl, 4" high 37. Final cleaning - construction -7.93 SF 0.00 0.11 0.00 0.87 Commercial 45.10 Totals: Closet 2 0.00







Hallway 2 158.24 SF Walls 36.93 SF Ceiling 36.93 SF Floor 195.17 SF Walls & Ceiling

4.10 SY Flooring 20.55 LF Ceil. Perimeter

17.55 LF Floor Perimeter

Opens into KITCHEN\_HALL

Opens into NORTH\_HALL

Height: 8' 8"


Missing Wall - Goes to Floor

**Missing Wall** 

3' X 6' 8" 3' X 6' 8" Door 2' 6" X 6' 8" Door **Missing Wall** 

**Opens into DATA** 1' 4 9/16" X 8' 8 1/16" Opens into COPY\_ROOM 4' 4 1/16" X 8' 8 1/16" Opens into COPY\_ROOM

DESCRIPTION QTY RESET REMOVE REPLACE TAX TOTAL 38. Suspended ceiling tile - 2' x 4' 36.93 SF 0.00 1.22 0.00 45.05 Totals: Hallway 2 0.00 45.05




**Toilet** Height: 8' 7"


> 187.38 SF Walls 216.99 SF Walls & Ceiling 3.29 SY Flooring 21.84 LF Ceil. Perimeter


29.61 SF Ceiling 29.61 SF Floor 21.84 LF Floor Perimeter

Door 3' X 6' 8" **Opens into ENTRY** 

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
39. Final cleaning - construction - Commercial	29.61 SF		0.00	0.11	0.00	3.26
Totals: Toilet	/				0.00	3.26

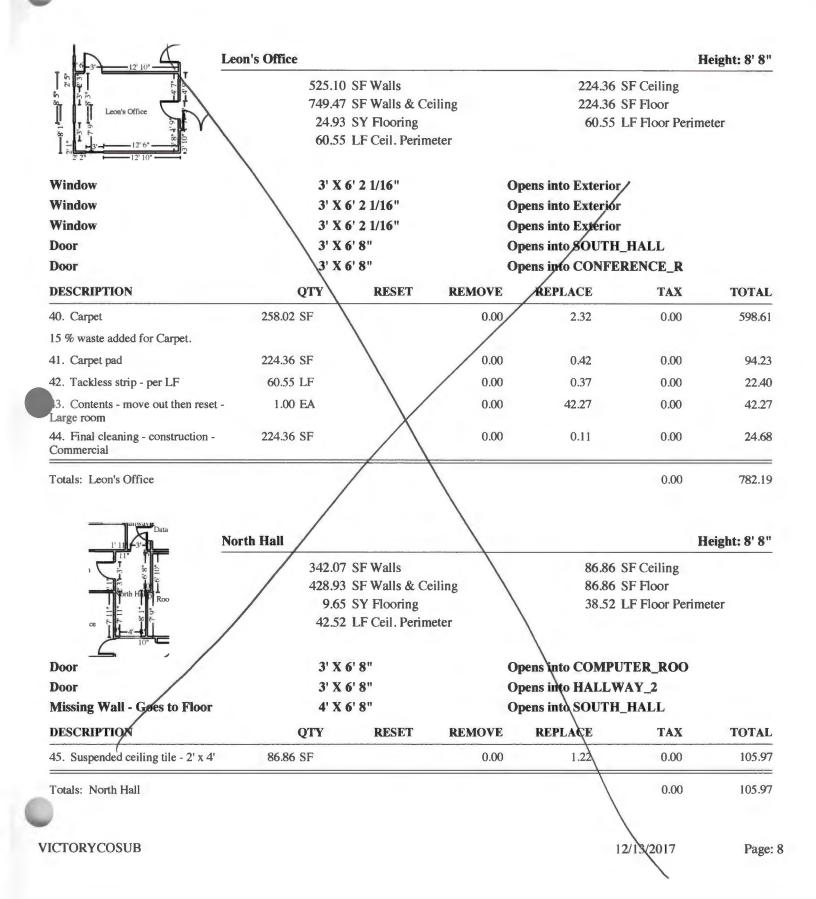



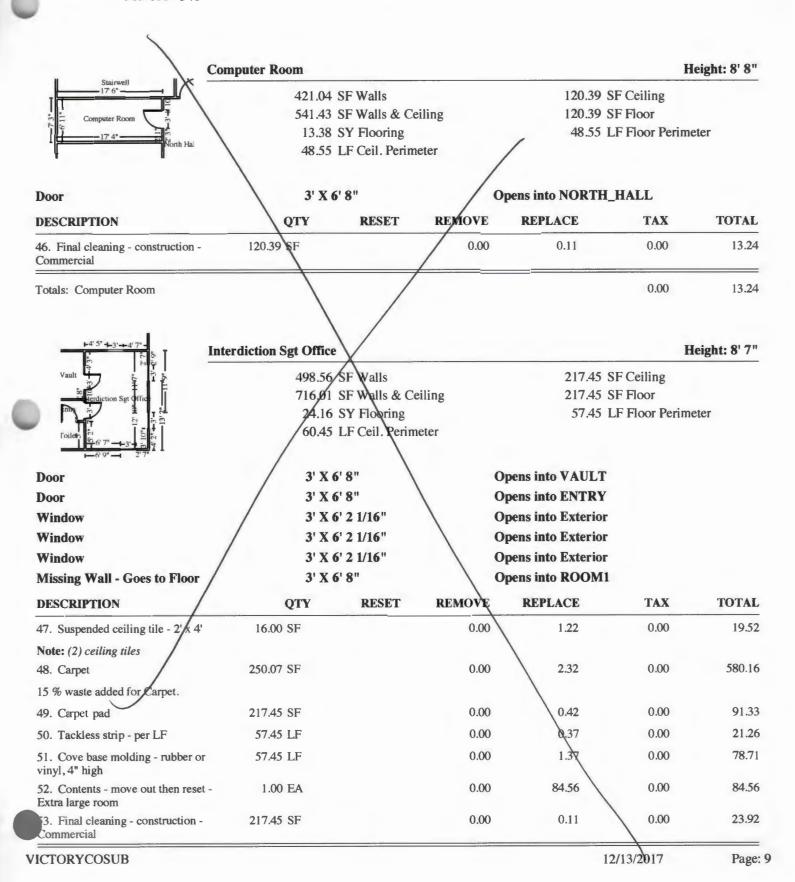

**VICTORYCOSUB** 

8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### **CONTINUED - Interdiction Sgt Office**


DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Totals: Interdiction Sgt Office					0.00	899.4
Stairw	vell			,		Height: 8' 8
Kitchen Hall	390.39	SF Walls		86.79	SF Ceiling	
12' 2" 3' 2" 4 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2		SF Walls & Ce	eiling	/	SF Floor	
17.4		SY Flooring LF Ceil. Perim	eter	44.19	LF Floor Per	rimeter
Missing Wall - Goes to Floor	3' 7"	X 6' 8"	ø	pens into KITCHI	EN_HALL	
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
54. Final cleaning - construction - Commercial	86.79 SF		0.00	0.11	0.00	9.5.
Totals: Stairwell					0.00	9.5
South	Hall				AR 851	Height: 8' 7
.6.11.11.11.10.10.10.10.10.10.10.10.10.10.		SF Walls			SF Ceiling	
Some and the second of the sec	786.51 23.11	SF Walls & Co SY Flooring LF Ceil. Perim		207.96	SF Ceiling SF Floor LF Floor Per	rimeter
Door	786.51 23.11	SF Walls & Co SY Flooring LF Ceil. Perim	eter	207.96	SF Floor LF Floor Per	rimeter
	786.51 23.11 72.89	SF Walls & Co SY Flooring LF Ceil. Perim	eter	207.96 5 65.89 1	SF Floor LF Floor Per	rimeter
Door	786.51 23.11 72.89 3' X 6	SF Walls & Co SY Flooring LF Ceil. Perim	o o	207.96 (65.89 ) pens into CONFE	SF Floor LF Floor Per RENCE_R OFFIC	rimeter
Door Door	786.51 23.11 72.89 3' X 6	SF Walls & Ce SY Flooring LF Ceil. Perim 6' 8" 6' 8" " X 6' 8"	0 0 0	207.96 3 65.89 1 pens into CONFEI pens into LEONS_	SF Floor LF Floor Per RENCE_R OFFIC	rimeter
Door Door Missing Wall - Goes to Floor	786.51 23.11 72.89 3' X ( 3' X ( 2' 11 3' X ( 3' X (	SF Walls & Ce SY Flooring LF Ceil. Perim 6' 8" " X 6' 8" 6' 8"	0 0 0 0	pens into CONFEI pens into LEONS_ pens into Exterior pens into Exterior pens into ENTRY	SF Floor LF Floor Per RENCE_R OFFIC	rimeter
Door Door Missing Wall - Goes to Floor Door	3' X 6 3' X 6 3' X 6 2' 11 3' X 6 3' X 6	SF Walls & Ce SY Flooring LF Ceil. Perim 6' 8" 6' 8" 6' 8" 6' 8" 6' 8"	0 0 0 0	pens into CONFEI pens into LEONS_ pens into Exterior pens into Exterior pens into Exterior pens into ENTRY pens into ROOM1	SF Floor LF Floor Per RENCE_R OFFIC	rimeter
Door Door Missing Wall - Goes to Floor Door Window	3' X 6 3' X 6 2' 11 3' X 6 3' X 6 3' X 6 3' X 8	SF Walls & Ce SY Flooring LF Ceil. Perim 6' 8" " X 6' 8" 6' 8" 6' 8" 6' 8"	0 0 0 0	pens into CONFEI pens into LEONS_ pens into Exterior pens into Exterior pens into ENTRY pens into ROOM1	SF Floor LF Floor Per RENCE_R OFFIC	rimeter
Door Door Missing Wall - Goes to Floor Door Window Window	3' X 6 3' X 6 3' X 6 2' 11 3' X 6 3' X 6 3' X 6 3' X 8	SF Walls & Ce SY Flooring LF Ceil. Perim 6' 8" " X 6' 8" 6' 8" 6' 8" 6' 8" 6' 8"	0 0 0 0 0	pens into CONFEI pens into LEONS_ pens into Exterior pens into Exterior pens into ENTRY pens into ROOM1 pens into ROOM1	SF Floor LF Floor Per RENCE_R OFFIC	rimeter
Door Door Missing Wall - Goes to Floor Door Window Window Window	3' X 6 3' X 6 3' X 6 2' 11 3' X 6 3' X 6 3' X 8 3' X 8 3' X 8	SF Walls & Ce SY Flooring LF Ceil. Perim 6' 8" " X 6' 8" 6' 8" 6' 8" 6' 8" 3' 3' 3'	0 0 0 0 0	pens into CONFEI pens into LEONS pens into Exterior pens into Exterior pens into ENTRY pens into ROOM1 pens into ROOM1 pens into ROOM1	SF Floor LF Floor Per RENCE_R OFFIC	rimeter
Door Door Missing Wall - Goes to Floor Door Window Window Window Missing Wall - Goes to Floor	3' X 6 3' X 6 3' X 6 2' 11 3' X 6 3' X 6 3' X 6 3' X 8 3' X 8 3' X 8 4' X 6	SF Walls & Ce SY Flooring LF Ceil. Perim 6' 8" 6' 8" " X 6' 8" 6' 8" 6' 8" 6' 8" 3' 3' 3' 6' 8"	0 0 0 0 0 0	pens into CONFEI pens into LEONS pens into Exterior pens into Exterior pens into ENTRY pens into ROOM1	SF Floor LF Floor Per RENCE_R OFFIC	rimeter
Door Door Door Missing Wall - Goes to Floor Door Window Window Window Missing Wall - Goes to Floor Door	3' X 6 3' X 6 3' X 6 2' 11 3' X 6 3' X 6 3' X 6 3' X 8 3' X 8 3' X 8 4' X 6	SF Walls & Ce SY Flooring LF Ceil. Perim 6' 8" " X 6' 8" 6' 8" 6' 8" 6' 8" 3' 3' 3'	0 0 0 0 0 0	pens into CONFEI pens into LEONS pens into Exterior pens into Exterior pens into ENTRY pens into ROOM1 pens into ROOM1 pens into ROOM1	SF Floor LF Floor Per RENCE_R OFFIC	rimeter

12/13/2017


Page: 10

7	CC	ONTINUED - S	South Hall			
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Totals: South Hall					0.00	19.52
Entry Entry					Н	leight: 8' 7'
to linter		SF Walls			SF Ceiling	
Entry 4" 18" 3' 4" 18"		SF Walls & Co	eiling		SF Floor LF Floor Perim	otor
Toilet		LF Ceil. Perin	neter	19.52	LF Floor Ferlin	etei
 Missing Wall - Goes to Floor	3' X	6' 8"	0	pens into SOUTH	HALL	
Door	3' X	6' 8"	0	pens into TOILET		
Door	3' X	6' 8"	6	pens into INTERI	DICTION	
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
56. Suspended ceiling tile - 2' x 4'  Note: (3) ceiling tiles	24.00 SF		0.00	1.22	0.00	29.28
Totals: Entry			\		0.00	29.28
Kitch	en Hall	/			I	leight: 8' 8"
7' 5'	145/36	SF Walls		27.12	SF Ceiling	
Kuchen Hall en	/	SF Walls & C	eiling \		SF Floor	
Stairwell	/	SY Flooring LF Ceil. Perin	neter	15.24	LF Floor Perim	eter
Door	/ 3' X	6' 8"	\0	pens into KITCH!	EN	
Missing Wall - Goes to Floor	3' 7"	X 6' 8"	\o	pens into STAIRV	VELL	
Missing Wall - Goes to Floor	3' X	6' 8"	þ	pens into HALLW	AY_2	
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
57. Final cleaning - construction - Commercial	27.12 SF		0.00	0.11	0.00	2.98
Totals: Kitchen Hall					0.00	2.98
r						



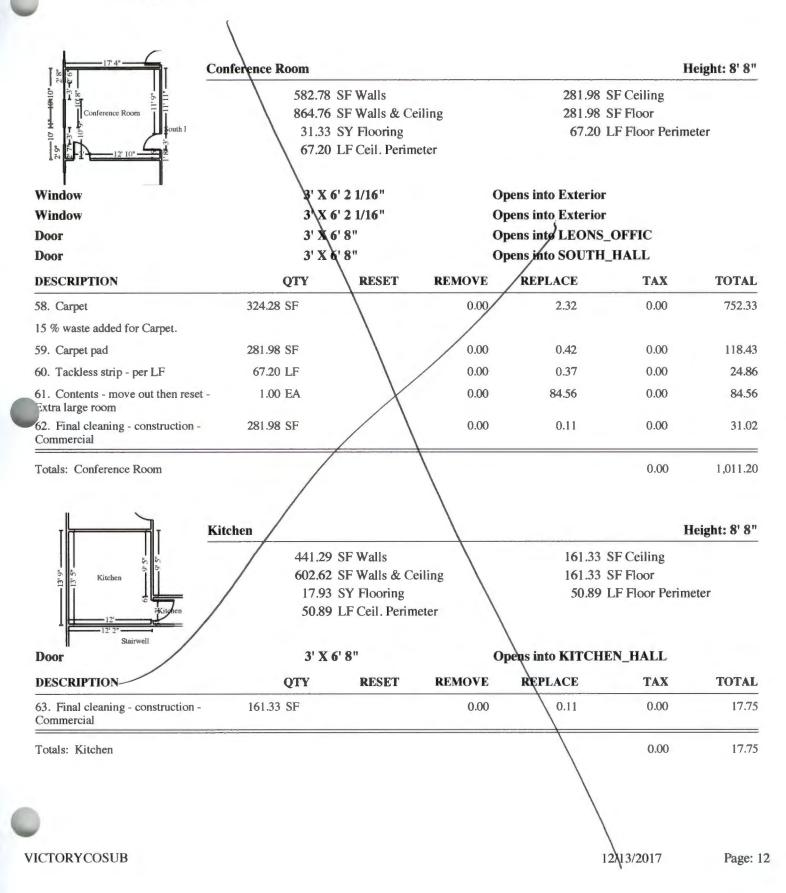



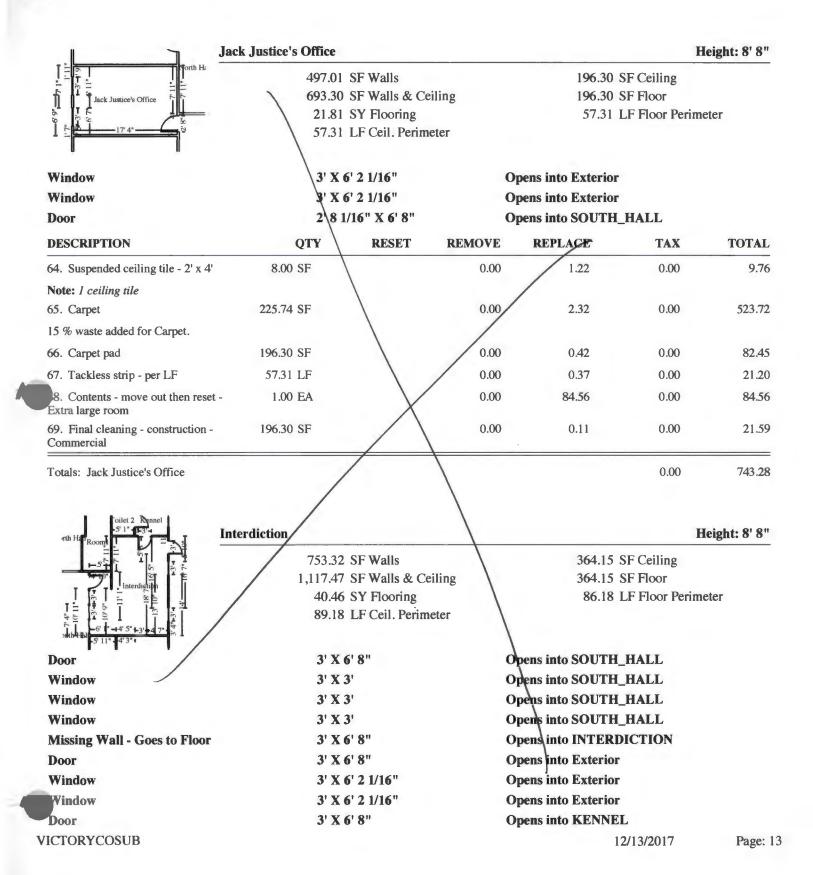





8380 Warren Parkway / Ste. 700 - Frisco, TX 75034

#### **CONTINUED - Interdiction**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
70. Suspended ceiling tile - 2' x 4'	16.00 SF	•	0.00	1.22	0.00	19.52
Note: (2) ceiling tiles						
71. Carpet	418.77 SF		0.00	2.32	0.00	971.55
15 % waste added for Carpet.				1		
72. Carpet pad	364.15 SF		0.00	0.42	0.00	152.94
73. Tackless strip - per LF	86 18 LF		0.00	0.37	0.00	31.89
74. Cove base molding - rubber or vinyl, 4" high	86.18 LF		0.00	1.37	0.00	118.07
75. Contents - move out then reset - Extra large room	1.00 EA		0.00	84.56	0.00	84.56
76. Final cleaning - construction - Commercial	364.15 SF	/	0.00	0.11	0.00	40.06
Totals: Interdiction					0.00	1,418.59

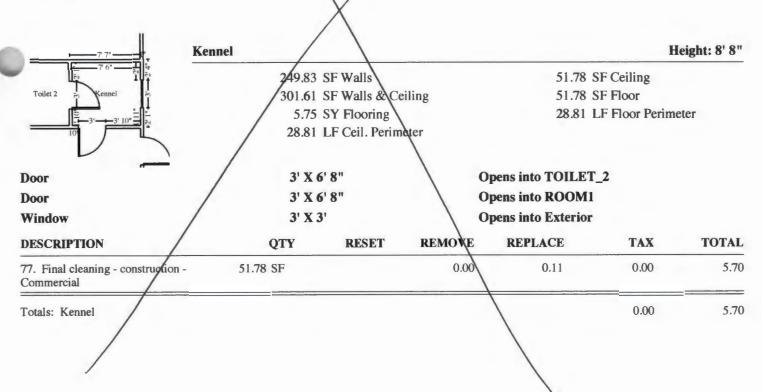



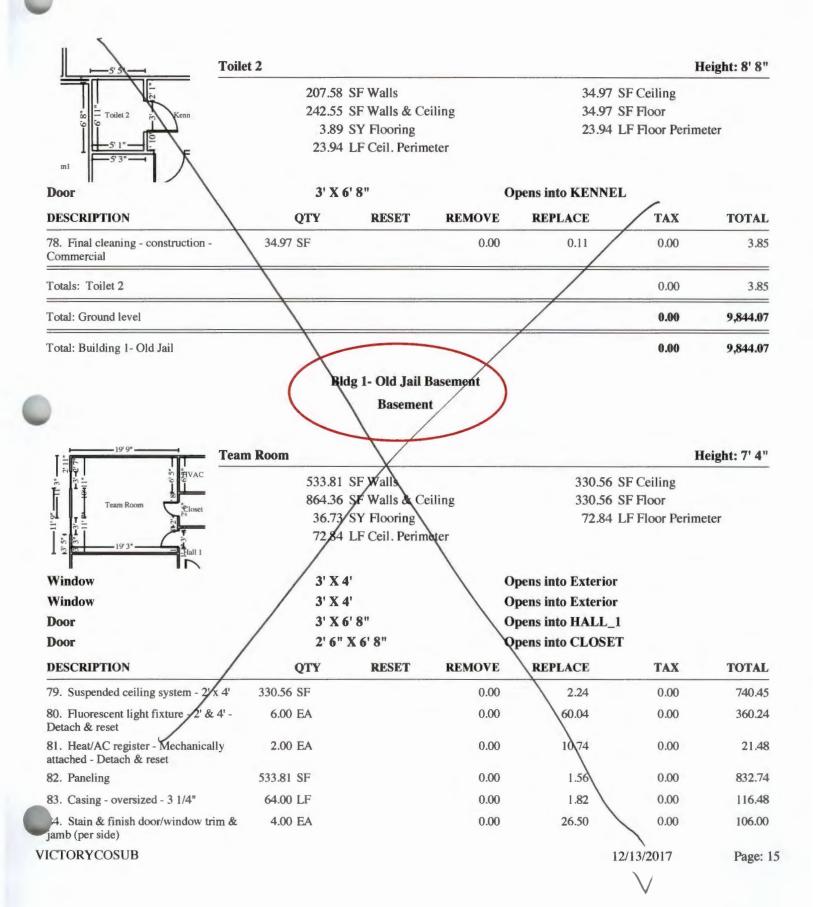



**VICTORYCOSUB** 

Virtus 8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
85. Cove base molding - rubber or rinyl, 4" high	72.84 LF		0.00	1.37	0.00	99.79
36. Contents - move out then reset -	1.00 EA		0.00	42.27	0.00	42.27
37. Final cleaning - construction - Commercial	330.56 SF		0.00	0.11	0.00	36.36
Note: All floor covering was removed prior	to this occurrence	2.				
Totals: Team Room				/	0.00	2,355.81
19 10* Storag	e 1				1	leight: 7' 4"
HVAC TO Storage 1		SF Walls & Ce	iling	331.90 S 331.90 S	SF Ceiling SF Floor	
12.1	36.88	SY Flooring		73.00 1	LF Floor Perim	eter
Hall 3. 79 44 6 4 3 4 3 9 5	/3.00	LF Ceil. Perim	eter			
Door	3' X	6' 8"	Or	ens into HVAC		
Window	3' X	4'	O	ens into Exterior		
Window	3' X	4'	OI	ens into Exterior		
Door	3' X	61 911	Or	ens into STORAC	CE 2	
DOOL		00/	/ 01		JE_4	
Door	3' X		\	ens into HALL_1		
			\			TOTAL
Door	3' X	6' 8'	O	oens into HALL_1	Į.	TOTAL 743.46
Door DESCRIPTION	3' X	6' 8'	O <sub>E</sub>	pens into HALL_1 REPLACE	TAX	
Door DESCRIPTION  88. Suspended ceiling system - 2' x 4'  39. Fluorescent light fixture - 2' & 4' -	3' X QTY 331.90 SF	6' 8'	REMOVE	REPLACE 2.24	TAX 0.00	743.46
Door  DESCRIPTION  38. Suspended ceiling system - 2' x 4'  39. Fluorescent light fixture - 2' & 4' - Detach & reset  90. Heat/AC register - Mechanically	3' X QTY 331.90 SF 6.00 EA	6' 8'	0.00 0.00	REPLACE 2.24 60.04	0.00 0.00	743.46 360.24
Door DESCRIPTION  38. Suspended ceiling system - 2' x 4' 39. Fluorescent light fixture - 2' & 4' - Detach & reset  90. Heat/AC register - Mechanically attached - Detach & reset	3' X QTY 331.90 SF 6.00 EA 2.00 EA	6' 8'	0.00 0.00 0.00	2.24 60.04 10.74	0.00 0.00 0.00	743.46 360.24 21.48
Door DESCRIPTION  38. Suspended ceiling system - 2' x 4' 39. Fluorescent light fixture - 2' & 4' - Detach & reset  90. Heat/AC register - Mechanically attached - Detach & reset  91. Paneling	3' X QTY 331.90 SF 6.00 EA 2.00 EA 534.95 SF	6' 8'	0.00 0.00 0.00 0.00	2.24 60.04 10.74 1.56	0.00 0.00 0.00 0.00	743.46 360.24 21.48 834.52
Door DESCRIPTION  88. Suspended ceiling system - 2' x 4' 89. Fluorescent light fixture - 2' & 4' - Detach & reset  90. Heat/AC register - Mechanically attached - Detach & reset  91. Paneling  92. Casing - oversized - 3 1/4"  93. Stain & finish door/window trim &	3' X QTY 331.90 SF 6.00 EA 2.00 EA 534.95 SF 82.00 LF	6' 8'	0.00 0.00 0.00 0.00 0.00	2.24 60.04 10.74 1.56 1.82	0.00 0.00 0.00 0.00 0.00	743.46 360.24 21.48 834.52 149.24
Door DESCRIPTION  38. Suspended ceiling system - 2' x 4' 39. Fluorescent light fixture - 2' & 4' - Detach & reset  90. Heat/AC register - Mechanically attached - Detach & reset  91. Paneling  92. Casing - oversized - 3 1/4"  93. Stain & finish door/window trim & Jamb (per side)  94. Cove base molding - rubber or	3' X QTY 331.90 SF 6.00 EA 2.00 EA 534.95 SF 82.00 LF 5.00 EA	6' 8'	0.00 0.00 0.00 0.00 0.00 0.00 0.00	2.24 60.04 10.74 1.56 1.82 26.50	0.00 0.00 0.00 0.00 0.00 0.00	743.46 360.24 21.48 834.52 149.24 132.50
Door DESCRIPTION  38. Suspended ceiling system - 2' x 4' 39. Fluorescent light fixture - 2' & 4' - Detach & reset  90. Heat/AC register - Mechanically attached - Detach & reset  91. Paneling  92. Casing - oversized - 3 1/4"  93. Stain & finish door/window trim & famb (per side)  94. Cove base molding - rubber or vinyl, 4" high  95. Contents - move out then reset -	3' X QTY 331.90 SF 6.00 EA 2.00 EA 534.95 SF 82.00 LF 5.00 EA 73.00 LF	6' 8'	0.00 0.00 0.00 0.00 0.00 0.00 0.00	2.24 60.04 10.74 1.56 1.82 26\50	0.00 0.00 0.00 0.00 0.00 0.00 0.00	743.46 360.24 21.48 834.52 149.24 132.50

12/13/2017

Page: 16





Hall 1 11" Sup	pply Room				H	leight: 7' 4'
22 4 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2	284.65	SF Walls		90.46	SF Ceiling	
Supply Room	375.11	SF Walls & Cei	ling	90.46	SF Floor	
		SY Flooring		38.84	LF Floor Perim	eter
8'3"	38.84	LF Ceil. Perime	eter			
Door	3' X	6' 8"	0	pens into HALLW	AY	
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTA
97. Suspended ceiling system - 2' x 4'	90.46 SF		0.00	2.24	0.00	202.6
98. Fluorescent light fixture - 2' & 4' - Detach & reset	1.00 EA		0.00	60.04	0.00	60.0
99. Light diffusing panel (i.e., cracked ice)	8.00 SF		0.00	1.43	0.00	11.4
100. Switch	1.00 EX		9.60	11.94	0.00	11.9
101. Paneling	284.65 SF		0.00	1.56	0.00	444.0
102. Casing - oversized - 3 1/4"	18.00 LF		0.00	1.82	0.00	32.7
103. Paint door/window trim & jamb - coats (per side)	1.00 EA		0.00	20.22	0.00	20.2
104. Vinyl tile	90.46 SF	\ /	0.00	2.51	0.00	227.0
105. Floor preparation for resilient flooring	90.46 SF		0.00	0.34	0.00	30.7
106. Clean floor, strip & wax	90.46 SF	$\wedge$	0.00	0.54	0.00	48.8
107. Cove base molding - rubber or vinyl, 4" high	38.84 LF		0.00	1.37	0.00	53.2
108. Final cleaning - construction - Commercial	90.46 SF	/	0.00	0.11	0.00	9.9
Totals: Supply Room					0.00	1,152.9
Sta						Ieight: 7' 4
H446. 3. +3. 61	orage 2					reight. / -
	/	SF Walls SF Walls & Ce	ilina	\	SF Ceiling SF Floor	
xom Storage 2	/	SY Flooring	iiiig	\	LF Floor Perim	eter
4'3'-42'9" -3'-7" 1	/	3 LF Ceil. Perimo	eter	\		
Door /	3' X	6' 8"	0	pens into STORA	GE 1	
Window	3' X			pens into Exterior		
Door		6' 8"		pens into HVAC		
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTA



Totals: Mens


8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### **CONTINUED - Storage 2** DESCRIPTION QTY RESET REMOVE REPLACE TAX TOTAL 131.25 SF 109. Suspended ceiling system - 2' 0.00 2.24 0.00 294.00 110. Fluorescent light fixture - 2' & 4' 2.00 EA 0.00 60.04 0.00 120.08 Detach & reset 35.87 SF 0.00 1.56 111. Paneling 0.00 523.96 0.00 1.82 0.00 112. Casing - oversized - 3 1/4" .00 LF 25.48 113. Stain & finish door/window trim 1.00 EA 0.00 26.50 0.00 26.50 & jamb (per side) 12.00 L 4.62 114. Shelving - Detach & reset 0.00 0.00 55.44 115. Glue down carpet - heavy traffic 150.93 SF 0.00 3.12 0.00 470.90 15 % waste added for Glue down carpet - heavy traffic. 6.00 131.25 SF 0.34 116. Floor prep (scrape rubber back 0.00 44.63 residue) 1.00 EA 0.00 42.27 0.00 117. Contents - move out then reset -42.27 Large room 118. Final cleaning - construction -131.25 SF 0.00 0.11 0.00 14.44 Commercial otals: Storage 2 0.00 1,617.70 Mens Height: 7' 4" 217.32 SF Walls 54.63 SF Ceiling 271.95/SF Walls & Ceiling 54.63 SF Floor 6.07 SY Flooring 29.66 LF Floor Perimeter .66 LF Ceil. Perimeter 3' X 6' 8" **Opens into HALLWAY** Door REPLACE RESET REMOVE DESCRIPTION QTY TAX TOTAL 54.63 SF 0.00 0.11 0.00 6.01 119. Final cleaning - construction -Commercial


VICTORYCOSUB 12/13/2017 Page: 18

0.00

6.01




8380 Warren Parkway / Ste. 700 - Frisco, TX 75034

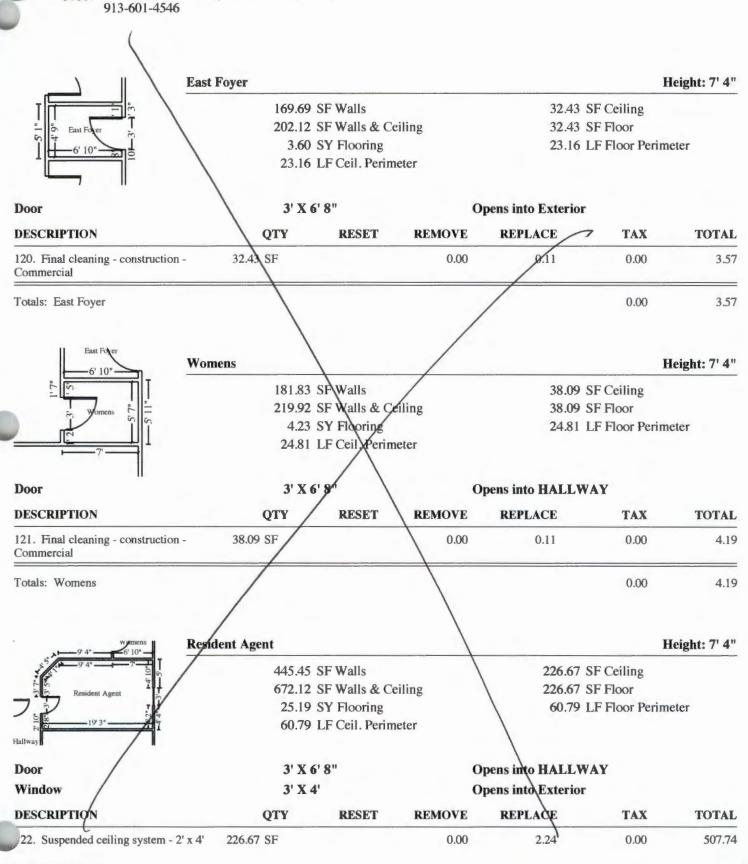



## **CONTINUED - Resident Agent**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
123. Fluorescent light fixture - 2' & 4' - Detach & reset	2.00 EA		0.00	60.04	0.00	120.08
124. Heat/AC register - Mechanically attached - Detach & reset	2.00 EA		0.00	10.74	0.00	21.48
125. R&R Paneling	445.45 SF		0.18	1.56	0.00	775.08
126. Casing - oversized - 3 1/4"	32.00 LF		0.00	1.82	0.00	58.24
127. Stain & finish door/window trim & jamb (per side)	2.00 EA		0.00	26.50	0.00	53.00
128. Clean window unit (per side) 10 - 20 SF	1.00 EA		0.00	8.32	0.00	8.32
129. Clean floor, strip & wax	226.67 SF		0.00	0.54	0.00	122.40
130. Cove base molding - rubber or vinyl, 4" high	60.79 LF		0.00	1.37	0.00	83.28
131. Contents - move out then reset - Large room	1.00 EA		0.00	42.27	0.00	42.27
132. Final cleaning - construction - Commercial	226.67 SF		9,60	0.11	0.00	24.93
Totals: Resident Agent					0.00	1,816.82



467.70 SF Walks

Kitchen

691.60 SF Walls & Ceiling

24.88 SY/Flooring

63.82 LF Ceil. Perimeter

Height: 7' 4"

223.90 SF Ceiling 223.90 SF Floor

63.82 LF Floor Perimeter

Window

Door


**Opens into Exterior Opens into STAIRWELL** 

Door	3' X 6' 8"		Opens into HALLWAY			
DESCRIPTION	/ QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
133. Suspended ceiling system - 2' x 4'	223.90 SF		0.00	2.24	0.00	501.54
134. Fluorescent light fixture - 2' & 4' -/ Detach & reset	2.00 EA		0.00	60.04	0.00	120.08
135. Heat/AC register - Mechanically attached - Detach & reset	1.00 EA		0.00	10.74	0.00	10.74
136. Paneling	467.70 SF		0.00	V.56	0.00	729.61
137. Casing - oversized - 3 1/4"	50.00 LF		0.00	1.82	0.00	91.00
38. Paint door/window trim & jamb - coats (per side)	3.00 EA		0.00	20.22	0.00	60.66



### **CONTINUED - Kitchen**


DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
139. Clean window blind horizontal or vertical	9.00 SF		0.00	0.71	0.00	6.39
140. Clean door - French (per side)	1.00 EA		0.00	12.30	0.00	12.30
141. Vinyl tile	223.90 SF		0.00	2.51	0.00	561.99
142. Floor preparation for resilient flooring	223.90 SF		0.00	0.34	0.00	76.13
143. Clean floor, strip & wax	223.90 SF		0.00	<del>-0.5</del> 4	0.00	120.91
144. Vinyl - metal transition strip	6.00 LF		0.00	1.88	0.00	11.28
145. Cove base molding - rubber or vinyl, 4" high	63.82 LF		0.00	1.37	0.00	87.43
146. Contents - move out then reset	1.00 EA		0.00	28.18	0.00	28.18
147. Final cleaning - construction - Commercial	223.90 Sk		0.00	0.11	0.00	24.63
Totals: Kitchen					0.00	2,442.87

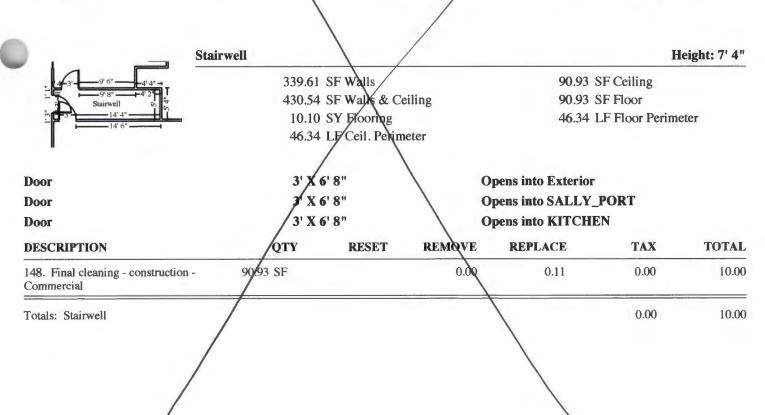




Hally	ay				H	eight: 7' 4	
ally Port	1,401.24	SF Walls		471.37 5	SF Ceiling		
	1,872.61	SF Walls & Ceiling		471.37 SF Floor			
Rejdent Ag	52.37	SY Flooring		191.21 I	LF Floor Perim	eter	
llight a blic Safe	191.21	LF Ceil. Perimeter	eter				
Door	3' X (	6' 8"	One	ens into KITCHE	N		
Door	3' X 6' 8"		_	ens into HALL_1			
Door			-	ens into SUPPLY			
Door	3' X 6' 8" 3' X 6' 8"		_	ens into MENS			
Door			Opens into WOMENS				
Door 3' X 6' 8" Door 3' X 6' 8" 2' X 6' 8"			_	ens into RESIDE			
			_	/			
			Opens into PUBLIC_SAFET				
			Opens into Exterior Opens into Exterior				
Door Door	3' X		Opens into Exterior Opens into JOINT_INTELL				
Door	3' X		Opens into JOINT_INTELL				
DESCRIPTION	QTY	\	MOVE	REPLACE	TAX	TOTA	
149. Vinyl tile	471.37 SF		0.00	2.51	0.00	1,183.	
150. Floor preparation for resilient	471.37 SF	X	0.00	0.34	0.00	160.2	
151. Clean floor, strip & wax	471.37 SF		0.00	0.54	0.00	254.5	
152. Vinyl - metal transition strip	9.00 LF		0.00	1.88	0.00	16.9	
153. Cove base molding - rubber or vinyl, 4" high	191.21 LF	/	0.00	1.37	0.00	261.	
154. Final cleaning - construction - Commercial	471.37 SF		900	0.11	0.00	51.8	
Totals: Hallway					0.00	1,928.0	



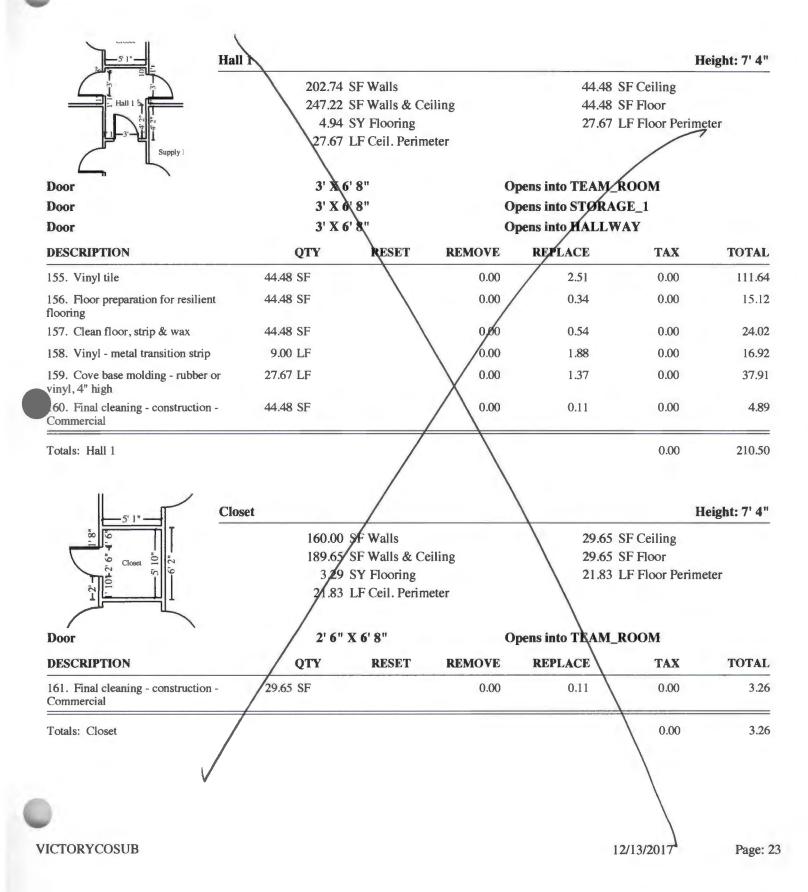

Virtus

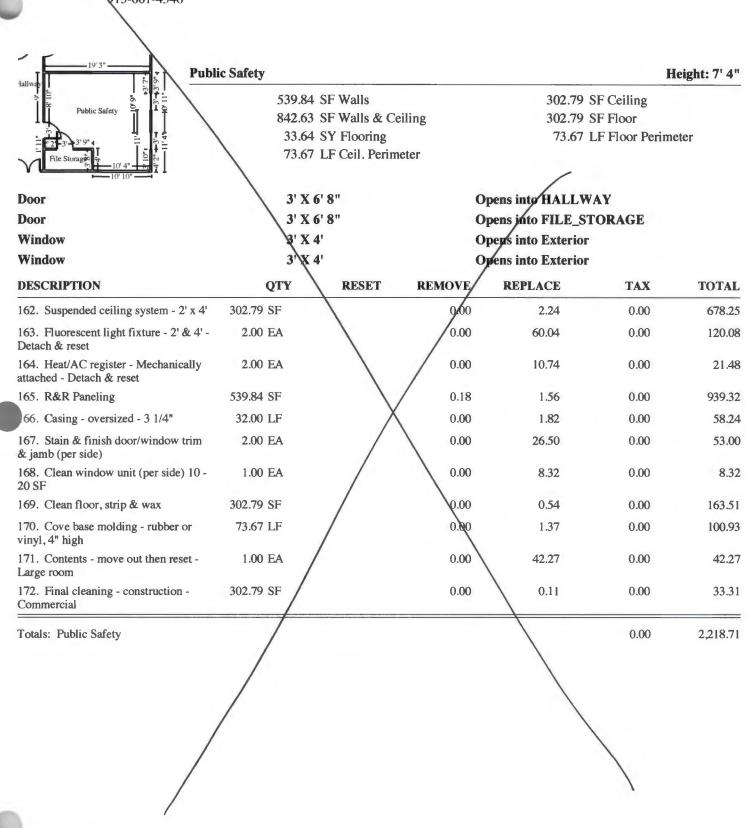



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

Joint	Intelligence				I	leight: 7' 4"	
	751.13	SF Walls		618.10 SF Ceiling			
Total lutefileupe Hallon	1,369.23 SF Walls & Ceiling			618.10 SF Floor			
20 1:		SY Flooring		102.50 L	F Floor Perim	eter	
	102.50	AF Ceil. Peri	meter				
Window	3' X	4'		Opens into Exterior			
Window	3' X	4'		<b>Opens into Exterior</b>			
Window	3' X	4'		Opens into Exterior			
Window	3' X	4'		Opens into Exterior			
Door	3' X	6' 8"		Opens into HALLW	AY		
Door	3' X	6' 8"		Opens into HALLW	AY		
DESCRIPTION	QTY	RESET	REMOVE	BEPLACE	TAX	TOTAL	
173. Suspended ceiling system - 2' x 4'	618.10 SF		0.00	2.24	0.00	1,384.54	
174. Fluorescent light fixture - 2' & 4' - Detach & reset	6.00 EA		0.00	60.04	0.00	360.24	
175. Heat/AC register - Mechanically ttached - Detach & reset	2.00 EA		0.00	10.74	0.00	21.48	
176. R&R Paneling	751.13 SF		0.18	1.56	0.00	1,306.96	
177. Casing - oversized - 3 1/4"	92.00 LF		0.00	1.82	0.00	167.44	
178. Stain & finish door/window trim & jamb (per side)	6.00 EA	/	0.00	26.50	0.00	159.00	
179. Clean window unit (per side) 10 - 20 SF	4.00 EA		0.00	8.32	0.00	33.28	
180. Clean window blind - horizontal or vertical	48.00 SF		0.00	0.71	0.00	34.08	
181. Glue down carpet - heavy traffic	710.81 SF		0.00	3.12	0.00	2,217.73	
15 % waste added for Glue down carpet -	heavy traffic.						
182. Floor prep (scrape rubber back residue)	618.10 SF		0.00	0.34	0.00	210.15	
183. Cove base molding - rubber or vinyl, 4" high	102.50 LF		0.00	1.37	0.00	140.43	
184. Contents - move out then reset - Large room	1.00 EA		0.00	42.27	0.00	42.27	
185. Final cleaning - construction - Commercial	6)8.10 SF		0.00	0.11	0.00	67.99	
Totals: Joint Intelligence					0.00	6,145.59	
Total: Basement		4			0.00	22,336.84	
Total: Bldg I- Old Jail Basement					0.00	22,336.84	





**Building 2- Old Courthouse** 

# Women's Restroom / Third Floor

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
188. Reglaze window, 10 - 16 sf	1.00 EA		0.00	97.05	0.00	97.05
189. Stain & finish door/window trim & jamb (per side)	2.00 EA		0.00	26.50	0.00	53.00
Totals: Women's Restroom / Third Floor					0.00	150.05



**Hearing Room 303** 

933.51 SF Walls 1,291.49 SF Walls & Ceiling 39.78 SY Flooring 287.38 SF Long Wall

77.79 LF Ceil. Perimete

LyWxH 23' 11 3/8" x 14' 11 3/8" x 12'

357.98 SF Ceiling 357.98 SF Floor

77.79 LF Floor Perimeter 179.38 SF Short Wall

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
190. Interior Plaster Repair - Min. Charge - Labor and Material	1.00 EA		0.00	166.83	0.00	166.83
191. Seal/prime then paint the walls and ceiling twice (3 coats)	1,291.49 SF	/	0.00	0.84	0.00	1,084.85
192. Light fixture - Detach & reset	1.00 EA		0.00	41.36	0.00	41.36
193. Mask and prep for paint - paper and tape (per LF)	158.00 LF		0.00	0.51	0.00	80.58
Note: Masking of wood casing and base	eboard.		1			
194. Mask or cover per square foot	357.98 SF		0.25	0.00	0.00	89.50
195. Final cleaning - construction - Commercial	357.98 SF		0.00	0.11	0.00	39.38
Totals: Hearing Room 303					0.00	1,502.50



Room 202 (Second Floor)

686.02 SF Walls 925.19 SF Walls & Ceiling 26.57 SY Flooring 177.33 SF Long Wall 61.90 LF Ceil. Perimeter LxWxH 16' x 14' 11 3/8" x 11' 1"

239.17 SF Ceiling239.17 SF Floor61.90 LF Floor Perimeter165.68 SF Short Wall

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL



# **CONTINUED - Room 202 (Second Floor)**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
196. Interior Plaster Repair - Min. Charge - Labor and Material	1.00 EA		0.00	166.83	0.00	166.83
197. Seal/prime then paint the walls and ceiling twice (3 coats)	925.19 SF		0.00	0.84	0.00	<i>7</i> 77.16
198. Ceiling fan - Detach & reset	1.00 EA		0.00	147.29	0.00	147.29
199. Recessed light fixture - Detach a reset trim only	5.00 EA		0.00	1.46	0,00	7.30
200. Outlet or switch cover	6.00 EA		0.00	2.23	0.00	13.38
201. Mask and prep for paint - paper and tape (per LF)	10.00 LF		0.00	0.51	0.00	86.70
Note: Masking of wood casing and baseboo	ard.					
202. Mask or cover per square foot	239.17 SF		0.25	0.00	0.00	59.79
203. Final cleaning - construction - Commercial	239.17 SF		0.00	0/1	0.00	26.31
Totals: Room 202 (Second Floor)		\			0.00	1,284.76
Total: Building 2- Old Courthouse			/		0.00	2,937.31

**Building 3 - Old Courthouse Tunnel** 

LxWxH 16' 1" x 9' 3" x 8'

405.33 SF Walls 554.10 SF Walls & Ceiling 16.53 SY Flooring

128.67 SF Long Wall

50.67 LF Ceil. Perimeter

148.77 SF Ceiling

148.77 SF Floor

50.67 LF Floor Perimeter

74.00 SF Short Wall

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
206. Drywall Repair - Minimum Charge - Labor and Material	1.00 EA		0.00	264.11	0.00	264.11
207. Texture drywall - light hand texture	148.77 SF		0.00	0.38	0.00	56.53
208. Paint the ceiling - two coats	148.77 SF		0.00	0.63	0.00	93.73
209. Light fixture - Detach & reset	2.00 EA		0.00	41.36	0.00	82.72
210. Mask or cover per square foot	148,77 SF		0.25	960	0.00	37.19
211. Mask wall - plastic, paper, tape (per LF)	90.67 LF		0.00	0.82	0.00	41.55
212. Final cleaning - construction - Commercial	148.77 SF		0.00	0.11	0.00	16.36
Totals: Building 3 - Old Courthouse Tu	nnel				0.00	592.19



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

**Building 4- New Courthouse** 

#### Roof

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
214. Roofing repair - hot material required - Minimum charge	1.00 EA		0.00	578.40	0.00	578.40
Totals: Roof					0.00	578.40



### **Employee Breakroom (Basement)**

LxWxH 22' x 18' x 8'

640.00 SF Walls 1,036.00 SF Walls & Ceiling 44.00 SY Flooring 176.00 SF Long Wall 80.00 LF Ceil. Perimeter

396.00 SF Ceiling 396.00 SF Floor 80.00 LF Floor Perimeter 144.00 SF Short Wall

DESCRIPTION QTY RESET REMOVE REPLACE TAX TOTAL 0.00 483.12 215. Suspended ceiling tile - 2' x 4' 396.00 SF 0.00 1.22 216. Clean and deodorize carpet 396.00 SF 0.00 0.27 0.00 106.92 NOT EMPLETE 217. Clean cove base molding - rubber 80.00 LF 0.00 0.18 0.00 14.40 or vinyl 218. Contents - move out then reset 1.00 EA 0.00 28.18 0.00 28.18 396.00 SF 0.25 0.00 0.00 99.00 219. Mask or cover per square foot 396.00 SF 0.00 0.11 220. Final cleaning - construction -0.00 43.56 Commercial Totals: Employee Breakroom (Basement) 0.00 775.18



### Stairwell (Second & Third Floors)

LxWxH 20' 4 13/16" x 7' 3 15/16" x 25'

1,386.45 SF Walls 1,535.95 SF Walls & Ceiling 16.61 SY Flooring 510.02 SF Long Wall

149.50 SF Floor 55.46 LF Floor Perimeter 183.20 SF Short Wall

149.50 SF Ceiling

55.46 LF Ceil. Perimeter

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
221. Seal/prime then paint the walls and ceiling twice (3 coats)	1,535.95 SF		0.00	0.84	0.00	1,290.20
222. Scaffold - per section (per week)	5.00 WK		0.00	38.40	0.00	192.00





### **CONTINUED - Stairwell (Second & Third Floors)**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
223. Scaffolding Setup & Take down - per hour	2.00 HR		0.00	20.66	0.00	41.32
224. Mask or cover per square foot	149.50 SF		0.25	0.00	0.00	37.38
225. Final cleaning - construction - Commercial	149.50 SF		0.00	0.11	0.00	16.45
Totals: Stairwell (Second & Third Floors	s)				0.00	1,577.35



### Women's Restroom / Second Floor

### LxWxH 12' 11 3/8" x 9' 2 1/16" x 8'

353.92 SF Walls 472.68 SF Walls & Ceiling 13.20 SY Flooring 103.59 SF Long Wall 44.24 LF Ceil. Perimeter 118.76 SF Ceiling 118.76 SF Floor 44.24 LF Floor Perimeter 73.38 SF Short Wall

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
26. Two coat plaster (no lath)	118.76 SF		0.00	2.78	0.00	330.15
227. Heat/AC register - Mechanically attached - Detach & reset	1.00 EA		0.00	10.74	0.00	10.74
228. Fluorescent light fixture - 2' & 4' - Detach & reset	3.00 EA		0.00	60.04	0.00	180.12
229. Mask or cover per square foot	118.76 SF		0.25	0.00	0.00	29.69
230. Mask wall - plastic, paper, tape (per LF)	44.24 LF		0.00	0.82	0.00	36.28
231. Final cleaning - construction - Commercial	118.76 SF		0.00	0.11	0.00	13.06
Totals: Women's Restroom / Second Flo	or				0.00	600.04



### **Third Floor Hallway**

### LxWxH 49' 3 15/16" x 8' 6 15/16" x 12'

1,389.75 SF Walls 1,812.89 SF Walls & Ceiling 47.02 SY Flooring 591.94 SF Long Wall 115.81 LF Ceil. Perimeter

423.14 SF Floor 115.81 LF Floor Perimeter

102.94 SF Short Wall

423.14 SF Ceiling

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
32. R&R Suspended ceiling tile - 2' x	72.00 SF		0.11	1.22	0.00	95.76





# **CONTINUED - Third Floor Hallway**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Note: (9) ceiling tiles						
233. R&R Batt insulation - 6" - R19 - paper faced	72.00 SF		0.17	0.65	0.00	59.04
234. R&R Cove base molding - rubber or vinyl, 4" high	115.81 LF		0.18	1.37	0.00	179.51
235. Vinyl tile	423.14 SF		0.00	2.51	0.00	1,062.08
Note: Considers replacement of the vinyl	floor tile throughou	t the entire wing	to the intersection.	. Some replacement ha	is been completed	d previously.
236. Clean floor, strip & wax	423.14 SF		0.00	0.54	0.00	228.50
237. Final cleaning - construction - Commercial	423.14 SF		0.00	0.11	0.00	46.55
Totals: Third Floor Hallway					0.00	1,671.44



# Second Floor Hallway

# LxWxH 52' 8 1/16" x 8' 6 15/16" x 12'

1,470.00 SF Walls 1,921.82 SF Walls & Ceiling 50.20 SY Flooring 632.06 SF Long Wall 122.50 LF Ceil. Perimeter 451.82 SF Ceiling 451.82 SF Floor

122.50 LF Floor Perimeter 102.94 SF Short Wall

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
238. R&R Suspended ceiling tile - 2' x 4'	104.00 SF		0.11	1.22	0.00	138.32
Note: (13) ceiling tiles						
239. R&R Batt insulation - 6" - R19 - paper faced	104.00 SF		0.17	0.65	0.00	85.28
240. R&R Cove base molding - rubber or vinyl, 4" high	122.50 LF		0.18	1.37	0.00	189.88
241. Vinyl tile	451.82 SF		0.00	2.51	0.00	1,134.07
Note: Considers replacement of the vinyl	floor tile throughou	t the entire wing	to the intersection.	. Some replacement ha	s been completed	d previously.
242. Clean floor, strip & wax	451.82 SF		0.00	0.54	0.00	243.98
243. Final cleaning - construction - Commercial	451.82 SF		0.00	0.11	0.00	49.70
Totals: Second Floor Hallway					0.00	1,841.23

Total: Building 4- New Courthouse

0.00 7,043.64


Building 5- Old Fire Station

Main Level

**VICTORYCOSUB** 

12/13/2017

Page: 30

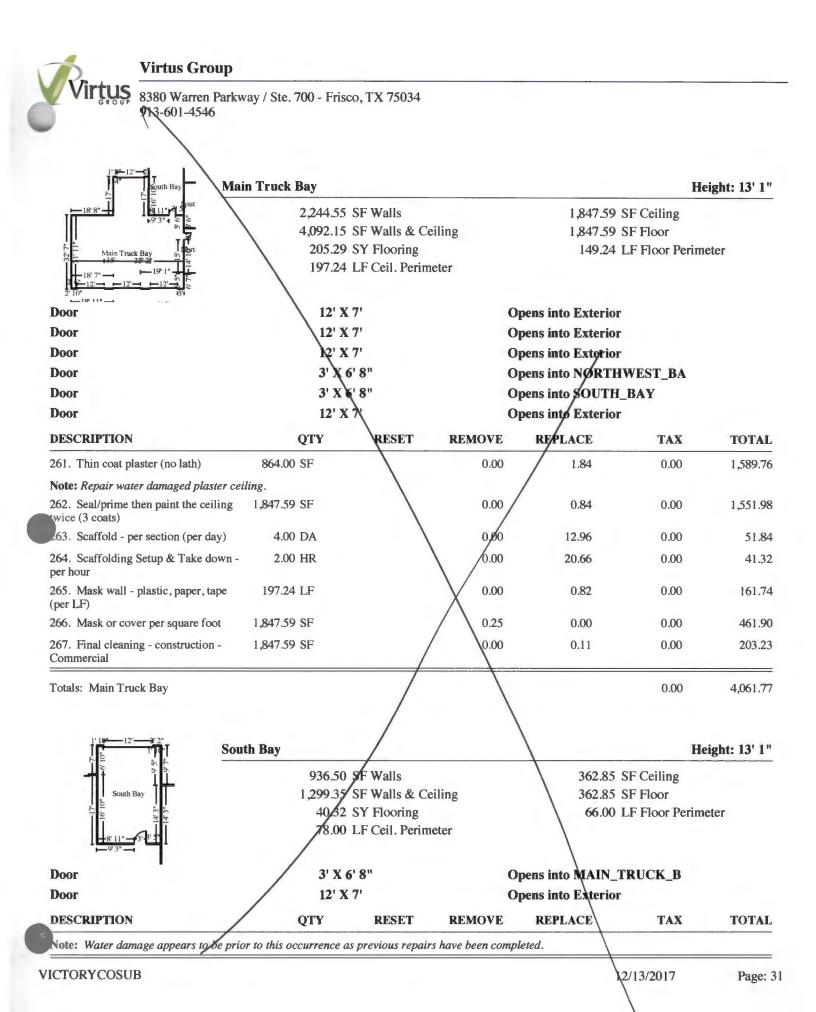





	C	ONTINUED - S	South Pov	1		
DEGEDINGTON				DEDT 1 CD		
DESCRIPTION Totals: South Bay	QTY	RESET	REMOVE	REPLACE	<b>TAX</b> 0.00	<b>TOTAL</b>
Northwest Bay 5 5 5 5 5 5 5 5 5 5 5 5 5 5 5 5 5 5 5	1,248.65	SF Walls SF Walls & Co	eiling	350.99	SF Ceiling SF Floor LF Floor Perim	e <b>ight: 13</b> ' 1'
Door Door	3' X	6' 8" 6' 8"	O	pens into MAIN_' pens into SOUTH		
Door		6' 8"	/	pens into SOUTH	_	
Door	12' X			pens into Exterior		
DESCRIPTION	QTY	RESET	REMOYE	REPLACE	TAX	TOTAL
268. Plasterer - per hour	8.00 HR		0.00	36.01	0.00	288.08
Note: Repair water damaged plaster of 269. Seal/prime then paint the ceiling twice (3 coats)	350.99 SF		0.00	0.84	0.00	294.83
270. Scaffold - per section (per day)	2.00 DA	X	0.00	12.96	0.00	25.92
271. Scaffolding Setup & Take down- per hour	2.00 HR		0.00	20.66	0.00	41.33
272. Mask wall - plastic, paper, tape (per LF)	75.03 LF		0.00	0.82	0.00	61.5
273. Mask or cover per square foot	350.99 SF		0.25	0.00	0.00	87.7:
274. Final cleaning - construction - Commercial	350.99 SF		900	0.11	0.00	38.6
Totals: Northwest Bay					0.00	838.0
Total: Main Level					0.00	4,899.80
Sec	cond Level					
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Note: Significant water damage to the deterioration has occurred.	plaster walls & ceiling	gs at full perimete	er. The damage has	s been occurring for	an extended time	ıs
Totals: Second Level					0.00	0.00
Total: Building 5- Old Fire Station					0.00	4,899.80
ICTORYCOSUB					2/13/2017	Page:



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

# **Building 6 - Precinct 1 Machine Storage**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
276. R&R Ridge vent - Metal rooting - floating ventilator	8.00 LF		2.45	17.64	0.00	160.72
Totals: Roof	\				0.00	160.72
Exte	erior- East Elevati	on				
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
277. R&R Wall/roof panel - ribbed - 26 gauge - up to 1"	1,664.00 SF		0.30	2.40	0.00	4,492.80
Note: The East wall consists of corrugal HGT	ted metal panels whic	h are rusted and	obsolete. Several p	panels damaged and fo	asteners loosened	l. 104' x 16'
278. R&R Metal inside corner post	32.00 LF		0.14	2.73	0.00	111.04
279. Downspout - Detach & reset	48.00 LF		9.00	2.40	0.00	115.20
80. Gutter - Detach & reset	104.00 LF		0.00	2.40	0.00	249.60
Totals: Exterior- East Elevation				,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,	0.00	4,968.64
Totals: Exterior- East Elevation					0.00	4,968.64
	th Elevation				0.00	4,968.64
	th Elevation QTY	RESET	REMOVE	REPLACE	0.00 TAX	4,968.64 TOTAL
DESCRIPTION  281. R&R Wall/roof panel - ribbed - 26 gauge - up to 1"	<b>QTY</b> 972.00 SF		0.30	2.40	<b>TAX</b> 0.00	TOTAI 2,624.40
DESCRIPTION  281. R&R Wall/roof panel - ribbed - 26 gauge - up to 1"  Note: The South wall consists of corruge	QTY 972.00 SF ated metal panels wh		0.30 d obsolete . Several	2.40 panels damaged and	TAX 0.00 fasteners loosene	TOTAI 2,624.40
DESCRIPTION  281. R&R Wall/roof panel - ribbed - 26 gauge - up to 1"	<b>QTY</b> 972.00 SF		0.30 d obsulete . Several 0.74	2.40	TAX 0.00 fasteners loosene 0.00	TOTAI 2,624.40 ed. 55.52
DESCRIPTION  281. R&R Wall/roof panel - ribbed - 26 gauge - up to 1"  Note: The South wall consists of corruge	QTY 972.00 SF ated metal panels wh		0.30 d obsolete . Several	2.40 panels damaged and	TAX 0.00 fasteners loosene	TOTAI 2,624.40
DESCRIPTION  281. R&R Wall/roof panel - ribbed - 26 gauge - up to 1"  Note: The South wall consists of corruge 282. R&R Metal inside corner post 283. R&R Gable trim for metal roofing - 26 gauge 284. R&R Roll-up door & hardware -	QTY 972.00 SF ated metal panels whit		0.30 d obsulete . Several 0.74	2.40 panels damaged and 2.73	TAX 0.00 fasteners loosene 0.00	TOTAI 2,624.40 ed. 55.52
DESCRIPTION  281. R&R Wall/roof panel - ribbed - 26 gauge - up to 1"  Note: The South wall consists of corruge 282. R&R Metal inside corner post 283. R&R Gable trim for metal roofing - 26 gauge	QTY 972.00 SF ated metal panels who		0.30 d obsolete . Several 0.74 0.49	2.40 panels damaged and 2.73 3.73	TAX 0.00 fasteners loosene 0.00 0.00	2,624.40 2,624.40 2d. 55.55 261.66 2,867.55
DESCRIPTION  281. R&R Wall/roof panel - ribbed - 26 gauge - up to 1"  Note: The South wall consists of corruge 282. R&R Metal inside corner post 283. R&R Gable trim for metal roofing - 26 gauge 284. R&R Roll-up door & hardware - 22' x 18' - 22 gauge 285. R&R Comm. overhead door	QTY 972.00 SF ated metal panels whit 16.00 LF 62.00 LF		0.30 d obsolete . Several 0.74 0.49 16.33	2.40  panels damaged and 2.73 3.73 2,851.20	TAX  0.00  fasteners loosene 0.00 0.00 0.00	TOTAL 2,624.40 ed. 55.52 261.64
DESCRIPTION  281. R&R Wall/roof panel - ribbed - 26 gauge - up to 1"  Note: The South wall consists of corruge 282. R&R Metal inside corner post 283. R&R Gable trim for metal roofing - 26 gauge 284. R&R Roll-up door & hardware - 22' x 18' - 22 gauge 285. R&R Comm. overhead door opener - Hoist/jackshaft - Heavy duty  Totals: South Elevation	QTY 972.00 SF ated metal panels whit 16.00 LF 62.00 LF		0.30 d obsolete . Several 0.74 0.49 16.33	2.40  panels damaged and 2.73 3.73 2,851.20	TAX  0.00  fasteners loosene 0.00 0.00 0.00 0.00	TOTAL 2,624.40 ed. 55.52 261.64 2,867.53 1,259.79



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

# **CONTINUED - Exterior Fencing**

DESCRIPTION	ТО	Y RESET	REMOVE	REPLACE	TAX	TOTAL
Note: Several feet of 6' chain link	fence surrounding th	he property were dam	aged and will need t	to be assessed for repa	ir cost.	
Totals: Exterior Fencing					0.00	0.00
Total: Building 6 - Precinct 1 Mac	chine Storage				0.00	12,198.2
	Br	ailding # 6- PCT 1	Storage Building			
		Roo			/	
		1				
15' 6"	Roof1					
F1 (A)		59.77 Surface Area		/	Number of Squ	
Rooft		51.62 Total Perimo	eter Length	15.50	Total Ridge Le	ngth
F2 (B)				/		
			\ /			
			\			
}	QT		кемоуе	REPLACE	TAX	***
DESCRIPTION 286. Metal roofing	159.77 SF		0.00	3.22	0.00	514.4
286. Metal roofing 287. Flashing - L flashing - color	159.77 SF					514.4
286. Metal roofing 287. Flashing - L flashing - color finish	159.77 SF 20.00 LF		0.00	3.22	0.00	514.46
286. Metal roofing 287. Flashing - L flashing - color finish Note: Metal edge coping at each	159.77 SF 20.00 LF		0.00	3.22	0.00	514.46 52.60
}	159.77 SF 20.00 LF		0.00	3.22	0.00	514.46 52.60 567.06
286. Metal roofing 287. Flashing - L flashing - color finish Note: Metal edge coping at each Totals: Roof1	159.77 SF 20.00 LF gable.		0.00	3.22	0.00	514.46 52.60 567.00
286. Metal roofing 287. Flashing - L flashing - color finish  Note: Metal edge coping at each  Totals: Roof1  Total: Roof	159.77 SF 20.00 LF gable.		0.00	3.22	0.00 0.00 0.00	514.46 52.60 567.00
286. Metal roofing 287. Flashing - L flashing - color finish Note: Metal edge coping at each Totals: Roof1 Total: Roof	159.77 SF 20.00 LF gable.		0.00 0.00	3.22	0.00 0.00 0.00	514.40 52.60 567.00
286. Metal roofing 287. Flashing - L flashing - color finish Note: Metal edge coping at each Totals: Roof1 Total: Roof	159.77 SF 20.00 LF gable.	Bldg 6 - PCT 1	0.00 0.00	3.22	0.00 0.00 0.00	514.46 52.60 567.00
286. Metal roofing 287. Flashing - L flashing - color finish Note: Metal edge coping at each Totals: Roof1 Total: Roof	159.77 SF 20.00 LF gable.	Bldg 6 - PCT 1	0.00 0.00	3.22	0.00 0.00 0.00	514.40 52.60 567.00
286. Metal roofing 287. Flashing - L flashing - color finish  Note: Metal edge coping at each  Totals: Roof  Total: Roof  Total: Building # 6- PCT 1 Storage	gable.  Roof1	Bldg 6 - PCT 1 Roo  578.70 Surface Are	Office Roof	3.22 2.63	0.00 0.00 0.00 0.00	514.46 52.60 567.00 567.00
286. Metal roofing 287. Flashing - L flashing - color finish  Note: Metal edge coping at each  Totals: Roof  Total: Roof  Total: Building # 6- PCT 1 Storage  FI(A)  Roofl	gable.  Roof1	Bldg 6 - PCT 1 Roo	Office Roof	3.22 2.63	0.00 0.00 0.00 0.00	514.46 52.60 567.00 567.00
286. Metal roofing 287. Flashing - L flashing - color finish  Note: Metal edge coping at each  Totals: Roof  Total: Roof  Total: Building # 6- PCT 1 Storag	gable.  Roof1	Bldg 6 - PCT 1 Roo  578.70 Surface Are	Office Roof	3.22 2.63	0.00 0.00 0.00 0.00	514.46 52.60 567.00 567.00
286. Metal roofing 287. Flashing - L flashing - color finish  Note: Metal edge coping at each  Totals: Roof  Total: Roof  Total: Building # 6- PCT 1 Storage  FI(A)  Roofl	gable.  Roof1	Bldg 6 - PCT 1 Roo 578.70 Surface Are 84.95 Total Perime	Office Roof	3.22 2.63	0.00 0.00 0.00 0.00	514.46 52.60 567.00 567.00



VICTORYCOSUB

8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

# **CONTINUED - Roof1**


DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
288. Remove Tear off, haul and dispose of comp. shingles - 3 tab	5.79 SQ		32.50	0.00	0.00	188.18
289. 3 tab - 25 yr composition shingle roofing - incl. felt	6.67 SQ		0.00	134.65	0.00	898.12
290. Ridge cap - composition shingles	30.50 LF		0.00	2.24	0.00	68.3
291. Drip edge	84.95 LF		0.00	1.30	0.00	110.4
Totals: Roof1					0.00	1,265.00
Total: Roof					0.00	1,265.0
Total: Bldg 6 - PCT 1 Office Roof					0.00	1,265.0
	В	uilding 6- PCT	1 Office			
		Interior				
		1				
1"→ +3'1"·	ak Room					Height: 8
Toilet	461.50	SF Walks		190.43 \$	SF Ceiling	
₹1 <b>1</b> 1	651.02	/.			-	
φ 11 '	031.93	SF Walls & Co	eiling	190.43 \$	SF Floor	
Break Room	21.16	SY Flooring			SF Floor LF Floor Perin	neter
δ <u>δ 11' γ 9'3"</u> σ σ σ σ σ σ σ σ σ σ σ σ σ σ σ σ σ σ σ	21.16					neter
Break Room  \$\frac{11}{3^2} \frac{11}{2^2} \cdot 3^3 \cdot 3^2 \cd	21.16	SY Flooring				neter
11 11 11 11 11 11 11 11 11 11 11 11 11	21.16 57.69	SY Flooring  LF Ceil. Perim	eter	57.69 I		neter
window  Door	21.16 57.69 3' X	SY Flooring LF Ceil. Perim 3' 6' 8"	eter O O	57.69 I pens into Exterior pens into Exterior		neter
₩indow	21.16 57.69 3' X 3' X	SY Flooring LF Ceil. Perim 3' 6' 8"	0 0 0	57.69 I pens into Exterior pens into Exterior pens into Exterior		neter
window  Door	21.16 57.69 3' X 3' X 3' X	SY Flooring LF Ceil. Perim 3' 6' 8" 3'	0 0 0 0	57.69 In pens into Exterior pens into Exterior pens into Exterior pens into OFFICE		neter
Window  Door  Window	21.16 57.69 3' X 3' X 3' X 3' X 3' X	SY Flooring LF Ceil. Perim 3' 6' 8" 3' 6' 8"	o o o	pens into Exterior pens into Exterior pens into Exterior pens into OFFICE pens into Exterior	F Floor Perin	neter
Window Door Window Door	21.16 57.69 3' X 3' X 3' X 3' X 3' X	SY Flooring LF Ceil. Perim 3' 6' 8" 3'	o o o	57.69 In pens into Exterior pens into Exterior pens into Exterior pens into OFFICE	F Floor Perin	neter
Window Door Window Door Window Window	21.16 57.69 3' X 3' X 3' X 3' X 3' X	SY Flooring LF Ceil. Perim 3' 6' 8" 3' 6' 8"	o o o	pens into Exterior pens into Exterior pens into Exterior pens into OFFICE pens into Exterior	F Floor Perin	
Window Door Window Door Window Door Window Door	21.16 57.69 3' X 3' X 3' X 3' X 2' 6"	SY Flooring LF Ceil. Perim  3' 6' 8" 3' 6' 8" 3' X 6' 8"	o o	pens into Exterior pens into Exterior pens into Exterior pens into OFFICE pens into Exterior pens into TOILET	F Floor Perin	TOTAI
Window Door Window Door Window Door Window Door Window Door Window Door DESCRIPTION	21.16 57.69 3' X 3' X 3' X 3' X 2' 6" QTY	SY Flooring LF Ceil. Perim  3' 6' 8" 3' 6' 8" 3' X 6' 8"	O O O O O O O O O O O O O O O O O O O	pens into Exterior pens into Exterior pens into Exterior pens into OFFICE pens into Exterior pens into TOILET REPLACE	LF Floor Perin	TOTAI
Window Door Window Door Window Door Window Door Window Door 292. R&R Vinyl tile 293. Floor preparation for resilient flooring	21.16 57.69 3' X 3' X 3' X 3' X 2' 6" QTY	SY Flooring LF Ceil. Perim  3' 6' 8" 3' 6' 8" 3' X 6' 8"	REMOVE 0.66	pens into Exterior pens into Exterior pens into Exterior pens into OFFICE pens into Exterior pens into TOILET REPLACE	TAX 0.00	TOTAI 603.66 64.75 102.83
Window Door Window Door Window Door Window Door Window Door 292. R&R Vinyl tile 293. Floor preparation for resilient	21.16 57.69 3' X 3' X 3' X 3' X 2' 6" QTY 190.43 SF 190.43 SF	SY Flooring LF Ceil. Perim  3' 6' 8" 3' 6' 8" 3' X 6' 8"	00 00 00 00 00 00 00 00 00 00 00 00 00	pens into Exterior pens into Exterior pens into Exterior pens into OFFICE pens into Exterior pens into TOILET REPLACE  2.51  0.34	TAX  0.00  0.00	TOTAI 603.66 64.75
Window Door Window Door Window Door Window Door DESCRIPTION  292. R&R Vinyl tile 293. Floor preparation for resilient flooring 294. Clean floor, strip & wax	21.16 57.69 3' X 3' X 3' X 3' X 2' 6" QTY 190.43 SF 190.43 SF	SY Flooring LF Ceil. Perim  3' 6' 8" 3' 6' 8" 3' X 6' 8"	REMOVE  0.66 0.00 0.00	pens into Exterior pens into Exterior pens into Exterior pens into OFFICE pens into Exterior pens into TOILET REPLACE  2.51  0.34  0.54	TAX  0.00  0.00	TOTAI 603.66 64.73 102.83

12/13/2017

Page: 35





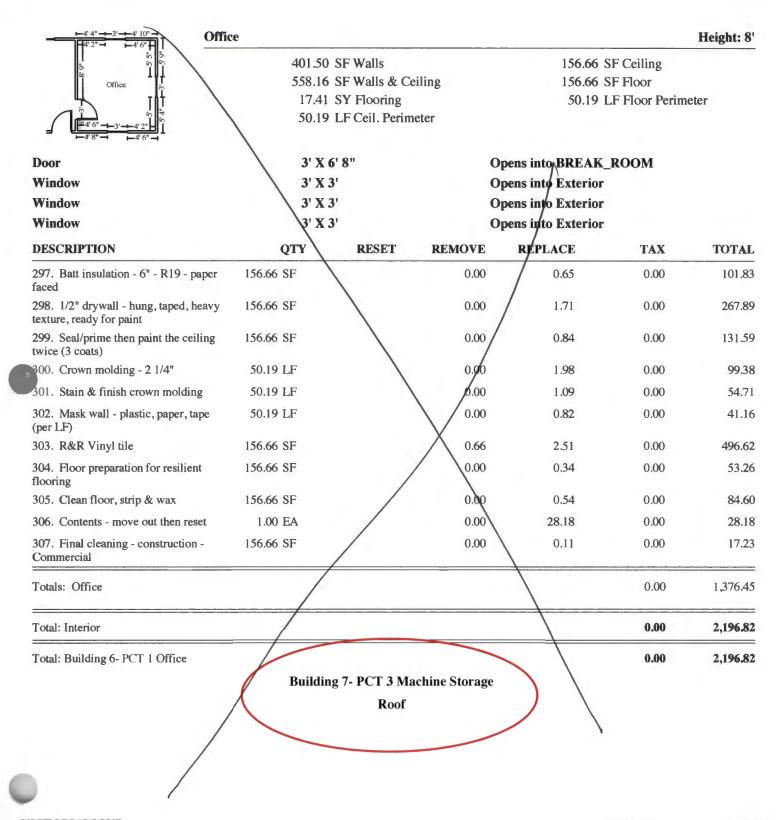



**VICTORYCOSUB** 

8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

Machin	ie Storage Shed	Roof				<u></u>
Machine Storage Shed Rook	•	Surface Area Total Perimeter	r Length	26.80 N	Number of Squ	ares
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
311. R&R Metal roofing - ribbed - 26 2, gauge - 1 1/8" to 1 1/2"	680.02 SF		0.30	3.30	0.00	9,648.08
312. Battens - 2x4 - for steel roofing	26.80 SQ		0.00	111.85	0.00	2,997.58
Totals: Machine Storage Shed Roof					0.00	12,645.66
Total: Roof					0.00	12,645.66
Total: Building 7- PCT 3 Machine Storage		/		1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	0.00	12,645.66
	`	\ /				
Exterio	or / Rear-West	Elevation	,			
DESCRIPTION	QTY	KESET	REMOVE	REPLACE	TAX	TOTAL
313. R&R Gutter - box - galvanized - 6"	100.00 LF		0.30	6.79	0.00	709.00
314. R&R Downspout - box - galvanized - 6"	28.00 LF		0.30	6.79	0.00	198.52
Totals: Exterior / Rear-West Elevation					0.00	907.52
	Bldg 7- 1	PCT 3 Machine	e / Sign Storage			
		Roof				
Sign S	torage Roof					
FI (A) 53 Sign Storage Poof		Surface Area Total Perimete	r Length		Number of Squ Fotal Ridge Le	
F2 (B)						
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
315. R&R Metal roofing - ribbed - 26 1 auge - 1 1/8" to 1 1/2"	,652.82 SF		0.30	3.30	0.00	5,950.16

Page: 37


12/13/2017


Virtus 8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

# **CONTINUED - Sign Storage Roof**

		INUED - Sign	Storage Roof			
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
316. R&R Rafters - 2x6 - 24" OC (3-5/12 Gable, per SF of floor)	1,291.11 SF		0.47	1.49	0.00	2,530.57
317. R&R Fascia - 1" x 6" - #1 pine	160.00 LF		0.20	4.04	0.00	678.40
318. R&R Sheathing - spaced 1" x 8"	1,632.82 SF		0.36	2.59	0.00	4,875.82
Totals: Sign Storage Roof					0.00	14,034.95
401 - 011	Storage Structur	Çe				Height: 10
15' 5" - 3' 16' 13' 10"	1,573.33	SF Walls		1,291.11 SF	Ceiling	
Sign Storage Structure	2,864.44	SF Walls & Co	eiling	1,291.11 SF	Floor	
-18' 6" -36' 11" - 27		SY Flooring		157.33 LF	Floor Peri	meter
36' 10" - 15' 10	157.33	LF Ceil. Perim	eter			
Door	3' Y	6' 8"		pens into Exterior		
Door		6' 8"	/	pens into Exterior		
Door		6' 8"	X	pens into Exterior		
Door		6' 8"		pens into Exterior		
Door		6' 8"		pens into Exterior		
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Note: Floor structure to remain intact.						
319. R&R Stud wall - 2" x 4" - 16" oc	1,573.33 SF		0.18	1.54	0.00	2,627.46
320. R&R Sheathing - spaced 1" x 8"	1,573.33 SF		0.36	2.59	0.00	4,641.32
321. R&R Aluminum corrugated sheet roofing034 - Agricultural	1,669.00 SF		0.30	3.18	0.00	5,808.12
322. R&R Metal outside corner post	40.00 LF		0.74	4.08	0.00	192.80
323. R&R Greenhouse door and frame	3.00 EA		4.42	500.01	0.00	1,513.29
324. Paint door or window opening - Large - 2 coats (per side)	3.00 EA	/	0.00	23.79	0.00	71.37
325. R&R Exterior door - metal - insulated - flush or panel style	1.00 EA		12.60	21 .23	0.00	223.83
326. Paint door slab only - 2 coats (per side)	8.00 EA		0.00	24.16	0.00	193.28
327. Paint door or window opening - 2 coats (per side)	1.00 FA		0.00	20.22	0.00	20.22
Totals: Sign Storage Structure					0.00	15,291.69
Total: Roof					0.00	29,326.64

8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

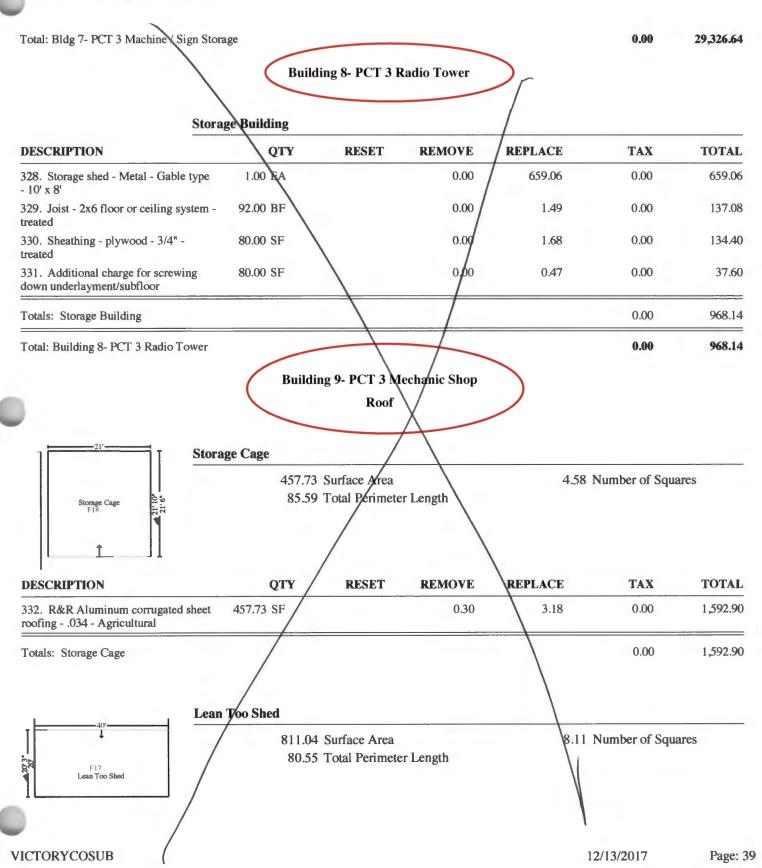

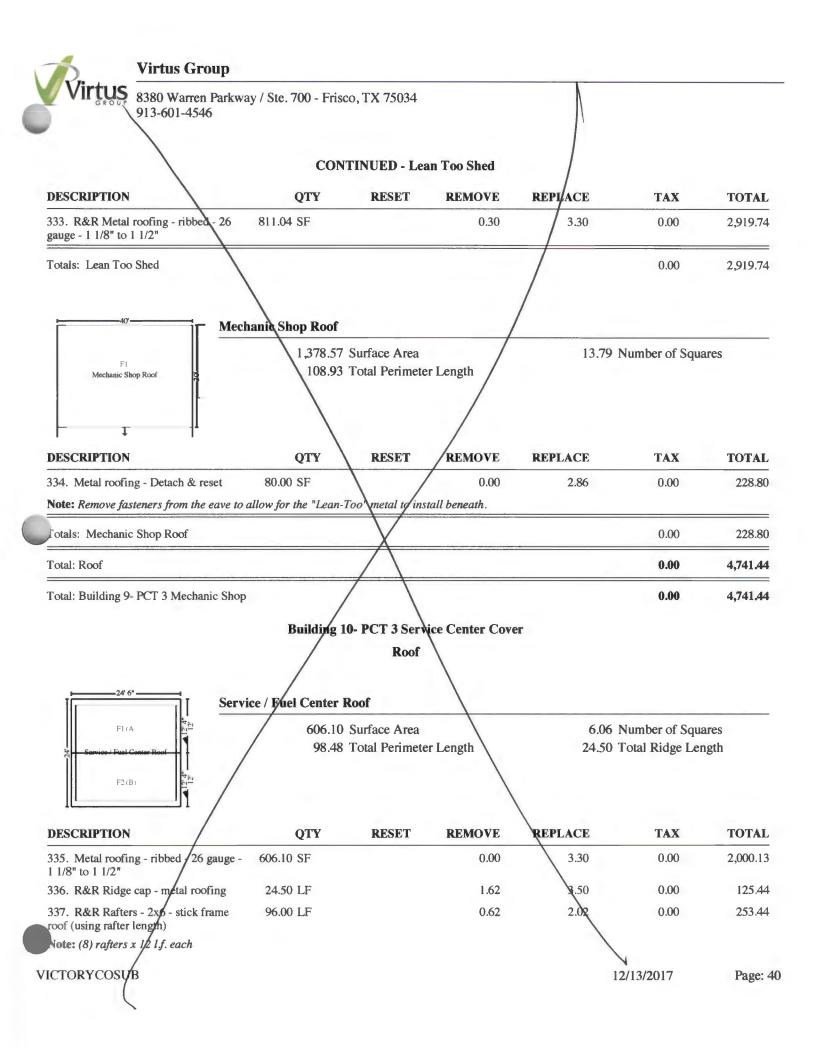



# CONTINUED - Service / Fuel Center Roof

DESCRIPTION	QTY	RESET	REMOVE /	REPLACE	TAX	TOTAL
338. Battens - 2x4 - for steel roofing	6.06 SQ		0.00	111.85	0.00	677.81
Totals: Service / Fuel Center Roof					0.00	3,056.82
Total: Roof					0.00	3,056.82
Total: Building 10- PCT 3 Service Cente	r Cover				0.00	3.056.82


Building 11- PCT 2 Truck Storage (Nursery Road)

### **Exterior / East Elevation**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
342. R&R Sectional overhead door, 12' x 12'	1.00 EA	$\wedge$	49.01	1,073.95	0.00	1,122.96
Totals: Exterior / East Elevation					0.00	1 122 96

# Roof

# South Truck Shed/Roof




1,320.42 Surface Area 165.29 Total Perimeter Length 13.20 Number of Squares61.00 Total Ridge Length

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
343. R&R Metal roofing - ribbed - 26 gauge - 1 1/8" to 1 1/2"	1,320.42 SF		0.30	3.30	0.00	4,753.52
344. R&R Vinyl-faced/laminated insulation - 3"	1,320.42 SF		0.14	0.62	0.00	1,003.52
345. R&R Ridge cap - metal roofing	61.00 LF		1.62	3.50	0.00	312.32
346. R&R Gable trim for metal roofing - 26 gauge	42.00 LF		0.49	3.73	0.00	177.24
347. Closure strips for metal roofing - inside and/or outside	183.00 LF		0.00	1.16	0.00	212.28

Totals: South Truck Shed Roof 0.00 6,458.88





Sign Storage Roof
648.54 Surface Area

73.24 Total Perimeter Length

6.49 Number of Squares30.00 Total Ridge Length

DESCRIPTION	Q TY	RESET	REMOVE	REPLACE	TAX	TOTAL
348. R&R Metal roofing - ribbed - 26 gauge - 1 1/8" to 1 1/2"	648.54 SF		0.30	3.30	0.00	2,334.74
349. R&R Ridge cap - metal roofing	30.00 LF		1.62	3.50	0.00	153.60
Totals: Sign Storage Roof					0.00	2,488.34

Sign Storage Lean-Too Shed

**East Truck Shed** 

Sign Storage Lean-Too Shed

361.25 Surface Area 84.08 Total Perimeter Length 3.61 Number of Squares

12/13/2017

Page: 42

DESCRIPTION	QTY/	RESET	REMOVE	REPLACE	TAX	TOTAL
350. R&R Metal roofing - ribbed - 26 gauge - 1 1/8" to 1 1/2"	361.25 SF		0.30	3.30	0.00	1,300.51
351. R&R Ridge cap - metal roofing	LF		1 62	3.50	0.00	0.00
352. R&R Rafters - 2x4 - stick frame roof (using rafter length)	208.00 LF		0.54	1.67	0.00	459.68
353. Counter battens - 1x4 - for steel roofing	3.61 SQ		0.00	59.06	0.00	213.21
354. R&R Post - wood - 4" x 4" treated lumber	3.00 EA		8.82	51.40	0.00	180.66
355. R&R Header - double 2" x 6"	30.00 LF		3.53	3.82	0.00	220.50
356. R&R 2" x 6" Ledger - treated (1 BF per LF)	30.00 LF		0.35	1.86	0.00	66.30
Totals: Sign Storage Lean-Too Shed					0.00	2,440.86
Total: Roof					0.00	11,388.08
					-	,

VICTORYCO\$UB

# **Virtus Group**

8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### **CONTINUED - East Truck Shed** DESCRIPTION RESET REMOVE REPLACE TAX TOTAL 357. R&R Aluminum corrugated sheet 1,036.00 SF 0.30 3.18 0.00 3,605.28 roofing - .034 - Agricultural East wall. 74' x 14' HGT Note: Considers replacement of the metal panels along the entire 358. R&R Gable trim for metal 60.00 LF 0.49 3.73 0.00 253.20 roofing - 26 gauge Totals: East Truck Shed 0.00 3,858.48 Total: Building 11- PCT 2 Truck Storage (Nursery Road) 0.00 16,369.52 Bldg #12- Patriot Park Metal Storage Structures Roof Vehicle Storage Roof 372.58 Surface Area 3.73 Number of Squares 79.05 Total Perimeter Length chicle Storage Ro DESCRIPTION OTY RESET REMOVE REPLACE TAX TOTAL 362. R&R Aluminum corrugated sheet 372.58 SF 0.30 3.18 0.00 1,296.57 roofing - .034 - Agricultural Totals: Vehicle Storage Roof 0.00 1,296.57 **Open Canopy** 648.83 Surface Area 6.49 Number of Squares 104.55 Total Perimeter Length Open Canop DESCRIPTION QTY RESET REMOVE REPLACE TAX TOTAL 363. R&R Metal roofing - probed - 26 648.83 SF 0.30 3.30 0.00 2,335.79 gauge - 1 1/8" to 1 1/2" Totals: Open Canopy 0.00 2,335.79 0.00 'otal: Roof 3,632.36

12/13/2017

Page: 43



DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
364. R&R Wall/roof panel - ribbed - 26 gauge - 1 1/8" to 1 1/2"	120.00 SF		0.30	2.48	0.00	333.60
365. Prime & paint metal siding	120.00 SF		0.00	0.58	0.00	69.60
366. R&R Downspout - aluminum - up to 5"	4.00 LF		0.30	3.62	0.00	54.88
367. Prime & paint gutter / downspout	14.00 LF		0.00	1.06	0.00	14.84
Totals: Exterior / Front South Elevation		and the second s		/	0.00	472.9

Total: Bldg #12- Patriot Park Metal Storage Structures

Office

Building #12- Patriot Park Office Interior Office



418.50 SF Walls

589.47 SF Walls & Ceiting 19.00 SY Flooring

52.31 LF Ceil. Perimeter

Height: 8'

0.00

4,105.28

170.97 SF Ceiling 170.97 SF Floor

52.31 LF Floor Perimeter

3' X 6' 8" Door **Opens into CLOSET** 3' X 6' 8' Door **Opens into Exterior** 

QTY RESET	REMOVE	REPLACE	TAX	TOTAL
170.97 SF	0.00	0.65	0.00	111.13
170.97 SF	0.0	1.06	0.00	181.23
170.97 SF	0.00	0.84	0.00	143.61
2,00 EA	4.90	55.78	0.00	121.36
4/8.50 SF	0.00	0.50	0.00	209.25
418.50 SF	0.00	1.56	0.00	652.86
10.00 LF	0.00	0.88	0.00	8.80
170.97 SF	0.00	0.11	0.00	18.81
	170.97 SF 170.97 SF 170.97 SF 200 EA 418.50 SF 418.50 SF 10.00 LF	170.97 SF 0.00 170.97 SF 0.00 170.97 SF 0.00 2,00 EA 4.90 478.50 SF 0.00 418.50 SF 0.00 10.00 LF 0.00	170.97 SF 0.00 0.65  170.97 SF 0.00 1.06  170.97 SF 0.00 0.84  2,00 EA 4.90 55.78  448.50 SF 0.00 0.50  418.50 SF 0.00 1.56  10.00 LF 0.00 0.88	170.97 SF       0.00       0.65       0.00         170.97 SF       0.00       1.06       0.00         170.97 SF       0.00       0.84       0.00         200 EA       4.90       55.78       0.00         478.50 SF       0.00       0.50       0.00         418.50 SF       0.00       1.56       0.00         10.00 LF       0.00       0.88       0.00

Totals: Office

**VICTORYCOSUB** 

12/13/2017


0.00

Page: 44

1,447.05



Closet



277.25 SF Walls

330.56 SF Walls & Ceiling 5.92 SY Flooring

34.66 LF Ceil. Perimeter

Height: 8'

53.31 SF Ceiling

53.31 SF Floor

34.66 LF Floor Perimeter

0.00

0.00

3' X 6' 8"	Opens into OFFICE
	3' X 6' 8"

DESCRIPTION	6 KA	RESET	REMOVE	REPLACE	TAX	TOTAL
376. Batt insulation - 6" - R19 - paper faced	53.31 SF		0.00	0.65	0.00	34.65
377. Sheathing - plywood - 1/2" CDX	53.31 SF		0.00	1.06	0.00	56.51
378. Seal/prime then paint the ceiling twice (3 coats)	53.31 SF		0.00	0.84	0.00	44.78
379. R&R Light fixture	2.00 EA		4.90	55.78	0.00	121.36
380. Batt insulation - 4" - R13 - paper faced	277.25 SF		0.00	0.50	0.00	138.63
381. Paneling	277.25 SF		0.00	1.56	0.00	432.51
82. Cove molding - 3/4"	10.00 LF	/	0.00	0.88	0.00	8.80
383. Detach & Reset Shelving - 24" - in place	39.00 LF	4.62	900	0.00	0.00	180.18
384. Final cleaning - construction - Commercial	53.31 SF		0.00	0.11	0.00	5.86
Totals: Closet					0.00	1,023.28
Total: Interior Office					0.00	2,470.33

0.00 2,470.33

Total: Building #12- Patriot Park Office

**Building 13- Patriot Park Comfort Station** 

QTY RESET REMOVE REPLACE TOTAL DESCRIPTION


Note: No damage noted to the CMU / block structure

Totals: Building 13- Patriot Park Comfort Station

**Building 14- New Jail Main Level** 







# **Patrol Office**

Height: 8' 4"

1,433.93	SF Walls
2,068.55	SF Walls & Ceiling
70.51	SY Flooring
172.18	LF Ceil. Perimeter

634.63 SF Ceiling 634.63 SF Floor 172.18 LF Floor Perimeter

Door	3' X 6' 8"	<b>Opens into Exterior</b>
Door	3' X 6' 8"	<b>Opens into Exterior</b>
Door	3' X 6' 8"	<b>Opens into Exterior</b>
Door	3' X 6' 8"	<b>Opens into Exterior</b>
Window - Goes to Floor	3' X 3' 6 15/16"	<b>Opens into Exterior</b>
Window - Goes to Floor	3' X 3' 6 15/16"	<b>Opens into Exterior</b>
Window - Goes to Floor	3' X 3' 6 15/16"	<b>Opens into Exterior</b>
Window - Goes to Floor	3' X 3' 6 15/16"	<b>Opens into Exterior</b>
Window - Goes to Floor	3' X 3' 6 15/16"	<b>Opens into Exterior</b>
Window - Goes to Floor	3' X 3' 6 15/16"	<b>Opens into Exterior</b>
Window - Goes to Floor	3' X 3' 6 15/16"	<b>Opens into Exterior</b>
Window - Goes to Floor	3' X 3' 6 15/16"	<b>Opens into Exterior</b>
Window - Goes to Floor	3' X 3' 6 15/16"	<b>Opens into Exterior</b>

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
388. R&R Suspended ceiling tile - 2' x 4'	634.63 SF		0.11	1.22	0.00	844.06
389. R&R Batt insulation - 6" - R19 - paper faced	634.63 SF		0.17	0.65	0.00	520.40
390. 5/8" drywall - hung, taped, heavy texture, ready for paint	254.70 SF		0.00	1.80	0.00	458.46
Note: Up 5'-6" to windows along the ext	terior walls only.					
391. Batt insulation - 6" - R19 - paper faced	255.00 SF		0.00	0.65	0.00	165.75
392. Seal/prime then paint the walls twice (3 coats)	1,433.93 SF		0.00	0.84	0.00	1,204.50
393. R&R Outlet	10.00 EA		2.96	11.88	0.00	148.40
394. Clean window unit (per side) 21 - 40 SF	9.00 EA		0.00	11.10	0.00	99.90
395. Clean window stool & apron	27.00 LF		0.00	0.49	0.00	13.23
396. Clean window blind - horizontal or vertical	189.00 SF		0.00	0.71	0.00	134.19
397. Cove base molding - rubber or vinyl, 4" high	86.09 LF		0.00	1.37	0.00	117.94
398. Clean floor - tile	634.63 SF		0.00	0.36	0.00	228.47
399. Mask or cover per square foot	634.63 SF		0.25	0.00	0.00	158.66
ICTORYCOSUB					12/13/2017	Page: 4




8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546



### **CONTINUED - Patrol Office**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
400. Contents - move out then reset - Extra large room	1.00 EA		0.00	84.56	0.00	84.56
401. Final cleaning - construction - Commercial	634.63 SF		0.00	0.11	0.00	69.81
Totals: Patrol Office					0.00	4,248.33



### **Conference Room**

Height: 8' 4"

640.60 SF Walls 883.30 SF Walls & Ceiling 26.97 SY Flooring 76.92 LF Ceil. Perimeter

242.69 SF Floor76.92 LF Floor Perimeter

242.69 SF Ceiling

Door Door

Window - Goes to Floor Window - Goes to Floor

Window - Goes to Floor

3' X 6' 8" 3' X 6' 8"

3' X 3' 6 15/16" 3' X 3' 6 15/16"

3' X 3' 6 15/16"

**Opens into Exterior** 

**Opens into RESTROOM** 

Opens into Exterior Opens into Exterior

Opens into Exterior

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
402. R&R Suspended ceiling tile - 2' x 4'	64.00 SF		0.11	1.22	0.00	85.12
Note: (8) tiles						
403. R&R Batt insulation - 6" - R19 - paper faced	64.00 SF		0.17	0.65	0.00	52.48
404. 5/8" drywall - hung, taped, heavy texture, ready for paint	67.00 SF		0.00	1.80	0.00	120.60
Note: Up 5'-6" to windows along the exte	erior walls only.					
405. Batt insulation - 6" - R19 - paper faced	67.00 SF		0.00	0.65	0.00	43.55
406. Seal/prime then paint the walls twice (3 coats)	640.60 SF		0.00	0.84	0.00	538.10
407. R&R Outlet	2.00 EA		2.96	11.88	0.00	29.68
408. Clean window unit (per side) 21 - 40 SF	3.00 EA		0.00	11.10	0.00	33.30
409. Clean window stool & apron	12.00 LF		0.00	0.49	0.00	5.88
410. Clean window blind - horizontal or vertical	63.00 SF		0.00	0.71	0.00	44.73
411. Cove base molding - rubber or rinyl, 4" high	76.92 LF		0.00	1.37	0.00	105.38
412. Glue down carpet - heavy traffic	279.10 SF		0.00	3.12	0.00	870.79
/ICTORYCOSUB					12/13/2017	Page: 47



### **CONTINUED - Conference Room**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
15 % waste added for Glue down carpet	- heavy traffic.					
413. Vinyl - metal transition strip	3.00 LF		0.00	1.88	0.00	5.64
414. Floor prep (scrape rubber back residue)	242.69 SF		0.00	0.34	0.00	82.51
415. Mask or cover per square foot	242.69 SF		0.25	0.00	0.00	60.67
416. Contents - move out then reset - Large room	1.00 EA		0.00	42.27	0.00	42.27
417. Final cleaning - construction - Commercial	242.69 SF		0.00	0.11	0.00	26.70
Totals: Conference Room			·		0.00	2,147.40

	4' 4" 3		<u> </u>
F	4' 2"	-7 1"—	<del> </del>
	Valdez		10' 10'
1	[]	_7'	
112	, –		<b>-</b> 11'

**Valdez Office** 

Height: 8' 4"

1/

363.57 SF Walls 482.68 SF Walls & Ceiling 13.23 SY Flooring 43.66 LF Ceil. Perimeter 119.11 SF Ceiling119.11 SF Floor43.66 LF Floor Perimeter

Door Window - Goes to Floor Window - Goes to Floor Window - Goes to Floor 3' X 6' 8" 3' X 3' 6 15/16" 3' X 3' 6 15/16" 3' X 3' 6 15/16" Opens into Exterior Opens into Exterior Opens into Exterior Opens into Exterior

			-		
QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
24.00 SF		0.11	1.22	0.00	31.92
24.00 SF		0.17	0.65	0.00	19.68
61.00 SF		0.00	1.80	0.00	109.80
rior walls only.					
61.00 SF		0.00	0.65	0.00	39.65
363.57 SF		0.00	0.84	0.00	305.40
1.00 EA		2.96	11.88	0.00	14.84
10.00 LF		0.00	8.75	0.00	87.50
3.00 EA		0.00	11.10	0.00	33.30
				12/13/2017	Page: 48
	24.00 SF  24.00 SF  61.00 SF  erior walls only. 61.00 SF  363.57 SF  1.00 EA  10.00 LF	24.00 SF  24.00 SF  61.00 SF  erior walls only. 61.00 SF  363.57 SF  1.00 EA  10.00 LF	24.00 SF 0.11  24.00 SF 0.17  61.00 SF 0.00  erior walls only. 61.00 SF 0.00  363.57 SF 0.00  1.00 EA 2.96 10.00 LF 0.00	24.00 SF       0.11       1.22         24.00 SF       0.17       0.65         61.00 SF       0.00       1.80         erior walls only.       0.00       0.65         363.57 SF       0.00       0.84         1.00 EA       2.96       11.88         10.00 LF       0.00       8.75	24.00 SF 0.11 1.22 0.00  24.00 SF 0.17 0.65 0.00  61.00 SF 0.00 1.80 0.00  erior walls only. 61.00 SF 0.00 0.65 0.00  363.57 SF 0.00 0.84 0.00  1.00 EA 2.96 11.88 0.00  10.00 LF 0.00 8.75 0.00  3.00 EA 0.00 11.10 0.00





### **CONTINUED - Valdez Office**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
426. Clean window blind - horizontal or vertical	63.00 SF		0.00	0.71	0.00	44.73
427. Cove base molding - rubber or vinyl, 4" high	43.66 LF		0.00	1.37	0.00	59.81
428. Clean floor - tile	119.11 SF		0.00	0.36	0.00	42.88
429. Mask or cover per square foot	119.11 SF		0.25	0.00	0.00	29.78
430. Contents - move out then reset	1.00 EA		0.00	28.18	0.00	28.18
431. Final cleaning - construction - Commercial	119.11 SF		0.00	0.11	0.00	13.10
Totals: Valdez Office					0.00	860.57

**VICTORYCOSUB** 

Classroom Height: 8' 4"

784.23 SF Walls 1,337.81 SF Walls & Ceiling 61.51 SY Flooring 94.17 LF Ceil. Perimeter 553.58 SF Ceiling 553.58 SF Floor 94.17 LF Floor Perimeter

12/13/2017

Page: 49

Door	3' X 6' 8"	<b>Opens into Exterior</b>
Door	3' X 6' 8"	<b>Opens into Exterior</b>
Door	3' X 6' 8"	<b>Opens into Exterior</b>
Window - Goes to Floor	3' X 3' 6 15/16"	<b>Opens into Exterior</b>
Window - Goes to Floor	3' X 3' 6 15/16"	<b>Opens into Exterior</b>
Window - Goes to Floor	3' X 3' 6 15/16"	<b>Opens into Exterior</b>
Window - Goes to Floor	3' X 3' 6 15/16"	<b>Opens into Exterior</b>
<b>Window - Goes to Floor</b>	3' X 3' 6 15/16"	<b>Opens into Exterior</b>
Window - Goes to Floor	3' X 3' 6 15/16"	<b>Opens into Exterior</b>

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
432. R&R Suspended ceiling tile - 2' x 4'	24.00 SF		0.11	1.22	0.00	31.92
Note: (3) tiles						
433. R&R Batt insulation - 6" - R19 - paper faced	24.00 SF		0.17	0.65	0.00	19.68
434. 5/8" drywall - hung, taped, heavy texture, ready for paint	125.00 SF		0.00	1.80	0.00	225.00
Note: Up 5'-6" to windows along the exte	erior walls only.					
435. Batt insulation - 6" - R19 - paper aced	125.00 SF		0.00	0.65	0.00	81.25





### **CONTINUED - Classroom**

DESCRIPTION	OTY	DECET	DEMOVE	DEDI ACE	TAN	TOTAL
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
436. Seal/prime then paint the walls twice (3 coats)	784.23 SF		0.00	0.84	0.00	658.75
437. R&R Outlet	2.00 EA		2.96	11.88	0.00	29.68
438. Clean window stool & apron	22.67 LF		0.00	0.49	0.00	11.11
439. Clean window unit (per side) 21 - 40 SF	6.00 EA		0.00	11.10	0.00	66.60
440. Clean window blind - horizontal or vertical	126.00 SF		0.00	0.71	0.00	89.46
441. Cove base molding - rubber or vinyl, 4" high	94.17 LF		0.00	1.37	0.00	129.01
442. Clean floor - tile	553.58 SF		0.00	0.36	0.00	199.29
443. Mask or cover per square foot	553.58 SF		0.25	0.00	0.00	138.40
444. Contents - move out then reset - Large room	1.00 EA		0.00	42.27	0.00	42.27
445. Final cleaning - construction - Commercial	553.58 SF		0.00	0.11	0.00	60.89
Totals: Classroom					0.00	1,783.31

		_4' 8"
Ī	2"4	0 1
/ II.	44	Jone
4	Ca	Thai Canfield's Off of
- "1.6"	- T	12, 10
Š	5' 10"	* C *
1	II	11'3"
L	1	Coos to Floor

# Captain Canfield's Office

180.10 SF Ceiling 180.10 SF Floor

54.67 LF Floor Perimeter

Height: 8' 4"

•		
Window - Goes to Floor	3' X 3' 6 15/16"	<b>Opens into Exterior</b>
<b>Window - Goes to Floor</b>	3' X 3' 6 15/16"	<b>Opens into Exterior</b>
Window - Goes to Floor	3' X 3' 6 15/16"	<b>Opens into Exterior</b>
Door	3' X 6' 8"	<b>Opens into Exterior</b>
Window - Goes to Floor	3' X 3' 6 15/16"	<b>Opens into Exterior</b>
Window - Goes to Floor	3' X 3' 6 15/16"	<b>Opens into Exterior</b>
Window - Goes to Floor	3' X 3' 6 15/16"	<b>Opens into Exterior</b>

455.27 SF Walls

20.01 SY Flooring

635.37 SF Walls & Ceiling

54.67 LF Ceil. Perimeter

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
446. R&R Suspended ceiling tile - 2' x 4'	40.00 SF		0.11	1.22	0.00	53.20
Note: (5) tiles 447. R&R Batt insulation - 6" - R19 - aper faced	40.00 SF		0.17	0.65	0.00	32.80





# **CONTINUED - Captain Canfield's Office**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
448. 5/8" drywall - hung, taped, heavy texture, ready for paint	90.44 SF		0.00	1.80	0.00	162.79
Note: Up 5'-6" to windows along the exte	erior walls only.					
449. Batt insulation - 6" - R19 - paper faced	90.44 SF		0.00	0.65	0.00	58.79
450. Seal/prime then paint the walls twice (3 coats)	455.27 SF		0.00	0.84	0.00	382.43
451. R&R Outlet	6.00 EA		2.96	11.88	0.00	89.04
452. Wrap custom window sill with aluminum (PER LF)	10.00 LF		0.00	8.75	0.00	87.50
453. Clean window unit (per side) 21 - 40 SF	4.00 EA		0.00	11.10	0.00	44.40
454. Clean window unit (per side) 3 - 9 SF	3.00 EA		0.00	5.82	0.00	17.46
455. Clean window blind - horizontal or vertical	96.00 SF		0.00	0.71	0.00	68.16
456. Cove base molding - rubber or vinyl, 4" high	54.67 LF		0.00	1.37	0.00	74.90
457. Clean floor - tile	180.10 SF		0.00	0.36	0.00	64.84
458. Mask or cover per square foot	180.10 SF		0.25	0.00	0.00	45.03
459. Contents - move out then reset - Large room	1.00 EA		0.00	42.27	0.00	42.27
460. Final cleaning - construction - Commercial	180.10 SF		0.00	0.11	0.00	19.81
Totals: Captain Canfield's Office	,				0.00	1,243.42

**-**7 6\* **-**



Jones Office	Height: 8' 4"

	4' 3" + -3' -		-3'-6"	1
	-4' 1" -4 7' 4	7 2	3' 9" -	ò
Off	Jon	es Offic		101
1	-6' 11	<u>-</u>	3'-1	
			1 1	

360.71 SF Walls 477.96 SF Walls & Ceiling 13.03 SY Flooring 43.31 LF Ceil. Perimeter

117.25 SF Floor 43.31 LF Floor Perimeter

117.25 SF Ceiling

Door	3' X 6' 8"	<b>Opens into Exterior</b>
Window - Goes to Floor	3' X 3' 6 15/16"	<b>Opens into Exterior</b>
Window - Goes to Floor	3' X 3' 6 15/16"	<b>Opens into Exterior</b>
Window - Goes to Floor	3' X 3' 6 15/16"	<b>Opens into Exterior</b>

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
161. R&R Suspended ceiling tile - 2' x	24.00 SF		0.11	1.22	0.00	31.92





### **CONTINUED - Jones Office**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Note: (3) tiles						
462. R&R Batt insulation - 6" - R19 - paper faced	24.00 SF		0.17	0.65	0.00	19.68
463. 5/8" drywall - hung, taped, heavy texture, ready for paint	61.00 SF		0.00	1.80	0.00	109.80
Note: Up 5'-6" to windows along the exte	erior walls only.					
464. Batt insulation - 6" - R19 - paper faced	61.00 SF		0.00	0.65	0.00	39.65
465. Seal/prime then paint the walls twice (3 coats)	360.71 SF		0.00	0.84	0.00	303.00
466. R&R Outlet	1.00 EA		2.96	11.88	0.00	14.84
467. Clean window stool & apron	9.00 LF		0.00	0.49	0.00	4.41
468. Clean window unit (per side) 21 - 40 SF	3.00 EA		0.00	11.10	0.00	33.30
469. Clean window blind - horizontal or vertical	63.00 SF		0.00	0.71	0.00	44.73
470. Cove base molding - rubber or vinyl, 4" high	43.31 LF		0.00	1.37	0.00	59.33
71. Clean floor - tile	117.25 SF		0.00	0.36	0.00	42.21
472. Mask or cover per square foot	117.25 SF		0.25	0.00	0.00	29.31
473. Contents - move out then reset	1.00 EA		0.00	28.18	0.00	28.18
474. Final cleaning - construction - Commercial	117.25 SF		0.00	0.11	0.00	12.90
Totals: Jones Office					0.00	773.26



Restroom

226.25 SF Walls

272.23 SF Walls & Ceiling

5.11 SY Flooring

27.17 LF Ceil. Perimeter

Height: 8' 4"

45.99 SF Ceiling 45.99 SF Floor

27.17 LF Floor Perimeter

Opens into CONFERENCE_R


DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
475. 5/8" drywall - hung, taped, heavy texture, ready for paint	49.00 SF		0.00	1.80	0.00	88.20
Note: Up 7' to windows along the exterior	wall only.					
476. Batt insulation - 6" - R19 - paper aced	49.00 SF		0.00	0.65	0.00	31.85





### **CONTINUED - Restroom**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
477. Seal/prime then paint the surface area twice (3 coats)	148.74 SF		0.00	0.84	0.00	124.94
478. Light fixture - Detach & reset	1.00 EA		0.00	41.36	0.00	41.36
479. Handicap grab bar - Stainless steel, 1 1/2" x 36"	1.00 EA		0.00	52.01	0.00	52.01
480. Clean ceramic tile	76.00 SF		0.00	0.30	0.00	22.80
Note: South wall only						
481. Clean door (per side)	1.00 EA		0.00	4.00	0.00	4.00
482. Clean door / window opening (per side)	1.00 EA		0.00	7.18	0.00	7.18
483. Clean window stool & apron	6.75 LF		0.00	0.49	0.00	3.31
484. Clean window unit (per side) 3 - 9 SF	2.00 EA		0.00	5.82	0.00	11.64
485. Clean window blind - horizontal or vertical	14.00 SF		0.00	0.71	0.00	9.94
486. R&R Tile base	27.17 LF		1.23	8.28	0.00	258.39
487. Clean floor - tile	45.99 SF		0.00	0.36	0.00	16.56
88. Mask or cover per square foot	45.99 SF		0.25	0.00	0.00	11.50
489. Contents - move out then reset	1.00 EA		0.00	28.18	0.00	28.18
490. Final cleaning - construction - Commercial	45.99 SF		0.00	0.11	0.00	5.06
Totals: Restroom					0.00	716.92



**Chief Deputy Boyd** 

Height: 8' 4"

591.73 SF Walls 863.55 SF Walls & Ceiling 30.20 SY Flooring 71.05 LF Ceil. Perimeter 271.82 SF Ceiling271.82 SF Floor71.05 LF Floor Perimeter

Window - Goes to Floor Window - Goes to Floor Door

Door

3' X 3' 6 15/16" 2' 1" X 3' 6 15/16" 3' X 6' 8" 3' X 6' 8" Opens into Exterior Opens into Exterior Opens into HALLWAY Opens into Exterior

DESCRIPTIONQTYRESETREMOVEREPLACETAXTOTAL491. Drywall Installer / Finisher - per2.00 HR0.0056.000.00112.00

Note: Repair of suspended ceiling grid



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

# **CONTINUED - Chief Deputy Boyd**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
492. R&R Suspended ceiling tile - 2' x 4'	32.00 SF		0.11	1.22	0.00	42.56
Note: (4) tiles						
493. R&R Batt insulation - 6" - R19 - paper faced	32.00 SF		0.17	0.65	0.00	26.24
494. 5/8" drywall - hung, taped, heavy texture, ready for paint	116.37 SF		0.00	1.80	0.00	209.47
Note: Up 5'-6" to windows along the exte	erior walls only.					
495. Batt insulation - 6" - R19 - paper faced	116.37 SF		0.00	0.65	0.00	75.64
496. Seal/prime then paint the walls twice (3 coats)	591.73 SF		0.00	0.84	0.00	497.05
497. Clean window unit (per side) 10 - 20 SF	2.00 EA		0.00	8.32	0.00	16.64
498. Clean window blind - horizontal or vertical	22.00 SF		0.00	0.71	0.00	15.62
499. Cove base molding - rubber or vinyl, 4" high	71.05 LF		0.00	1.37	0.00	97.34
500. Clean floor - tile	271.82 SF		0.00	0.36	0.00	97.86
01. Mask or cover per square foot	271.82 SF		0.25	0.00	0.00	67.96
502. Contents - move out then reset - Large room	1.00 EA		0.00	42.27	0.00	42.27
503. Final cleaning - construction - Commercial	271.82 SF		0.00	0.11	0.00	29.90
Totals: Chief Deputy Boyd	/	18 1911 1911 1911			0.00	1,330.55





Restroom Hall Hall Hall Hall Hall Hall Hall Hal
2 Swell O.Comor, Ollins
6 11. 6 7. 7. 7. 1. 6 12. 8. 7. 7. 7. 7. 7. 7. 7. 7. 7. 7. 7. 7. 7.
3' 10" 12' 9"

# Sheriff O'Connor's Office

Height: 9'


	662.44	SF Walls		330.66 S	F Ceiling	
Skirit O'Comor's Office	993.10	SF Walls & Ceilin	ng	330.66 S	F Floor	
m ≥ 24	36.74	SY Flooring		73.60 L	F Floor Perim	eter
11 0 11 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	73.60	LF Ceil. Perimete	er			
3' 10" 12' 9" Window - Goes to Floor	3' X 3	o' 6 15/16"		Opens into Exterior		
Window - Goes to Floor	3' X 2	,		Opens into Exterior		
Window - Goes to Floor	3' X 2	1		Opens into Exterior		
Window - Goes to Floor	3' X 2	1	-	Opens into Exterior		
Window - Goes to Floor	3' X 2	21		Opens into Exterior		
Window - Goes to Floor	3' X 2	21		Opens into Exterior		
Window - Goes to Floor	3' X 2	21		Opens into Exterior		
Window - Goes to Floor	3' X 3	3' 6 15/16"		Opens into Exterior		
Door	3' X 6	5' 8"		Opens into Exterior		
Door	3' X 6	5' 8"		Opens into HALLWA	AY	
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTA

PESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
504. R&R Suspended ceiling tile - 2' x 4'	8.00 SF		0.11	1.22	0.00	10.64
Note: (1) tiles						
505. R&R Batt insulation - 6" - R19 - paper faced	8.00 SF		0.17	0.65	0.00	6.56
506. 5/8" drywall - hung, taped, heavy texture, ready for paint	48.00 SF		0.00	1.80	0.00	86.40
Note: Up 5'-6" to windows along the exte	erior walls only.					
507. Batt insulation - 6" - R19 - paper faced	48.00 SF		0.00	0.65	0.00	31.20
508. Seal/prime then paint the walls twice (3 coats)	662.44 SF		0.00	0.84	0.00	556.45
509. Clean window unit (per side) 10 - 20 SF	8.00 EA		0.00	8.32	0.00	66.56
510. Clean window blind - horizontal or vertical	58.00 SF		0.00	0.71	0.00	41.18
511. Cove base molding - rubber or vinyl, 4" high	73.60 LF		0.00	1.37	0.00	100.83
512. Clean floor - tile	330.66 SF		0.00	0.36	0.00	119.04
513. Mask or cover per square foot	330.66 SF		0.25	0.00	0.00	82.67
514. Contents - move out then reset - Extra large room	1.00 EA		0.00	84.56	0.00	84.56
515. Final cleaning - construction - Commercial	330.66 SF		0.00	0.11	0.00	36.37
Totals: Sheriff O'Connor's Office				-	0.00	1,222.46

	Totals:	Sheriff	O'Connor's	Office
١,	ICTOD	VCOC	LID	







### Courts

Height: 8'

728.02 SF Walls
1,162.20 SF Walls & Ceiling
48.24 SY Flooring
91.00 LF Ceil. Perimeter

434.17 SF Ceiling 434.17 SF Floor 91.00 LF Floor Perimeter

Door 3' X 6' 8"

**Opens into Exterior** 

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
516. Clean and deodorize carpet	434.17 SF		0.00	0.27	0.00	117.23
517. Contents - move out then reset - Extra large room	1.00 EA		0.00	84.56	0.00	84.56
Totals: Courts					0.00	201.79
Total: Main Level					0.00	14,528.01



### **Records Restroom**

LxWxH 6' 2 1/16" x 4' 5 1/16" x 8'

169.50 SF Walls
196.79 SF Walls & Ceiling
3.03 SY Flooring
49.38 SF Long Wall
21.19 LF Ceil. Perimeter

27.29 SF Ceiling27.29 SF Floor21.19 LF Floor Perimeter35.38 SF Short Wall

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
518. 5/8" drywall - hung, taped, heavy texture, ready for paint	27.29 SF		0.00	1.80	0.00	49.12
519. Batt insulation - 6" - R19 - paper faced	27.29 SF		0.00	0.65	0.00	17.74
520. Seal/prime then paint the surface area twice (3 coats)	285.17 SF		0.00	0.84	0.00	239.54
521. Bathroom ventilation fan - Detach & reset	1.00 EA		0.00	44.80	0.00	44.80
522. Light fixture - Detach & reset	1.00 EA		0.00	41.36	0.00	41.36
523. Clean light bar	1.00 EA		0.00	10.18	0.00	10.18
524. Clean ceramic tile	49.36 SF		0.00	0.30	0.00	14.81
Note: (1) long wall only						
525. Clean door (per side)	1.00 EA		0.00	4.00	0.00	4.00
526. Clean door / window opening (per side)	1.00 EA		0.00	7.18	0.00	7.18
527. Clean baseboard	21.19 LF		0.00	0.19	0.00	4.03







#### **CONTINUED - Records Restroom**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
528. Clean floor - tile	27.29 SF		0.00	0.36	0.00	9.82
529. Mask or cover per square foot	27.29 SF		0.25	0.00	0.00	6.82
530. Final cleaning - construction - Commercial	27.29 SF		0.00	0.11	0.00	3.00
Totals: Records Restroom					0.00	452.40



#### **Dispatch Server Room**

LxWxH 10' x 9' 8 1/16" x 8'

314.75 SF Walls 411.47 SF Walls & Ceiling 10.75 SY Flooring 80.00 SF Long Wall

39.34 LF Ceil. Perimeter

96.72 SF Ceiling 96.72 SF Floor 39.34 LF Floor Perimeter 77.38 SF Short Wall

DESCRIPTION QTY RESET REMOVE REPLACE TAX TOTAL 31. Drywall patch / small repair, 1.00 EA 0.00 45.40 0.00 45.40 ready for paint 532. Texture drywall - heavy hand 314.75 SF 0.00 0.58 0.00 182.56 texture 533. Seal/prime then paint the walls 314.75 SF 0.00 0.84 0.00 264.39 twice (3 coats) 534. Contents - move out then reset 0.00 1.00 EA 28.18 0.00 28.18 535. Clean floor - tile 96.72 SF 0.00 0.36 0.00 34.82 536. Final cleaning - construction -96.72 SF 0.00 0.11 0.00 10.64 Commercial 0.00 96.72 SF 0.25 0.00 24.18 537. Mask or cover per square foot Totals: Dispatch Server Room 0.00 590.17 Total: Building 14- New Jail 0.00 15,570.58

### **Building 15- Hewitt Hangar Roof**



#### **South Elevation**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
539. Reglaze window, 1 - 9 sf	286.00 EA		0.00	42.44	0.00	12,137.84
lote: Based on the quote obtained fi	rom local glass contracto	or, Mitchell Glass	which reflects \$47	7 per pane for putty ap	plication and di	fficult access.



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

**CONTINUED - South Elevation** 

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
540. Specialty multi- lite window unit - Extra large	1.00 EA		0.00	580.02	0.00	580.02
541. Add. charge for a retrofit window, 24-40 sf - difficult	1.00 EA		0.00	180.53	0.00	180.53
Totals: South Elevation					0.00	12.898.39

North Elevation


QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
134.00 LF		1.21	13.87	0.00	2,020.72

Note: (2) high volume downspouts constructed of 6" schedule 40 PVC extending from the upper eave to the ground 67 lf. each

Totals: North Elevation	0.00	2,020.72

Total: Exterior 0.00 14,919.11

Roof



### **Pitched Metal Roof**

22,325.77 Surface Area 490.02 Total Perimeter Length 223.26 Number of Squares121.00 Total Ridge Length

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Note: No visible storm damage to the	e 24 gauge ,standing sear	m metal roof syst	em.			
Totals: Pitched Metal Roof					0.00	0.00
Tomas, Theriod Memi 1000		_ /			0.00	



#### **South Flat Roof**

4,225.03 Surface Area 311.52 Total Perimeter Length 42.25 Number of Squares

**VICTORYCOSUB** 

12/13/2017

Page: 58



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

CONTINUED - South Flat Roof

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Note: No visible storm damag	e to the 3 ply built-up roof syste	em.				
Totals: South Flat Roof					0.00	0.00
33 1	North Flat Roof					
Prist Rod	3,998.72	Surface Area		39.99	Number of Squ	ares
F5	341.23	Total Perimete	er Length			
iquh Flat R						

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
543. Remove Tear off, haul and dispose of 3 ply built-up roofing	39.99 SQ		33.07	0.00	0.00	1,322.47
544. Built-up 3 ply roofing - in place	39.99 SQ		0.00	195.56	0.00	7,820.44
45. R&R Flash parapet wall only - itumen	153.00 LF		1.18	7.58	0.00	1,340.28
546. R&R Membrane roofing - cant strips - wood	153.00 LF		0.40	2.20	0.00	397.80
547. R&R Counterflashing - Apron flashing	153.00 LF		0.34	5.14	0.00	838.44
548. R&R Gravel stop	341.23 LF		0.20	1.18	0.00	470.90
549. R&R Flashing - pipe jack	3.00 EA		4.14	23.34	0.00	82.44
550. R&R Furnace vent - rain cap and storm collar, 8"	1.00 EA		6.30	57.82	0.00	64.12
551. Fiberboard - 1"	3.998.72 SF		0.00	0.65	0:00	2,599.17

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

552. Insulation - ISO board, 3" 39.99 SQ 0.00 218.42 0.00 8,734.62

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

553. Insulation - ISO board. 4" 13.20 SQ 0.00 266.88 0.00 3,522.82

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when neurred, subject to limits.



DESCRIPTION

### **Virtus Group**

8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### **CONTINUED - North Flat Roof**

This item did not previously exist or ex	pands the scope of repairs, but is required by cur	rent building codes. The code ungrade cost is	payable when

RESET

incurred, subject to limits.

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

Note: Considers tapered insulation to comply with 1/4" per foot drainage requirements.

554. 2" x 6" lumber (1 BF per LF)

360.00 LF

0.00

REMOVE

1.73

REPLACE

0.00

622.80

**TOTAL** 

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

**Note:** Double perimeter band (3") installed to fasten perimeter coping after installation of insulation.

555. Steel wall coping

180.00 LF

0.00

9.37

0.00

1.686.60

29,816.02

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

Total: Roof				0.00	14,896.91
Totals: North Flat Roof				0.00	14,896.91
558. Tarp - all-purpose poly - per sq ft (labor and material)	3,998.72 SF	0.00	0.51	0.00	2,039.35
57. Additional charge for high roof (2 stories or greater)	39.99 SQ	0.00	9.91	0.00	396.30
556. Remove Additional charge for high roof (2 stories or greater)	39.99 SQ	3.11	0.00	0.00	124.37
, 3					

**Building 15 - Hewitt Hangar Interior** 

Main Level



Total: Building 15- Hewitt Hangar Roof

Larry's Office

Height: 8'

0.00

420.00 SF Walls 586.99 SF Walls & Ceiling

18.55 SY Flooring

52.50 LF Ceil. Perimeter

166.99 SF Ceiling 166.99 SF Floor

52.50 LF Floor Perimeter

Door 3' X 6' 8"

Opens into BREAK\_AREA

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
559. Clean light fixture - fluorescent	4.00 EA		0.00	7.78	0.00	31.12



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546



# **CONTINUED - Larry's Office**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
560. Mask and cover light fixture	4.00 EA		0.00	9.25	0.00	37.00
561. Heat/AC register - Mechanically attached - Detach & reset	1.00 EA		0.00	10.74	0.00	10.74
562. Clean register - heat / AC	1.00 EA		0.00	3.14	0.00	3.14
563. Crown molding - 3 1/4"	52.50 LF		0.00	2.49	0.00	130.73
564. Seal & paint crown molding - two coats	52.50 LF		0.00	0.97	0.00	50.93
565. 5/8" drywall - hung, taped, heavy texture, ready for paint	420.00 SF		0.00	1.80	0.00	756.00
566. Seal/prime then paint the walls and ceiling twice (3 coats)	586.99 SF		0.00	0.84	0.00	493.07
567. Batt insulation - 4" - R13 - paper faced	210.00 SF		0.00	0.50	0.00	105.00
568. Outlet	1.00 EA		0.00	11.88	0.00	11.88
569. Clean door (per side)	1.00 EA		0.00	4.00	0.00	4.00
570. Paint door slab only - 2 coats (per side)	1.00 EA		0.00	24.16	0.00	24.16
71. Clean door / window opening per side)	1.00 EA		0.00	7.18	0.00	7.18
572. Paint door or window opening - 2 coats (per side)	1.00 EA		0.00	20.22	0.00	20.22
573. Cove base molding - rubber or vinyl, 4" high	52.50 LF		0.00	1.37	0.00	71.93
574. Glue down carpet - heavy traffic	192.04 SF		0.00	3.12	0.00	599.16
15 % waste added for Glue down carpet -	heavy traffic.					
575. Floor prep (scrape rubber back residue)	166.99 SF		0.00	0.34	0.00	56.78
576. Final cleaning - construction - Commercial	166.99 SF		0.00	0.11	0.00	18.37
Totals: Larry's Office					0.00	2,431.41

11 - 5 9° - 3′ - 0′ 8° - 10′ 10° - 11′ - 11′ - 12′ 10° - 11′ - 12′ 10° - 11′ - 11′ - 12′ 10° - 11′ 2° - 12′ 10° - 11′ 2° - 12′ 10° - 11′ 2° - 12′ 10° - 11′ 2° - 12′ 10° - 11′ 2° - 12′ 10° - 11′ 2° - 12′ 10° - 11′ 2° - 12′ 10° - 11′ 2° - 12′ 10°

**Waiting Area** 

1

Height: 8'

565.33 SF Walls 882.95 SF Walls & Ceiling 35.29 SY Flooring 73.17 LF Ceil. Perimeter 317.61 SF Ceiling 317.61 SF Floor

70.17 LF Floor Perimeter

Door
Missing Wall - Goes to Floor


3' X 6' 8" 3' X 6' 8" Opens into Exterior
Opens into BREAK\_AREA



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

# **CONTINUED - Waiting Area**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
577. Suspended ceiling tile - 2' x 4'	317.61 SF		0.00	1.22	0.00	387.48
578. Batt insulation - 6" - R19 - paper faced	317.61 SF		0.00	0.65	0.00	206.45
579. Drywall Installer / Finisher - per hour	2.00 HR		0.00	56.00	0.00	112.00
Note: Cost to repair ceiling grid.						
580. 5/8" drywall - hung, taped, heavy texture, ready for paint	565.33 SF		0.00	1.80	0.00	1,017.59
581. Clean light fixture - fluorescent	4.00 EA		0.00	7.78	0.00	31.12
582. Seal/prime then paint the walls twice (3 coats)	565.33 SF		0.00	0.84	0.00	474.88
583. Batt insulation - 4" - R13 - paper faced	565.33 SF		0.00	0.50	0.00	282.67
584. Outlet	9.00 EA		0.00	11.88	0.00	106.92
585. Clean door (per side)	1.00 EA		0.00	4.00	0.00	4.00
586. Paint door slab only - 2 coats (per side)	1.00 EA		0.00	24.16	0.00	24.16
587. Clean door / window opening per side)	2.00 EA		0.00	7.18	0.00	14.36
588. Paint door or window opening - 2 coats (per side)	2.00 EA		0.00	20.22	0.00	40.44
589. Clean cabinetry - upper - faces only	3.00 LF		0.00	3.92	0.00	11.76
590. Seal & paint cabinetry - upper - faces only	3.00 LF		0.00	11.40	0.00	34.20
591. Cove base molding - rubber or vinyl, 4" high	70.17 LF		0.00	1.37	0.00	96.13
592. Glue down carpet - heavy traffic	365.25 SF		0.00	3.12	0.00	1,139.58
15 % waste added for Glue down carpet -	heavy traffic.					
593. Floor prep (scrape rubber back residue)	317.61 SF		0.00	0.34	0.00	107.99
594. Final cleaning - construction - Commercial	317.61 SF		0.00	0.11	0.00	34.94
Totals: Waiting Area		·			0.00	4,126.67





**Break Area** 

544.08 SF Walls 848.79 SF Walls & Ceiling 33.86 SY Flooring 70.51 LF Ceil. Perimeter

Height: 8' 304.70 SF Ceiling

Opens into TOILET\_1 Opens into WAITING\_AREA

304.70 SF Floor

67.51 LF Floor Perimeter

Door Missing Wall - Goes to Floor Door

2' 8 1/16" X 6' 8" 3' X 6' 8" 3' X 6' 8" Opens into LARRYS\_OFFI

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
595. Suspended ceiling tile - 2' x 4'	304.70 SF		0.00	1.22	0.00	371.73
596. Batt insulation - 6" - R19 - paper faced	304.70 SF		0.00	0.65	0.00	198.06
597. Drywall Installer / Finisher - per hour	2.00 HR		0.00	56.00	0.00	112.00
Note: Cost to repair ceiling grid.						
598. 5/8" drywall - hung, taped, heavy texture, ready for paint	544.08 SF		0.00	1.80	0.00	979.34
599. Clean light fixture - fluorescent	4.00 EA		0.00	7.78	0.00	31.12
600. Seal/prime then paint the walls twice (3 coats)	544.08 SF		0.00	0.84	0.00	457.03
601. Batt insulation - 4" - R13 - paper faced	544.08 SF		0.00	0.50	0.00	272.04
602. Outlet	6.00 EA		0.00	11.88	0.00	71.28
603. Clean door (per side)	2.00 EA		0.00	4.00	0.00	8.00
604. Paint door slab only - 2 coats (per side)	2.00 EA		0.00	24.16	0.00	48.32
605. Clean door / window opening (per side)	3.00 EA		0.00	7.18	0.00	21.54
606. Paint door or window opening - 2 coats (per side)	3.00 EA		0.00	20.22	0.00	60.66
607. Cabinetry - upper (wall) units - Detach & reset	4.00 LF		0.00	32.25	0.00	129.00
608. Clean cabinetry - upper - faces only	4.00 LF		0.00	3.92	0.00	15.68
609. Seal & paint cabinetry - upper - faces only	4.00 LF		0.00	11.40	0.00	45.60
610. Cabinetry - lower (base) units - Detach & reset	4.00 LF		0.00	37.71	0.00	150.84
611. Clean cabinetry - lower - faces only	4.00 LF		0.00	3.92	0.00	15.68
612. Seal & paint cabinetry - lower - aces only	4.00 LF		0.00	13.67	0.00	54.68






### **CONTINUED - Break Area**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
613. Sink - single - Detach & reset	1.00 EA		0.00	99.82	0.00	99.82
614. Clean sink and faucet	1.00 EA		0.00	9.56	0.00	9.56
615. Cove base molding - rubber or vinyl, 4" high	67.51 LF		0.00	1.37	0.00	92.49
616. Glue down carpet - heavy traffic	350.41 SF		0.00	3.12	0.00	1,093.28
15 % waste added for Glue down carpet	- heavy traffic.					
617. Floor prep (scrape rubber back residue)	304.70 SF		0.00	0.34	0.00	103.60
618. Final cleaning - construction - Commercial	304.70 SF		0.00	0.11	0.00	33.52
Totals: Break Area					0.00	4,474.87

Height: 8'



321.11 SF Walls

378.51 SF Walls & Ceiling

6.38 SY Flooring

40.14 LF Ceil. Perimeter

57.41 SF Ceiling

40.14 LF Floor Perimeter

57.41 SF Floor

2' 8 1/16" X 6' 8" Door

Toilet 1

# Opens into BREAK\_AREA

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
619. Clean the walls	321.11 SF		0.00	0.20	0.00	64.22
620. Seal/prime then paint the walls twice (3 coats)	321.11 SF		0.00	0.84	0.00	269.73
621. Clean cabinetry - upper - faces only	2.50 LF		0.00	3.92	0.00	9.80
622. Clean vanity - faces only	3.00 LF		0.00	3.62	0.00	10.86
623. Clean sink and faucet	1.00 EA		0.00	9.56	0.00	9.56
624. Paint door slab only - 2 coats (per side)	3.00 EA		0.00	24.16	0.00	72.48
625. Paint door or window opening - 2 coats (per side)	3.00 EA		0.00	20.22	0.00	60.66
626. Clean light bar	1.00 EA		0.00	10.18	0.00	10.18
627. Bathroom mirror - Detach & reset	1.00 SF		0.00	5.34	0.00	5.34
628. Clean mirror	6.00 SF		0.00	0.39	0.00	2.34
629. Clean shower - Light	1.00 EA		0.00	17.93	0.00	17.93
630. Clean shower door - Light	1.00 EA		0.00	7.57	0.00	7.57
631. Clean toilet	1.00 EA		0.00	12.05	0.00	12.05
VICTORYCOSUB					12/13/2017	Page: 6








### **CONTINUED - Toilet 1**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
632. Clean cove base molding - rubber or vinyl	40.14 LF		0.00	0.18	0.00	7.23
633. Clean floor, strip & wax	57.41 SF		0.00	0.54	0.00	31.00
Totals: Toilet l					0.00	590.95



**Washing Area** 

Height: 8'

156.53 SF Walls185.40 SF Walls & Ceiling3.21 SY Flooring21.51 LF Ceil. Perimeter

28.88 SF Floor 19.18 LF Floor Perimeter

28.88 SF Ceiling

**Missing Wall - Goes to Floor Door** 

2' 4" X 6' 8" 2' 8 1/16" X 6' 8" Opens into TOILET\_2
Opens into Exterior


DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
634. Suspended ceiling tile - 2' x 2'	28.88 SF		0.00	1.23	0.00	35.52
635. Batt insulation - 6" - R19 - paper faced	28.88 SF		0.00	0.65	0.00	18.77
636. Detach & Reset Ceiling diffusers/grills - circular - 8"-10" diameter	1.00 EA	14.65	0.00	0.00	0.00	14.65
637. Clean the walls	156.53 SF		0.00	0.20	0.00	31.31
638. Seal/prime then paint the walls twice (3 coats)	156.53 SF		0.00	0.84	0.00	131.49
639. Clean vanity - faces only	3.00 LF		0.00	3.62	0.00	10.86
640. Clean countertop	5.25 SF		0.00	0.41	0.00	2.15
641. Clean sink and faucet	1.00 EA		0.00	9.56	0.00	9.56
642. Interior door unit	1.00 EA		0.00	116.05	0.00	116.05
643. Door knob - interior	1.00 EA		0.00	28.65	0.00	28.65
644. Stain & finish door slab only (per side)	2.00 EA		0.00	37.80	0.00	75.60
645. Paint door or window opening - 2 coats (per side)	2.00 EA		0.00	20.22	0.00	40.44
646. Clean light bar	1.00 EA		0.00	10.18	0.00	10.18
647. Bathroom mirror - Detach & reset	1.00 SF		0.00	5.34	0.00	5.34
648. Clean mirror	6.00 SF		0.00	0.39	0.00	2.34
49. Clean cove base molding - rubber or vinyl	19.18 LF		0.00	0.18	0.00	3.45



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546



DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
650. Clean floor, strip & wax	28.88 SF		0.00	0.54	0.00	15.60
Totals: Washing Area					0.00	551.96



Toilet 2 Height: 8'

108.53 SF Walls121.89 SF Walls & Ceiling1.48 SY Flooring15.51 LF Ceil. Perimeter


13.36 SF Floor13.18 LF Floor Perimeter

13.36 SF Ceiling

Missing Wall - Goes to Floor2' 4" X 6' 8"Opens into WASHING\_AREADESCRIPTIONQTYRESETREMOVEREPLACETAX651. Suspended ceiling tile - 2' x 2'13.36 SF0.001.230.00

651. Suspended ceiling tile - 2' x 2'	13.36 SF	0.00	1.23	0.00	16.43
652. Batt insulation - 6" - R19 - paper aced	13.36 SF	0.00	0.65	0.00	8.68
653. Bathroom ventilation fan - Detach & reset	1.00 EA	0.00	44.80	0.00	44.80
654. Clean the walls	108.53 SF	0.00	0.20	0.00	21.71
655. Seal/prime then paint the walls twice (3 coats)	108.53 SF	0.00	0.84	0.00	91.17
656. Paint door or window opening - 2 coats (per side)	2.00 EA	0.00	20.22	0.00	40.44
657. Clean toilet	1.00 EA	0.00	12.05	0.00	12.05
658. Clean cove base molding - rubber or vinyl	13.18 LF	0.00	0.18	0.00	2.37
659. Clean floor, strip & wax	13.36 SF	0.00	0.54	0.00	7.21

Totals: Toilet 2 ) 0.00 244.86



Workshop Height: 9' 3"

1,124.50 SF Walls 1,945.73 SF Walls & Ceiling 91.25 SY Flooring 130.22 LF Ceil. Perimeter 821.23 SF Ceiling 821.23 SF Floor

120.22 LF Floor Perimeter

3' X 6' 8" 10' X 8' Opens into ROYS\_OFFICE
Opens into Exterior

VICTORYCOSUB

Door

12/13/2017

Page: 66

**TOTAL** 







# **CONTINUED - Workshop**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
660. R&R Suspended ceiling system - 2' x 4'	821.23 SF		0.22	2.24	0.00	2,020.23
661. R&R Batt insulation - 6" - R19 - paper faced	821.23 SF		0.17	0.65	0.00	673.41
662. Fluorescent light fixture - 2' & 4' - Detach & reset	8.00 EA		0.00	60.04	0.00	480.32
663. Clean light fixture - fluorescent	8.00 EA		0.00	7.78	0.00	62.24
664. Detach & Reset Ceiling diffusers/grills - circular - 8"-10" diameter	3.00 EA	14.65	0.00	0.00	0.00	43.95
665. Cold air return cover - Detach & reset	1.00 EA		0.00	14.65	0.00	14.65
666. Seal w/stain blocker then paint the walls twice (3 coats)	1,124.50 SF		0.00	0.86	0.00	967.07
667. Clean door (per side)	1.00 EA		0.00	4.00	0.00	4.00
668. Clean door / window opening (per side)	1.00 EA		0.00	7.18	0.00	7.18
669. Clean overhead door & hardware - Large	1.00 EA		0.00	33.45	0.00	33.45
570. Clean floor	821.23 SF		0.00	0.25	0.00	205.31
671. Epoxy finish - two coats over concrete floor	821.23 SF		0.00	2.96	0.00	2,430.84
672. Contents - move out then reset - Extra large room	1.00 EA		0.00	84.56	0.00	84.56
673. Mask or cover per square foot	821.23 SF		0.25	0.00	0.00	205.31
674. Final cleaning - construction - Commercial	821.23 SF		0.00	0.11	0.00	90.34
Totals: Workshop					0.00	7,322.86





Roy's Office

552.89 SF Walls 774.16 SF Walls & Ceiling 24.59 SY Flooring 59.77 LF Ceil. Perimeter Height: 9' 3"

221.27 SF Ceiling 221.27 SF Floor

59.77 LF Floor Perimeter

Door 3' X 6' 8" Opens into Exterior
Door 3' X 6' 8" Opens into WORKSHOP

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
575. R&R Suspended ceiling tile - 2' x	221.27 SF		0.11	1.22	0.00	294.29
VICTORYCOSUB					12/13/2017	Page: 67







# **CONTINUED - Roy's Office**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
676. R&R Batt insulation - 6" - R19 - paper faced	221.27 SF		0.17	0.65	0.00	181.45
677. Clean paneling	552.89 SF		0.00	0.22	0.00	121.64
678. Clean light fixture	2.00 EA		0.00	5.86	0.00	11.72
679. Detach & Reset Ceiling diffusers/grills - circular - 8"-10" diameter	1.00 EA	14.65	0.00	0.00	0.00	14.65
680. Paint door slab only - 2 coats (per side)	2.00 EA		0.00	24.16	0.00	48.32
681. Paint door or window opening - 2 coats (per side)	3.00 EA		0.00	20.22	0.00	60.66
682. Clean door (per side)	2.00 EA		0.00	4.00	0.00	8.00
683. Clean door / window opening (per side)	3.00 EA		0.00	7.18	0.00	21.54
684. Glue down carpet - heavy traffic	254.46 SF		0.00	3.12	0.00	793.92
15 % waste added for Glue down carpet -	heavy traffic.					
685. Floor prep (scrape rubber back residue)	221.27 SF		0.00	0.34	0.00	75.23
586. Mask or cover per square foot	221.27 SF		0.25	0.00	0.00	55.32
687. Final cleaning - construction - Commercial	221.27 SF		0.00	0.11	0.00	24.34
Totals: Roy's Office					0.00	1,711.08

Height: 8' 6"

#### Storage Area/Room

683.92 SF Walls 1,127.54 SF Walls & Ceiling 49.29 SY Flooring 91.17 LF Ceil. Perimeter

443.63 SF Ceiling 443.63 SF Floor

78.17 LF Floor Perimeter

Door 13' X 7' **Opens into Exterior** Door 3' X 6' 8" **Opens into OFFICE** 4' X 6' 8" Door **Opens into Exterior** Door 4' X 6' 8" **Opens into Exterior** 

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
688. Suspended ceiling system - 2' x 4'	443.63 SF		0.00	2.24	0.00	993.73
689. Batt insulation - 6" - R19 - paper aced	443.63 SF		0.00	0.65	0.00	288.36





### **CONTINUED - Storage Area/Room**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
690. Fluorescent light fixture - 2' & 4' - Detach & reset	6.00 EA		0.00	60.04	0.00	360.24
691. Clean light fixture - fluorescent	6.00 EA		0.00	7.78	0.00	46.68
692. Stud wall - 2" x 4" - 16" oc	119.71 SF		0.00	1.54	0.00	184.35
693. 5/8" drywall - hung, taped, heavy texture, ready for paint	683.92 SF	0 /	0.00	1.80	0.00	1,231.06
694. Seal/prime then paint the walls twice (3 coats)	683.92 SF	(/	0.00	0.84	0.00	574.49
695. Batt insulation - 4" - R13 - paper faced	512.94 SF		0.00	0.50	0.00	256.47
696. Paint door slab only - 2 coats (per side)	2.00 EA		0.00	24.16	0.00	48.32
697. Paint door or window opening - 2 coats (per side)	2.00 EA		0.00	20.22	0.00	40.44
698. Cove base molding - rubber or vinyl, 4" high	78.17 LF		0.00	1.37	0.00	107.09
699. Final cleaning - construction - Commercial	443.63 SF		0.00	0.11	0.00	48.80
700. Mask or cover per square foot	443.63 SF		0.25	0.00	0.00	110.91
Totals: Storage Area/Room					0.00	4,290.94

13' 12' 6" 1

Office

817.92 SF Walls 1,209.18 SF Walls & Ceiling

43.47 SY Flooring 96.23 LF Ceil. Perimeter Height: 8' 6"

391.26 SF Ceiling 391.26 SF Floor

96.23 LF Floor Perimeter

Door Door 3' X 6' 8" 3' X 6' 8" Opens into STORAGE\_AREA Opens into Exterior

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
701. Suspended ceiling system - 2' x 4'	391.26 SF		0.00	2.24	0.00	876.42
702. Batt insulation - 6" - R19 - paper faced	391.26 SF		0.00	0.65	0.00	254.32
703. Fluorescent light fixture - 2' & 4' - Detach & reset	6.00 EA		0.00	60.04	0.00	360.24
704. Clean light fixture - fluorescent	6.00 EA		0.00	7.78	0.00	46.68
705. Light bulb - Fluorescent tube - 4' soft white - mat. only	4.00 EA		0.00	4.50	0.00	18.00





### **CONTINUED - Office**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
706. 5/8" drywall - hung, taped, heavy texture, ready for paint	817.92 SF		0.00	1.80	0.00	1,472.26
707. Seal/prime then paint the walls twice (3 coats)	817.92 SF		0.00	0.84	0.00	687.05
708. Batt insulation - 4" - R13 - paper faced	817.92 SF	,	0.00	0.50	0.00	408.96
709. Outlet	4.00 EA	1	0.00	11.88	0.00	47.52
710. Interior door unit	1.00 EA		0.00	116.05	0.00	116.05
711. Door knob - interior	1.00 EA		0.00	28.65	0.00	28.65
712. Paint door or window opening - 2 coats (per side)	2.00 EA		0.00	20.22	0.00	40.44
713. Cove base molding - rubber or vinyl, 4" high	96.23 LF		0.00	1.37	0.00	131.84
714. Glue down carpet - heavy traffic	449.95 SF		0.00	3.12	0.00	1,403.84
15 % waste added for Glue down carpet -	heavy traffic.					
715. Floor prep (scrape rubber back residue)	391. <b>26</b> SF		0.00	0.34	0.00	133.03
716. Final cleaning - construction - Commercial	391.26 SF		0.00	0.11	0.00	43.04
717. Mask or cover per square foot	391.26 SF		0.25	0.00	0.00	97.82
718. Paint door slab only - 2 coats (per side)	2.00 EA		0.00	24.16	0.00	48.32
Totals: Office				•	0.00	6,214.48
Total: Main Level					0.00	31,960.08
Total: Building 15 - Hewitt Hangar Interi	or				0.00	31,960.08

Building 16 - FBO Hangar Roof
Exterior

### **South Elevation**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
725. R&R PVC schedule 40 conduit 6"	i, 134.00 LF		1.21	13.87	0.00	2,020.72
Note: (2) high volume downspouts co	onstructed of 6" schedule	40 PVC extendir	ng from the upper	eave to the ground.67	l.f. each	
726. Detach & Reset Gutter / downspout - box - galvanized - 6"	120.00 LF	2.40	0.00	0.00	0.00	288.00
Potals: South Elevation					0.00	2,308.72





### **West Elevation**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
727. R&R Wall/roof panel - ribbed - 24 gauge - 1 1/8" to 1 1/2"	3,324.00 SF		0.30	2.97	0.00	10,869.48
Note: Metal wall panels above the bloc matched and is obsolete requiring the e			ls damaged in vari	ious locations within	n the wall. The me	al cannot be
728. Prime & paint metal wall panels	3,324.00 SF		0.00	0.62	0.00	2,060.88
729. Battens - 2x2 - for steel roofing	33.33 SQ		0.00	96.90	0.00	3,229.68
Note: Battens secured to the steel fram.	ing to fasten the new w	vall panels. Also i	epair of damaged	steel mullions		
730. R&R Metal outside corner post	30.00 LF		0.74	4.08	0.00	144.60
731. R&R Gable trim for metal roofing - 26 gauge	178.00 LF		0.49	3.73	0.00	751.16
732. R&R Metal J trim	86.00 LF		0.61	2.02	0.00	226.18
733. Metal Structure Installer - per hour	32.00 HR		0.00	44.55	0.00	1,425.60
Note: Additional cost for lost production (2) men x 2 days x 8 HOURS per day =		ight, working from	n a lift and compli	ance to safety regul	ations.	
734. Letters - metal - Detach & reset	30.00 LF		0.00	51.96	0.00	1,558.80
lote: Large wall mounted sign						
Totals: West Elevation					0.00	20,266.38
Total: Exterior					0.00	22,575.10





### **South Flat Roof**

3,867.38 Surface Area332.92 Total Perimeter Length

38.67 Number of Squares

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
735. Remove Tear off, haul and dispose of 3 ply built-up roofing	38.67 SQ		33.07	0.00	0.00	1,278.82
736. Built-up 3 ply roofing - in place	38.67 SQ		0.00	195.56	0.00	7,562.31
737. Elastomeric roof primer	3,867.38 SF		0.00	0.28	0.00	1,082.87
738. Elastomeric roof coating - Flat roof	3,867.38 SF		0.00	1.53	0.00	5,917.09
39. R&R Flash parapet wall only - oitumen	149.00 LF		1.18	7.58	0.00	1,305.24



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546



#### **CONTINUED - South Flat Roof**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
740. R&R Membrane roofing - cant strips - wood	149.00 LF		0.40	2.20	0.00	387.40
741. R&R Counterflashing - Apron flashing	149.00 LF		0.34	5.14	0.00	816.52
742. R&R Gravel stop	183.00 LF		0.20	1.18	0.00	252.54
743. R&R Furnace vent - rain cap and storm collar, 8"	2.00 EA		6.30	57.82	0.00	128.24
744. Fiberboard - I"	3.867.38 SF		0.00	0.65	0.00	2,513.80
,	3.867.38 SF		0.00	0.65	0.00	2,513

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

745: Insulation - ISO board: 3"

38.67 SQ

0.00

218.42

0.00

8,446.30

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

746. Insulation - ISO board, 4"

12:76 SQ

0.00

266.88

0.00

3,405.39

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

this item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

Note: Considers tapered insulation to comply with 1/4" per foot drainage requirements.

747. 2" x 6" lumber (1 BF per LF)

360.00 LF

0.00

1.73

0.00

622.80

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

**Note:** Double perimeter band (3") installed to fasten perimeter coping after installation of insulation.

748. Steel wall coping

180.00 LF

0.00

9.37

0:00

1.686.60

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

749. Remove Additional charge for high roof (2 stories or greater)	38.67 SQ	3.11	0.00	0.00	120.26
750. Additional charge for high roof (2 stories or greater)	38.67 SQ	0.00	9.91	0.00	383.22

Totals: South Flat Roof 0.00 19,234.51

VICTORYCOSUB

12/13/2017

Page: 72



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546



#### **North Flat Roof**

3,833.60 Surface Area 298.11 Total Perimeter Length 38.34 Number of Squares

DESCRIPTION

DESCRIPTION

QTY

RESET

REMOVE

REPLACE

TAX

TOTAL


Note: No visible storm damage to the 3 ply built-up roof system. The roofing is very worn and in need of maintenance. Both gutters remain intact.

Totals: North Flat Roof



0.00


0.00



#### **Pitched Metal Roof**

21,492.38 Surface Area 359.48 Total Perimeter Length 214.92 Number of Squares 120.00 Total Ridge Length

DESCRIPTION	VIY	RESET	REMOVE	REPLACE	TAX	TOTAL
751. Metal Structure Installer - per hour	16.00 HR		0.00	44.55	0.00	712.80
Note: Repair (2) damaged standing see	um panels at the South	east corner of the	Hangar roof. (2)	men x 8 hours each du	e to height and c	onditions.
752. Material Only Standing seam metal roofing	178.00 SF		0.00	2.05	0.00	364.90
753. R&R Gable trim for metal roofing - 26 gauge	89.00 LF		0.49	3.73	0.00	375.58
Totals: Pitched Metal Roof					0.00	1,453.28



#### Roof4

602.72 Surface Area 88.26 Total Perimeter Length 6.03 Number of Squares

19.00 Total Ridge Length

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
754. R&R Metal roofing - ribbed - 26	602.72 SF		0.30	3.30	0.00	2,169.80





#### **CONTINUED - Roof4**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
755. Vinyl-faced/laminated insulation - 2"	SF		0.00	0.46	0.00	0.00
756. Elastomeric roof primer	602.72 SF	1/	0.00	0.28	0.00	168.76
757. Elastomeric roof coating - Rib roof	602.72 SF		0.00	2.11	0.00	1,271.74
758. R&R Eave trim for metal roofing - 26 gauge	36.00 LF		0.49	3.43	0.00	141.12
759. R&R Flashing - pipe jack	1.00 EA		4.14	23.34	0.00	27.48
760. R&R Ridge cap - metal roofing	19.00 LF		1.62	3.50	0.00	97.28
761. R&R Gable trim for metal roofing - 26 gauge	36.00 LF		0.49	3.73	0.00	151.92
762. R&R Valley metal - (W) profile	8.00 LF		0.34	3.64	0.00	31.84
763. Closure strips for metal roofing - inside and/or outside	76.00 LF		0.00	1.16	0.00	88.16
Totals: Roof4					0.00	4,148.10
Total: Roof					0.00	24,835.89
Total: Building 16 - FBO Hangar Roof					0.00	47,410.99

Building #16 - FBO Hangar Interior

Main Level

1.1.9	— 10' 5'		-
91	4	2 4 4 4 4 4 4 4 4 4 4 4 4 4 4 4 4 4 4 4	te
7'3"	Break R	oom 5	
1	6' 10" -		-

Break Room Height: 8' 4"

380.79 SF Walls 554.67 SF Walls & Ceiling 19.32 SY Flooring 45.72 LF Ceil. Perimeter 173.88 SF Ceiling 173.88 SF Floor 45.72 LF Floor Perimeter


Window Door Missing Wall 4' X 4' 3' X 6' 8" 8' 11 15/16" X 8' 3 15/16" Opens into Exterior
Opens into OFFICE
Opens into HALLWAY

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
764. R&R Suspended ceiling tile - 2' x 4'	173.88 SF		0.11	1.22	0.00	231.26
765. R&R Batt insulation - 6" - R19 - paper faced	173.88 SF		0.17	0.65	0.00	142.58
766. R&R Recessed light fixture	1.00 EA		6.55	98.35	0.00	104.90



#### **CONTINUED - Break Room**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
767. 5/8" - drywall per LF - up to 2' tall	27.28 LF		0.00	6.02	0.00	164.23
768. Batt insulation - 4" - R13 - paper faced	54.56 SF		0.00	0.50	0.00	27.28
769. Texture drywall - heavy hand texture	380.79 SF		0.00	0.58	0.00	220.86
770. Seal/prime then paint the walls twice (3 coats)	380.79 SF		0.00	0.84	0.00	319.86
771. Casing - 2 1/4"	18.00 LF		0.00	1.24	0.00	22.32
772. Paint door slab only - 2 coats (per side)	1.00 EA		0.00	24.16	0.00	24.16
773. Paint door or window opening - 2 coats (per side)	2.00 EA		0.00	20.22	0.00	40.44
774. Clean window unit (per side) 10 - 20 SF	1.00 EA		0.00	8.32	0.00	8.32
775. Clean window blind - horizontal or vertical	16.00 SF		0.00	0.71	0.00	11.36
776. Ice maker - Detach & reset	1.00 EA		0.00	122.16	0.00	122.16
777. Trim board - 1" x 6" - installed (cedar)	45.72 LF		0.00	3.98	0.00	181.97
Note: Baseboard						
778. Clean floor - tile	173.88 SF		0.00	0.36	0.00	62.60
779. Mask or cover per square foot	173.88 SF		0.25	0.00	0.00	43.47
780. Final cleaning - construction - Commercial	173.88 SF		0.00	0.11	0.00	19.13
Totals: Break Room					0.00	1,746.90



**Quite Room 2** 

263.14 SF Walls 326.72 SF Walls & Ceiling

7.06 SY Flooring

31.90 LF Ceil. Perimeter

Height: 8' 3"

63.58 SF Ceiling 63.58 SF Floor

31.90 LF Floor Perimeter

3' X 6' 8"

**Opens into HALLWAY** 

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
781. 5/8" - drywall per LF - up to 2'	24.00 LF		0.00	6.02	0.00	144.48

Note: Includes (1) long wall and (2) short walls.


Door





### **CONTINUED - Quite Room 2**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
782. Batt insulation - 4" - R13 - paper faced	48.00 SF		0.00	0.50	0.00	24.00
783. Texture drywall - heavy hand texture	263.14 SF		0.00	0.58	0.00	152.62
784. Seal/prime then paint the walls twice (3 coats)	263.14 SF		0.00	0.84	0.00	221.04
785. Paint door slab only - 2 coats (per side)	1.00 EA	. /	0.00	24.16	0.00	24.16
786. Paint door or window opening - 2 coats (per side)	1.00 EA		0.00	20.22	0.00	20.22
787. Outlet	2.00 EA		0.00	11.88	0.00	23.76
788. Trim board - 1" x 6" - installed (cedar)	31.90 LF		0.00	3.98	0.00	126.96
Note: Baseboard						
789. Clean floor - tile	63.58 SF		0.00	0.36	0.00	22.89
790. Mask or cover per square foot	63.58 SF		0.25	0.00	0.00	15.90
791. Final cleaning - construction - Commercial	63.58 SF		0.00	0.11	0.00	6.99
Totals: Quite Room 2					0.00	783.02



Quite Room 1

O4 OF Walls

Height: 8' 3"

332.84 SF Walls 430.21 SF Walls & Ceiling 10.82 SY Flooring

10.82 SY Flooring 40.34 LF Ceil. Perimeter 97.38 SF Ceiling 97.38 SF Floor

40.34 LF Floor Perimeter

Door 3' X 6' 8" Opens into HALLWAY

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
792. 5/8" - drywall per LF - up to 2' tall	28.17 LF		0.00	6.02	0.00	169.58
Note: Includes (1) long wall and (2) show	rt walls.					
793. Batt insulation - 4" - R13 - paper faced	56.34 SF		0.00	0.50	0.00	28.17
794. Texture drywall - heavy hand texture	332.84 SF		0.00	0.58	0.00	193.05
795. Seal/prime then paint the walls twice (3 coats)	332.84 SF		0.00	0.84	0.00	279.59
796. Paint door slab only - 2 coats (per ide)	1.00 EA		0.00	24.16	0.00	24.16

**VICTORY COSUB** 

12/13/2017

Page: 76



### **CONTINUED - Quite Room 1**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
797. Paint door or window opening - 2 coats (per side)	1.00 EA		0.00	20.22	0.00	20.22
798. Outlet	2.00 EA		0.00	11.88	0.00	23.76
799. Trim board - 1" x 6" - installed (cedar)	40.34 LF	/	0.00	3.98	0.00	160.55
Note: Baseboard		, /				
800. Clean floor - tile	97.38 SF		0.00	0.36	0.00	35.06
801. Mask or cover per square foot	97.38 SF		0.25	0.00	0.00	24.35
802. Final cleaning - construction - Commercial	97.38 SF		0.00	0.11	0.00	10.71
Totals: Quite Room 1					0.00	969.20

on 51° 6° 8' 10° 0 51° 13' 4" 6° 10° 1 51° 13' 4" 6° 10° 1 51° 13' 4" 6° 10° 1 51° 13' 4" 6° 10° 1 51°

Hallway	
Add way	

Height: 8' 4"

568.87 SF Walls 829.71 SF Walls & Ceiling 28.98 SY Flooring 73.91 LF Ceil. Perimeter 260.84 SF Ceiling260.84 SF Floor66.91 LF Floor Perimeter

Missing Wall	8' 11	15/16" X 8' 3 1	5/16"
Door	3' X	6' 8"	
Door	3' X	6' 8"	
Door	3' X	6' 8"	
Missing Wall - Goes to Floor	4' X	6' 8"	
Missing Wall - Goes to Floor	3' X	6' 8"	
DESCRIPTION	OTV	DECET	DEA


Opens into BREAK\_ROOM
Opens into QUITE\_ROOM\_2
Opens into QUITE\_ROOM\_1
Opens into Exterior
Opens into LOUNGE

Missing Wall - Goes to Floor	3' X 6' 8"		0	Opens into BUSINESS_CEN		
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
803. R&R Suspended ceiling tile - 2' x 4'	64.00 SF		0.11	1.22	0.00	85.12
Note: (8) tiles						
804. R&R Batt insulation - 6" - R19 - paper faced	64.00 SF		0.17	0.65	0.00	52.48
805. Recessed light fixture - Detach & reset trim only	1.00 EA		0.00	1.46	0.00	1.46
806. 5/8" - drywall per LF - up to 2' tall	66.91 LF		0.00	6.02	0.00	402.80
807. Batt insulation - 4" - R13 - paper faced	58.00 SF		0.00	0.50	0.00	29.00
808. Texture drywall - heavy hand exture	568.87 SF		0.00	0.58	0.00	329.94



### **CONTINUED - Hallway**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
809. Seal/prime then paint the walls twice (3 coats)	568.87 SF		0.00	0.84	0.00	477.85
810. Casing - 2 1/4"	92.00 LF		0.00	1.24	0.00	114.08
811. Paint door slab only - 2 coats (per side)	2.00 EA		0.00	24.16	0.00	48.32
812. Paint French door slab only - 2 coats (per side)	2.00 EA		0.00	46.22	0.00	92.44
813. Paint door or window opening - 2 coats (per side)	3.00 EA		0.00	20.22	0.00	60.66
814. Paint door or window opening - Large - 2 coats (per side)	1.00 EA		0.00	23.79	0.00	23.79
815. Cabinetry - upper (wall) units - Detach & reset	4.00 LF		0.00	32.25	0.00	129.00
816. Shelving - Detach & reset	6.00 LF		0.00	4.62	0.00	27.72
817. Outlet	3.00 EA		0.00	11.88	0.00	35.64
818. Trim board - 1" x 6" - installed (cedar)	66.91 LF		0.00	3.98	0.00	266.30
Note: Baseboard						
19. Clean floor - tile	260.84 SF		0.00	0.36	0.00	93.90
820. Mask or cover per square foot	260.84 SF		0.25	0.00	0.00	65.21
821. Final cleaning - construction - Commercial	260.84 SF		0.00	0.11	0.00	28.69
Totals: Hallway					0.00	2,364.40



Office Height: 8' 4"

> 362.27 SF Walls 480.24 SF Walls & Ceiling

13.11 SY Flooring

117.97 SF Floor 43.50 LF Floor Perimeter

43.50 LF Ceil. Perimeter

Window Door

4' X 4' 3' X 6' 8"

**Opens into Exterior** Opens into BREAK\_ROOM

117.97 SF Ceiling

QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
32.00 SF		0.11	1.22	0.00	42.56
32.00 SF		0.17	0.65	0.00	26.24
11.00 LF		0.00	6.02	0.00	66.22
	32.00 SF 32.00 SF	32.00 SF 32.00 SF	32.00 SF 0.11 32.00 SF 0.17	32.00 SF 0.11 1.22 32.00 SF 0.17 0.65	32.00 SF 0.11 1.22 0.00 32.00 SF 0.17 0.65 0.00



#### **CONTINUED - Office**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Note: Exterior wall only						
825. Batt insulation - 4" - R13 - paper faced	22.00 SF		0.00	0.50	0.00	11.00
826. Texture drywall - heavy hand texture	362.27 SF		0.00	0.58	0.00	210.12
827. Seal/prime then paint the walls twice (3 coats)	362.27 SF		0.00	0.84	0.00	304.31
828. Paint door slab only - 2 coats (per side)	1.00 EA		0.00	24.16	0.00	24.16
829. Paint door or window opening - 2 coats (per side)	2.00 EA	1/	0.00	20.22	0.00	40.44
830. Clean window unit (per side) 10 - 20 SF	1.00 EA		0.00	8.32	0.00	8.32
831. Clean window blind - horizontal or vertical	16.00 SF		0.00	0.71	0.00	11.36
832. Trim board - 1" x 6" - installed (cedar)	43.50 LF		0.00	3.98	0.00	173.13
Note: Baseboard						
833. Clean floor - tile	117.97 SF		0.00	0.36	0.00	42.47
334. Mask or cover per square foot	117.97 SF		0.25	0.00	0.00	29.49
835. Final cleaning - construction - Commercial	117.97 SF		0.00	0.11	0.00	12.98
Totals: Office					0.00	1,002.80



**Business Center** 

Height: 8'

376.00 SF Walls 528.23 SF Walls & Ceiling 16.91 SY Flooring 49.50 LF Ceil. Perimeter

152.23 SF Ceiling 152.23 SF Floor 46.50 LF Floor Perimeter

Missing Wall - Goes to Floor

3' X 6' 8"

### **Opens into HALLWAY**

DESCRIPTION	OTY	RESET	REMOVE	REPLACE	TAX	TOTAL
836. R&R Suspended ceiling tile - 2' x 4'	24.00 SF		0.11	1.22	0.00	31.92
Note: (3) tiles						
837. R&R Batt insulation - 6" - R19 - paper faced	24.00 SF		0.17	0.65	0.00	19.68
838. 5/8" - drywall per LF - up to 2'	11.42 LF		0.00	6.02	0.00	68.75
AT A D II I						

Note: Rear wall only





Door

DESCRIPTION

Missing Wall - Goes to Floor

8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### **CONTINUED - Business Center**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
839. Batt insulation - 4" - R13 - paper faced	22.84 SF		0.00	0.50	0.00	11.42
840. Texture drywall - heavy hand texture	376.00 SF		0.00	0.58	0.00	218.08
841. Seal/prime then paint the walls twice (3 coats)	376.00 SF		0.00	0.84	0.00	315.84
842. Paint French door slab only - 2 coats (per side)	1.00 EA	,	0.00	46.22	0.00	46.22
843. Paint door or window opening - 2 coats (per side)	1.00 EA		0.00	20.22	0.00	20.22
844. Clean desk - secretary	3.00 EA		0.00	20.50	0.00	61.50
845. Outlet	4.00 EA		0.00	11.88	0.00	47.52
846. Trim board - 1" x 6" - installed (cedar)	46.50 LF		0.00	3.98	0.00	185.07
Note: Baseboard						
847. Clean floor - tile	152.23 SF		0.00	0.36	0.00	54.80
848. Mask or cover per square foot	152.23 SF		0.25	0.00	0.00	38.06
349. Mask wall - plastic, paper, tape per LF)	49.50 LF		0.00	0.82	0.00	40.59
850. Final cleaning - construction - Commercial	152.23 SF		0.00	0.11	0.00	16.75
Totals: Business Center					0.00	1,176.42

Height: 9' 10" Lounge 778.12 SF Walls 456.47 SF Ceiling 1,234.59 SF Walls & Ceiling 456.47 SF Floor 50.72 SY Flooring 75.24 LF Floor Perimeter 93.47 LF Ceil. Perimeter 7' 2" X 9' 9 15/16" **Missing Wall Opens into FOYER\_ENTRY Missing Wall** 7' 3/4" X 9' 9 15/16" **Opens into ENTRY** Opens into JANITORS\_CLO 3' X 6' 8" Door Window 4' X 4' **Opens into Exterior** Window 4' X 4' **Opens into Exterior** Window 4' X 4' **Opens into Exterior** 

VICTORYCOSUB 12/13/2017 Page: 80

RESET

REMOVE

**Opens into Exterior** 

REPLACE

**Opens into HALLWAY** 

TAX

TOTAL

3' X 6' 8"

4' X 6' 8"

QTY





# **CONTINUED - Lounge**


DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
851. Drywall Installer / Finisher - per hour	2.00 HR		0.00	56.00	0.00	112.00
Note: Detach & Reset / repair suspended	ceiling wall angle a	t East wall.				
852. R&R Suspended ceiling tile - 2' x 4'	456.47 SF		0.11	1.22	0.00	607.10
853. R&R Batt insulation - 6" - R19 - paper faced	456.47 SF		0.17	0.65	0.00	374.31
854. Recessed light fixture - Detach & reset trim only	4.00 EA		0.00	1.46	0.00	5.84
855. Cold air return cover - Detach & reset	2.00 EA		0.00	14.65	0.00	29.30
856. 5/8" drywall - hung, taped, ready for texture	267.00 SF		0.00	1.37	0.00	365.79
857. 5/8" - drywall per LF - up to 2' tall	25.50 LF	1/	0.00	6.02	0.00	153.51
858. Texture drywall - heavy hand texture	778.12 SF		0.00	0.58	0.00	451.31
859. Seal/prime then paint the walls twice (3 coats) - 2 colors	778.12 SF		0.00	1.03	0.00	801.46
60. Casing - 2 1/4"	143.00 LF		0.00	1.24	0.00	177.32
861. Paint door slab only - 2 coats (per side)	2.00 EA		0.00	24.16	0.00	48.32
862. Paint door or window opening - 2 coats (per side)	6.00 EA		0.00	20.22	0.00	121.32
863. Heat/AC register - Mechanically attached - Detach & reset	1.00 EA		0.00	10.74	0.00	10.74
864. R&R Exit sign - internal power	1.00 EA		7.35	215.26	0.00	222.61
865. Outlet or switch cover	4.00 EA		0.00	2.23	0.00	8.92
866. Trim board - 1" x 6" - installed (cedar)	75.24 LF		0.00	3.98	0.00	299.46
Note: Baseboard						
867. Clean floor - tile	456.47 SF		0.00	0.36	0.00	164.33
868. Mask or cover per square foot	456.47 SF		0.25	0.00	0.00	114.12
869. Final cleaning - construction - Commercial	456.47 SF		0.00	0.11	0.00	50.21
Totals: Lounge					0.00	4,117.97



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

Mens





412.33 SF Walls 533.36 SF Walls & Ceiling 13.45 SY Flooring 49.51 LF Ceil. Perimeter

121.04 SF Ceiling 121.04 SF Floor 49.51 LF Floor Perimeter


Height: 8' 4"

Door	3' X 6' 8"	Opens into RESTROOM_HAL
------	------------	-------------------------

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
870. R&R Suspended ceiling tile - 2' x 2'	8.00 SF		0.13	1.23	0.00	10.88
Note: (2) tiles						
871. Batt insulation - 6" - R19 - paper faced	8.00 SF		0.00	0.65	0.00	5.20
872. 5/8" - drywall per LF - up to 2' tall	31.67 LF		0.00	6.02	0.00	190.65
873. Batt insulation - 4" - R13 - paper faced	31.67 SF		0.00	0.50	0.00	15.84
874. Texture drywall - heavy hand exture	412.33 SF		0.00	0.58	0.00	239.15
875. Seal/prime then paint the walls twice (3 coats)	412.33 SF		0.00	0.84	0.00	346.36
876. Outlet	1.00 EA		0.00	11.88	0.00	11.88
877. Paint door or window opening - 2 coats (per side)	1.00 EA		0.00	20.22	0.00	20.22
878. Bathroom mirror - Detach & reset	1.00 SF		0.00	5.34	0.00	5.34
879. Handicap grab bar - Detach & reset	1.00 EA		0.00	19.21	0.00	19.21
880. Remove Paper towel dispenser	1.00 EA		8.82	0.00	0.00	8.82
881. Clean vanity - faces only	2.00 LF		0.00	3.62	0.00	7.24
882. Clean toilet partition - per stall	2.00 EA		0.00	14.67	0.00	29.34
883. Trim board - 1" x 6" - installed (cedar)	49.51 LF		0.00	3.98	0.00	197.05
Note: Baseboard						
884. Clean floor - tile	121.04 SF		0.00	0.36	0.00	43.57
885. Mask or cover per square foot	121.04 SF		0.25	0.00	0.00	30.26
886. Final cleaning - construction - Commercial	121.04 SF		0.00	0.11	0.00	13.31
Totals: Mens					0.00	1,194.32



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546





#### **Restroom Hall**

Height: 8' 4"

253.92 SF Walls311.63 SF Walls & Ceiling6.41 SY Flooring30.49 LF Ceil. Perimeter

57.71 SF Ceiling57.71 SF Floor30.49 LF Floor Perimeter

Door Door 3' X 6' 8" 3' X 6' 8" Opens into NEUTRAL\_TOIL Opens into MENS

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
887. R&R Suspended ceiling tile - 2' x 2'	57.71 SF		0.13	1.23	0.00	78.48
888. R&R Batt insulation - 6" - R19 - paper faced	57.71 SF		0.17	0.65	0.00	47.32
889. 5/8" - drywall per LF - up to 2' tall	30.49 LF		0.00	6.02	0.00	183.55
890. Batt insulation - 4" - R13 - paper faced	60.98 SF		0.00	0.50	0.00	30.49
891. Texture drywall - heavy hand exture	253.92 SF		0.00	0.58	0.00	147.27
892. Seal/prime then paint the walls twice (3 coats)	253.92 SF		0.00	0.84	0.00	213.29
893. Paint door slab only - 2 coats (per side)	2.00 EA		0.00	24.16	0.00	48.32
894. Paint door or window opening - 2 coats (per side)	2.00 EA		0.00	20.22	0.00	40.44
895. Trim board - 1" x 6" - installed (cedar)	30.49 LF		0.00	3.98	0.00	121.35
Note: Baseboard						
896. Clean floor - tile	57.71 SF		0.00	0.36	0.00	20.78
897. Mask or cover per square foot	57.71 SF		0.25	0.00	0.00	. 14.43
898. Final cleaning - construction - Commercial	57.71 SF		0.00	0.11	0.00	6.35
Totals: Restroom Hall					0.00	952.07

**VICTORYCOSUB** 

12/13/2017

Page: 83



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546



Neutral Toilet

Height: 8' 4"

227.55 SF Walls274.18 SF Walls & Ceiling5.18 SY Flooring27.32 LF Ceil. Perimeter

46.63 SF Ceiling46.63 SF Floor27.32 LF Floor Perimeter

Door	3' X 6' 8"		Opens into RESTROOM_HAL			
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
899. R&R Suspended ceiling tile - 2' x 2'	4.00 SF		0.13	1.23	0.00	5.44
Note: (1) tile						
900. Batt insulation - 6" - R19 - paper faced	4.00 SF		0.00	0.65	0.00	2.60
901. 5/8" - drywall per LF - up to 2' tall	27.32 LF		0.00	6.02	0.00	164.47
902. Batt insulation - 4" - R13 - paper faced	54.65 SF		0.00	0.50	0.00	27.33
903. Texture drywall - heavy hand exture	227.55 SF		0.00	0.58	0.00	131.98
904. Seal/prime then paint the walls twice (3 coats)	227.55 SF		0.00	0.84	0.00	191.14
905. Sink - wall mounted - Detach & reset	1.00 EA		0.00	163.12	0.00	163.12
906. Sink faucet - Detach & reset	1.00 EA		0.00	80.35	0.00	80.35
907. Toilet - Detach	1.00 EA		0.00	29.11	0.00	29.11
908. Outlet	1.00 EA		0.00	11.88	0.00	11.88
909. Paint door or window opening - 2 coats (per side)	1.00 EA		0.00	20.22	0.00	20.22
910. Trim board - 1" x 6" - installed (cedar)	27.32 LF		0.00	3.98	0.00	108.73
Note: Baseboard						
911. Clean floor - tile	46.63 SF		0.00	0.36	0.00	16.79
912. Mask or cover per square foot	46.63 SF		0.25	0.00	0.00	11.66
913. Final cleaning - construction - Commercial.	46.63 SF		0.00	0.11	0.00	5.13

**VICTORYCOSUB** 

Totals: Neutral Toilet

12/13/2017

0.00

Page: 84

969.95




Missing Wall

8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546



7' 2" X 8'



Foyer/Entry

237.33 SF Walls 317.36 SF Walls & Ceiling 8.89 SY Flooring

36.83 LF Ceil. Perimeter

80.03 SF Ceiling 80.03 SF Floor 29.67 LF Floor Perimeter

Height: 8'


Door 3' X 6' 8"
Window 5' 10" X 4'
Door 3' X 6' 8"

Opens into Exterior
Opens into DISPATCH
Opens into DISPATCH
Opens into LOUNGE

DESCRIPTION	QTY RESET	REMOVE	REPLACE	TAX	TOTAL
DESCRIPTION	Q11 KDSE1	REMOTE	REI LACE	IAA	TOTAL
914. 5/8" - drywall per LF - up to 2' tall	14.83 LF	0.00	6.02	0.00	89.28
915. Texture drywall - heavy hand texture	237.33 SF	0.00	0.58	0.00	137.65
916. Seal/prime then paint the walls and ceiling twice (3 coats)	317.36 SF	0.00	0.84	0.00	266.58
917. Paint door slab only - 2 coats (per lide)	2.00 EA	0.00	24.16	0.00	48.32
918. Paint door or window opening - 2 coats (per side)	2.00 EA	0.00	20.22	0.00	40.44
919. Trim board - 1" x 6" - installed (cedar)	14.83 LF	0.00	3.98	0.00	59.02
Note: Baseboard					
920. Clean floor - tile	80.03 SF	0.00	0.36	0.00	28.81
921. Mask or cover per square foot	80.03 SF	0.25	0.00	0.00	20.01
922. Final cleaning - construction - Commercial	80.03 SF	0.00	0.11	0.00	8.80
Totals: Foyer/Entry				0.00	698.91



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

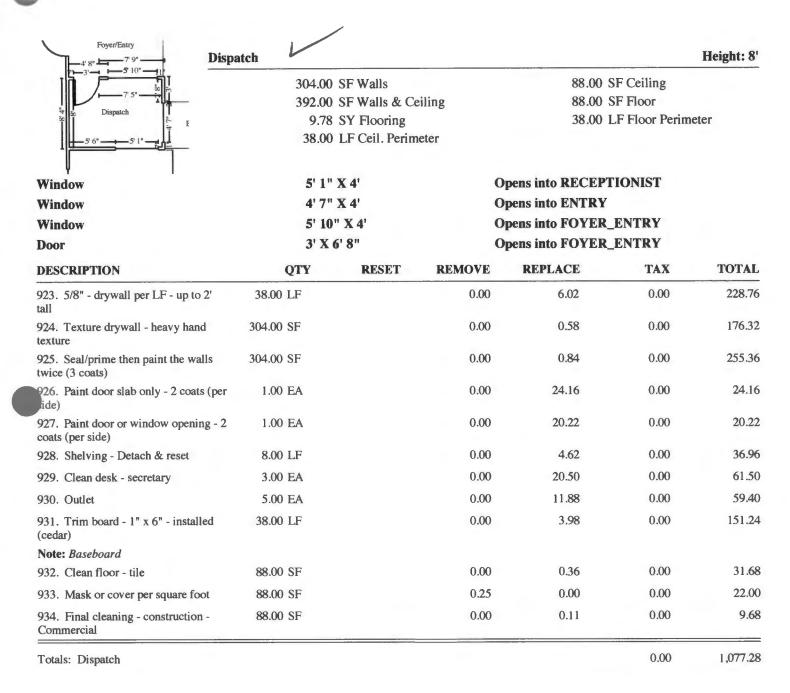





	<del></del> 7' 1"		
-4.7"	Entry	51	Supply Closes
<u>_</u> <u>}_</u>		1.2"	2

Entry

Height: 8'

90.67 SF Walls

129.51 SF Walls & Ceiling

4.32 SY Flooring

18.40 LF Ceil. Perimeter

38.84 SF Ceiling

38.84 SF Floor

11.33 LF Floor Perimeter

Window Missing Wall

Door

**Missing Wall** 

4' 7" X 4'

7' 3/4" X 8'

3' X 6' 8"

7' 3/4" X 8'

Opens into DISPATCH

**Opens into LOUNGE** 

Opens into SUPPLY\_CLOSE

**Opens into RECEPTIONIST** 

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
935. R&R Suspended ceiling tile - 2' x 4'	38.84 SF		0.11	1.22	0.00	51.65
936. Remove Batt insulation - 6" - R19 - paper faced	38.84 SF		0.17	0.00	0.00	6.60
937. Install Batt insulation - 6" - R19 - paper faced	38.84 SF		0.00	0.23	0.00	8.93
938. Recessed light fixture - Detach & eset trim only	1.00 EA		0.00	1.46	0.00	1.46
939. 5/8" - drywall per LF - up to 2' tall	11.33 LF		0.00	6.02	0.00	68.21
940. Texture drywall - heavy hand texture	90.67 SF		0.00	0.58	0.00	52.59
941. Seal/prime then paint the walls twice (3 coats)	90.67 SF		0.00	0.84	0.00	76.16
942. Casing - 2 1/4"	18.00 LF		0.00	1.24	0.00	22.32
943. Paint door slab only - 2 coats (per side)	1.00 EA		0.00	24.16	0.00	24.16
944. Paint door or window opening - 2 coats (per side)	1.00 EA		0.00	20.22	0.00	20.22
945. Shelving - Detach & reset	5.00 LF		0.00	4.62	0.00	23.10
946. Heat/AC register - Mechanically attached - Detach & reset	1.00 EA		0.00	10.74	0.00	10.74
947. Outlet	1.00 EA		0.00	11.88	0.00	11.88
948. Trim board - 1" x 6" - installed (cedar)	11.33 LF		0.00	3.98	0.00	45.09
Note: Baseboard						
949. Clean floor - tile	38.84 SF		0.00	0.36	0.00	13.98
950. Mask or cover per square foot	38.84 SF		0.25	0.00	0.00	9.71
951. Final cleaning - construction - Commercial	38.84 SF		0.00	0.11	0.00	4.27
Cotals: Entry					0.00	451.07


**VICTORY COSUB** 

12/13/2017

Page: 87







## Receptionist / Waiting



342.77 SF Ceiling

Height: Peaked

334.10 SF Floor

71.77 LF Floor Perimeter

13' 8"I		
Door	3' X 6' 8"	<b>Opens into SURVEILLANCE</b>
Window	3' X 5'	<b>Opens into Exterior</b>
Window	3' X 5'	<b>Opens into Exterior</b>
Window	3' X 5'	<b>Opens into Exterior</b>
Window	3' X 5'	<b>Opens into Exterior</b>
Window	3' X 5'	<b>Opens into Exterior</b>
Door	3' X 6' 8"	<b>Opens into Exterior</b>
Window	3' X 5'	<b>Opens into Exterior</b>
Window	3' X 5'	<b>Opens into Exterior</b>
Window	3' X 5'	<b>Opens into Exterior</b>
Window	3' X 5'	<b>Opens into Exterior</b>
Window	3' X 5'	<b>Opens into Exterior</b>
Window	3' X 5'	<b>Opens into Exterior</b>
Window	3' X 5'	<b>Opens into Exterior</b>
Window	5' 1" X 4'	<b>Opens into DISPATCH</b>
Missing Wall	7' 3/4" X 8' 5 1/16"	<b>Opens into ENTRY</b>

688.64 SF Walls

1,031.41 SF Walls & Ceiling

73.22 LF Ceil. Perimeter

37.12 SY Flooring

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
952. Batt insulation - 8" - R25 - unfaced batt	342.77 SF		0.00	0.82	0.00	281.07
953. 5/8" drywall - hung only (no tape or finish)	342.77 SF		0.00	0.98	0.00	335.91
954. Siding - tongue & groove - cedar	342.77 SF		0.00	4.18	0.00	1,432.78
Note: Solid ceiling installation						
955. Track lighting - track only	12.00 LF		0.00	17.64	0.00	211.68
956. Fixture (can) for track lighting	6.00 EA		0.00	25.47	0.00	152.82
957. 5/8" - drywall per LF - up to 2' tall	12.42 LF		0.00	6.02	0.00	74.77
958. Batt insulation - 4" - R13 - paper faced	25.00 SF		0.00	0.50	0.00	12.50
959. Texture drywall - heavy hand texture	287.39 SF		0.00	0.58	0.00	166.69
960. Seal/prime then paint the surface area twice (3 coats)	287.39 SF		0.00	0.84	0.00	241.41
961. Heat/AC register - Mechanically attached - Detach & reset	1.00 EA		0.00	10.74	0.00	10.74
VICTORYCOSUB					12/13/2017	Page: 88



# CONTINUED - Receptionist / Waiting

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
962. Clean countertop	8.00 SF		0.00	0.41	0.00	3.28
963. Clean window unit (per side) 10 - 20 SF	12.00 EA		0.00	8.32	0.00	99.84
964. Clean window unit (per side) 3 - 9 SF	7.00 EA		0.00	5.82	0.00	40.74
965. Clean window blind - horizontal or vertical	180.00 SF		0.00	0.71	0.00	127.80
966. Paint door slab only - 2 coats (per side)	1.00 EA		0.00	24.16	0.00	24.16
967. Paint door or window opening - 2 coats (per side)	1.00 EA		0.00	20.22	0.00	20.22
968. Paint door or window opening - Large - 2 coats (per side)	1.00 EA		0.00	23.79	0.00	23.79
969. Trim board - 1" x 6" - installed (cedar)	12.42 LF		0.00	3.98	0.00	49.43
Note: Baseboard						
970. R&R Outlet	1.00 EA		2.96	11.88	0.00	14.84
971. Clean floor - tile	334.10 SF		0.00	0.36	0.00	120.28
72. Mask wall - plastic, paper, tape (per LF)	73.22 LF		0.00	0.82	0.00	60.04
973. Mask or cover per square foot	334.10 SF		0.25	0.00	0.00	83.53
974. Contents - move out then reset - Large room	1.00 EA		0.00	42.27	0.00	42.27
975. Final cleaning - construction - Commercial	334.10 SF		0.00	0.11	0.00	36.75
Totals: Receptionist / Waiting					0.00	3,667.34
Total: Main Level					0.00	21,171.65
Total: Building #16 - FBO Hangar Interio	or				0.00	21,171.65

interior

Building 17 - Hangar B

#### Roof


DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL

Note: The 3 ply built-up roofing at both the North & South flat sections showed no visible damage. The north flat roof section had notable wear and needs some maintenance. The 24 gauge standing seam roof appeared undamaged.

Totals: Roof 0.00

**Exterior** 

0.00



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546



DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
982. Reglaze window, 1 - 9 sf	200.00 EA		0.00	42.44	0.00	8,488.00
Note: Based on the quote obtained from	local glass contracto	r, Mitchell Glass	which reflects \$47	per pane for putty ap	plication and di	fficult access.
983. Tarp - all-purpose poly - per sq ft (labor and material)	1,335.00 SF		0.00	0.51	0.00	680.85
Note: Temporary cover over section of b	oroken windows. Insta	alled battens to w	indow frames to se	ecure tarping.		
984. R&R Gutter - box - galvanized - 6*	29.00 LF		0.30	6.79	0.00	205.61
Note: Lower section of eave						
985. R&R Gutter - box - galvanized - 6"	120.00 LF		0.30	6.79	0.00	850.80
Note: Upper eave to be replaced comple	etely.					
986. R&R Downspout - box - galvanized - 6*	18.00 LF		0.30	6,79	0.00	127.62
987. R&R PVC schedule 40 conduit, 6*	126.00 LF		1.21	13.87	0.00	1,900.08
Note: (2) High volume downspouts cons.	tructed of 6" schedule	e 40 PVC extendi	ng from the upper	eave to the ground 6.	3 lf. each.	
988. R&R Hangar door - metal sliding v/ entry door- 13' x 16' -	1.00 EA		44.12	3,698.56	0.00	3,742.68
Note: This cost is subject to adjustment	once quotes are recei	ved.				
Totals: South Elevation					0.00	15,995.64
Total: Exterior					0.00	15,995.64
Inte	rior					
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
989. Roll-up door & hardware - 14' x	1.00 EA		0.00	1,834.13	0.00	1,834.13

	0.000	PEGER	PERFORE	DEDI LOD	m	momit
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
989. Roll-up door & hardware - 14' x 14' - 22 gauge	1.00 EA		0.00	1,834.13	0.00	1,834.13
Totals: Interior					0.00	1,834.13
Total: Building 17 - Hangar B					0.00	17,829.77

Building 18 - Hangar C

# Building 18 - Hangar C

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
3,176. Special Doors - Hangar Door - Wood Bi-Fold	3,600.00 SF	10	0.00	44.00	0.00	158,400.00
178. Reglaze 1/4" annealed/float glass - single pane	1,200.00 SF	MM)	0.00	6.10	0.00	7,320.00
VICTORYCOSUB		10			12/13/2017	Page: 9



# **CONTINUED - Building 18 - Hangar C**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
3,179. Fascia - metal - 6"	120.00 LF		0.00	3.02	0.00	362.40
3,180. Outside/Inside corner - 26 gauge	240.00 LF		0.00	4.06	0.00	974.40
Total: Building 18 - Hangar C		Parket		4	0.00	167,056.80

### Roof

FI Hanger C \$7

Hanger C

27,243.40 Surface Area 544.33 Total Perimeter Length 272.43 Number of Squares

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
,167. Temporary shoring post - Screw jack (per day)	3,200.00 EA		0.00	25.99	0.00	83,168.00
Shoring system for roof support during replacement where damaged or deficient		and progressive re	elocation around po	erimeter through c	ourse of lamella roc	f framing
3,177. Rafters - curved	8,800.00 LF		0.00	8.44	0.00	74,272.00
ALLOWANCE FOR LAMELLA ROOF	FRAMING REPAIL	RS AT PERIMET	TER			
3,156. Remove Metal roofing - High grade	21,794. SF 72		0.30	0.00	0.00	6,538.42
3,159. Remove Built-up 3 ply roofing - in place	272.43 SQ		33.07	0.00	0.00	9,009.26
3,160. R&R Sheathing - 1" x 6" - tongue and groove	9,081.13 SF		0.38	2.32	0.00	24,519.05
3,164. Ice & water shield	27,243. SF 40		0.00	1.02	0.00	27,788.27
3,163. Hat channel, 24" OC	27,243. SF 40		0.00	0.62	0.00	16,890.91
3,161. Metal roofing - Premium grade	27,243. SF 40		0.00	5.62	0.00	153,107.91
Radius metal over barrel roof frame of h	angar					
3,168. Endwall flashing for metal roofing - 26 gauge	260.00 LF		0.00	4.10	0.00	1,066.00
3,169. Wall/roof panel - ribbed - 24 gauge - 1 1/8" to 1 1/2"	960.00 SF		0.00	2.97	0.00	2,851.20
Parapet roof to wall						
3,170. Scissor lift - 26' platform height electric powered	120.00 DA		0.00	144.00	0.00	17,280.00
VICTORYCOSUB					12/13/2017	Page: 9





8380 Warren Parkway / Ste. 700 - Frisco, TX 75034

### **CONTINUED - Hanger C**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2 lifts for carpenters to replace damage	d lamella roof frame fr	om truss to ledge	r board			
3,171. Telehandler/forklift and operator	320.00 HR	-	0.00	67.31	0.00	21,539.20
3,172. General Laborer - per hour	320.00 HR		0.00	20.66	0.00	6,611.20
Labor hours for safety spotter and load	ing of materials on Sky	track				
3,173. Temporary fencing	240.00 LF		0.00	4.20	0.00	1,008.00
3,175. Fall protection harness and lanyard - per day	240.00 DA		0.00	6.40	0.00	1,536.00
6 men x 40 days						
Totals: Hanger C					0.00	447,185.42

### **Shed Ext**

Shed Ext

2,756.22 Surface Area 175.93 Total Perimeter Length 27.56 Number of Squares

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
3,155. R&R Metal roofing - High grade	2,756.22 SF		0.30	5.22	0.00	15,214.34
3,157. Rafters - 2x10 - stick frame roof (using rafter length)	1,600.00 LF		0.00	2.82	0.00	4,512.00
3,174. Purlin/girt, 2x6 - treated	1,240.00 LF		0.00	2.03	0.00	2,517.20
Totals: Shed Ext					0.00	22,243.54
Total: Roof					0.00	469,428.96
Total: Building 18 - Hangar C					0.00	636,485.76

### **General Conditions**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
3,181. Dumpster load - Approx. 40 yards, 7-8 tons of debris	20.00 EA		790.08	0.00	0.00	15,801.60
3,182. Commercial Supervision / Project Management - per hour	720.00 HR		0.00	47.69	0.00	34,336.80



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

# **CONTINUED - General Conditions**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Note: 60 days x 8 hours for Project Man 60 days x 4 hours for Pro						
3,183. Taxes, insurance, permits & fees (Bid Item)	1.00 EA		0.00	62,400.00	0.00	62,400.00
Architectural & Engineer fees for shoring	g and repair design - 8	8%				
Totals: General Conditions					0.00	112,538.40

Building #19 - Precinct 4 -Truck Storage Roof


# Truck Shed / Storage

3,156.96 Surface Area 264.51 Total Perimeter Length 31.57 Number of Squares

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
995. R&R Metal roofing - ribbed - 24 gauge - 1 1/8" to 1 1/2"	3,156.96 SF	1	0.30	3.70	0.00	12,627.84
996. R&R Aluminum sidewall/endwall flashing - mill finish	31.00 LF		0.34	3.86	0.00	130.20
997. Metal Structure Installer - per hour	32.00 HR		0.00	44.55	0.00	1,425.60
Note: (2) men x 2 days @ 8 hours per da	y to fabricate the str	uctural steel she	d frame.			
998. R&R Steel purlins - C-shape - 8"	400.00 LF		1.84	6.74	0.00	3,432.00
Note: (8) purlins 50 l.f. each						
999. R&R Post - 2 7/8" diameter metal 10'	2.00 EA		8.82	41.42	0.00	100.48
Note: Actual posts were 2 7/8" diameter	x 10' height. (8' heig	ht above ground	and 2' in the groun	d) spaced at 8' and s	et in concrete.	
1,000. R&R Angle - L 1 1/2" x 1 1/2" x 1 1/2" x 1/4" thick	16.00 LF		0.83	4.26	0.00	81.44
Note: (3) 1' steel brackets welded to each	h post to bolt the 2"x	4" battens. (46 pc	osts x 3)			
Totals: Truck Shed / Storage		1 1 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2			0.00	17,797.56








#### **Truck Shed Extension**

1,521.30 Surface Area 156.44 Total Perimeter Length 15.21 Number of Squares

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Note: This section was not visibly damaged.						
Totals: Truck Shed Extension					0.00	0.00
Total: Roof					0.00	17,797.56
Total: Building #19 - Precinct 4 -Truck Storage					0.00	17.797.56

Building 20 - Precinct 4 - Building Roof
Roof




#### Metal

8,108.01 Surface Area 234.41 Total Perimeter Length 81.08 Number of Squares 101.00 Total Ridge Length

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,006. R&R Metal roofing - ribbed - 24 gauge - 1 1/8" to 1 1/2"	3,952.65 SF		0.30	3.70	0.00	15,810.61
Note: South slop only which transitions	into the Truck Shed.	Remaining metal .	slopes showed no	visible damage.		
1,007. R&R Ridge cap - metal roofing	101.00 LF		1.62	3.50	0.00	517.12
1,008. R&R Closure strips for metal roofing - inside and/or outside	202.00 LF		0.49	1.16	0.00	333.30
1,009. R&R Skylight panels	8.00 EA		7.35	280.00	0.00	2,298.80
1,010. R&R Aluminum sidewall/endwall flashing - mill finish	41.00 LF		0.34	3.86	0.00	172.20
1,011. Detach & Reset Ridge vent - Metal roofing - floating ventilator	20.00 LF	10.71	0.00	0.00	0.00	214.20
Totals: Metal					0.00	19,346.23




8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546



#### Elevated / Flat BUR

699.46 Surface Area 58.00 Total Perimeter Length 6.99 Number of Squares

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Note: No visible damage to this section of roof.						
Totals: Elevated / Flat BUR		All I			0.00	0.00



# 2 Story / BUR

2,772.49 Surface Area 203.87 Total Perimeter Length 27.72 Number of Squares 43.00 Total Ridge Length

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,012. Remove Tear off, haul and dispose of 3 ply built-up roofing	27.72 SQ		33.07	0.00	0.00	916.70
1,013. Built-up 3 ply roofing - in place	27.72 SQ		0.00	195.56	0.00	5,420.92
1,014. R&R Gravel stop	203.87 LF		0.20	1.18	0.00	281.34
1,015. R&R Flash parapet wall only - bitumen	40.00 LF		1.18	7.58	0.00	350.40
1,016. R&R Membrane roofing - cant strips - wood	40.00 LF		0.40	2.20	0.00	104.00
1,017. R&R Counterflashing - Apron flashing	40.00 LF		0.34	5.14	0.00	219.20
1,018. R&R Flashing - pipe jack	1.00 EA		4.14	23.34	0.00	27.48
1,019. R&R Furnace vent - rain cap and storm collar, 8"	2.00 EA		6.30	57.82	0.00	128.24
1,020. Detach & Reset Exhaust cap - through roof - 6" to 8"	1.00 EA	41.00	0.00	0.00	0.00	41.00
1.021. Fiberboard - 1"	2.772.49 SF		0.00	0.65	0.00	1,802.12

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

.022. Insulation - ISO board, 3"

27:72 SQ

0.00

218.42

0.00


6,054.60





# CONTINUED - 2 Story / BUR

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
This item did not previously exist or expa incurred, subject to limits.	nds the scope of rep	airs, but is requir	ed by current build	ing codes. The code u	pgrade cost is pa	yable when
Note: Roof is pitched satisfactorily so tap	ered insulation is no	ot required for dr	alnage.			
1,023. 2" x 6" lumber (1 BF per LF)	418.00 LF		0.00	1.73	0.00	723.1
This item did not previously exist or expaincurred, subject to limits.	nds the scope of rep	airs, but is require	ed by current build	ing codes. The code u	pgrade cost is pa	yable when
This item did not previously exist or expa incurred, subject to limits.	nds the scope of rep	airs, but is requir	ed by current build	ing codes. The code u	pgrade cost is pa	yable when
Note: Double perimeter band (3") installe	ed to fasten perimete	er coping after in	stallation of insula	tion.		
1,024. Steel wall coping	209.00 LF		<del>0.00</del>	9.37	0.00	1,958.3
This item did not previously exist or expa incurred, subject to limits.	nds the scope of rep	airs, but is requir	ed by current build	ing codes. The code u	pgrade cost is pa	yable when
This item did not previously exist or expa incurred, subject to limits.	nds the scope of rep	airs, but is requir	ed by current build	ing codes. The code u	pgrade cost is pa	yable when
1,025. Remove Additional charge for high roof (2 stories or greater)	27.72 SQ		3.11	0.00	0.00	86.21
1,026. Additional charge for high roof (2 stories or greater)	27.72 SQ		0.00	9.91	0.00	274.71
Totals: 2 Story / BUR					0.00	7,850.20
Meta		Surface Area		33.89	Number of Squ	ares
Mall of	231.46	Total Perimete	er Length			
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Note: No visible damage to this section o	f roof.					
Totals: Metal1					0.00	0.00
الت						
Meta	al 2					
8	95.44	Total Perimete	er Length			



# **CONTINUED - Metal 2**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Note: No visible damage to this section of roof.						
Totals: Metal 2					0.00	0.00
Total: Roof						27,196.43
Total: Building 20 - Precinct 4 - Building Roof					0.00	27,196.43

# **Building #20 - Precinct 4 - Building Interior** Main Level

Height: 8' 9"

11'8"-1'						- Birth	
4.4.4	500.16	SF Walls		218.1	2 SF Ceiling		
Office 2	718.28 SF Walls & Ceiling			218.12 SF Floor			
9'8"	24.24 SY Flooring			56.4	3 LF Floor Perim	eter	
7 4" 3' -3' -3' -3' -3' -3' -3' -3' -3' -3'	59.51	LF Ceil. Perim	eter				
₩indow	3' X	5'	O	pens into Exter	ior		
Window	3' X	5'		pens into Exter			
Window	3' X			pens into Exter			
Window	3' X 5'			pens into Exter			
Window	3' X 5'		Opens into Exterior				
Missing Wall - Goes to Floor	3' 1" X 6' 8"		Opens into HALL_2				
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL	
1,027. 5/8" drywall - hung, taped, heavy texture, ready for paint	718.28 SF		0.00	1.80	0.00	1,292.90	
1,028. Seal/prime then paint the walls and ceiling twice (3 coats)	718.28 SF		0.00	0.84	0.00	603.36	
1,029. Blown-in insulation - 8" depth - R19	218.12 SF		0.00	0.50	0.00	109.06	
1,030. Batt insulation - 6" - R19 - paper faced	500.16 SF		0.00	0.65	0.00	325.10	
1,031. Fluorescent - two tube - 8' - strip light	2.00 EA		0.00	117.89	0.00	235.78	
1,032. Light bulb - Fluorescent tube - 8' cool white - mat. only	4.00 EA		0.00	7.48	0.00	29.92	
1,033. Heat/AC register - Mechanically attached - Detach & reset	1.00 EA		0.00	10.74	0.00	10.74	
,034. Paint door or window opening - 2 coats (per side)	1.00 EA		0.00	20.22	0.00	20.22	
ICTORYCOSUB					12/13/2017	Page:	



#### **CONTINUED - Office 2**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,035. Clean window unit (per side) 10 - 20 SF	5.00 EA		0.00	8.32	0.00	41.60
1,036. Clean window blind - horizontal or vertical	45.00 SF		0.00	0.71	0.00	31.95
1,037. Window trim set (casing & stop)	60.00 LF		0.00	2.50	0.00	150.00
1,038. Paint door/window trim & jamb - 2 coats (per side)	5.00 EA		0.00	20.22	0.00	101.10
1,039. Outlet	5.00 EA		0.00	11.88	0.00	59.40
1,040. Clean floor	218.12 SF		0.00	0.25	0.00	54.53
1,041. Final cleaning - construction - Commercial	218.12 SF		0.00	0.11	0.00	23.99
Totals: Office 2			-	-	0.00	3,089.65

Hallway

5' 2"

Hall 2

Hall 2

11'1

196.74 SF Walls

Hall 2

233.40 SF Walls & Ceiling

4.07 SY Flooring

24.83 LF Ceil. Perimeter

Height: 8' 9"

36.67 SF Ceiling

36.67 SF Floor

21.75 LF Floor Perimeter

Door Door

Missing Wall - Goes to Floor

3' X 6' 8"

3' X 6' 8"

3' 1" X 6' 8"

Opens into BREAK\_ROOM

Opens into OFFICE\_1

Opens into OFFICE\_2


0 1 11 0		_		_	
QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
233.40 SF		0.00	1.80	0.00	420.12
233.40 SF		0.00	0.84	0.00	196.06
36.67 SF		0.00	0.50	0.00	18.34
196.74 SF		0.00	0.65	0.00	127.88
1.00 EA		0.00	85.33	0.00	85.33
2.00 EA		0.00	4.50	0.00	9.00
36.00 LF		0.00	1.24	0.00	44.64
2.00 EA		0.00	24.16	0.00	48.32
	233.40 SF 233.40 SF 36.67 SF 196.74 SF 1.00 EA 2.00 EA 36.00 LF	233.40 SF 233.40 SF 36.67 SF 196.74 SF 1.00 EA 2.00 EA 36.00 LF	233.40 SF 0.00 233.40 SF 0.00 36.67 SF 0.00 196.74 SF 0.00 1.00 EA 0.00 2.00 EA 0.00 36.00 LF 0.00	233.40 SF       0.00       1.80         233.40 SF       0.00       0.84         36.67 SF       0.00       0.50         196.74 SF       0.00       0.65         1.00 EA       0.00       85.33         2.00 EA       0.00       4.50         36.00 LF       0.00       1.24	233.40 SF       0.00       1.80       0.00         233.40 SF       0.00       0.84       0.00         36.67 SF       0.00       0.50       0.00         196.74 SF       0.00       0.65       0.00         1.00 EA       0.00       85.33       0.00         2.00 EA       0.00       4.50       0.00         36.00 LF       0.00       1.24       0.00





#### **CONTINUED - Hall 2**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,050. Paint door or window opening - 2 coats (per side)	2.00 EA		0.00	20.22	0.00	40.44
1,051. Breaker panel - 200 to 300 amp - Detach & reset	1.00 EA		0.00	875.01	0.00	875.01
1,052. Outlet	2.00 EA	10	0.00	11.88	0.00	23.76
1,053. Clean floor	36.67 SF		0.00	0.25	0.00	9.17
1,054. Final cleaning - construction - Commercial	36.67 SF	1	0.00	0.11	0.00	4.03
Totals: Hall 2		7			0.00	1,902.10



333.87 SF Walls
421.02 SF Walls & Ceiling

9.68 SY Flooring38.16 LF Ceil. Perimeter

Height: 8' 9"

87.15 SF Ceiling 87.15 SF Floor

38.16 LF Floor Perimeter

Window Door 3' X 5' 3' X 6' 8" Opens into Exterior Opens into HALL\_2

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,055. 5/8" drywall - hung, taped, heavy texture, ready for paint	421.02 SF		0.00	1.80	0.00	757.84
1,056. Seal/prime then paint the walls and ceiling twice (3 coats)	421.02 SF		0.00	0.84	0.00	353.66
1,057. Blown-in insulation - 8" depth - R19	87.15 SF		0.00	0.50	0.00	43.58
1,058. Batt insulation - 6" - R19 - paper faced	333.87 SF		0.00	0.65	0.00	217.02
1,059. Fluorescent - two tube - 8' - strip light	1.00 EA		0.00	117.89	0.00	117.89
1,060. Light bulb - Fluorescent tube - 8' cool white - mat. only	2.00 EA		0.00	7.48	0.00	14.96
1,061. Heat/AC register - Mechanically attached - Detach & reset	1.00 EA		0.00	10.74	0.00	10.74
1,062. Exterior door - metal - insulated - flush or panel style	1.00 EA		0.00	211.23	0.00	211.23
1,063. Door knob - interior	1.00 EA		0.00	28.65	0.00	28.65
1,064. Paint door slab only - 2 coats per side)	1.00 EA		0.00	24.16	0.00	24.16



#### **CONTINUED - Break Room**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,065. Paint door or window opening - 2 coats (per side)	1.00 EA		0.00	20.22	0.00	20.22
1,066. Clean window unit (per side) 10 - 20 SF	1.00 EA		0.00	8.32	0.00	8.32
1,067. Clean window blind - horizontal or vertical	15.00 SF		0.00	0.71	0.00	10.65
1,068. Window trim set (casing & stop)	15.00 LF		0.00	2.50	0.00	37.50
1,069. Paint door/window trim & jamb - 2 coats (per side)	1.00 EA		0.00	20.22	0.00	20.22
1,070. Outlet	4.00 EA		0.00	11.88	0.00	47.52
1,071. Clean floor	87.15 SF		0.00	0.25	0.00	21.79
1,072. Contents - move out then reset - Large room	1.00 EA		0.00	42.27	0.00	42.27
1,073. Final cleaning - construction - Commercial	87.15 SF		0.00	0.11	0.00	9.59
Totals: Break Room			1		0.00	1,997.81

ay	9' 8"	₫,
Hall 2	4 10 - A 10.	
	Office 1	-21'2"
13, 1	11' 4" — 4' 3" ← 10' 3"	
	5" 4' 5" 10' 5"	<u>U</u>

Door

Door

Door

Window

**VICTORYCOSUB** 

Office 1

881.70 SF Walls 1,186.01 SF Walls & Ceiling 33.81 SY Flooring 70.98 LF Ceil. Perimeter

3' X 6' 8"

3' X 6' 8"

3' X 6' 8"

3' X 5'

Height: 12' 5"
304.32 SF Ceiling

Page: 100

70.98 LF Floor Perimeter

12/13/2017

304.32 SF Floor

Opens into HALL\_2
Opens into HALLWAY
Opens into Exterior
Opens into Exterior
Opens into Exterior

3' X :	3' X 5'		<b>Opens into Exterior</b>		
QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,186.01 SF		0.00	1.80	0.00	2,134.82
1,186.01 SF		0.00	0.84	0.00	996.25
- 304.32 SF		0.00	0.50	0.00	152.16
881.70 SF		0.00	0.65	0.00	573.11
2.00 EA		0.00	117.89	0.00	235.78
	QTY  1,186.01 SF  1,186.01 SF  - 304.32 SF  881.70 SF	QTY RESET  1,186.01 SF  1,186.01 SF  - 304.32 SF  881.70 SF	QTY         RESET         REMOVE           1,186.01 SF         0.00           1,186.01 SF         0.00           - 304.32 SF         0.00           881.70 SF         0.00	QTY         RESET         REMOVE         REPLACE           1,186.01 SF         0.00         1.80           1,186.01 SF         0.00         0.84           - 304.32 SF         0.00         0.50           881.70 SF         0.00         0.65	QTY         RESET         REMOVE         REPLACE         TAX           1,186.01 SF         0.00         1.80         0.00           1,186.01 SF         0.00         0.84         0.00           - 304.32 SF         0.00         0.50         0.00           881.70 SF         0.00         0.65         0.00





# **CONTINUED - Office 1**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,079. Light bulb - Fluorescent tube - 8' cool white - mat. only	4.00 EA		0.00	7.48	0.00	29.92
1,080. Heat/AC register - Mechanically attached - Detach & reset	1.00 EA		0.00	10.74	0.00	10.74
1,081. Casing - 2 1/4"	36.00 LF		0.00	1.24	0.00	44.64
1,082. Paint door slab only - 2 coats (per side)	2.00 EA		0.00	24.16	0.00	48.32
1,083. Paint door or window opening - 2 coats (per side)	2.00 EA		0.00	20.22	0.00	40.44
1,084. Clean window unit (per side) 10 - 20 SF	2.00 EA		0.00	8.32	0.00	16.64
1,085. Window trim set (casing & stop)	26.00 LF	1	0.00	2.50	0.00	65.00
1,086. Paint door/window trim & jamb - 2 coats (per side)	2.00 EA		0.00	20.22	0.00	40.44
1,087. Clean floor	304.32 SF		0.00	0.25	0.00	76.08
1,088. Final cleaning - construction - Commercial	304.32 SF	X	0.00	0.11	0.00	33.48
otals: Office 1	A CONTRACTOR OF THE PARTY OF TH		E.		0.00	4,497.82

Women showershower is the second of the seco

160.38 SF Ceiling160.38 SF Floor72.84 LF Floor Perimeter

Height: 8' 7"

Door 3' X 6' 8" Opens into OFFICE\_1

Door 3' X 6' 8" Opens into Exterior

Missing Wall - Goes to Floor 2' 6" X 6' 8" Opens into MENS

Missing Wall - Goes to Floor 2' 6" X 6' 8" Opens into SHOWER\_2

Door 3' X 6' 8" Opens into WOMEN

17.82 SY Flooring

77.84 LF Ceil. Perimeter

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,089. 5/8" drywall - hung, taped, heavy texture, ready for paint	794.80 SF		0.00	1.80	0.00	1,430.64
1,090. Seal/prime then paint the walls and ceiling twice (3 coats)	794.80 SF		0.00	0.84	0.00	667.63
1,091. Blown-in insulation - 8" depth - R19	160.38 SF		0.00	0.50	0.00	80.19





# **CONTINUED - Hallway**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,092. Batt insulation - 6" - R19 - paper faced	634.42 SF		0.00	0.65	0.00	412.37
1,093. Fluorescent - two tube - 8' - strip light	2.00 EA		0.00	117.89	0.00	235.78
1,094. Light bulb - Fluorescent tube - 8' cool white - mat. only	4.00 EA		0.00	7.48	0.00	29.92
1,095. Casing - 2 1/4"	36.00 LF		0.00	1.24	0.00	44.64
1,096. Paint door slab only - 2 coats (per side)	2.00 EA		0.00	24.16	0.00	48.32
1,097. Paint door or window opening - 2 coats (per side)	2.00 EA		0.00	20.22	0.00	40.44
1,098. Outlet	2.00 EA		0.00	11.88	0.00	23.76
1,099. Clean floor	160.38 SF		0.00	0.25	0.00	40.10
1,100. Final cleaning - construction - Commercial	160.38 SF		0.00	0.11	0.00	17.64
Totals: Hallway					0.00	3,071.43



Storage

677.21 SF Walls 845.63 SF Walls & Ceiling 18.71 SY Flooring 54.18 LF Ceil. Perimeter Height: 12' 6"

168.41 SF Ceiling 168.41 SF Floor

54.18 LF Floor Perimeter

Door	3' X 6' 8"	Opens into Exterior


DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,101. 5/8" drywall - hung, taped, heavy texture, ready for paint	845.63 SF		0.00	1.80	0.00	1,522.13
1,102. Seal/prime then paint the walls and ceiling twice (3 coats)	845.63 SF		0.00	0.84	0.00	710.33
1,103. Blown-in insulation - 8" depth - R19	168.41 SF		0.00	0.50	0.00	84.21
1,104. Batt insulation - 6" - R19 - paper faced	338.61 SF		0.00	0.65	0.00	220.10
1,105. Fluorescent - two tube - 8' - strip light	2.00 EA		0.00	117.89	0.00	235.78
1,106. Light bulb - Fluorescent tube - 8' cool white - mat. only	4.00 EA		0.00	7.48	0.00	29.92
1,107. Paint door slab only - 2 coats per side)	1.00 EA		0.00	24.16	0.00	24.16



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

# **CONTINUED - Storage**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,108. Paint door or window opening - 2 coats (per side)	1.00 EA		0.00	20.22	0.00	20.22
1,109. Shelving - Detach & reset	54.18 LF		0.00	4.62	0.00	250.31
1,110. Outlet	2.00 EA		0.00	11.88	0.00	23.76
1,111. Clean floor	168.41 SF		0.00	0.25	0.00	42.10
1,112. Final cleaning - construction - Commercial	168.41 SF		0.00	0.11	0.00	18.53
Totals: Storage					0.00	3,181,55



**Shower 1** 

202.07 SF Walls 238.20 SF Walls & Ceiling 4.01 SY Flooring 25.50 LF Ceil. Perimeter 36.13 SF Ceiling 36.13 SF Floor

Height: 8' 7"

23.00 LF Floor Perimeter

Missing Wall - Goes to Floor

2' 6" X 6' 8"


**Opens into MENS** 

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,113. 1/2" water rock (greenboard) hung, taped ready for texture	238.20 SF		0.00	1.35	0.00	321.57
1,114. Seal/prime then paint the ceiling twice (3 coats)	36.13 SF		0.00	0.84	0.00	30.35
1,115. Blown-in insulation - 8" depth - R19	36.13 SF		0.00	0.50	0.00	18.07
1,116. Batt insulation - 4 <sup>n</sup> - R13 - paper faced	202.07 SF		0.00	0.50	0.00	101.04
1,117. Fiberglass reinforced plastic (FRP) paneling	202.07 SF		0.00	3.87	0.00	782.01
1,118. Shower head only	1.00 EA		0.00	43.38	0.00	43.38
1,119. Shower faucet	1.00 EA		0.00	173.63	0.00	173.63
1,120. Clean floor	36.13 SF		0.00	0.25	0.00	9.03
1,121. Final cleaning - construction - Commercial	36.13 SF		0.00	0.11	0.00	3.97
Totals: Shower 1					0.00	1.483.05










Shower 2 Height: 8' 7"

203.50 SF Walls240.34 SF Walls & Ceiling4.09 SY Flooring25.67 LF Ceil. Perimeter

36.83 SF Floor 23.17 LF Floor Perimeter

36.83 SF Ceiling

Missing Wall - Goes to Floor	2' 6"	X 6' 8"	<b>Opens into HALLWAY</b>			
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,122. 1/2" water rock (greenboard) hung, taped ready for texture	240.34 SF		0.00	1.35	0.00	324.46
1,123. Seal/prime then paint the ceiling twice (3 coats)	36.83 SF		0.00	0.84	0.00	30.94
1,124. Blown-in insulation - 8" depth - R19	36.83 SF		0.00	0.50	.00.00	18.42
1,125. Batt insulation - 4" - R13 - paper faced	203.50 SF		0.00	0.50	0.00	101.75
1,126. Fiberglass reinforced plastic (FRP) paneling	203.50 SF		0.00	3.87	0.00	787.55
1,127. Shower head only	1.00 EA		0.00	43.38	0.00	43.38
1,128. Shower faucet	1.00 EA		0.00	173.63	0.00	173.63
1,129. Clean floor	36.83 SF		0.00	0.25	0.00	9.21
1,130. Final cleaning - construction - Commercial	36.83 SF		0.00	0.11	0.00	4.05
Totals: Shower 2					0.00	1,493.39



Women Height: 8' 7"

277.36 SF Walls342.52 SF Walls & Ceiling7.24 SY Flooring32.33 LF Ceil. Perimeter

65.17 SF Floor 32.33 LF Floor Perimeter

65.17 SF Ceiling

Door 3' X 6' 8" Opens into HALLWAY

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,131. 5/8" drywall - hung, taped, heavy texture, ready for paint	342.52 SF		0.00	1.80	0.00	616.54
1,132. Seal/prime then paint the walls and ceiling twice (3 coats)	342.52 SF		0.00	0.84	0.00	287.72
1,133. Blown-in insulation - 8" depth - R19	65.17 SF		0.00	0.50	0.00	32.59



# **CONTINUED - Women**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,134. Batt insulation - 4" - R13 - paper faced	277.36 SF		0.00	0.50	0.00	138.68
1,135. Fluorescent - two tube - 4' - fixture w/lens	1.00 EA		0.00	85.33	0.00	85.33
1,136. Light bulb - Fluorescent tube - 4' soft white - mat. only	2.00 EA		0.00	4.50	0.00	9.00
1,137. Interior door - Colonist - pre- hung unit	1.00 EA		0.00	116.05	0.00	116.05
1,138. Door knob - interior - High grade	1.00 EA		0.00	40.21	0.00	40.21
1,139. Paint door slab only - 2 coats (per side)	1.00 EA		0.00	24.16	0.00	24.16
1,140. Paint door or window opening - 2 coats (per side)	1.00 EA		0.00	20.22	0.00	20.22
1,141. Window trim set (casing & stop)	15.00 LF		0.00	2.50	0.00	37.50
1,142. Paint door/window trim & jamb - 2 coats (per side)	1.00 EA	8	0.00	20.22	0.00	20.22
1,143. Switch	1.00 EA	1000	0.00	11.94	0.00	11.94
1,144. Sink - wall mounted - Detach & eset	1.00 EA		0.00	163.12	0.00	163.12
1,145. Sink faucet - Detach & reset	1.00 EA		0.00	80.35	0.00	80.35
1,146. Clean sink and faucet	1.00 EA		0.00	9.56	0.00	9.56
1,147. Toilet	1.00 EA	44	0.00	322.81	0.00	322.81
1,148. Toilet seat	1.00 EA		0.00	41.25	0.00	41.25
1,149. Angle stop valve	3.00 EA	-	0.00	23.88	0.00	71.64
1,150. Clean floor	65.17 SF		0.00	0.25	0.00	16.29
1,151. Final cleaning - construction - Commercial	65.17 SF		0.00	0.11	0.00	7.17
Totals: Women					0.00	2,152.35





T. Z	
13' 10" -5' 2" -8" 8" +2	16 11"
Ļ.	Mags 50
3, 10	7' 10" — 4 — 101 7
- oo	8'
	Dressing Room
	3'3', 2'6"
	3'3'11'
Vind	low

Mens

Height: 9' 4"

677.45	SF Walls
880.98	SF Walls & Ceiling
22.61	SY Flooring
76.20	LF Ceil. Perimeter

203.53 SF Ceiling 203.53 SF Floor 71.20 LF Floor Perimeter

Willdow
Window
Door
Missing Wall - Goes to Floor
Missing Wall - Goes to Floor

3' X 5' 3' X 5' 3' X 6' 8" 2' 6" X 6' 8" 2' 6" X 6' 8" Opens into Exterior
Opens into Exterior
Opens into DRESSING\_ROO
Opens into SHOWER\_1
Opens into HALLWAY


DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,152. 5/8" drywall - hung, taped, heavy texture, ready for paint	880.98 SF	100000000000000000000000000000000000000	0.00	1.80	0.00	1,585.76
1,153. Seal/prime then paint the walls and ceiling twice (3 coats)	880.98 SF	and a	0.00	0.84	0.00	740.02
1,154. Blown-in insulation - 8" depth - R19	203.53 SF		0.00	0.50	0.00	101.77
1,155. Batt insulation - 4" - R13 - paper faced	677.45 SF		0.00	0.50	0.00	338.73
1,156. Fluorescent - two tube - 4' - fixture w/lens	1.00 EA		0.00	85.33	0.00	85.33
1,157. Light bulb - Fluorescent tube - 4' soft white - mat. only	2.00 EA		0.00	4.50	0.00	9.00
1,158. Interior door - Colonist - pre- hung unit	1.00 EA		0.00	116.05	0.00	116.05
1,159. Door knob - interior - High grade	1.00 EA		0.00	40.21	0.00	40.21
1,160. Paint door slab only - 2 coats (per side)	1.00 EA		0.00	24.16	0.00	24.16
1,161. Paint door or window opening - 2 coats (per side)	1.00 EA		0.00	20.22	0.00	20.22
1,162. Window trim set (casing & stop)	15.00 LF		0.00	2.50	0.00	37.50
1,163. Paint door/window trim & jamb - 2 coats (per side)	1.00 EA		0.00	20.22	0.00	20.22
1,164. Switch	1.00 EA		0.00	11.94	0.00	11.94
1,165. Sink - wall mounted - Detach & reset	2.00 EA		0.00	163.12	0.00	326.24
1,166. Sink faucet - Detach & reset	2.00 EA		0.00	80.35	0.00	160.70
1,167. Clean sink and faucet	2.00 EA		0.00	9.56	0.00	19.12
1,168. Remove Service sink - corner - floor mounted	1.00 EA		40.10	0.00	0.00	40.10





# **CONTINUED - Mens**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,169. Detach & Reset Urinal - stall type	1.00 EA	235.78	0.00	0.00	0.00	235.78
1,170. Toilet	2.00 EA		0.00	322.81	0.00	645.62
1,171. Toilet seat	2.00 EA		0.00	41.25	0.00	82.50
1,172. Angle stop valve	3.00 EA		0.00	23.88	0.00	71.64
1,173. Clean floor	203.53 SF		0.00	0.25	0.00	50.88
1,174. Final cleaning - construction - Commercial	203.53 SF		0.00	0.11	0.00	22.39
Totals: Mens	W 1				0.00	4,785.88



# **Dressing Room**

315.14 SF Walls 386.26 SF Walls & Ceiling 7.90 SY Flooring 33.78 LF Ceil. Perimeter Height: 9' 4"

71.12 SF Ceiling71.12 SF Floor33.78 LF Floor Perimeter

33.78 LF Floor Fermicu

Door	3' X 6'	3"	Opens into MENS		
DESCRIPTION	OTY	DECET	DEMOVE	DEBLACE	

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,175. 5/8" drywall - hung, taped, heavy texture, ready for paint	386.26 SF		0.00	1.80	0.00	695.27
1,176. Seal/prime then paint the walls and ceiling twice (3 coats)	386.26 SF		0.00	0.84	0.00	324.46
1,177. Blown-in insulation - 8" depth - R19	71.12 SF		0.00	0.50	0.00	35.56
1,178. Batt insulation - 4" - R13 - paper faced	315.14 SF		0.00	0.50	0.00	157.57
1,179. Fluorescent - two tube - 4' - fixture w/lens	1.00 EA		0.00	85.33	0.00	85.33
1,180. Light bulb - Fluorescent tube - 4' soft white - mat. only	2.00 EA		0.00	4.50	0.00	9.00
1,181. Interior door - Colonist - pre- hung unit	1.00 EA		0.00	116.05	0.00	116.05
1,182. Door knob - interior - High grade	1.00 EA		0.00	40.21	0.00	40.21
1,183. Paint door slab only - 2 coats (per side)	1.00 EA		0.00	24.16	0.00	24.16
1,184. Paint door or window opening - 2 coats (per side)	1.00 EA		0.00	20.22	0.00	20.22
,185. Window trim set (casing & stop)	15.00 LF		0.00	2.50	0.00	37.50





# **CONTINUED - Dressing Room**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,186. Paint door/window trim & jamb - 2 coats (per side)	1.00 EA		0.00	20.22	0.00	20.22
1,187. Switch	1.00 EA		0.00	11.94	0.00	11.94
1,188. Clean floor	71.12 SF		0.00	0.25	0.00	17.78
1,189. Final cleaning - construction - Commercial	71.12 SF		0.00	0.11	0.00	7.82
Totals: Dressing Room					0.00	1,603.09



**Truck Bay 1** 

Height: 24'

2,197.00 SF Walls 2,803.45 SF Walls & Ceiling 67.38 SY Flooring 93.58 LF Ceil. Perimeter 606.45 SF Ceiling 606.45 SF Floor

86.58 LF Floor Perimeter

Missing Wall
Door

15' 7" X 24' 7' X 7' Opens into Exterior
Opens into Exterior

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,190. 1/2" Cement board	306.64 SF		0.00	2.34	0.00	717.54
Note: Up 8' on the north wall only (34'-	4")					
1,191. Seal/prime then paint the surface area twice (3 coats)	306.64 SF		0.00	0.84	0.00	257.58
1,192. Scaffold - per section (per day)	2.00 DA		0.00	12.96	0.00	25.92
Totals: Truck Bay 1					0.00	1.001.04

# **Electrical**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,193. Electrician - per hour	24.00 HR		0.00	84.00	0.00	2,016.00
Totals: Electrical					0.00	2,016.00
Total: Main Level					0.00	32,275.16
Total: Building #20 - Precinct 4 - Building Interior					0.00	32,275.16


# **Building 21 - North T Hangar Roof**





Roof






7,297.29 Surface Area 359.68 Total Perimeter Length 72.97 Number of Squares 118.00 Total Ridge Length

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,198. Metal roofing - ribbed - 26 gauge - 1 1/8" to 1 1/2"	7,297.29 SF		0.00	3.30	0.00	24,081.06
Note: (3) metal panels were damaged at fasteners loosened and determined that to						
1,199. Ridge cap - metal roofing	118.00 LF		0.00	3.50	0.00	413.00
1,200. Gable trim for metal roofing - 26 gauge	124.00 LF		0.00	3.73	0.00	462.52
1,201. Ridge end cap for metal roofing	2.00 EA		0.00	17.41	0.00	34.82
1,202. Exhaust cap - through flat roof	5.00 EA		0.00	77.26	0.00	386.30
,203. Closure strips for metal roofing - inside and/or outside	472.00 LF		0.00	1.16	0.00	547.52
Totals: Roof1					0.00	25,925.22
Total: Roof					0.00	25,925.22
Total: Building 21 - North T Hangar Roo	of				0.00	25,925.22

# Building # 21 - North T Hangar Interior / Exterior Main Level



Door

# Airfield Storage / Southeast Corner

2,015.79 SF Walls 2,697.96 SF Walls & Ceiling 73.56 SY Flooring 123.66 LF Ceil. Perimeter 682.17 SF Ceiling 662.00 SF Floor

121.67 LF Floor Perimeter

Height: Peaked

4' X 3' Opens into Exterior 3' X 6' 8" Opens into Exterior

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
204. Steel purlins - C-shape - 8"	56.00 LF		0.00	6.74	0.00	377.44

Note: (2) vertical columns measuring 16 l.f. each and 24 l.f. for the door frame.



# **CONTINUED - Airfield Storage / Southeast Corner**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,205. Temporary shoring post - Screw jack (per day)	4.00 DA		0.00	25.99	0.00	103.96
Note: Support to allow replacement of the	he vertical purlins					
1,206. Steel purlins - C-shape - 8"	61.00 LF		0.00	6.74	0.00	411.14
Note: Base channel						
1,207. Steel purlins - Z-shape - 8"	121.32 LF		0.00	6.73	0.00	816.48
Note: (2) 24 lf. and (4) 18'-4"						
1,208. Wall/roof panel - ribbed - 24 gauge - up to 1"	1,392.00 SF		0.00	2.82	0.00	3,925.44
Note: Considers the entire East elevation	n and 24 l.f. of the Se	outheast corner.				
1,209. Metal outside corner post	32.00 LF		0.00	4.08	0.00	130.56
1,210. Exterior door - metal - insulated - flush or panel style	1.00 EA		0.00	211.23	0.00	211.23
1,211. Door lockset - exterior - High grade	1.00 EA		0.00	56.16	0.00	56.16
1,212. Paint door slab only - 2 coats (per side)	2.00 EA		0.00	24.16	0.00	48.32
2.213. Paint door or window opening - coats (per side)	2.00 EA		0.00	20.22	0.00	40.44
1,214. Detach & Reset Aluminum window, horiz. slider 12-23 sf	1.00 EA	68.71	0.00	0.00	0.00	68.71
1,215. Fluorescent - two tube - 8' - fixture w/lens	1.00 EA		0.00	133.01	0.00	133.01
1,216. Outlet	1.00 EA		0.00	11.88	0.00	11.88
1,217. Switch	1.00 EA		0.00	11.94	0.00	11.94
1,218. Electrician - per hour	4.00 HR		0.00	84.00	0.00	336.00
1,219. Scaffold - per section (per day)	8.00 DA		0.00	12.96	0.00	103.68
Totals: Airfield Storage / Southeast Cor-	ner				0.00	6,786.39
Total: Main Level					0.00	6,786.39
Total: Building # 21 - North T Hangar Ir	nterior / Exterior				0.00	6,786.39

Building 22 - South T Hangar Roof

Roof



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

Roof1



13,114.44 Surface Area 627.35 Total Perimeter Length 131.14 Number of Squares 264.00 Total Ridge Length

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL.
1,225. R&R Metal roofing - ribbed - 26 gauge - 1 1/8" to 1 1/2"	13,114. SF 44		0.30	3.30	0.00	47,211.98
Note: Several metal panels were damage longer available. We suggest complete re				ed and determined the	at the existing pa	nel is no
1,226. R&R Ridge cap - metal roofing	264.00 LF		1.62	3.50	0.00	1,351.68
1,227. R&R Gable trim for metal roofing - 26 gauge	98.00 LF		0.49	3.73	0.00	413.56
1,228. R&R Ridge end cap for metal roofing	2.00 EA		3.16	17.41	0.00	41.14
1,229. R&R Exhaust cap - through flat roof	11.00 EA		5.29	77.26	0.00	908.05
,230. Closure strips for metal roofing - nside and/or outside	1,056.00 LF		0.00	1.16	0.00	1,224.96
Totals: Roof1					0.00	51,151.37
Total: Roof					0.00	51.151.37

#### **Exterior / South Elevation**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,231. Hangar Door (Bid Item)- 20'	1.00 EA		0.00	49,244.00	0.00	49,244.00
metal sliding				,		

Note: Per proposal from Alamo Door Systems. The high winds blew one of the 20' x 12' steel hangar doors off the metal track damaging the track. Alamo Door Systems proposed to detach the door and replace the steel rail because it is rusted out and is not functional. The existing track is not available ,therefore the entire row of track must be saw cut out and a new rail installed with proper drainage to prevent rusting. The track/rail was functional prior to this event albeit it was rusted and deteriorating. To properly repair this door and rail, the repairs require completion as outlined by Alamo Door Systems.

 Totals: Exterior / South Elevation
 0.00
 49,244.00

 Total: Building 22 - South T Hangar Roof
 0.00
 100,395.37

Building 23 - Office- Elections & JP 3

Main Level


VICTORYCOSUB

12/13/2017

Page: 111



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

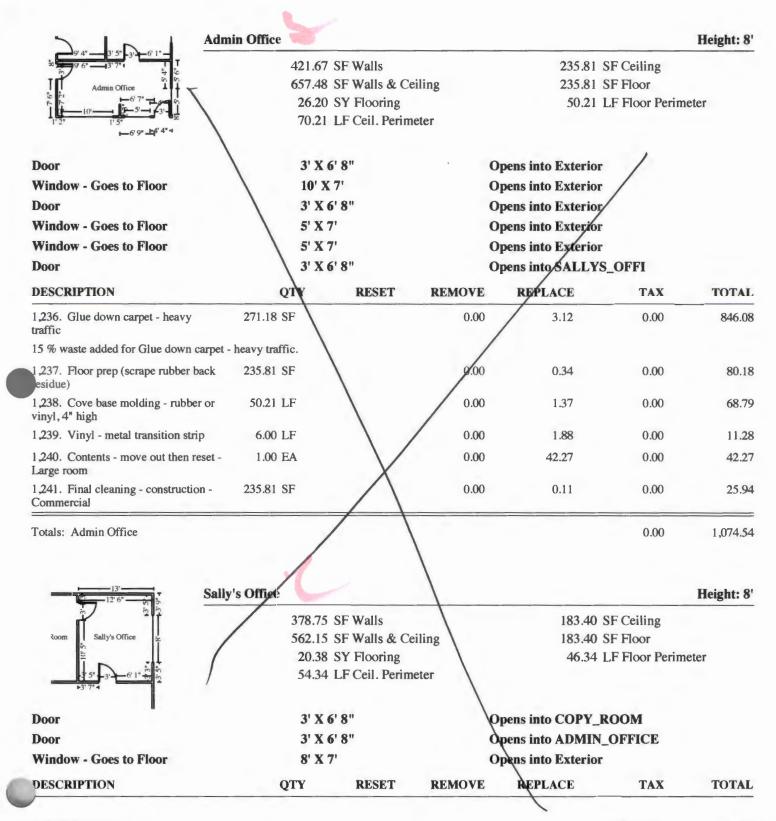



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

# CONTINUED - Sally's Office

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,242. Glue down carpet - heavy traffic	210.91 SF		0.00	3.12	0.00	658.04
15 % waste added for Glue down carpet - I	avy traffic.					
1,243. Floor prep (scrape rubber back residue)	183.40 SF		0.00	0.34	0.00	62.36
1,244. Cove base molding - rubber or vinyl, 4" high	46.14 LF		0.00	1.37	0.00	63.49
1,245. Contents - move out then reset	1.00 KA		0.00	28.18	0.00	28.18
1,246. Final cleaning - construction - Commercial	183.40 SP		0.00	0.11	0.00	20.17
Totals: Sally's Office					0.00	832.24

9 10\*

Sal

Sal

9 4\*

9 6\*

**Copy Room** 

384.17 SF Walls

521.18 SF Walls & Ceiling 15.22 SY Flooring

48.02 LF Ceil. Perimeter

Height: 8'

137.01 SF Ceiling 137.01 SF Floor

48.02 LF Floor Perimeter

Door Door

3'X 6' 8"

Opens into Exterior
Opens into SALLYS\_OFFI

DESCRIPTION	OTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,247. Glue down carpet - heavy traffic	157.57 SF		0.00	3.12	0.00	491.62
15 % waste added for Glue down carpet	heavy traffic.					
1,248. Floor prep (scrape rubber back residue)	137.01 SF		0.00	0.34	0.00	46.58
1,249. Cove base molding - rubber or vinyl, 4" high	48.02 LF		0.00	1.37	0.00	65.79
1,250. Vinyl - metal transition strip	3.00 LF		0.0	1.88	0.00	5.64
1,251. Contents - move out then reset	1.00 EA		0.00	28.18	0.00	28.18
1,252. Final cleaning construction - Commercial	137.01 SF		0.00	0.11	0.00	15.07
Totals: Copy Room					0.00	652.88
Total: Main Level					0.00	2,559.66
Total: Building 23 - Office- Elections &	JP 3				0.00	2,559.66

**VICTORYCOSUB** 

12/13/2017

Page: 113





#### **Building # 24- Airport Terminal with Storage Vaults**

General Exterior / Airstrip Fencing

/						
DESCRIPTION -	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,254. Chain link fence - fabric only - 6' high - galvanized  Note: Re-stretch and re-secure 680 lf. of	4,080.00 LF	ric along the We.	0.00	5.48 wind.	0.00	22,358.4
Totals: General Exterior / Airstrip Fencin	ng				0.00	22,358.40

**Terminal Roof** 

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,255. Metal Structure Installer - per	4.00 HR		0.00	44.55	0.00	178.20

Note: Considers time for inspection, re-securing and caulking of the gable trim at the South gable and the wall flashing along the North wall at the roof transition.

Totals: Terminal Roof 0.00 178.20

#### **Airport Terminal Exterior- Porte Cochere**

LxWxH 33' 8 1/16" x 25' x 12'

1,408.13 SF Walls 2,249.92 SF Walls & Ceiling 93.53 SY Flooring 404.06 SF Long Wall 117.34 LF Ceil. Perimeter 841.80 SF Ceiling 841.80 SF Floor 117.34 LF Floor Perimeter 300.00 SF Short Wall

DESCRIPTION QTY RESET REMOVE REPLACE TAX TOTAL 1,256. R&R Soffit - metal 841.80 SF 0.18 3.48 0.00 3,080.98 Note: Porte Cochere ceiling 1,257. R&R Recessed light fixture -1.00 EA 6.55 115.58 0.00 122.13 High grade 1,258. Recessed light fixture - Detach 6.00 EA 0.00 86.71 0.00 520.26 & reset entire unit Totals: Airport Terminal Exterior- Porte Cochere 0.00 3,723.37

#### South Baggage Area

DESCRIPTION	QT	Y RESET	REMOVE	REPLACE	TAX	TOTAL
				the latest and the la		





8380 Warren Parkway / Ste. 700 - Frisco, TX 75034

# CONTINUED - South Baggage Area

1.						
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,259. R&R Suspended ceiling tile - 2' x 2'	40.00 SF		0.13	1.23	0.00	54.40
Note: (10) tiles						
1,260. R&R Batt insulation - 6" - R19 - paper faced	40.00 SF		0.17	0.65	0.00	32.80
1,261. Seal/prime then paint the surface area twice (3 coats)	628.00 SF		0.00	0.84	0.00	527.52
Note: South wall only						
1,262. Mask or cover per square foot	208.00 SF		0.25	0.00	0.00	52.00
1,263. Mask and prep for paint - tape only (per LF)	52.00 LF		0.00	0.39	0.00	20.28
Note: Masking of the wood baseboard						
1,264. Final cleaning - construction - Commercial	1,040.00 SF		0.00	0.11	0.00	114.40
Totals: South Baggage Area					0.00	801.40

# Check-In Area

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,265. R&R Suspended ceiling tile - 2' x 2'	16.00 SF		0.13	1.23	0.00	21.76
Note: (4) tiles						
1,266. R&R Batt insulation - 6" - R19 - paper faced	16.00 SF		0.17	0.65	0.00	13.12
Totals: Check-In Area					0.00	34.88

# **Airline Operations Room**

LxWxH 17' 5 1/16" x 14' 9 15/16" x 8'

516.00 SF Walls 774.33 SF Walls & Ceiling 28.70 SY Flooring 139.38 SF Long Wall

258.33 SF Floor 64.50 LF Floor Perimeter

258.33 SF Ceiling

ong Wall 118.62 SF Short Wall

64.50 LF Ceil. Perimeter

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,267. R&R Suspended ceiling tile - 2' x 2'	258.33 SF		0.13	1.23	0.00	351.33
Note: (10) tiles 1,268. R&R Batt insulation - 6" - R19 -	258.33 SF		0.17	0.65	0.00	211.83
VICTORYCOSUB					12/13/2017	Page: 115




8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546



# **CONTINUED - Airline Operations Room**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,269. Mask or cover per square foot	258.33 SF		0.25	0.00	0.00	64.58
1,270. Final cleaning - construction - Commercial	258.33 SF		0.00	0.11	0.00	28.42
Totals: Airline Operations Room					0.00	656.16

#### **South Storage Vault**



# South Storage Vault Roof

1,186.00 Surface Area 190.00 Total Perimeter Length 11.86 Number of Squares

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
,271. Remove Tear off, haul and dispose of gravel ballast	11.86 SQ		35.06	0.00	0.00	415.81
1,272. Remove Tear off, haul and dispose of 3 ply built-up roofing	11.86 SQ		33.07	0.00	0.00	392.21
1,273. Built-up roof with granulated cap sheet - in place	11.86 SQ		0.00	287.69	0.00	3,412.00
Note: The modified bitumen cap sheet to	be insta <mark>ll</mark> ed in lieu o	f ballast which is	restricted by code	. as it pertains to hurr	ricane requireme	nts.
1,274. R&R Gravel stop	258.00 LF		0.20	1.18	0.00	356.04
1,275. Flash parapet wall only - bitumen	74.00 LF		0.00	7.58	0.00	560.92
Note: Around base of elevated roof section	n / full perimeter.					
1,276. Membrane roofing - cant strips - wood	74.00 LF		0.00	2.20	0.00	162.80
1,277. 2" x 12" lumber (2 BF per LF)	LF		0.00	2.66	0.00	0.00
Note: SErves as counterflashing surround	ling the elevated roo	of section.				
1,278. Prime & paint exterior fascia - wood, 6"- 8" wide	68.00 LF		0.00	1.37	0.00	93.16
1,279. Insulation - ISO board, 3 1/2"	11.86 SQ		0.00	248.82	0.00	2.951.01
This item did not previously exist or expa	nds the scope of rep	airs, but is require	ed by current build	ling codes. The code u	pgrade cost is pa	vable when

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

1,280. Insulation - ISO board, 4"

5.93 SQ

0.00

266.88

0.00

1,582.60

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when neurred, subject to limits.

Note: Considers tapered insulation to comply with 1/4" per foot drainage requirements.

**VICTORYCOSUB** 

12/13/2017

Page: 116





# **CONTINUED - South Storage Vault Roof**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,281. 2" x 6" lumber (1 BF per LF)	380.00 LF		0.00	1.73	0.00	657.40
This item did not previously exist or expincurred, subject to limits.	oands the scope of repa	airs, but is require	ed by current build	ling codes. The code u	pgrade cost is pa	yable when
Note: Double perimeter band (3") install	lled to fasten perimete	r coping after in	stallation of in <mark>sul</mark> a	tion.		
1,282. Steel wall coping	258.00 LF		0,60	9.87	0.00	2,417.46
This item did not previously exist or expincurred, subject to limits.	oands the scope of repa	airs, but is require	ed by current build	ling codes. The code u	pgrade cost is pa	yable when

# **Exterior**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,283. Reglaze window, 10 - 16 sf	1.00 EA		0.00	97.05	0.00	97.05
Totals: Exterior					0.00	97.05

#### Interior

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,284. Clean with pressure/chemical 1, spray - Very heavy	186.00 SF		0.00	0.47	0.00	557.42
Note: High winds broke a window and blew	over stored barrica	ides onto a bar	rel of oil causing	it to spill.		
1,285. Contents - move out then reset - Extra large room	1.00 EA		0.00	84.56	0.00	84.56
Totals: Interior					0.00	641.98
Total: South Storage Vault					0.00	6,131.97

# North Storage Vault

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Note: No visible damage to the Built-Up	ntenance is needed.					
Totals: North Storage Vault			115		0.00	0.00
Total: Building # 24- Airport Terminal wi	ith Storage Vaults		100-	8	0.00	33,884.38

# **Building 25 - Airport Maintenance & Firestation**



**VICTORYCOSUB** 

# **Virtus Group**

8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

# **Building 25 Roof**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Note: No visible damage to the 12-	15 year old 3 ply Built-Up	roof with alumin	um coating. Some	maintenance is neede	d.	
Totals: Building 25 Roof					0.00	0.00

		Main Lev	/el			
	kroom				Н	leight: 9' 1"
\$\frac{1}{5}\frac{1}{5	571.55	SF Walls		210.44 SF	Ceiling	
Breakroom		SF Walls & Co	eiling	210.44 SF	_	
S. T. 10" +3"	23.38	SY Flooring		62.92 LH	Floor Perim	eter
	62.92	LF Ceil. Perin	neter			
Toilet Hall	3' X	5'	0	pens into Exterior		
Window	3' X	5'		pens into Exterior		
Door	3' X	6' 8"		pens into HALL		
Window	3' X	5'		pens into Exterior		
Window	3' X	5'		pens into Exterior		
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,292. 5/8" - drywall per LF - up to 2' tall	62.92 LF		0.00	6.02	0.00	378.78
1,293. Batt insulation - 4" - R13 - paper faced	125.85 SF		0.00	0.50	0.00	62.9
1,294. Texture drywall - heavy hand texture	571.55 SF		0.00	0.58	0.00	331.5
1,295. Seal/prime then paint the walls twice (3 coats)	571.55 SF		0.00	0.84	0.00	480.1
1,296. Clean window unit (per side) 10 - 20 SF	4.00 EA		0.00	8.32	0.00	33.2
1,297. Window blind - aluminum - 1" - 14.1 to 20 SF	4.00 EA		0.00	71.21	0.00	284.8
1,298. Seal & paint wood window (per side)	4.00 EA		0.00	36.04	0.00	144.1
1,299. Paint door or window opening - 2 coats (per side)	5.00 EA		0.00	20.22	0.00	101.1
1,300. Paint door slab only - 2 coats (per side)	1.00 EA		0.00	24.16	0.00	24.1
1,301. Clean cabinetry - upper - inside and out	7.50 LF		0.00	8.14	0.00	61.0
302. Outlet	2.00 EA		0.00	11.88	0.00	23.7
1,303. Vinyl tile	210.44 SF		0.00	2.51	0.00	528.2


Page: 118

12/13/2017



#### **CONTINUED - Breakroom**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,304. Floor preparation for resilient flooring	210.44 SF		0.00	0.34	0.00	71.55
1,305. Contents - move out then reset - Large room	1.00 EA		0.00	42.27	0.00	42.27
1,306. Mask or cover per square foot	210.44 SF		0.25	0.00	0.00	52.61
1,307. Final cleaning - construction - Commercial	210.44 SF		0.00	0.11	0.00	23.15
Totals: Breakroom					0.00	2.643.44



Toilet

263.42 SF Walls 315.42 SF Walls & Ceiling 5.78 SY Flooring

29.00 LF Ceil. Perimeter

Height: 9' 1"

52.00 SF Ceiling 52.00 SF Floor

29.00 LF Floor Perimeter

Window

Door

3' X 5'

3' X 6' 8"

Opens into Exterior
Opens into HALL


DESCRIPTION REMOVE RESET REPLACE TAX QTY TOTAL 1,308. 5/8" - drywall per LF - up to 2' 29.00 LF 0.00 6.02 0.00 174.58 tall 1,309. Batt insulation - 6" - R19 -58.00 SF 0.00 0.65 0.00 37.70 paper faced 1,310. Texture drywall - heavy hand 263.42 SF 0.00 0.58 0.00 152.78 texture 1,311. Seal/prime then paint the walls 315.42 SF 0.00 0.84 0.00 264.95 and ceiling twice (3 coats) 1312. Window screen, 1 - 9 SF 1.00 EA 0.00 26.82 0.00 26.82 1,313. Clean window unit (per side) 10 0.00 8.32 1.00 EA 0.00 8.32 - 20 SF 1,314. Paint door or window opening -0.00 20.22 0.00 2.00 EA 40.44 2 coats (per side) 1,315. Paint door slab only - 2 coats 0.00 0.00 1.00 EA 24.16 24.16 (per side) 1,316. Bathroom mirror - Detach & 2.00 SF 0.00 5.34 0.00 10.68 reset 1,317. Toilet 1.00 EA 322.81 0.00 322.81 0.00 1,318. Toilet seat 1.00 EA 0.00 41.25 0.00 41.25 1,319. Angle stop valve 1.00 EA 0.00 23.88 0.00 23.88 1,320. Clean urinal 1.00 EA 0.00 11.65 0.00 11.65 VICTORYCOSUB 12/13/2017 Page: 119





#### **CONTINUED - Toilet**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,321. Clean sink and faucet	1.00 EA		0.00	9.56	0.00	9.56
1,322. Soap dispenser - Detach & reset	1.00 EA		0.00	8.78	0.00	8.78
1,323. Wall heater - Detach & reset	1.00 EA		0.00	179.20	0.00	179.20
1,324. Clean floor	52.00 SF		0.00	0.25	0.00	13.00
1,325. Mask or cover per square foot	52.00 SF		0.25	0.00	0.00	13.00
1,326. Final cleaning - construction - Commercial	52.00 SF		0.00	0.11	0.00	5.72
Totals: Toilet					0.00	1.369.28



Hall Height: 9' 1"

192.36 SF Walls 218.93 SF Walls & Ceiling 2.95 SY Flooring 21.18 LF Ceil. Perimeter 26.58 SF Ceiling26.58 SF Floor21.18 LF Floor Perimeter

Door Door Door 3' X 6' 8" 3' X 6' 8" 3' X 6' 8" Opens into TOILET
Opens into BREAKROOM
Opens into FRONT\_OFFICE

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,327. 5/8" drywall - hung, taped, ready for texture	218.93 SF		0.00	1.37	0.00	299.93
1,328. Batt insulation - 4" - R13 - paper faced	192.36 SF		0.00	0.50	0.00	96.18
1,329. Texture drywall - heavy hand texture	218.93 SF		0.00	0.58	0.00	126.98
1,330. Seal/prime then paint the walls and ceiling twice (3 coats)	218.93 SF		0.00	0.84	0.00	183.90
1,331. Casing - 2 1/4"	75.00 LF		0.00	1.24	0.00	93.00
1,332. Paint door or window opening - 2 coats (per side)	4.00 EA		0.00	20.22	0.00	80.88
1,333. Paint door slab only - 2 coats (per side)	3.00 EA		0.00	24.16	0.00	72.48
1,334. Cove base molding - rubber or vinyl, 4" high	21.18 LF		0.00	1.37	0.00	29.02
1,335. Clean floor	26.58 SF		0.00	0.25	0.00	6.65
1,336. Mask or cover per square foot	26.58 SF		0.25	0.00	0.00	6.65
,337. Final cleaning - construction - Commercial	26.58 SF		0.00	0.11	0.00	2.92
CTORYCOSUB					12/13/2017	Page: 120





# **CONTINUED - Hall**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Totals: Hall					0.00	998.59

**Front Office** 

Height: 9' 1"

533.01 SF Walls 692.41 SF Walls & Ceiling 17.71 SY Flooring 58.68 LF Ceil. Perimeter

159.39 SF Floor

159.39 SF Ceiling

58.68 LF Floor Perimeter

Window 3' 6" X 5" Window 3' 6" X 5' Door 3' X 6' 8" Door 3' X 6' 8"

**Opens into Exterior Opens into Exterior Opens into Exterior Opens into HALL** 

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
,338. Light fixture - Detach & reset	2.00 EA		0.00	41.36	0.00	82.72
1,339. 5/8" drywall - hung, taped, ready for texture	692.41 SF		0.00	1.37	0.00	948.60
1,340. Batt insulation - 6" - R19 - paper faced	159.39 SF		0.00	0.65	0.00	103.60
1,341. Batt insulation - 4" - R13 - paper faced	533.01 SF		0.00	0.50	0.00	266.51
1,342. Texture drywall - heavy hand texture	533.01 SF		0.00	0.58	0.00	309.15
1,343. Seal/prime then paint the walls twice (3 coats)	533.01 SF		0.00	0.84	0.00	447.73
1,344. Wood window - single hung, 9- 12 sf	2.00 EA		0.00	364.42	0.00	728.84
1,345. Additional charge for a retrofit window, 12-23 sf	2.00 EA		0.00	75.80	0.00	151.60
1,346. Window trim set (casing & stop)	3.00 LF		0.00	2.50	0.00	7.50
1,347. Window stool & apron	12.00 LF		0.00	4.32	0.00	51.84
1,348. Seal & paint wood window (per side)	2.00 EA		0.00	36.04	0.00	72.08
1,349. Casing - 2 1/4"	36.00 LF		0.00	1.24	0.00	44.64
1,350. Paint door or window opening - 2 coats (per side)	5.00 EA		0.00	20.22	0.00	101.10
1,351. Paint door slab only - 2 coats (per side)	2.00 EA		0.00	24.16	0.00	48.32
,352. Outlet	4.00 EA		0.00	11.88	0.00	47.52

**VICTORYCOSUB** Page: 121 12/13/2017




8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546



# **CONTINUED - Front Office**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,353. Cove base molding - rubber or vinyl, 4" high	58.68 LF		0.00	1.37	0.00	80.39
1,354. Clean floor	159.39 SF		0.00	0.25	0.00	39.85
1,355. Mask or cover per square foot	159.39 SF		0.25	0.00	0.00	39.85
1,356. Final cleaning - construction - Commercial	159.39 SF		0.00	0.11	0.00	17.53
Totals: Front Office					0.00	3,589.37



**Truck Bays** 

2,811.59 SF Walls 4,766.36 SF Walls & Ceiling 217.20 SY Flooring 188.20 LF Ceil. Perimeter 1,954.77 SF Ceiling 1,954.77 SF Floor

152.20 LF Floor Perimeter

Height: 18'

Door Door Door Door Door

3' X 6' 8" 3' X 6' 8" 3' X 6' 8" 12' X 16' 12' X 16' 12' X 16' Opens into TRAINING\_ROO
Opens into JIMBOS\_OFFI
Opens into Exterior
Opens into Exterior
Opens into Exterior

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,357. R&R Comm. overhead door opener - Trolley type - Heavy duty	1.00 EA		21.42	1,102.37	0.00	1,123.79
1,358. R&R Sectional overhead door, 16' x 12'	1.00 EA		50.13	1,833.18	0.00	1,883.31
1,359. Doors (Bid Item)	2.00 EA		0.00	360.00	0.00	720.00
Note: Considers adjusting and servicing th	he remaining (2) ov	erhead doors and	d syncing the open	ers.		
1,360. Wood window - single hung, 9- 12 sf	4.00 EA		0.00	364.42	0.00	1,457.68
1,361. Add. charge for a retrofit window, 12-23 sf - difficult	4.00 EA		0.00	139.74	0.00	558.96
1,362. Seal & paint wood window (per side)	4.00 EA		0.00	36.04	0.00	144.16
Totals: Truck Bays					0.00	5,887.90





	ning Room	OF WALL		750.22		leight: 9' 2"	
20.5	,	1,048.96 SF Walls 1,808.28 SF Walls & Ceiling			759.33 SF Ceiling 759.33 SF Floor		
Training Room			elling		LF Floor Perim	atom	
s Offi		SY Flooring LF Ceil. Perim	atar	114.57	Lr Floor Perilli	etei	
2'9 4 11'	114.57	LF Cell. Perill	leter				
Door	<b>3' X</b>	6' 8"	0	pens into JIMBO	SOFFI		
Door		3' X 6' 8"		pens into TRUCK			
Window	3' X			pens into Exterior			
Window				pens into Exterior			
Window		3' X 4' 3' X 4'		pens into Exterior			
Window	3' X			pens into Exterior			
		6' 8"		pens into Exterior			
Door							
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL	
1,363. Remove Tear off painted acoustic ceiling (popcorn) texture	759.33 SF		0.54	0.00	0.00	410.04	
,364. Clean acoustic ceiling tile - leavy	759.33 SF		0.00	0.30	0.00	227.8	
1,365. Heat/AC register - Mechanically attached - Detach & reset	5.00 EA		0.00	10.74	0.00	53.7	
1,366. Fluorescent - two tube - 4' - fixture w/lens	8.00 EA		0.00	85.33	0.00	682.6	
1,367. 5/8" - drywall per LF - up to 2' all	114.37 LF		0.00	6.02	0.00	688.5	
1,368. Batt insulation - 4" - R13 - paper faced	228.74 SF		0.00	0.50	0.00	114.3	
1,369. Texture drywall - heavy hand exture	1,048.96 SF		0.00	0.58	0.00	608.4	
1,370. Seal/prime then paint the walls twice (3 coats)	1,048.96 SF		0.00	0.84	0.00	881.1	
1,371. Casing - 2 1/4"	34.00 LF		0.00	1.24	0.00	42.1	
Note: (1) door and (2) windows							
1,372. Clean door (per side)	3.00 EA		0.00	4.00	0.00	12.0	
1,373. Paint door slab only - 2 coats (per side)	3.00 EA		0.00	24.16	0.00	72.4	
1,374. Paint door or window opening - 2 coats (per side)	7.00 EA		0.00	20.22	0.00	141.5	
1,375. Clean window unit (per side) 10 - 20 SF	4.00 EA		0.00	8.32	0.00	33.2	
1,376. Clean window blind - horizontal or vertical	48.00 SF		0.00	0.71	0.00	34.0	
,377. Window stool & apron	6.00 LF		0.00	4.32	0.00	25.9	





# **CONTINUED - Training Room**

DESCRIPTION	_ QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,378. Dry Erase board - Detach & reset	2.00 SF		0.00	5.34	0.00	10.68
1,379. Install Laminated plastic cabinets - full height unit - Comm grade	2.67 LF		0.00	62.62	0.00	167.20
I,380. Laminated plastic cabinets - lower unit - Comm grade	15.00 LF		0.00	237.66	0.00	3,564.90
1,381. Laminated plastic cabinets - upper unit - Comm grade	6.00 LF		0.00	132.75	0.00	796.50
I,382. Install Countertop - post formed plastic laminate	15.00 LF		0.00	8.49	0.00	127.35
1,383. Clean cabinetry - lower - inside and out	4.00 LF		0.00	8.14	0.00	32.56
1,384. Clean countertop	8.00 SF		0.00	0.41	0.00	3.28
1,385. Outlet	7.00 EA		0.00	11.88	0.00	83.16
1,386. Clean floor, strip & wax	759.33 SF		0.00	0.54	0.00	410.04
1,387. Mask wall - plastic, paper, tape (per LF)	114.37 LF		0.00	0.82	0.00	93.78
388. Final cleaning - construction - Commercial	759.33 SF		0.00	0.11	0.00	83.53
1,389. Mask or cover per square foot	759.33 SF		0.25	0.00	0.00	189.83
Totals: Training Room					0.00	9,590.86

Door Window

#### Jimbo's Office

528.03 SF Walls 704.18 SF Walls & Ceiling

19.57 SY Flooring

56.04 LF Ceil. Perimeter

Height: 9' 5"

176.15 SF Ceiling 176.15 SF Floor

56.04 LF Floor Perimeter

Door 3' X 6' 8"
Door 3' X 6' 8"

3' X 6' 8"

3' X 4'

Opens into TRUCK\_BAYS
Opens into TRUCK\_BAYS

Opens into TRAINING\_ROO

**Opens into Exterior** 

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,390. 5/8" - drywall per LF - up to 4' tall	28.02 LF		0.00	8.73	0.00	244.61
1,391. Batt insulation - 6" - R19 - paper faced	112.08 SF		0.00	0.65	0.00	72.85



# **CONTINUED - Jimbo's Office**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,392. Texture drywall - heavy hand texture	528.03 SF		0.00	0.58	00.00	306.26
1,393. Seal/prime then paint the walls twice (3 coats)	528.03 SF		0.00	0.84	0.00	443.55
1,394. Heat/AC register - Mechanically attached - Detach & reset	1.00 EA		0.00	10.74	0.00	10.74
1,395. Casing - oversized - 3 1/4"	18.00 LF		0.00	1.82	0.00	32.76
1,396. Paint door slab only - 2 coats (per side)	3.00 EA		0.00	24.16	0.00	72.48
1,397. Paint door or window opening - 2 coats (per side)	3.00 EA		0.00	20.22	0.00	60.66
1,398. Clean window unit (per side) 10 - 20 SF	1.00 EA		0.00	8.32	0.00	8.32
1,399. Clean window blind - horizontal or vertical	12.00 SF		0.00	0.71	0.00	8.52
1,400. Window trim set (casing & stop)	16.00 LF		0.00	2.50	0.00	40.00
1,401. Window stool & apron	3.00 LF		0.00	4.32	0.00	12.96
,402. Paint door/window trim & jamb 2 coats (per side)	1.00 EA		0.00	20.22	0.00	20.22
1,403. Outlet	3.00 EA		0.00	11.88	0.00	35.64
1,404. Phone, TV, or speaker outlet	2.00 EA		0.00	14.98	0.00	29.96
1,405. Baseboard - 8" paint grade - 2 piece	56.04 LF		0.00	4.00	0.00	224.16
1,406. Paint baseboard, oversized - two coats	56.04 LF		0.00	1.01	0.00	56.60
1,407. Clean floor, strip & wax - several layers of wax	176.15 SF		0.00	0.64	0.00	112.74
1,408. Mask or cover per square foot	176.15 SF		0.25	0.00	0.00	44.04
1,409. Contents - move out then reset - Large room	1.00 EA		0.00	42.27	0.00	42.27
1,410. Final cleaning - construction - Commercial	176.15 SF		0.00	0.11	0.00	19.38
Totals: Jimbo's Office			A STATE OF THE STA		0.00	1,898.72
Total: Main Level		-	The second of		0.00	25,978.16
Total: Building 25 - Airport Maintenance					0.00	25,978.16

# Building # 25 - Electrical Vault with Generator Roof





# Flat / Built-Up with Aggregate




710.67 Surface Area75.84 Total Perimeter Length

7.11 Number of Squares

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,411. Remove Tear off, haul and dispose of 3 ply built-up roofing	7.11 SQ		33.07	0.00	0.00	235.13
1,412. Remove Built-up roofing - gravel ballast	7.11 SQ		35.06	0.00	0.00	249.28
1,413. Built-up roof with granulated cap sheet - in place	7.11 SQ		0.00	287.69	0.00	2,045.48
Note: The modified bitumen cap sheet w	vill be installed in lieu	of the aggregate	which is non-com	pliant to code require	ments.	
1,414. R&R Fiberboard - 1/2"	710.67 SF		0.26	0.56	0.00	582.75
1,415. R&R Gravel stop	75.84 LF		0.20	1.18	0.00	104.66
1,416. R&R Steel wall coping	75.84 LF		0.34	9.37	0.00	736.41
,417. R&R Curb flashing	24.00 LF		1.10	12.22	0.00	319.68
Totals: Flat / Built-Up with Aggregate					0.00	4,273.39

#### Metal



510.78 Surface Area66.32 Total Perimeter Length

5.11 Number of Squares

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,418. R&R Metal roofing - ribbed - 26 gauge - 1 1/8" to 1 1/2"	510.78 SF		0.30	3.30	0.00	1,838.80
1,419. R&R Aluminum sidewall/endwall flashing - mill finish	42.00 LF		0.34	3.86	0.00	176.40
1,420. R&R Gable trim for metal roofing - 26 gauge	24.00 LF		0.49	3.73	0.00	101.28
1,421. R&R Closure strips for metal roofing - inside and/or outside	42.00 LF		0.49	1.16	0.00	69.30
Totals: Metal					0.00	2,185.78
otal: Roof					0.00	6,459.17





Total: Building # 25 - Electrical Vault with Generator

0.00

6,459.17

#### **Building 26 - Bridge Street Annex**

#### Roof

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,426. Exhaust fan - Commercial - large	1.00 EA		0.00	1,498.98	0.00	1,498.98
Totals: Roof		1			0.00	1.498.98



# **Emergency Operation Center / Elevator Mechanical**

LxWxH 11' x 7' x 10' 3 15/16"

371.81 SF Walls
448.81 SF Walls & Ceiling
77.00 SF Ceiling
77.00 SF Floor
8.56 SY Flooring
36.00 LF Floor Perimeter
113.61 SF Long Wall
36.00 LF Ceil. Perimeter

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,427. Plaster - Labor Minimum	1.00 EA		0.00	162.20	0.00	162.20
1,428. Seal block with masonry sealer	371.81 SF		0.00	0.57	0.00	211.93
1,429. Seal/prime then paint the walls and ceiling twice (3 coats)	448.81 SF		0.00	0.84	0.00	377.00
1,430. Mask or cover per square foot	77.00 SF		0.25	0.00	0.00	19.25
1,431. Elevator - Commercial - 3 stop - hydraulic	1.00 EA		0.00	87,711.20	0.00	87,711.20

Note: Per proposal from Thyssenkrupp. Water entered the elevator mechanical room from ground level, exposing the control panel. This system is obsolete, therefore the entire system must be upgraded to current configurations.

Totals: Emergency Operation Center / Elevator Mechanical

0.00

88,481.58



#### **EOC RegionalTraining Center**

LxWxH 29' 5 1/16" x 18' 1" x 8' 6"

807.59 SF Walls

1,339.64 SF Walls & Ceiling

532.05 SF Ceiling

532.05 SF Floor

59.12 SY Flooring

95.01 LF Floor Perimeter

250.09 SF Long Wall

95.01 LF Ceil. Perimeter

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
,432. Suspended ceiling tile - 2' x 2'	12.00 SF		0.00	1.23	0.00	14.76



# CONTINUED - EOC RegionalTraining Center

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Note: (3) tiles			100			
1,433. Batt insulation - 6" - R19 - paper faced	12.00 SF		0.00	0.65	0.00	7.80
1,434. Cove base molding - rubber or vinyl, 4" high	95.01 LF		0.00	1.37	0.00	130.16
1,435. Carpet tile - High grade	532.05 SF		0.00	3.35	0.00	1,782.37
1,436. Floor prep (scrape rubber back residue)	532.05 SF		0.00	0.34	0.00	180.90
1,437. Contents - move out then reset - Extra large room	1.00 EA		0.00	84.56	0.00	84.56
1,438. Final cleaning - construction - Commercial	532.05 SF		0.00	0.11	0.00	58.53
Totals: EOC RegionalTraining Center					0.00	2,259.08



**EOC Library** 

LxWxH 18' x 9' x 8' 6"

459.00 SF Walls 621.00 SF Walls & Ceiling 18.00 SY Flooring 153.00 SF Long Wall 54.00 LF Ceil. Perimeter 162.00 SF Ceiling 162.00 SF Floor 54.00 LF Floor Perimeter 76.50 SF Short Wall

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,439. Suspended ceiling tile - 2' x 2'	4.00 SF		0.00	1.23	0.00	4.92
Note: (1) tiles						
1,440. Batt insulation - 6" - R19 - paper faced	4.00 SF		0.00	0.65	0.00	2.60
1,441. Cove base molding - rubber or vinyl, 4" high	54.00 LF		0.00	1.37	0.00	73.98
1,442. Carpet tile - High grade	162.00 SF		0.00	3.35	0.00	542.70
1,443. Floor prep (scrape rubber back residue)	162.00 SF		0.00	0.34	0.00	55.08
1,444. Contents - move out then reset - Extra large room	1.00 EA		0.00	84.56	0.00	84.56
1,445. Final cleaning - construction - Commercial	162.00 SF		0.00	0.11	0.00	17.82
Totals: EOC Library					0.00	781.66





### **Historical Commission Office (1st Floor)**

### LxWxH 18' 8 1/16" x 16' 2 1/16" x 12' 3 15/16"

859.12 SF Walls 1,161.08 SF Walls & Ceiling 33.55 SY Flooring 230.19 SF Long Wall 69.69 LF Ceil. Perimeter 301.96 SF Ceiling 301.96 SF Floor 69.69 LF Floor Perimeter 199.37 SF Short Wall

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,446. Suspended ceiling tile - 2' x 2'	48.00 SF		0.00	1.23	0.00	59.04
1,447. Clean window unit (per side) 21 - 40 SF	1.00 EA		0.00	11.10	0.00	11.10
1,448. Clean window blind - horizontal or vertical	30.00 SF		0.00	0.71	0.00	21.30
1,449. Glue down carpet - heavy traffic	347.25 SF		0.00	3.12	0.00	1,083.42
15~% waste added for Glue down carpet -	heavy traffic.					
1,450. Floor prep (scrape rubber back residue)	301.96 SF		0.00	0.34	0.00	102.67
1,451. Contents - move out then reset - arge room	1.00 EA		0.00	42.27	0.00	42.27
1,452. Final cleaning - construction - Commercial	301.96 SF		0.00	0.11	0.00	33.22
1,453. Batt insulation - 6" - R19 - paper faced	48.00 SF		0.00	0.65	0.00	31.20
Totals: Historical Commission Office (1	st Floor)			\	0.00	1,384.22

### Storage(1st Floor)

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,454. Suspended ceiling tile - 2' x 2'	12.00 SF		0.00	1.23	0.00	14.76
Note: (3) tiles						
1,455. Batt insulation - 6" - R19 - paper faced	12.00 SF	_ \	0.00	0.65	0.00	7.80
Totals: Storage(1st Floor)					0.00	22.56







### East Foyer & Hallway (1st Floor)

#### LxWxH 10' 3" x 6' 5 1/16" x 12' 3 15/16"

411.07 SF Walls
476.89 SF Walls & Ceiling
65.82 SF Ceiling
65.82 SF Floor
7.31 SY Flooring
33.34 LF Floor Perimeter
126.36 SF Long Wall
33.34 LF Ceil. Perimeter



### Subroom 1: Hallway

### LxWxH 89' 1" x 4' x 9' 11 3/8"

1,852.02 SF Walls 2,208.35 SF Walls & Ceiling 39.59 SY Flooring 886.22 SF Long Wall 186.17 LF Ceil. Perimeter 356.33 SF Ceiling 356.33 SF Floor 186.17 LF Floor Perimeter 39.79 SF Short Wall

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,456. Specialty wood window unit, 33-40 sf	1.00 EA		0.00	3,429.60	0.00	3,429.60
* lote: This window is 4'-1" x 8'-8", 12 lite an identical window unit which the Cou						st was from
1,457. Window blind - aluminum - 2" - 32.1 to 42 SF	1.00 EA		0.00	164.93	0.00	164.93
1,458. Suspended ceiling tile - 2' x 2'	422.16 SF		0.00	1.23	0.00	519.26

my nau replaceu recentis	. This cost may need to be dajus	siea once a proposa	i is obtained.	
1.00 EA	0.00	164.93	0.00	164.93
422.16 SF	0.00	1.23	0.00	519.26
422.16 SF	0.00	0.65	0.00	274.40
1.00 EA	0.00	98.35	0.00	98.35
1.00 EA	0.00	10.89	0.00	10.89
1.00 EA	13.28	0.00	0.00	13.28
1.00 EA	0.00	264.11	0.00	264.11
ndow /				
2,263.08 SF	0.00	0.84	0.00	1,900.99
1.00 EA	0.00	20.22	0.00	20.22
219.51 LF	0.00	0.39	0.00	85.61
rd				
422.16 SF	0.25	0.00	0.00	105.54
422.16 SF	0.00	0.11	0.00	46.44
	1.00 EA  422.16 SF  422.16 SF  1.00 EA  1.00 EA  1.00 EA  1.00 EA  1.00 EA  2,263.08 SF  1.00 EA  219.51 LF	1.00 EA 0.00  422.16 SF 0.00  1.00 EA 0.00  1.00 EA 0.00  1.00 EA 13.28  1.00 EA 0.00  1.00 EA 0.00	1.00 EA 0.00 164.93  422.16 SF 0.00 1.23  422.16 SF 0.00 0.65  1.00 EA 0.00 98.35  1.00 EA 0.00 10.89  1.00 EA 13.28 0.00  1.00 EA 0.00 264.11  adow  2,263.08 SF 0.00 0.84  1.00 EA 0.00 0.39  ard  422.16 SF 0.25 0.00	422.16 SF





Subroom 2: Extension 2

### **CONTINUED - East Foyer & Hallway (1st Floor)**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Totals: East Foyer & Hallway (1st Floor)					0.00	6,933.62


96.50 LF Ceil. Perimeter



#### 



Subroom 1: Extension	LxWxH 25' 8 1/16" x 15' 5 1/16" x 8'
657.50 SF Walls	395.91 SF Ceiling
1,053.41 SF Walls & Ceiling	395.91 SF Floor
43.99 SY Flooring	82.19 LF Floor Perimeter
205.38 SF Long Wall	123.38 SF Short Wall
82.19 LF Ceil. Perimeter	



176.00 SF Walls	28.88 SF Ceiling
204.88 SF Walls & Ceiling	28.88 SF Floor
3.21 SY Flooring	22.00 LF Floor Perimeter
53.38 SF Long Wall	34.62 SF Short Wall
22.00 LF Ceil. Perimeter	

0.00	1.22		
	1.22	0.00	58.56
0.00	0.54	0.00	531.73
	0.00	0.00 0.54	0.00 0.54 0.00

LxWxH 6' 8 1/16" x 4' 3 15/16" x 8'

### **Virtus Group**



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546



### Stairwell Atrium (2nd Floor)

### LxWxH 9' 5 1/16" x 9' 5 1/16" x 11' 2 1/16"

421.04 SF Walls 509.82 SF Walls & Ceiling 9.86 SY Flooring

105.26 SF Long Wall 37.69 LF Ceil. Perimeter 88.77 SF Ceiling 88.77 SF Floor

37.69 LF Floor Perimeter

105.26 SF Short Wall

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,471. Drywall Repair - Minimum Charge - Labor and Material	1.00 EA		0.00	264.11	0.00	264.11
1,472. Light fixture - Detach & reset	1.00 EA		0.00	41.36	0.00	41.36
1,473. Seal & paint wood window (per side) - Large	1.00 EA		0.00	47.96	0.00	47.96
1,474. Seal/prime then paint the walls twice (3 coats)	421.04 SF		0.00	0.84	0.00	353.67
1,475. Vinyl tile	88.77 SF		0.00	2.51	0.00	222.81
1,476. Floor preparation for resilient flooring	88.77 SF		0.00	0.34	0.00	30.18
J,477. Clean floor, strip & wax	88.77 SF		0.00	0.54	0.00	47.94
,478. Final cleaning - construction - Commercial	88.77 SF		0.00	0.11	0.00	9.76
1,479. Mask or cover per square foot	88.77 SF		0.25	0.00	0.00	22.19
Totals: Stairwell Atrium (2nd Floor)					0.00	1,039.98

### County Clerk Cage (2nd Floor)

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,480. Suspended ceiling tile - 2' x 4'	320.00 SF		0.00	1.22	0.00	390.40
Note: (40) tiles						
1,481. Batt insulation - 6" - R19 - paper faced	320.00 SF		0.00	0.65	0.00	208.00
1,482. Fluorescent - acoustic grid fixture - four tube, 2'x 4'	1.00 EA		0.00	171.94	0.00	171.94
1,483. Reglaze window, 1 - 9 sf	2.00 EA		0.00	54.58	0.00	109.16
1,484. Final cleaning - construction - Commercial	3,628.00 SF		0.00	0.11	0.00	399.08
Totals: County Clerk Cage (2nd Floor)					0.00	1,278.58
Total: Building 26 - Bridge Street Anne	ex			1	0.00	104,270.55

**Building 27 - Extension Service** 





Roof



### Flat Built- Up with Aggregate




4,691.67 Surface Area 350.34 Total Perimeter Length 46.92 Number of Squares

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,488. Remove Tear off, haul and dispose of 4 ply built-up roofing	46.92 SQ		43.92	0.00	0.00	2,060.73
1,489. Remove Built-up roofing - gravel ballast	46.92 SQ		35.06	0.00	0.00	1,645.02
1,490. Built-up roof with granulated cap sheet - in place	46.92 SQ		0.00	287.69	0.00	13,498.4
Note: The modified bitumen cap sheet i	is being used in lieu of	ballast to comply	with code require	ements.		
1,491. R&R Gravel stop	350.34 LF		0.20	1.18	0.00	483.4
1,492. R&R Fiberboard - 1"	4,691.67 SF		0.26	0.65	0.00	4,269.42
,493. R&R Flashing - pipe jack	10.00 EA		4.14	23.34	0.00	274.80
1,494. R&R Furnace vent - rain cap and storm collar, 8"	1.00 EA		6.30	57.82	0.00	64.12
1.495. Insulation - ISO board, 3"	46.92 SQ		0.00	218.42	0.00	10.248.2
This item did not previously exist or ex incurred, subject to limits.	pands the scope of rep	pairs, but is requir	ed by current build	ling codes. The code u	pgrade cost is pa	ayable when
1.496. Insulation - ISO board. 4"	23.46 SQ		0.00	266.88	0.00	6.261.0
This item did not previously exist or ex incurred, subject to limits.	pands the scope of rep	pairs, but is requir	ed by current build	ling codes. The code u	pgrade cost is pa	ayable when
Note: Considers tapered insulation to	comply with 1/4" per fe	oot drainage requ	irements.			
1.497. 2" x 6" lumber (1 BF per LF)	700.69 LF		0.00	1.73	0.00	1,212.19
This item did not previously exist or ex incurred, subject to limits.	pands the scope of rep	pairs, but is requir	ed by current build	ding codes. The code u	pgrade cost is pa	ayable when
Note: Double perimeter band (3") insta	alled to fasten perimet	er coping after in	stallation of insula	tion.		
1.498. Steel wall coping	350.34 LF		0.00	9.37	0.00	3.282.6
This item did not previously exist or ex incurred, subject to limits.	pands the scope of rep	pairs, but is requir	ed by current build	ling codes. The code u	pgrade cost is pa	ayable when
This item did not previously exist or ex incurred, subject to limits.	pands the scope of rep	pairs, but is requir	ed by current build	ling codes. The code u	pgrade cost is p	ayable when
Totals: Flat Built- Up with Aggregate					0.00	22,295.9
Total: Roof					0.00	22,295.9



# Building #27 - Extension Service Interior Main Level



Office 1 Height: 7' 10"

335.14 SF Walls
448.93 SF Walls & Ceiling
113.79 SF Ceiling
113.79 SF Floor
12.64 SY Flooring
42.81 LF Floor Perimeter
42.81 LF Ceil. Perimeter

Window 3' X 3' Opens into Exterior
Door 3' X 6' 8" Opens into HALLWAY

Door	3 A 0 6		Opens into HALLWAT				
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL	
1,499. R&R Suspended ceiling tile - 2' x 4'	113.79 SF		0.11	1.22	0.00	151.34	
500. Batt insulation - 6" - R19 - paper faced	113.79 SF		0.00	0.65	0.00	73.96	
1,501. Clean the walls	335.14 SF		0.00	0.20	0.00	67.03	
1,502. Clean door (per side)	2.00 EA		0.00	4.00	0.00	8.00	
1,503. Clean door / window opening (per side)	2.00 EA		0.00	7.18	0.00	14.36	
1,504. Clean window unit (per side) 10 - 20 SF	4.00 EA		0.00	8.32	0.00	33.28	
1,505. Clean window blind - horizontal or vertical	60.00 SF		0.00	0.71	0.00	42.60	
1,506. Clean cove base molding - rubber or vinyl	42.81 LF		0.00	0.18	0.00	7.71	
1,507. Clean floor, strip & wax	113.79 SF		0.00	0.54	0.00	61.45	
1,508. Mask or cover per square foot	113.79 SF		0.25	0.00	0.00	28.45	
1,509. Final cleaning - construction - Commercial	113.79 SF		0.00	0.11	0.00	12.52	
Totals: Office 1					0.00	500.70	





### **Managers Office**


Height: 7' 10"

399.15 SF Walls 560.28 SF Walls & Ceiling 17.90 SY Flooring 50.99 LF Ceil. Perimeter 161.13 SF Ceiling161.13 SF Floor50.99 LF Floor Perimeter

Door 3' X 6' 8"
Window 3' X 3'
Window 3' X 3'
Door 3' X 6' 8"

Opens into FOYER\_ENTRY
Opens into Exterior
Opens into Exterior
Opens into HALLWAY

				_		
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,510. Clean the walls	399.15 SF		0.00	0.20	0.00	79.83
1,511. Clean door (per side)	2.00 EA		0.00	4.00	0.00	8.00
1,512. Clean door / window opening (per side)	2.00 EA		0.00	7.18	0.00	14.36
1,513. Clean window unit (per side) 10 - 20 SF	2.00 EA		0.00	8.32	0.00	16.64
514. Clean window blind - horizontal or vertical	30.00 SF		0.00	0.71	0.00	21.30
1,515. Clean cove base molding - rubber or vinyl	50.99 LF		0.00	0.18	0.00	9.18
1,516. Clean floor, strip & wax	161.13 SF		0.00	0.54	0.00	87.01
1,517. Mask or cover per square foot	161.13 SF		0.25	0.00	0.00	40.28
1,518. Final cleaning - construction - Commercial	161.13 SF		0.00	0.11	0.00	17.72
Totals: Managers Office					0.00	294.32



Foyer/Entry

Height: 7' 4"

195.45 SF Walls 276.05 SF Walls & Ceiling 8.96 SY Flooring 26.67 LF Ceil. Perimeter 80.60 SF Ceiling 80.60 SF Floor 26.67 LF Floor Perimeter

Window 3' X 3'
Door 3' X 6' 8"
Door 3' X 6' 8"
Missing Wall 9' 8 1/16" X 7' 3 15/16"


Opens into SECRETARY
Opens into Exterior
Opens into MANAGERS\_OFF
Opens into HALLWAY





### **CONTINUED - Foyer/Entry**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,519. Clean the walls	195.45 SF		0.00	0.20	0.00	39.09
1,520. Seal/prime then paint the walls twice (3 coats)	195.45 SF		0.00	0.84	0.00	164.18
1,521. Outlet or switch cover	2.00 EA		0.00	2.23	0.00	4.46
1,522. Cove base molding - rubber or vinyl, 4" high	26.67 LF		0.00	1.37	0.00	36.54
1,523. Clean floor, strip & wax	80.60 SF		0.00	0.54	0.00	43.52
1,524. Mask or cover per square foot	80.60 SF	Section Section 5	0.25	0.00	0.00	20.15
1,525. Final cleaning - construction - Commercial	80.60 SF		0.00	0.11	0.00	8.87
Totals: Foyer/Entry					0.00	316.81



Secretary

261.29 SF Walls 340.19 SF Walls & Ceiling 8.77 SY Flooring

35.66 LF Ceil. Perimeter

Height: 7' 4"

Page: 136

78.90 SF Ceiling 78.90 SF Floor

35.66 LF Floor Perimeter

Window 3' X 3' Window 3' X 3' 3' X 6' 8" Door

**Opens into Exterior** Opens into FOYER\_ENTRY **Opens into HALLWAY** 

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,526. Clean light fixture - fluorescent	2.00 EA		0.00	7.78	0.00	15.56
1,527. Clean the walls	261.29 SF		0.00	0.20	0.00	52.26
1,528. Clean window unit (per side) 10 - 20 SF	1.00 EA		0.00	8.32	0.00	8.32
1,529. Clean window blind - horizontal or vertical	15.00 SF		0.00	0.71	0.00	10.65
1,530. Interior door - Detach & reset	1.00 EA	The state of the s	0.00	45.27	0.00	45.27
1,531. Casing - 2 1/4"	18.00 LF		0.00	1.24	0.00	22.32
1,532. Stain & finish door/window trim & jamb (per side)	1.00 EA		0.00	26.50	0.00	26.50
1,533. Stain & finish door slab only (per side)	1.00 EA		0.00	37.80	0.00	37.80
1,534. Clean cove base molding - rubber or vinyl	35.66 LF		0.00	0.18	0.00	6.42
1,535. Clean floor, strip & wax	78.90 SF		0.00	0.54	0.00	42.61
ICTORYCOSUB					12/13/2017	Page: 13





### **CONTINUED - Secretary**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,536. Mask or cover per square foot	78.90 SF		0.25	0.00	0.00	19.73
1,537. Final cleaning - construction - Commercial	78.90 SF		0.00	0.11	0.00	8.68
Totals: Secretary					0.00	296.12

### **Yellow Office**

Height: 7' 10"

353.49 SF Walls 480.85 SF Walls & Ceiling 14.15 SY Flooring 45.16 LF Ceil. Perimeter 127.36 SF Ceiling127.36 SF Floor45.16 LF Floor Perimeter

Window Window

Door

3' X 3' 3' X 3' 3' X 6' 8" Opens into Exterior
Opens into Exterior
Opens into HALLWAY

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,538. Clean light fixture - fluorescent	2.00 EA		0.00	7.78	0.00	15.56
1,539. Clean the walls	353.49 SF		0.00	0.20	0.00	70.70
1,540. Seal/prime then paint the walls twice (3 coats)	353.49 SF		0.00	0.84	0.00	296.93
1,541. Clean window unit (per side) 10 - 20 SF	2.00 EA		0.00	8.32	0.00	16.64
1,542. Clean window blind - horizontal or vertical	30.00 SF		0.00	0.71	0.00	21.30
1,543. Outlet or switch cover	7.00 EA		0.00	2.23	0.00	15.61
1,544. Interior door - Detach & reset	1.00 EA		0.00	45.27	0.00	45.27
1,545. Stain & finish door/window trim & jamb (per side)	1.00 EA		0.00	26.50	0.00	26.50
1,546. Stain & finish door slab only (per side)	1.00 EA		0.00	37.80	0.00	37.80
1,547. Clean cove base molding - rubber or vinyl	45.16 LF		0.00	0.18	0.00	8.13
1,548. Clean floor, strip & wax	127.36 SF		0.00	0.54	0.00	68.77
1,549. Mask or cover per square foot	127.36 SF		0.25	0.00	0.00	31.84
1,550. Final cleaning - construction - Commercial	127.36 SF		0.00	0.11	0.00	14.01
Totals: Yellow Office	=				0.00	669.06

### **Virtus Group**



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

	Hallway
11-3'-	—10° 7° ——
n F	-10° 5*
40	
Oraz	ige Office Y
9'1"	8'1"-
3' 1" ←3'-	+3'-+3'-2'1'
▶3'3" •	2'3"
<b>─</b> 9'3"	Q121
<b>─</b> 6'3" <b>─</b>	1 0 3

### **Orange Office**

Height: 7' 10"

403.06 SF Walls 567.09 SF Walls & Ceiling 18.22 SY Flooring 51.49 LF Ceil. Perimeter 164.02 SF Ceiling 164.02 SF Floor 51.49 LF Floor Perimeter

 Window
 3' X 3'

 Window
 3' X 3'

 Window
 3' X 3'

 Door
 3' X 6' 8"

Opens into Exterior
Opens into Exterior
Opens into Exterior
Opens into HALLWAY

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,551. Suspended ceiling system - 2' x 4'	164.02 SF		0.00	2.24	0.00	367.40
1,552. Batt insulation - 6" - R19 - paper faced	164.02 SF		0.00	0.65	0.00	106.61
1,553. Fluorescent - acoustic grid fixture - four tube, 2'x 4'	2.00 EA		0.00	171.94	0.00	343.88
554. Seal/prime then paint the walls wice (3 coats)	403.06 SF		0.00	0.84	0.00	338.57
1,555. Clean window unit (per side) 10 - 20 SF	3.00 EA		0.00	8.32	0.00	24.96
1,556. Clean window blind - horizontal or vertical	45.00 SF		0.00	0.71	0.00	31.95
1,557. Reglaze window, 1 - 9 sf	1.00 EA		0.00	54.58	0.00	54.58
1,558. Outlet or switch cover	7.00 EA		0.00	2.23	0.00	15.61
1,559. Stain & finish door/window trim & jamb (per side)	1.00 EA		0.00	26.50	0.00	26.50
1,560. Stain & finish door slab only (per side)	1.00 EA		0.00	37.80	0.00	37.80
1,561. Clean cove base molding - rubber or vinyl	51.49 LF		0.00	0.18	0.00	9.27
1,562. Clean floor, strip & wax	164.02 SF		0.00	0.54	0.00	88.57
1,563. Mask or cover per square foot	164.02 SF		0.25	0.00	0.00	41.01
1,564. Final cleaning - construction - Commercial	164.02 SF		0.00	0.11	0.00	18.04
Totals: Orange Office					0.00	1,504.75





**VICTORYCOSUB** 

8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

Hall	way				H	leight: 7' 4"		
	1,737.90	SF Walls		684.57	SF Ceiling			
ering R brown a basis a space of many action A "	2,422.47 SF Walls & Ceiling			684.57 SF Floor				
O and Masser State and Control of the Control of th	76.06	SY Flooring		237.16 1	LF Floor Perim	eter		
	237.16	LF Ceil. Perim	eter					
Missing Wall	5' 8 1	1/16" X 7' 3 15/	16"	Opens into MEETIN	G_ROOM			
Door	3' X	6' 8"		<b>Opens into OFFICE</b>	_2			
Door	3' X	6' 8"		Opens into BREAK	ROOM			
Door	3' X	6' 8"		Opens into DOUBLI	E_OFFIC			
Door	3' X	6' 8"		Opens into ORANG	E_OFFIC			
Door	3' X	6' 8"		Opens into YELLO	W_OFFIC			
Door	3' X	6' 8"		Opens into SECRET	ARY			
Missing Wall	9'8:	1/16" X 7' 3 15/	16"	Opens into FOYER_	ENTRY			
Door	3' X 6' 8"			Opens into MANAGERS_OFF				
Door	3' X 6' 8"			Opens into OFFICE_1				
Door	3' X 6' 8"			Opens into Exterior				
Door	3' X 6' 8"			Opens into ANDERSON_OFF				
Door	3' X 6' 8"			Opens into WILHEI	LM_OFFI			
Door	3' X	6' 8"		Opens into CONFERENCE_R				
Door	3' X	6' 8"		Opens into DOUBL	E_OFFI2			
Door	3' X	6' 8"		Opens into DOUBL	E_OFFI1			
Door	3' X	6' 8"		Opens into DATA_C	CLOSET			
Door	3' X	6' 8"		Opens into MEN				
Door	3' X	6' 8"		Opens into WOMEN	1			
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL		
1,565. Suspended ceiling system - 2' x 4'	684.57 SF		0.00	2.24	0.00	1,533.44		
1,566. Batt insulation - 6" - R19 - paper faced	684.57 SF		0.00	0.65	0.00	444.97		
1,567. Fluorescent - acoustic grid fixture - four tube, 2'x 4'	14.00 EA		0.00	171.94	0.00	2,407.16		
1,568. 5/8" - drywall per LF - up to 4' tall	237.16 LF		0.00	8.73	0.00	2,070.41		
1,569. Texture drywall - heavy hand texture	1,737.90 SF		0.00	0.58	0.00	1,007.98		
1,570. Seal/prime then paint the walls twice (3 coats)	1,737.90 SF		0.00	0.84	0.00	1,459.84		
1,571. Outlet	8.00 EA		0.00	11.88	0.00	95.04		
572. Switch	1.00 EA		0.00	11.94	0.00	11.94		


12/13/2017

Page: 139



### **CONTINUED - Hallway**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,573. Stain & finish door/window trim & jamb (per side)	17.00 EA	1	0.00	26.50	0.00	450.50
1,574. Stain & finish door slab only (per side)	17.00 EA		0.00	37.80	0.00	642.60
1,575. Cove base molding - rubber or vinyl, 4" high	237.16 LF		0.00	1.37	0.00	324.91
1,576. Clean floor, strip & wax	684.57 SF		0.00	0.54	0.00	369.67
1,577. Mask or cover per square foot	684.57 SF		0.25	0.00	0.00	171.14
1,578. Final cleaning - construction - Commercial	684.57 SF		0.00	0.11	0.00	75.30
Totals: Hallway					0.00	11,064.90



**Double Office #3** 

473.52 SF Walls 689.64 SF Walls & Ceiling 24.01 SY Flooring 60.49 LF Ceil. Perimeter 216.13 SF Ceiling 216.13 SF Floor 60.49 LF Floor Perimeter

Height: 7' 10"

 Window
 3' X 3'

 Window
 3' X 3'

 Window
 3' X 3'

 Door
 3' X 6' 8"

Opens into Exterior
Opens into Exterior
Opens into Exterior
Opens into HALLWAY

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,579. Suspended ceiling system - 2' x 4'	216.13 SF		0.00	2.24	0.00	484.13
1,580. Batt insulation - 6" - R19 - paper faced	216.13 SF		0.00	0.65	0.00	140.48
1,581. Fluorescent - acoustic grid fixture - four tube, 2'x 4'	4.00 EA		0.00	171.94	0.00	687.76
1,582. Seal plaster with masonry sealer	146.19 SF		0.00	0.57	0.00	83.33
Note: Exterior wall only						
1,583. 5/8" drywall - hung, taped, heavy texture, ready for paint	473.52 SF		0.00	1.80	0.00	852.34
1,584. Seal/prime then paint the walls twice (3 coats)	473.52 SF		0.00	0.84	0.00	397.76
1,585. Batt insulation - 4" - R13 - paper faced	327.33 SF		0.00	0.50	0.00	163.67
1,586. Switch	1.00 EA		0.00	11.94	0.00	11.94
1,587. Outlet	5.00 EA		0.00	11.88	0.00	59.40
VICTORYCOSUB					12/13/2017	Page: 140





Door

VICTORYCOSUB

8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

### **CONTINUED - Double Office #3**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,588. CAT5 data/phone outlet	6.00 EA		0.00	49.42	0.00	296.52
1,589. Clean window unit (per side) 10 - 20 SF	2.00 EA	0 /	0.00	8.32	0.00	16.64
1,590. Clean window blind - horizontal or vertical	30.00 SF		0.00	0.71	0.00	21.30
1,591. Stain & finish door/window trim & jamb (per side)	1.00 EA		0.00	26.50	0.00	26.50
1,592. Stain & finish door slab only (per side)	1.00 EA		0.00	37.80	0.00	37.80
1,593. Cove base molding - rubber or vinyl, 4" high	60.49 LF		0.00	1.37	0.00	82.87
1,594. Clean floor, strip & wax	216.13 SF		0.00	0.54	0.00	116.71
1,595. Mask or cover per square foot	216.13 SF		0.25	0.00	0.00	54.03
1,596. Final cleaning - construction - Commercial	216.13 SF		0.00	0.11	0.00	23.77
Totals: Double Office #3				A STATE OF THE STA	0.00	3,556.95

Brea	ak Room	Height: 7' 10"
	473.52 SF Walls	216.13 SF Ceiling
Break Room	689.64 SF Walls & Ceiling	216.13 SF Floor
10' 10"	24.01 SY Flooring	60.49 LF Floor Perimeter
-4' 9" -3'3' -4' 10"4' 11"5'8'11'11' 1" -	60.49 LF Ceil. Perimeter	
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior

			•				
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL	
1,597. Suspended ceiling system - 2' x 4'	216.13 SF		0.00	2.24	0.00	484.13	
1,598. Batt insulation - 6" - R19 - paper faced	216.13 SF		0.00	0.65	0.00	140.48	
1,599. Fluorescent - acoustic grid fixture - four tube, 2'x 4'	4.00 EA	1 -	0.00	171.94	0.00	687.76	
1,600. Seal plaster with masonry sealer	142.87 SF		0.00	0.57	0.00	81.44	
Note: Exterior wall only							
1,601. 5/8" drywall - hung, taped, leavy texture, ready for paint	473.52 SF		0.00	1.80	0.00	852.34	

**Opens into HALLWAY** 

Page: 141

12/13/2017



### **CONTINUED - Break Room**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,602. Seal/prime then paint the walls twice (3 coats)	473.52 SF		0.00	0.84	0.00	397.76
1,603. Batt insulation - 4" - R13 - paper faced	330.65 SF		0.00	0.50	0.00	165.33
1,604. Switch	1.00 EA		0.00	11.94	0.00	11.94
1,605. Outlet	6.00 EA	•	0.00	11.88	0.00	71.28
1,606. CAT5 data/phone outlet	2.00 EA		0.00	49.42	0.00	98.84
1,607. Clean window unit (per side) 10 - 20 SF	3.00 EA		0.00	8.32	0.00	24.96
1,608. Clean window blind - horizontal or vertical	45.00 SF		0.00	0.71	0.00	31.95
1,609. Stain & finish door/window trim & jamb (per side)	1.00 EA		0.00	26.50	0.00	26.50
1,610. Stain & finish door slab only (per side)	1.00 EA		0.00	37.80	0.00	37.80
1,611. Cabinetry - upper (wall) units	8.00 LF		0.00	91.28	0.00	730.24
1,612. Seal & paint cabinetry - upper - inside and out	8.00 LF		0.00	21.79	0.00	174.32
,613. Cabinetry - lower (base) units	8.00 LF		0.00	126.22	0.00	1,009.76
1,614. Seal & paint cabinetry - lower - inside and out	8.00 LF		0.00	26.15	0.00	209.20
1,615. Countertop - post formed plastic laminate	8.00 LF		0.00	34.60	0.00	276.80
1,616. Sink - single	1.00 EA		0.00	186.17	0.00	186.17
1,617. Sink faucet - Kitchen	1.00 EA		0.00	162.59	0.00	162.59
1,618. P-trap assembly - ABS (plastic)	1.00 EA		0.00	41.10	0.00	41.10
1,619. Angle stop valve	2.00 EA		0.00	23.88	0.00	47.76
1,620. Cove base molding - rubber or vinyl, 4" high	60.49 LF		0.00	1.37	0.00	82.87
1,621. Clean floor, strip & wax	216.13 SF		0.00	0.54	0.00	116.71
1,622. Mask or cover per square foot	216.13 SF		0.25	0.00	0.00	54.03
1,623. Final cleaning - construction - Commercial	216.13 SF		0.00	0.11	0.00	23.77
Totals: Break Room		<del></del>			0.00	6,227.83





101-3'8' 8"	
8' 6"	
Office 2	
5' 11" 6' 2"	
2' 10"-3'-3'-3' 1"	
F3' → F3' 3' →	

Office 2

369.14 SF Walls 508.08 SF Walls & Ceiling 15.44 SY Flooring 47.16 LF Ceil. Perimeter 138.94 SF Ceiling 138.94 SF Floor

47.16 LF Floor Perimeter

Height: 7' 10"

Window Window Door 3' X 3' 3' X 3' 3' X 6' 8" Opens into Exterior
Opens into Exterior
Opens into HALLWAY

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,624. Suspended ceiling system - 2' x 4'	138.94 SF		0.00	2.24	0.00	311.23
1,625. Batt insulation - 6" - R19 - paper faced	138.94 SF		0.00	0.65	0.00	90.31
1,626. Fluorescent - acoustic grid fixture - four tube, 2'x 4'	2.00 EA		0.00	171.94	0.00	343.88
1,627. Seal plaster with masonry sealer	80.26 SF		0.00	0.57	0.00	45.75
Note: Exterior wall only						
1,628. 5/8" drywall - hung, taped, heavy texture, ready for paint	369.14 SF		0.00	1.80	0.00	664.45
1,629. Seal/prime then paint the walls twice (3 coats)	369.14 SF		0.00	0.84	0.00	310.08
1,630. Batt insulation - 4" - R13 - paper faced	288.88 SF		0.00	0.50	0.00	144.44
1,631. Switch	1.00 EA		0.00	11.94	0.00	11.94
1,632. Outlet	8.00 EA		0.00	11.88	0.00	95.04
1,633. CAT5 data/phone outlet	2.00 EA		0.00	49.42	0.00	98.84
1,634. Clean window unit (per side) 10 - 20 SF	2.00 EA		0.00	8.32	0.00	16.64
1,635. Clean window blind - horizontal or vertical	30.00 SF		0.00	0.71	0.00	21.30
1,636. Stain & finish door/window trim & jamb (per side)	1.00 EA		0.00	26.50	0.00	26.50
1,637. Stain & finish door slab only (per side)	1.00 EA		0.00	37.80	0.00	37.80
1,638. Cove base molding - rubber or vinyl, 4" high	47.16 LF		0.00	1.37	0.00	64.61
1,639. Clean floor, strip & wax	138.94 SF		0.00	0.54	0.00	75.03
1,640. Mask or cover per square foot	138.94 SF		0.25	0.00	0.00	34.74
1,641. Final cleaning - construction - Commercial	138.94 SF		0.00	0.11	0.00	15.28
Totals: Office 2					0.00	2,407.86





7irtus 8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

-8'8"-45'9"-4 15'7"13'43'43'45'8"1 -8'8"-45'9"-4	Meeting Room	Height: 7' 10"
2 5 5 5 5 5 5 5 5 5 5 5 5 5 5 5 5 5 5 5	732.03 SF Walls	588.38 SF Ceiling
No Meeting Room &	1,320.41 SF Walls & Ceiling	588.38 SF Floor
	65.38 SY Flooring	93.15 LF Floor Perimeter
\$ 11133 \$ \$ 1	93.15 LF Ceil. Perimeter	
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Door	3' X 6' 8"	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Missing Wall	5' 8 1/16" X 7' 9 15/16"	Opens into HALLWAY
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,642. Suspended ceiling system - 2' x 4'	588.38 SF		0.00	2.24	0.00	1,317.97
1,643. Batt insulation - 6" - R19 - paper faced	588.38 SF		0.00	0.65	0.00	382.45
1,644. Fluorescent - acoustic grid fixture - four tube, 2'x 4'	14.00 EA		0.00	171.94	0.00	2,407.16
1,645. Seal plaster with masonry sealer	500.03 SF		0.00	0.57	0.00	285.02
1,646. R&R Stud wall - 2" x 4" - 16" oc	232.00 SF		0.13	1.54	0.00	387.44
1,647. 5/8" drywall - hung, taped, heavy texture, ready for paint	732.03 SF		0.00	1.80	0.00	1,317.65
1,648. Seal/prime then paint the walls twice (3 coats)	732.03 SF		0.00	0.84	0.00	614.91
1,649. Batt insulation - 6" - R19 - paper faced	232.00 SF		0.00	0.65	0.00	150.80
1,650. Outlet	8.00 EA		0.00	11.88	0.00	95.04
1,651. Thermostat	1.00 EA		0.00	77.17	0.00	77.17
1,652. CAT5 data/phone outlet	2.00 EA		0.00	49.42	0.00	98.84
1,653. R&R Emergency lighting - battery - Commercial	1.00 EA		7.35	242.19	0.00	249.54
1,654. Clean window unit (per side) 10 20 SF	10.00 EA		0.00	8.32	0.00	83.20



### **CONTINUED - Meeting Room**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,655. Clean window blind - horizontal or vertical	150.00 SF		0.00	0.71	0.00	106.50
1,656. Prime & paint door slab only - exterior (per side)	1.00 EA	10	0.00	29.41	0.00	29.41
1,657. Paint door or window opening - 2 coats (per side)	1.00 EA		0.00	20.22	0.00	20.22
1,658. Stain & finish door/window trim & jamb (per side)	2.00 EA	400	0.00	26.50	0.00	53.00
1,659. Stain & finish door slab only (per side)	2.00 EA		0.00	37.80	0.00	75.60
1,660. Cove base molding - rubber or vinyl, 4" high	93.15 LF		0.00	1.37	0.00	127.62
1,661. Clean floor, strip & wax	588.38 SF		0.00	0.54	0.00	317.73
1,662. Mask or cover per square foot	588.38 SF		0.25	0.00	0.00	147.10
1,663. Final cleaning - construction - Commercial	588.38 SF		0.00	0.11	0.00	64.72
Totals: Meeting Room					0.00	8,409.09



Women

332.61 SF Walls 444.53 SF Walls & Ceiling 12.44 SY Flooring 42.49 LF Ceil, Perimeter Height: 7' 10"

111.92 SF Ceiling 111.92 SF Floor

42.49 LF Floor Perimeter

Window Window Door 3' X 3' 3' X 3' 3' X 6' 8"

Opens into Exterior Opens into Exterior Opens into HALLWAY


DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,664. Suspended ceiling system - 2' x 4'	111.92 SF		0.00	2.24	0.00	250.70
1,665. Batt insulation - 6" - R19 - paper faced	111.92 SF		0.00	0.65	0.00	72.75
1,666. Fluorescent - acoustic grid fixture - four tube, 2'x 4'	2.00 EA		0.00	171.94	0.00	343.88
1,667. R&R Bathroom ventilation fan	1.00 EA		10.36	76.67	0.00	87.03
1,668. Prep wall for wallpaper	332.61 SF		0.00	0.32	0.00	106.44
1,669. R&R Wallpaper	332.61 SF		0.49	1.52	0.00	668.55
,670. Clean window unit (per side) 10 - 20 SF	2.00 EA		0.00	8.32	0.00	16.64
VICTORY COSUB					12/13/2017	Page: 14:



### **CONTINUED - Women**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,671. Clean window blind - horizontal or vertical	30.00 SF		0.00	0.71	0.00	21.30
1,672. Stain & finish door/window trim & jamb (per side)	1.00 EA		0.00	26.50	0.00	26.50
1,673. Stain & finish door slab only (per side)	1.00 EA		0.00	37.80	0.00	37.80
1,674. Bathroom mirror - Detach & reset	1.00 SF		0.00	5.34	0.00	5.34
1,675. Clean mirror	12.00 SF		0.00	0.39	0.00	4.68
1,676. Clean sink and faucet	1.00 EA		0.00	9.56	0.00	9.56
1,677. Clean toilet	2.00 EA		0.00	12.05	0.00	24.10
1,678. Soap dispenser - Detach & reset	1.00 EA		0.00	8.78	0.00	8.78
1,679. Clean soap dispenser	1.00 EA		0.00	3.91	0.00	3.91
1,680. Clean towel dispenser	1.00 EA		0.00	3.89	0.00	3.89
1,681. Clean cove base molding - rubber or vinyl	42.49 LF		0.00	0.18	0.00	7.65
1,682. Clean floor, strip & wax	111.92 SF		0.00	0.54	0.00	60.44
,683. Mask or cover per square foot	111.92 SF		0.25	0.00	0.00	27.98
1,684. Final cleaning - construction - Commercial	111.92 SF		0.00	0.11	0.00	12.31
Totals: Women					0.00	1 200 23

Totals: Women 0.00 1,800.23



285.73 SF Walls 360.73 SF Walls & Ceiling

8.33 SY Flooring 36.50 LF Ceil, Perimeter 75.00 SF Ceiling 75.00 SF Floor

36.50 LF Floor Perimeter


Height: 7' 10"

Door	3' X 6' 8"		Opens into HALLWAY			
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,685. Suspended ceiling system - 2' x 4'	75.00 SF		0.00	2.24	0.00	168.00
1,686. Batt insulation - 6" - R19 - paper faced	75.00 SF		0.00	0.65	0.00	48.75
1,687. Fluorescent - acoustic grid fixture - four tube, 2'x 4'	1.00 EA		0.00	171.94	0.00	171.94
,688. R&R Bathroom ventilation fan	1.00 EA		10.36	76.67	0.00	87.03
1,689. Clean the walls	285.73 SF		0.00	0.20	0.00	57.15
VICTORYCOSUB					12/13/2017	Page: 146



### **CONTINUED - Men**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,690. Stain & finish door/window trim & jamb (per side)	1.00 EA		0.00	26.50	0.00	26.50
1,691. Stain & finish door slab only (per side)	1.00 EA		0.00	37.80	0.00	37.80
1,692. Clean mirror	12.00 SF		0.00	0.39	0.00	4.68
1,693. Clean urinal	1.00 EA		0.00	11.65	0.00	11.65
1,694. Clean sink and faucet	1.00 EA		0.00	9.56	0.00	9.56
1,695. Clean toilet	1.00 EA		0.00	12.05	0.00	12.05
1,696. Clean soap dispenser	1.00 EA		0.00	3.91	0.00	3.91
1,697. Clean towel dispenser	1.00 EA		0.00	3.89	0.00	3.89
1,698. Clean cove base molding - rubber or vinyl	36.50 LF		0.00	0.18	0.00	6.57
1,699. Clean floor, strip & wax	75.00 SF		0.00	0.54	0.00	40.50
1,700. Mask or cover per square foot	75.00 SF		0.25	0.00	0.00	18.75
1,701. Final cleaning - construction - Commercial	75.00 SF		0.00	0.11	0.00	8.25
Totals: Men					0.00	716.98



VICTORYCOSUB

**Data Closet** 

276.51 SF Walls346.94 SF Walls & Ceiling7.83 SY Flooring35.32 LF Ceil. Perimeter

Height: 7' 10"

70.43 SF Floor 35.32 LF Floor Perimeter

12/13/2017

Page: 147

70.43 SF Ceiling

Door	3' X 6' 8"	Opens into HALLWAY

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,702. Suspended ceiling system - 2' x 4'	70.43 SF		0.00	2.24	0.00	157.76
1,703. Batt insulation - 6" - R19 - paper faced	70.43 SF		0.00	0.65	0.00	45.78
1,704. Fluorescent - acoustic grid fixture - four tube, 2'x 4'	1.00 EA		0.00	171.94	0.00	171.94
1,705. Seal/prime then paint the walls twice (3 coats)	276.51 SF		0.00	0.84	0.00	232.27
1,706. Stain & finish door/window trim & jamb (per side)	1.00 EA		0.00	26.50	0.00	26.50
,707. Stain & finish door slab only (per side)	1.00 EA		0.00	37.80	0.00	37.80



### **CONTINUED - Data Closet**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,708. Cove base molding - rubber or vinyl, 4" high	35.32 LF		0.00	1.37	0.00	48.39
1,709. Clean floor, strip & wax	70.43 SF		0.00	0.54	0.00	38.03
1,710. Mask or cover per square foot	70.43 SF		0.25	0.00	0.00	17.61
1,711. Final cleaning - construction - Commercial	70.43 SF		0.00	0.11	0.00	7.75
Totals: Data Closet					0.00	783.83



### **Double Office #2**

527.01 SF Walls 782.69 SF Walls & Ceiling 28.41 SY Flooring 67.32 LF Ceil. Perimeter 255.68 SF Ceiling255.68 SF Floor67.32 LF Floor Perimeter

Height: 7' 10"

Vindow3' X 3'Opens into ExteriorWindow3' X 3'Opens into ExteriorWindow3' X 3'Opens into ExteriorDoor3' X 6' 8"Opens into HALLWAY

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,712. Suspended ceiling system - 2' x 4'	255.68 SF		0.00	2.24	0.00	572.72
1,713. Batt insulation - 6" - R19 - paper faced	255.68 SF		0.00	0.65	0.00	166.19
1,714. Fluorescent - acoustic grid fixture - four tube, 2'x 4'	2.00 EA		0.00	171.94	0.00	343.88
1,715. Seal/prime then paint the walls twice (3 coats)	527.01 SF		0.00	0.84	0.00	442.69
1,716. Clean window unit (per side) 10 - 20 SF	3.00 EA		0.00	8.32	0.00	24.96
1,717. Clean window blind - horizontal or vertical	45.00 SF		0.00	0.71	0.00	31.95
1,718. Outlet or switch cover	7.00 EA		0.00	2.23	0.00	15.61
1,719. Stain & finish door/window trim & jamb (per side)	1.00 EA		0.00	26.50	0.00	26.50
1,720. Stain & finish door slab only (per side)	1.00 EA		0.00	37.80	0.00	37.80
1,721. Clean cove base molding - rubber or vinyl	67.32 LF		0.00	0.18	0.00	12.12
1,722. Clean floor, strip & wax	255.68 SF		0.00	0.54	0.00	138.07
TICTORYCOSUB					12/13/2017	Page: 14



### **CONTINUED - Double Office #2**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,723. Mask or cover per square foot	255.68 SF		0.25	0.00	0.00	63.92
1,724. Final cleaning - construction - Commercial	255.68 SF		0.00	0.11	0.00	28.12
Totals: Double Office #2					0.00	1,904.53

10 4
10' 5"
-4'4" -3'-3'3'-3'-1'5"
-4' 2" - 1' 3
13' 2" 1-4' 3" -
7' 2"
Double Ounds #A"
16'7"
1' 16'9"
Hallway
Italiway

### **Double Office #1**

500.92 SF Walls 737.30 SF Walls & Ceiling 26.27 SY Flooring 63.99 LF Ceil. Perimeter Height: 7' 10"
236.39 SF Ceiling

236.39 SF Floor 63.99 LF Floor Perimeter

 Window
 3' X 3'

 Window
 3' X 3'

 Window
 3' X 3'

 Window
 3' X 3'

 Door
 3' X 6' 8"

Opens into Exterior
Opens into Exterior
Opens into Exterior
Opens into Exterior
Opens into HALLWAY

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,725. Suspended ceiling system - 2' x 4'	236.39 SF	1	0.00	2.24	0.00	529.51
1,726. Batt insulation - 6" - R19 - paper faced	236.39 SF		0.00	0.65	0.00	153.65
1,727. Fluorescent - acoustic grid fixture - four tube, 2'x 4'	2.00 EA		0.00	171.94	0.00	343.88
1,728. Seal/prime then paint the walls twice (3 coats)	500.92 SF		0.00	0.84	0.00	420.77
1,729. Clean window unit (per side) 10 - 20 SF	4.00 EA		0.00	8.32	0.00	33.28
1,730. Clean window blind - horizontal or vertical	60.00 SF		0.00	0.71	0.00	42.60
1,731. Outlet or switch cover	7.00 EA		0.00	2.23	0.00	15.61
1,732. Stain & finish door/window trim & jamb (per side)	1.00 EA		0.00	26.50	0.00	26.50
1,733. Stain & finish door slab only (per side)	1.00 EA		0.00	37.80	0.00	37.80
1,734. Clean cove base molding - rubber or vinyl	63.99 LF		0.00	0.18	0.00	11.52
1,735. Clean floor, strip & wax	236.39 SF		0.00	0.54	0.00	127.65
,736. Mask or cover per square foot	236.39 SF		0.25	0.00	0.00	59.10




### **Virtus Group**

8380 Warren Parkway / Ste. 700 - Frisco, TX 75034

### **CONTINUED - Double Office #1**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,737. Final cleaning - construction - Commercial	236.39 SF		0.00	0.11	0.00	26.00
Totals: Double Office #1					0.00	1,827.87



**Conference Room** 

572.67 SF Walls 862.13 SF Walls & Ceiling 32.16 SY Flooring

73.16 LF Ceil. Perimeter

Height: 7' 10"

289.45 SF Ceiling 289.45 SF Floor

73.16 LF Floor Perimeter

Window Window Window Door 3' X 3' 3' X 3' 3' X 3'

3' X 6' 8"

Opens into Exterior Opens into Exterior Opens into Exterior

Opens into HALLWAY


DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,738. Clean light fixture - fluorescent	8.00 EA		0.00	7.78	0.00	62.24
1,739. Clean the walls	572.67 SF		0.00	0.20	0.00	114.53
1,740. Seal/prime then paint the walls twice (3 coats)	572.67 SF	)	0.00	0.84	0.00	481.04
1,741. Clean window unit (per side) 10 - 20 SF	3.00 EA	/	0.00	8.32	0.00	24.96
1,742. Clean window blind - horizontal or vertical	45.00 SF		0.00	0.71	0.00	31.95
1,743. Casing - 2 1/4"	18.00 LF		0.00	1.24	0.00	22.32
1,744. Stain & finish door/window trim & jamb (per side)	1.00 EA		0.00	26.50	0.00	26.50
1,745. Stain & finish door slab only (per side)	1.00 EA		0.00	37.80	0.00	37.80
1,746. Outlet or switch cover	10.00 EA		0.00	2.23	0.00	22.30
1,747. Clean cove base molding - rubber or vinyl	73.16 LF		0.00	0.18	0.00	13.17
1,748. Clean floor, strip & wax	289.45 SF		0.00	0.54	0.00	156.30
1,749. Mask or cover per square foot	289.45 SF		0.25	0.00	0.00	72.36
1,750. Final cleaning - construction - Commercial	289.45 SF		0.00	0.11	0.00	31.84
Totals: Conference Room					0.00	1 097 31


Totals: Conference Room 0.00 1,097.31





2'3'+3'+3'+2'4 Ande	rson Office				He	eight: 7' 10'
5' 2" - 5	335,14	SF Walls		113.79 S	F Ceiling	
Anderson Office	448.93	SF Walls & Co	eiling	113.79 S		
6 + 4 + 6 5 2 ± 1 = 1		SY Flooring		42.81 L	F Floor Perime	eter
3 -61 - 1	42.81	LF Ceil. Perim	eter			
Window	3' X 3	3'	o	pens into Exterior		
Window	3' X 3'		O	pens into Exterior		
Window	3' X 3	3'	o	pens into Exterior		
Window	3' X 3	3'	o	pens into Exterior		
Door	3' X (	5' 8"	0	pens into HALLW	AY.	
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,751. R&R Suspended ceiling tile - 2'	113.79 SF		0.11	1.22	0.00	151.34
,752. Batt insulation - 6" - R19 - paper faced	113.79 SF		0.00	0.65	0.00	73.9
,753. Clean the walls	335.14 SF		0.00	0.20	0.00	67.03
,754. Clean door (per side)	2.00 EA		0.00	4.00	0.00	8.0
,755. Clean door / window opening per side)	2.00 EA		0.00	7.18	0.00	14.30
,756. Clean window unit (per side) 10 20 SF	4.00 EA		0.00	8.32	0.00	33.2
,757. Clean window blind - norizontal or vertical	60.00 SF		0.00	0.71	0.00	42.6
,758. Clean cove base molding - ubber or vinyl	42.81 LF		0.00	0.18	0.00	7.7
,759. Clean floor, strip & wax	113.79 SF		0.00	0.54	0.00	61.4
,760. Mask or cover per square foot	113.79 SF		0.25	0.00	0.00	28.4
,761. Final cleaning - construction -	113.79 SF		0.00	0.11	0.00	12.5
Totals: Anderson Office					0.00	500.70





### Wilhelm Office

Height: 7' 10"

382.19 SF Walls 530.78 SF Walls & Ceiling 16.51 SY Flooring 48.82 LF Ceil. Perimeter

148.59 SF Floor48.82 LF Floor Perimeter

148.59 SF Ceiling

Window 3' X 3'
Window 3' X 3'
Door 3' X 6' 8"

Opens into Exterior Opens into Exterior Opens into HALLWAY

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,762. Clean the walls	382.19 SF		0.00	0.20	0.00	76.44
1,763. Clean door (per side)	2.00 EA		0.00	4.00	0.00	8.00
1,764. Clean door / window opening (per side)	2.00 EA		0.00	7.18	0.00	14.36
1,765. Clean window unit (per side) 10 - 20 SF	2.00 EA		0.00	8.32	0.00	16.64
1,766. Clean window blind - porizontal or vertical	30.00 SF		0.00	0.71	0.00	21.30
1,767. Clean cove base molding - rubber or vinyl	48.82 LF		0.00	0.18	0.00	8.79
1,768. Clean floor, strip & wax	148.59 SF		0.00	0.54	0.00	80.24
1,769. Mask or cover per square foot	148.59 SF		0.25	0.00	0.00	37.15
1,770. Final cleaning - construction - Commercial	148.59 SF		0.00	0.11	0.00	16.34
Totals: Wilhelm Office					0.00	279.26
Total: Main Level	1				0.00	44,159.10

### **Electrical**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,771. Electrician - per hour	30.00 HR		0.00	84.00	0.00	2,520.00
Note: Check entire system and repla	ice wiring to fixtures @ th	he South end of b	uilding.			
Totals: Electrical					0.00	2,520.00

HVAC

DESCRIPTION QTY RESET REMOVE REPLACE TAX TOTAL

VICTORYCOSUB

12/13/2017

Page: 152



### **Virtus Group**

8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

### **CONTINUED - HVAC**

				//			
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	U TAX	TOTAL	
1,772. Ductwork - hot or cold air	30.00 LF		0.00	23.71	0.00	711.30	
1,773. Ductwork - flexible - insulated - 10" round	440.00 LF		0.00	7.74	0.00	3,405.60	
1,774. Heat/AC register - Mechanically attached	22.00 EA		0.00	16.78	0.00	369.16	
1,775. Furnace - check, heavy clean, replace filters and service	1.00 EA		0.00	163.61	0.00	163.61	
1,776. Clean ductwork - Interior (PER REGISTER)	4.00 EA		0.00	23.18	0.00	92.72	
Note: Rooms @ north end of huilding							

Note: Rooms @ north end of building

Totals: HVAC

Total: Building #27 - Extension Service Interior

0.00 4,742.39

0.00 51,421.49

### **Building 28 - Juvenile Detention Center**

Roo

DESCRIPTION QTY RESET REMOVE REPLACE TAX TOTAL

Note: The retrofit, standing seam roof had just been replaced and had not been approved for payment. A skylight and a fresh air vent were blown off during this event. The roofing contractor completed the repairs at no cost to the county.

Totals: Roof

0.00

0.00



#### **Male Unit Office**

253.25 SF Walls

315.05 SF Walls & Ceiling

6.87 SY Flooring

70.62 SF Long Wall

31.66 LF Ceil. Perimeter

### LxWxH 8' 9 15/16" x 7' x 8'

61.80 SF Ceiling 61.80 SF Floor

01.00 01 11001

31.66 LF Floor Perimeter

56.00 SF Short Wall

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,781. Suspended ceiling tile - 2' x 4'	61.80 SF		0.00	1.22	0.00	75.40
1,782. Batt insulation - 6" - R19 - paper faced	61.80 SF		0.00	0.65	0.00	40.17
1,783. Mask or cover per square foot	61.80 SF		0.25	0.00	0.00	15.45
1,784. Final cleaning - construction - Commercial	61.80 SF		0.00	0.11	0.00	6.80
Totals: Male Unit Office					0.00	137.82



### **Virtus Group**

8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

Total: Building 28 - Juvenile Detention Center

0.00

137.82

<b>Building 29</b>	- Highway	Patrol Modular
Building		

Buil	ding	1/				
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Note: No damage noted						
Totals: Building 29 - Highway Patrol M	odular Building				0.00	0.00
	- Build	ing 30 - Healf	h Department			

### Roof

QTY \	RESET	REMOVE	REPLACE	TAX	TOTAL
oof with aggregate w	vhich is associate	d with this event.	Some pre-existing iss	ues noted.	
\				0.00	0.00
	Exterior				
QTY	RESET	/REMOVE	REPLACE	TAX	TOTAL
1.00 EA		0.00	2,279.66	0.00	2,279.66
		#.E.E.E.E.E.E.E.E.E.E.E.E.E.E.E.E.E.E.E			
	X			0.00	2,279.66
	oof with aggregate w	eof with aggregate which is associate  Exterior  QTY RESET	exterior  QTY  RESET  REMOVE	exterior  QTY  RESET  REMOVE  REPLACE	Of with aggregate which is associated with this event. Some pre-existing issues noted.    Compared to the pre-existing issues noted

### **Storage Building**

DESCRIPTION	QTY /	RESET	REMOVE	REPLACE	TAX	TOTAL
1,788. Storage shed - Metal - Gable type - 10' x 8'	1.00 EA		0.00	659.06	0.00	659.06
1,789. Joist - 2x6 floor or ceiling system - treated	92.00 BF		0.00	1.49	0.00	137.08
1,790. Sheathing - plywood - 3/4" - treated	80.00 SF		0.00	1.68	0.00	134.40
1,791. Additional charge for screwing down underlayment/subfloor	80.00 SF		0.00	0.47	0.00	37.60
1,792. Excavation (Bid Item)	1.00 EA		0.00	360.00	0.00	360.00

**VICTORYCOSUB** 


otals: Storage Building

12/13/2017

0.00

Page: 154

1,328.14






Total: Exterior

0.00

3,607.80

#### Interior

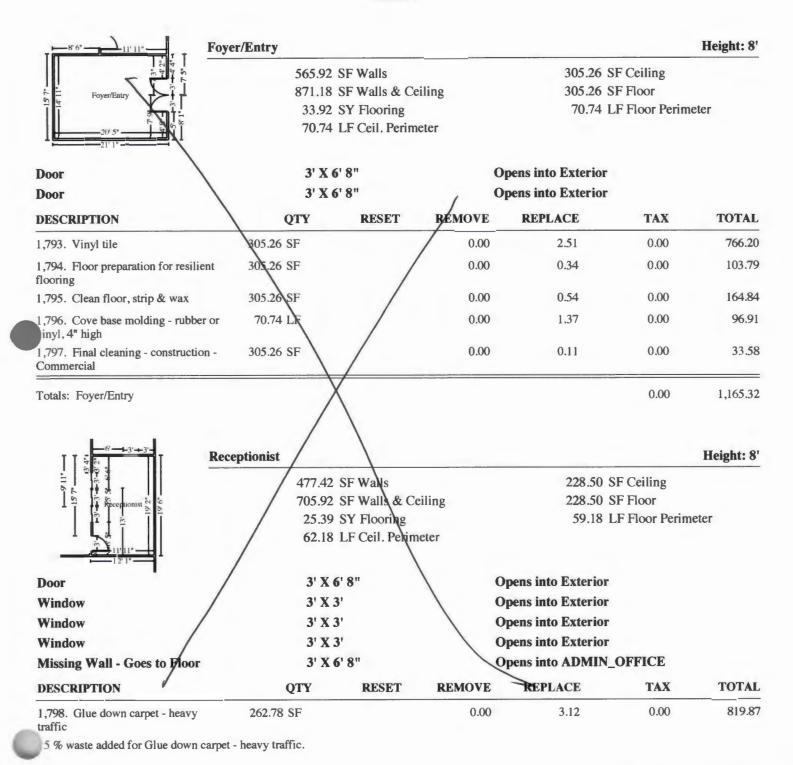





CONTINUED - Recei	eptionis	st
-------------------	----------	----

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,799. Floor prep (scrape rubber back residue)	228.50 SF		0.00	0.34	0.00	77.69
1,800. Cove base molding - rubber or vinyl, 4" high	59.18 LF		0.00	1.37	0.00	81.08
1,801. Carpet - metal transition strip	3.00 LF \		0.00	1.88	0.00	5.64
1,802. Contents - move out then reset - Extra large room	1.00 EA		0.00	84.56	0.00	84.56
1,803. Final cleaning - construction - Commercial	228.50 SF	\	0.00	0.11	0.00	25.14
Totals: Receptionist					0.00	1,093.98



**Admin Office** 

Height: 8'

548.08 SF Walls 829.24 SF Walls & Ceiling 31.24 SY Flooring 71.01 LF Ceil. Rerimeter 281.16 SF Ceiling 281.16 SF Floor

68.01 LF Floor Perimeter

Door Missing Wall - Goes to Floor 3' X 6' 8" 3' X 6' 8"/ Opens into Exterior
Opens into RECEPTIONIST

Wilsonia Wall - Odes to Floor	3 A 0 0/		Opens into Recel Horist			
DESCRIPTION	QTY	/ RESET	REMOVE	REPLACE	TAX	TOTAL
1,804. Glue down carpet - heavy traffic	323.33 SF		0.00	3.12	0.00	1,008.79
15 % waste added for Glue down carpet -	heavy traffic.		1			
1,805. Floor prep (scrape rubber back residue)	281.16 SF		0.00	0.34	0.00	95.59
1,806. Cove base molding - rubber or vinyl, 4" high	68.01 LF		0.00	1.37	0.00	93.17
1,807. Carpet - metal transition strip	3,00 LF		0.00	1.88	0.00	5.64
1,808. Contents - move out then reset - Extra large room	1.00 EA		0.00	84.56	0.00	84.56
1,809. Final cleaning - construction - Commercial	281.16 SF		0.00	0.11	0.00	30.93
Totals: Admin Office					0.00	1,318.68

VICTORYCOSUB

12/13/2017

Page: 156





**VICTORYCOSUB** 

8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

	Manager's Office					Height: 8
*\ \ \tau_{\text{fig}}	\ 413.42	SF Walls		165.91	SF Ceiling	
Manager's Office	579.33	SF Walls & Co	eiling	165.91	SF Floor	
1 1 2	18.43	SY Flooring		51.68 1	LF Floor Perime	eter
	51.68	LF Ceil. Perim	neter			
Door	\3' X (	5' 8"	Ор	ens into Exterior		
DESCRIPTION	QTY	RESET	REMOVE /	REPLACE	TAX	TOTAL
1,810. Glue down carpet - heavy traffic	190.80 SF		0.90	3.12	0.00	595.30
15 % waste added for Glue down car	pet - heavy traffic.		/			
1,811. Floor prep (scrape rubber bac residue)	ck 165.91 SF		0.00	0.34	0.00	56.4
1,812. Cove base molding - rubber ovinyl, 4" high	or 51.68 LF		0.00	1.37	0.00	70.80
1,813. Carpet - metal transition strip	3.00 LF		0.00	1.88	0.00	5.64
1,814. Contents - move out then rese Extra large room	et - 1.00 EA		0.00	84.56	0.00	84.50
815. Final cleaning - construction - Commercial	- 165.91 SF		0.00	0.11	0.00	18.25
Totals: Manager's Office		X			0.00	830.90
<b>\</b>						
\   F	Breastfeeding Counse	llor				Height: 8
		/				
	349.42	SF Walls		118.23	SF Ceiling	
1.5		SF Walls SF Walls & C	ęiling		SF Ceiling SF Floor	
Breastfeeding Counsellor:	467.64 13.14	SF Walls & C SY Flooring	\	118.23	_	eter
1.5	467.64 13.14	SF Walls & C	\	118.23	SF Floor	eter
1.5	467.64 13.14	SF Walls & C SY Flooring LF Ceil. Perim	neter	118.23	SF Floor	eter
Breastfeeding Counsellor	467.64 13.14 43.68	SF Walls & C SY Flooring LF Ceil. Perim	neter	118.23 S 43.68 D	SF Floor	eter TOTAI
Breastfeeding Counsellor	467.64 13.14 43.68	SF Walls & C SY Flooring LF Ceil. Perim	Op	118.23 S 43.68 D	SF Floor LF Floor Perim	
Door DESCRIPTION  1,816. Glue down carpet - heavy	467.64 13.14 43.68 3' X 0 QTY	SF Walls & C SY Flooring LF Ceil. Perim	Op	43.68 Pens into Exterior REPLACE	SF Floor LF Floor Perime	тотаі
Door DESCRIPTION  1,816. Glue down carpet - heavy traffic	467.64 13.14 43.68 3' X O QTY 136.96 SF	SF Walls & C SY Flooring LF Ceil. Perim	Op	43.68 Pens into Exterior REPLACE	SF Floor LF Floor Perime	<b>TOTAI</b> 424.2
Door  DESCRIPTION  1,816. Glue down carpet - heavy traffic  15 % waste added for Glue down car  1,817. Floor prep (scrape rubber back)	467.64 13.14 43.68 3' X 0 QTY 136.96 SF rpet - beavy traffic.	SF Walls & C SY Flooring LF Ceil. Perim	Op REMOVE 0.00	118.23 S 43.68 D ens into Exterior REPLACE 3.12	SF Floor LF Floor Perimo TAX 0.00	тотаі

Page: 157

12/13/2017



Virtus 8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

### **CONTINUED - Breastfeeding Counsellor**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,820. Contents - move out then recet - Extra large room	1.00 EA		0.00	84.56	0.00	84.50
1,821. Final cleaning - construction - Commercial	118.23 SF		0.00	0.11	0.00	13.0
Totals: Breastfeeding Counsellor					0.00	627.4
Dietici	an					Height: 8
11'11'	1	SF Walls		1/2 12 (	SF Ceiling	
6 8 1 0		SF Walls & Co	eiling /		SF Floor	
Dietician		SY Flooring	/		LF Floor Perim	eter
		LF Ceil. Perim	eter /			
£ 1						
Door	3' X	6' 8"	/ 0	pens into Exterior		
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTA
822. Glue down carpet - heavy	163.45 SF		0.00	3.12	0.00	509.9
traffic	anus tenffin					
15 % waste added for Glue down carpet - he	142.13 SF		0,00	0.34	0.00	48.3
1,823. Floor prep (scrape rubber back residue)	142.13 51		0.00	0.54	0.00	40.3
1,824. Cove base molding - rubber or vinyl, 4" high	47.69 LF		0.00	1.37	0.00	65.3
1,825. Carpet - metal transition strip	3.00 LF		0.00	1.88	0.00	5.6
1,826. Contents - move out then reset -	1.00 EA		0.00	84.56	0.00	84.5
Extra large room  1,827. Final cleaning - construction -	142.13 SF		0.00	0.11	0.00	15.6
Commercial	142.13 51		0.00	0.77	0.00	15.0
Totals: Dietician		7417			0.00	729.4
Total: Interior					0.00	5,765.8
Total: Building 30 - Health Department					0.00	9,373.6
	Build	ing 31 - 4-H Ac	tivity Center			
Roof						
	0.771	DECEM	REMOVE	REPLACE	TAV	TOTA
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	IUIA



### **CONTINUED - Roof**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Totals: Roof					0.00	0.00

### **Exterior / South Elevation**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,830. Detach & Reset Gutter / downspout - box - galvanized - 7" to 8"	40.00 LF	2.40	0.00	0.00	0.00	96.00
Totals: Exterior / South Elevation					0.00	96.00

### Interior

15' 6' Womens 15' 4' 15' 4'

Womens

527.25 SF Walls 729.75 SF Walls & Ceiling 22.50 SY Flooring 57.00 LF Ceil. Perimeter Height: 9' 3"
202.50 SF Ceiling

202.50 SF Floor 57.00 LF Floor Perimeter

Door 3' X 6' 8" Opens into HALLWAY

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,831. Drywall Installer / Finisher - per hour	2.00 HR		0.00	56.00	0.00	112.00
Note: Time required to repair the suspend	ded ceiling grid.					
1,832. 5/8" drywall - hung, taped, ready for texture	250.00 SF		0.00	1.37	0.00	342.50
Note: 27 l.f along the rear / South wall.						
1,833. Batt insulation - 4" - R13 - paper faced	250.00 SF		0.00	0.50	0.00	125.00
1,834. Texture drywall - heavy hand texture	527.25 SF		0.00	0.58	0.00	305.81
1,835. Seal/prime then paint the walls twice (3 coats)	527.25 SF		0.00	0.84	0.00	442.89
1,836. Ground fault interrupter (GFI) outlet	1.00 EA		0.00	23.41	0.00	23.41
1,837. Clean light fixture - fluorescent	4.00 EA		0.00	7.78	0.00	31.12
1,838. Towel Dispenser - Detach & reset	2.00 EA		0.00	10.25	0.00	20.50
,839. Soap dispenser - Detach & reset	2.00 EA		0.00	8.78	0.00	17.56



### **CONTINUED - Womens**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,840. Bathroom mirror - Detach & reset	1.00 SF		0.00	5.34	0.00	5.34
1,841. Vanity - Detach & reset	7.00 LF		0.00	32.25	0.00	225.75
1,842. Vanity top - Detach & reset	7.00 LF		0.00	17.83	0.00	124.81
1,843. Backsplash - flat laid/solid surface - Detach	3.00 LF		0.00	0.77	0.00	2.31
1,844. Angle stop valve	4.00 EA		0.00	23.88	0.00	95.52
1,845. Sink faucet - Detach & reset	2.00 EA		0.00	80.35	0.00	160.70
1,846. Toilet partition - Detach & reset	2.00 EA		0.00	161.11	0.00	322.22
1,847. Toilet - Detach & reset	1.00 EA		0.00	162.71	0.00	162.71
1,848. Cove base molding - rubber or vinyl, 4" high	57.00 LF		0.00	1.37	0.00	78.09
1,849. Clean floor, strip & wax	202.50 SF		0.00	0.54	0.00	109.35
1,850. Final cleaning - construction - Commercial	202.50 SF		0.00	0.11	0.00	22.28
1,851. Mask or cover per square foot	202.50 SF		0.25	0.00	0.00	50.63
otals: Womens					0.00	2,780,50



Hallway

1,449.64 SF Walls 2,076.84 SF Walls & Ceiling 69.69 SY Flooring 147.50 LF Ceil. Perimeter Height: 9' 10"

627.20 SF Ceiling 627.20 SF Floor 147.50 LF Floor Perimeter

Door	3' X	3' X 6' 8"		<b>Opens into WOMENS</b>		
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,852. 5/8" drywall - hung, taped, ready for texture	70.00 SF		0.00	1.37	0.00	95.90
1,853. Batt insulation - 6" - R19 - paper faced	70.00 SF		0.00	0.65	0.00	45.50
1,854. Texture drywall - heavy hand texture	138.00 SF		0.00	0.58	0.00	80.04
1,855. Seal/prime then paint the surface area twice (3 coats)	138.00 SF		0.00	0.84	0.00	115.92
1,856. Exit sign - Detach & reset	1.00 EA		0.00	53.76	0.00	53.76
1,857. Cove base molding - rubber or rinyl, 4" high	147.50 LF		0.00	1.37	0.00	202.08
1,858. Clean floor, strip & wax	627.20 SF		0.00	0.54	0.00	338.69
VICTORYCOSUB					12/13/2017	Page: 16



### **Virtus Group**

8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546



### **CONTINUED - Hallway**


DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,859. Final cleaning - construction - Commercial	627.20 SF		0.00	0.11	0.00	68.99
1,860. Mask or cover per square foot	627.20 SF		0.25	0.00	0.00	156.80
Totals: Hallway					0.00	1,157.68
Total: Interior					0.00	3,938.18
Total: Building 31 - 4-H Activity Center					0.00	4,034.18

### **Building 32 - Fire Marshall & TSA Office**

## Training Room

DESCRIPTION	OTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,863. Suspended ceiling tile - 2' x 2'	4.00 SF		0.00	1.23	0.00	4.92
Note: (1) tile						
864. Batt insulation - 6" - R19 -	4.00 SF		0.00	0.65	0.00	2.60
Totals: Training Room					0.00	7.52

### Interior



Hallway Height: 9'

239.11 SF Walls

52.91 SF Ceiling

292.02 SF Walls & Ceiling

52.91 SF Floor

52.91 SF Floor

26.57 LF Floor Perimeter

26.57 LF Ceil. Perimeter

3' X 6' 8" **Opens into Exterior** Door 9' 5 1/16" X 9' Opens into COMPUTER\_ROO Missing Wall **Opens into STORAGE** Door 3' X 6' 8" 3' X 6' 8" Opens into BREAK\_ROOM Door **Opens into WOMENS** Door 3' X 6' 8" **Opens into MENS** Door 3' X 6' 8"

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
,865. Seal/prime then paint the walls	239.11 SF		0.00	0.84	0.00	200.85





### **CONTINUED - Hallway**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,866. Clean door / window opening (per side)	3.00 EA		0.00	7.18	0.00	21.54
1,867. Clean drinking fountain	1.00 EA		0.00	19.32	0.00	19.32
1,868. Clean floor, strip & wax	52.91 SF		0.00	0.54	0.00	28.57
1,869. Mask or cover per square foot	52.91 SF		0.25	0.00	0.00	13.23
1,870. Final cleaning - construction - Commercial	52.91 SF		0.00	0.11	0.00	5.82
1,871. Clean door (per side)	3.00 EA		0.00	4.00	0.00	12.00
Totals: Hallway					0.00	301.33

1	9 5 Hailway
I	= Stor
	N N N
16' 4"	Somputer Room &
119	16'3" - Toffic
Ш	33" -6'3" - 6
11	3'-3'-3'-3
0	3'7"1-6'5"-
	<b>—</b> 6.7° <b>—</b> ₹

Computer Room

Height: 9'

374.20 SF Walls 524.90 SF Walls & Ceiling 16.74 SY Flooring 41.58 LF Ceil. Perimeter 150.70 SF Ceiling 150.70 SF Floor

41.58 LF Floor Perimeter

Window - Goes to Floor Window - Goes to Floor Window - Goes to Floor Door Missing Wall

3' X 9' 3' X 9' 3' X 9' 3' X 6' 8" 9' 5 1/16" X 9' Opens into Exterior
Opens into Exterior
Opens into Exterior
Opens into OFFICE\_2
Opens into HALLWAY


DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,872. 5/8" - drywall per LF - up to 2' tall	41.58 LF		0.00	6.02	0.00	250.31
1,873. Batt insulation - 4" - R13 - paper faced	83.16 SF		0.00	0.50	0.00	41.58
1,874. Vapor barrier - visqueen - 6mil	124.73 SF		0.00	0.21	0.00	26.19
1,875. Texture drywall - heavy hand texture	374.20 SF		0.00	0.58	0.00	217.04
1,876. Seal/prime then paint the walls twice (3 coats)	374.20 SF		0.00	0.84	0.00	314.33
1,877. R&R Outlet or switch cover	6.00 EA		0.37	2.23	0.00	15.60
1,878. Thermostat - Detach & reset	2.00 EA		0.00	35.88	0.00	71.76
1,879. Clean window unit (per side) 10 - 20 SF	3.00 EA		0.00	8.32	0.00	24.96
1,880. Cove base molding - rubber or inyl, 4" high	41.58 LF		0.00	1.37	0.00	56.96





### **CONTINUED - Computer Room**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,881. Install Computer access floor - 12" height	150.70 SF		0.00	1.47	0.00	221.53
1,882. Clean floor	150.70 SF		0.00	0.25	0.00	37.68
1,883. Mask wall - plastic, paper, tape (per LF)	8.00 LF		0.00	0.82	0.00	6.56
1,884. Final cleaning - construction - Commercial	150.70 SF		0.00	0.11	0.00	16.58
Totals: Computer Room					0.00	1,301.08



Office 2

264.09 SF Walls 349.85 SF Walls & Ceiling 9.53 SY Flooring 37.18 LF Ceil. Perimeter 85.75 SF Ceiling 85.75 SF Floor

29.34 LF Floor Perimeter

Height: 9'

Door
Window - Goes to Floor
Window - Goes to Floor

Door

3' X 6' 8" 3' X 6' 8" 4' X 9' 3' 10" X 9'

Opens into COMPUTER\_ROO
Opens into RECEPTIONIST
Opens into Exterior

**Opens into Exterior** 

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,885. 5/8" - drywall per LF - up to 2' tall	29.34 LF		0.00	6.02	0.00	176.63
1,886. Batt insulation - 4" - R13 - paper faced	58.69 SF		0.00	0.50	0.00	29.35
1,887. Texture drywall - heavy hand texture	264.09 SF		0.00	0.58	0.00	153.17
1,888. Seal/prime then paint the walls twice (3 coats) - 2 colors	264.09 SF		0.00	1.03	0.00	272.01
1,889. R&R Outlet or switch cover	7.00 EA		0.37	2.23	0.00	18.20
1,890. Clean window unit (per side) 10 - 20 SF	3.00 EA		0.00	8.32	0.00	24.96
1,891. Interior door - Detach & reset - slab only	1.00 EA		0.00	12.27	0.00	12.27
1,892. Clean door (per side)	2.00 EA		0.00	4.00	0.00	8.00
1,893. Clean door / window opening (per side)	2.00 EA		0.00	7.18	0.00	14.36
1,894. Cove base molding - rubber or vinyl, 4" high	29.34 LF		0.00	1.37	0.00	40.20
,895. Carpet tile - High grade	85.75 SF		0.00	3.35	0.00	287.26
ICTORYCOSUB					12/13/2017	Page: 163



### **CONTINUED - Office 2**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,896. Floor prep (scrape rubber back residue)	85.75 SF		0.00	0.34	0.00	29.16
1,897. Mask wall - plastic, paper, tape (per LF)	8.50 LF		0.00	0.82	0.00	6.97
1,898. Final cleaning - construction - Commercial	85.75 SF		0.00	0.11	0.00	9.43
Totals: Office 2					0.00	1,081.97

_	8' 5" — 3' 4" • Rear Hall
rage in	8'3" —3'2"
	n receptionist Fre Mars
ce 2	8'1"—8'11" %
	⊕ -7 10" - +3'-1 -3'-1 -3'-4
	8' 3" 4' 1" 1

Receptionist

Height: 9'

490.50 SF Walls 671.29 SF Walls & Ceiling 20.09 SY Flooring 54.50 LF Ceil. Perimeter 180.79 SF Ceiling 180.79 SF Floor 54.50 LF Floor Perimeter

Door Window - Goes to Floor Door

Window - Goes to Floor Door 3' X 6' 8"

3' X 9' 3' X 6' 8"

3' X 9' 3' X 6' 8" Opens into OFFICE\_2

**Opens into Exterior** 

Opens into Exterior

**Opens into Exterior** 

Opens into FIRE\_MARSHAL

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,899. 5/8" - drywall per LF - up to 2' tall	54.50 LF		0.00	6.02	0.00	328.09
1,900. Batt insulation - 4" - R13 - paper faced	109.00 SF		0.00	0.50	0.00	54.50
1,901. Texture drywall - heavy hand texture	490.50 SF		0.00	0.58	0.00	284.49
1,902. Seal/prime then paint the walls twice (3 coats) - 2 colors	490.50 SF		0.00	1.03	0.00	505.22
1,903. R&R Outlet or switch cover	9.00 EA		0.37	2.23	0.00	23.40
1,904. Clean window unit (per side) 10 - 20 SF	2.00 EA		0.00	8.32	0.00	16.64
1,905. Clean door (per side)	1.00 EA	`	0.00	4.00	0.00	4.00
1,906. Clean door / window opening (per side)	1.00 EA		0.00	7.18	0.00	7.18
1,907. Cove base molding - rubber or vinyl, 4" high	54.50 LF		0.00	1.37	0.00	74.67
1,908. Carpet tile - High grade	180.79 SF		0.00	3.35	0.00	605.65
,909. Floor prep (scrape rubber back residue)	180.79 SF		0.00	0.34	0.00	61.47
VICTORYCOSUB					12/13/2017	Page: 16





### **CONTINUED - Receptionist**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,910. Mask wall - plastic, paper, tape (per LF)	8.50 LF		0.00	0.82	0.00	6.97
1,911. Final cleaning - construction - Commercial	180.79 SF		0.00	0.11	0.00	19.89
Totals: Receptionist					0.00	1,992.17

$\perp$	Rear Hall
	6' 4" 3 4' 4" 4
mist	m Fre Marshall's Office o
	<u>\$\frac{\frac{1}{2}}{\infty} 7' 3"6' 6° </u>
-	1'4" 9"
	►4' 4" <b>1</b> —6' 10" <b>→</b>

#### Fire Marshall's Office

Height: 9'

477.00 SF Walls 642.29 SF Walls & Ceiling 18.37 SY Flooring 53.00 LF Ceil. Perimeter 165.29 SF Ceiling165.29 SF Floor53.00 LF Floor Perimeter

Window - Goes to Floor
Window - Goes to Floor
Window - Goes to Floor

3' X 6' 8" 3' X 9' 3' X 9' 3' X 9' Opens into RECEPTIONIST
Opens into Exterior
Opens into Exterior
Opens into Exterior

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,912. 5/8" - drywall per LF - up to 2' tall	26.50 LF		0.00	6.02	0.00	159.53
1,913. Batt insulation - 4" - R13 - paper faced	26.50 SF		0.00	0.50	0.00	13.25
1,914. Texture drywall - heavy hand texture	477.00 SF		0.00	0.58	0.00	276.66
1,915. Seal/prime then paint the walls twice (3 coats) - 2 colors	477.00 SF		0.00	1.03	0.00	491.31
1,916. R&R Outlet or switch cover	6.00 EA		0.37	2.23	0.00	15.60
1,917. Clean window unit (per side) 10 - 20 SF	3.00 EA		0.00	8.32	0.00	24.96
1,918. Clean window blind - horizontal or vertical	36.00 SF		0.00	0.71	0.00	25.56
1,919. Clean door (per side)	1.00 EA		0.00	4.00	0.00	4.00
1,920. Clean door / window opening (per side)	1.00 EA		0.00	7.18	0.00	7.18
1,921. Shelving - Detach & reset	53.00 LF		0.00	4.62	0.00	244.86
1,922. Cove base molding - rubber or vinyl, 4" high	53.00 LF		0.00	1.37	0.00	72.61
1,923. Carpet tile - High grade	165.29 SF		0.00	3.35	0.00	553.72
,924. Floor prep (scrape rubber back residue)	165.29 SF		0.00	0.34	0.00	56.20






#### **CONTINUED - Fire Marshall's Office**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,925. Mask wall - plastic, paper, tape (per LF)	8.50 LF		0.00	0.82	0.00	6.97
1,926. Final cleaning - construction - Commercial	165.29 SF		0.00	0.11	0.00	18.18
Totals: Fire Marshall's Office					0.00	1,970.59
Total: Interior					0.00	6,647.14
Total: Building 32 - Fire Marshall & TSA	A Office				0.00	6,654.66

## Building #33 - Officers Club Roof

#### Roof1



7,282.89 Surface Area 710.84 Total Perimeter Length 72.83 Number of Squares 140.42 Total Ridge Length

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,929. Remove Tear off, haul and dispose of comp. shingles - 3 tab	72.83 SQ		32.50	0.00	0.00	2,366.98
1,930. Remove Additional layer of comp. shingles, remove (no haul off)	145.66 SQ		13.86	0.00	0.00	2,018.85
Note: 2 layers of shingles and 2 layers of	f temporary covering					
1,931. 3 tab - 25 yr composition shingle roofing - incl. felt	80.33 SQ		0.00	134.65	0.00	10,816.43
1,932. R&R Drip edge	435.00 LF		0.20	1.30	0.00	652.50
1,933. R&R Flashing - pipe jack	5.00 EA		4.14	23.34	0.00	137.40
1,934. R&R Furnace vent - rain cap and storm collar, 6"	5.00 EA		6.30	50.50	0.00	284.00
1,935. R&R Curb flashing - Modified Bitumen	40.00 LF		1.10	12.22	0.00	532.80
Note: Flashing around the base of (5) ri	dge vents.					
1,936. General Laborer - per hour	8.00 HR		0.00	20.66	0.00	165.28
Note: Additional labor required to remodump.	ve shingles from roof	f due to difficult of	access. (3) sides of	f the roof are either fe	nced off or inacc	cessible to
1,937. R&R Tarp - all-purpose poly - per sq ft (labor and material)	7,282.89 SF		0.05	0.51	0.00	4,078.41





Washroom

#### **CONTINUED - Roof1**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Totals: Roof1					0.00	21,052.65
Total: Roof					0.00	21,052.65
Total: Building #33 - Officers Club					0.00	21,052.65

## Building 33 - Officers Club Interior Interior

allway

247.75 SF Walls
300.36 SF Walls & Ceiling
5.85 SY Flooring

30.01 LF Ceil. Perimeter

52.61 SF Ceiling 52.61 SF Floor 27.01 LF Floor Perimeter

Height: 8' 11"

Door
Missing Wall - Goes to Floor

3' X 6' 8" 3' X 6' 8" Opens into HALLWAY
Opens into MENS

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL	
1,938. Clean light fixture	1.00 EA		0.00	5.86	0.00	5.86	
1,939. Clean the walls - Light	247.75 SF		0.00	0.15	0.00	37.16	
1,940. Paint the walls - two coats	247.75 SF		0.00	0.63	0.00	156.08	
1,941. Paint door slab only - 2 coats (per side)	1.00 EA		0.00	24.16	0.00	24.16	
1,942. Paint door or window opening - 2 coats (per side)	1.00 EA		0.00	20.22	0.00	20.22	
1,943. Bathroom mirror - Detach & reset	2.00 SF		0.00	5.34	0.00	10.68	
1,944. Soap dispenser - Detach & reset	1.00 EA		0.00	8.78	0.00	8.78	
1,945. Remove Paper towel dispenser	1.00 EA		8.82	0.00	0.00	8.82	
1,946. Clean sink and faucet	2.00 EA		0.00	9.56	0.00	19.12	
1,947. Paint baseboard, oversized - two coats	27.01 LF		0.00	1.01	0.00	27.28	
1,948. Seal & paint base shoe or quarter round	27.01 LF		0.00	0.52	0.00	14.05	
1,949. Clean floor, strip & wax	52.61 SF		0.00	0.54	0.00	28.41	





3' 4" 63' 3" Foye	r				Не	eight: 8' 11"
38.6	357.19	SF Walls		88.63 SI	F Ceiling	
Foyer	445.82	SF Walls & Ce	eiling	88.63 SI	F Floor	
	9.85	SY Flooring		40.03 L	F Floor Perim	eter
	40.03	LF Ceil. Perim	eter			
Door	3' X	6' 8"	0	pens into COAT_R	ООМ	
Door	2' 8 1	/16" X 6' 8"	O	pens into HALLWA	Y	
Door	2' 8 1	/16" X 6' 8"	O	pens into HALLWA	Y	
Door	3' X	6' 8"	O	pens into OFFICE		
Door	2' 8 1	/16" X 6' 8"	O	pens into Exterior		
Door	2' 8 1	/16" X 6' 8"	O	pens into Exterior		
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,950. 1/2" - drywall per LF - up to 4' tall	80.07 LF		0.00	8.30	0.00	664.58
Note: 2 layers						
1,951. Texture drywall - heavy hand exture	357.19 SF		0.00	0.58	0.00	207.17
1,952. Paint the walls and ceiling - two coats	445.82 SF		0.00	0.63	0.00	280.87
1,953. Light fixture - Detach & reset	1.00 EA		0.00	41.36	0.00	41.36
1,954. Clean light fixture	1.00 EA		0.00	5.86	0.00	5.86
1,955. Casing - Detach & reset	54.00 LF		0.00	1.10	0.00	59.40
1,956. Paint casing - two coats	54.00 LF		0.00	0.93	0.00	50.22
1,957. Paint French door slab only - 2 coats (per side)	5.00 EA		0.00	46.22	0.00	231.10
1,958. Paint full louvered door slab only - 2 coats (per side)	1.00 EA		0.00	33.05	0.00	33.05
1,959. Paint door or window opening - 2 coats (per side)	2.00 EA		0.00	20.22	0.00	40.44
1,960. Paint door or window opening - Large - 2 coats (per side)	2.00 EA		0.00	23.79	0.00	47.58
1,961. Outlet or switch cover	1.00 EA		0.00	2.23	0.00	2.23
1,962. Exit sign - Detach & reset	1.00 EA		0.00	53.76	0.00	53.76
1,963. Baseboard - 3 1/4"	40.03 LF		0.00	1.94	0.00	77.66
1,964. Paint baseboard, oversized - two coats	40.03 LF		0.00	1.01	0.00	40.43
1,965. Sand, stain, and finish wood floor	88.63 SF		0.00	3.07	0.00	272.09
1,966. Add for dustless floor sanding	88.63 SF		0.00	0.80	0.00	70.90
,967. Mask or cover per square foot	88.63 SF		0.25	0.00	0.00	22.16





## **CONTINUED** - Foyer

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Totals: Foyer					0.00	2,200.86

Totals: Foyer					0.00	2,200.86
118 5 3°4 Halls	way				Н	leight: 8' 11"
Schro	435.51	SF Walls		142.70	6 SF Ceiling	
Haliwa H	578.27	SF Walls & Co	eiling	142.70	6 SF Floor	
и — — — — — — — — — — — — — — — — — — —	15.86	SY Flooring		46.24	4 LF Floor Perin	neter
20 54 7 5 8 1 1 1 2 5 5 1 1 1 1 1 1 1 1 1 1 1 1 1 1	56.41	LF Ceil. Perim	eter	1		
Missing Wall - Goes to Floor	5' 3"	X 6' 8"	(	Opens into BAR_	_DINING	
Door	3' X 6	5' 8"		Opens into WASH	IROOM	
Door	2' 8 1	/16" X 6' 8"	(	Opens into FOYE	R	
Door	2' 8 1	/16" X 6' 8"	(	Opens into FOYE	R	
Missing Wall - Goes to Floor	4' 11'	X 6' 8"	(	Opens into HALL	_EXTENSI	
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
968. 1/2" - drywall per LF - up to 4' tall	92.49 LF		0.00	8.30	0.00	767.67
Note: 2 layers						
1,969. Texture drywall - heavy hand texture	435.51 SF		0.00	0.58	0.00	252.60
1,970. Paint the walls and ceiling - two	578.27 SF		0.00	0.63	0.00	364.31


DESCRIPTION	VII	INDSE I	REMIOTE	ILLI LIKEL	- 1 - 1 - 1	I O I I I I
,968. 1/2" - drywall per LF - up to 4' tall	92.49 LF		0.00	8.30	0.00	767.67
Note: 2 layers						
1,969. Texture drywall - heavy hand texture	435.51 SF		0.00	0.58	0.00	252.60
1,970. Paint the walls and ceiling - two coats	578.27 SF		0.00	0.63	0.00	364.31
1,971. Light fixture - Detach & reset	2.00 EA		0.00	41.36	0.00	82.72
1,972. Clean light fixture	2.00 EA		0.00	5.86	0.00	11.72
1,973. Casing - Detach & reset	77.00 LF		0.00	1.10	0.00	84.70
1,974. Paint casing - two coats	77.00 LF		0.00	0.93	0.00	71.61
1,975. Paint French door slab only - 2 coats (per side)	2.00 EA		0.00	46.22	0.00	92.44
1,976. Paint door slab only - 2 coats (per side)	1.00 EA		0.00	24.16	0.00	24.16
1,977. Paint door or window opening - 2 coats (per side)	1.00 EA		0.00	20.22	0.00	20.22
1,978. Paint door or window opening - Large - 2 coats (per side)	3.00 EA		0.00	23.79	0.00	71.37
1,979. Outlet or switch cover	1.00 EA		0.00	2.23	0.00	2.23
1,980. Exit sign - Detach & reset	1.00 EA		0.00	53.76	0.00	53.76
1,981. Baseboard - 3 1/4"	46.24 LF		0.00	1.94	0.00	89.71
1,982. Paint baseboard, oversized - wo coats	46.24 LF		0.00	1.01	0.00	46.70



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034

#### **CONTINUED - Hallway**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,983. Sand, stain, and finish wood floor	142.76 SF		0.00	3.07	0.00	438.27
1,984. Add for dustless floor sanding	142.76 SF		0.00	0.80	0.00	114.21
1,985. Mask or cover per square foot	142.76 SF		0.25	0.00	0.00	35.69
Totals: Hallway					0.00	2.624.0



Mens Height: 8' 11"

293.26 SF Walls 369.89 SF Walls & Ceiling 8.51 SY Flooring 35.11 LF Ceil. Perimeter 76.63 SF Ceiling 76.63 SF Floor

Opens into WASHROOM

32.11 LF Floor Perimeter

Missing Wall - Goes to Floor

Window


3' X 6' 8"

3' X 5' Opens into Exterior

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,986. Clean light fixture	2.00 EA		0.00	5.86	0.00	11.72
1,987. Clean the walls - Light	293.26 SF		0.00	0.15	0.00	43.99
1,988. Paint the walls - two coats	293.26 SF		0.00	0.63	0.00	184.75
1,989. Paint door or window opening - 2 coats (per side)	2.00 EA		0.00	20.22	0.00	40.44
1,990. Clean window unit (per side) 10 - 20 SF	1.00 EA		0.00	8.32	0.00	8.32
1,991. Seal & paint wood window (per side)	2.00 EA		0.00	36.04	0.00	72.08
1,992. Clean urinal	2.00 EA		0.00	11.65	0.00	23.30
1,993. Clean toilet	2.00 EA		0.00	12.05	0.00	24.10
1,994. Clean toilet partition - per stall	1.00 EA		0.00	14.67	0.00	14.67
1,995. Paint baseboard, oversized - two coats	32.11 LF		0.00	1.01	0.00	32.43
1,996. Seal & paint base shoe or quarter round	32.11 LF		0.00	0.52	0.00	16.70
1,997. Clean floor, strip & wax	76.63 SF		0.00	0.54	0.00	41.38
Totals: Mens					0.00	513.88



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546



Womens

442.09 SF Walls 589.45 SF Walls & Ceiling

16.37 SY Flooring

49.12 LF Ceil. Perimeter

Height: 9'

147.35 SF Ceiling

147.35 SF Floor

49.12 LF Floor Perimeter

Window Window

Door

3' X 5' 3' X 5'

3' X 6' 8"


**Opens into Exterior Opens into Exterior** 

Opens into HALL\_EXTENSI

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
1,998. Clean light fixture	2.00 EA		0.00	5.86	0.00	11.72
1,999. Clean the walls - Light	442.09 SF		0.00	0.15	0.00	66.31
2,000. Paint the walls - two coats	442.09 SF		0.00	0.63	0.00	278.52
2,001. Paint door slab only - 2 coats (per side)	1.00 EA		0.00	24.16	0.00	24.16
2,002. Paint door or window opening - 2 coats (per side)	1.00 EA		0.00	20.22	0.00	20.22
,003. Clean window unit (per side) 10 - 20 SF	2.00 EA		0.00	8.32	0.00	16.64
2,004. Seal & paint wood window (per side)	2.00 EA		0.00	36.04	0.00	72.08
2,005. Clean window blind - horizontal or vertical	30.00 SF		0.00	0.71	0.00	21.30
2,006. Bathroom mirror - Detach & reset	2.00 SF		0.00	5.34	0.00	10.68
2,007. Soap dispenser - Detach & reset	1.00 EA		0.00	8.78	0.00	8.78
2,008. Remove Paper towel dispenser	1.00 EA		8.82	0.00	0.00	8.82
2,009. Clean sink and faucet	2.00 EA		0.00	9.56	0.00	19.12
2,010. Clean toilet	2.00 EA		0.00	12.05	0.00	24.10
2,011. Clean toilet partition - per stall	2.00 EA		0.00	14.67	0.00	29.34
2,012. Paint baseboard, oversized - two coats	49.12 LF		0.00	1.01	0.00	49.61
2,013. Seal & paint base shoe or quarter round	49.12 LF		0.00	0.52	0.00	25.54
2,014. Clean floor, strip & wax	147.35 SF		0.00	0.54	0.00	79.57
Totals: Womens					0.00	766.51







Hall Extension

88.37 SF Ceiling

331.04 SF Walls419.40 SF Walls & Ceiling9.82 SY Flooring40.78 LF Ceil. Perimeter

88.37 SF Floor 35.86 LF Floor Perimeter

Height: 8' 11"

Missing Wall - Goes to Floor


Door Door 4' 11" X 6' 8" 3' X 6' 8" 3' X 6' 8" Opens into HALLWAY
Opens into Exterior
Opens into WOMENS

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,015. 1/2" - drywall per LF - up to 4' tall	35.86 LF		0.00	8.30	0.00	297.64
2,016. Batt insulation - 6" - R19 - paper faced	165.52 SF		0.00	0.65	0.00	107.59
2,017. Texture drywall - heavy hand texture	331.04 SF		0.00	0.58	0.00	192.00
2,018. Paint the walls and ceiling - two coats	419.40 SF		0.00	0.63	0.00	264.22
,019. Light fixture - Detach & reset	1.00 EA		0.00	41.36	0.00	41.36
2,020. Clean light fixture	1.00 EA		0.00	5.86	0.00	5.86
2,021. Casing - Detach & reset	54.00 LF		0.00	1.10	0.00	59.40
2,022. Paint casing - two coats	54.00 LF		0.00	0.93	0.00	50.22
2,023. Prime & paint door slab only - exterior (per side)	1.00 EA		0.00	29.41	0.00	29.41
2,024. Paint door slab only - 2 coats (per side)	1.00 EA		0.00	24.16	0.00	24.16
2,025. Paint door or window opening - 2 coats (per side)	2.00 EA		0.00	20.22	0.00	40.44
2,026. Paint door or window opening - Large - 2 coats (per side)	1.00 EA		0.00	23.79	0.00	23.79
2,027. Outlet or switch cover	1.00 EA		0.00	2.23	0.00	2.23
2,028. Exit sign - Detach & reset	1.00 EA		0.00	53.76	0.00	53.76
2,029. R&R Chair rail - 2 1/2"	14.00 LF		0.24	1.85	0.00	29.26
2,030. Paint chair rail - two coats	35.86 LF		0.00	0.93	0.00	33.35
2,031. Baseboard - 3 1/4"	35.86 LF		0.00	1.94	0.00	69.57
2,032. Paint baseboard, oversized - two coats	35.86 LF		0.00	1.01	0.00	36.22
2,033. R&R Oak flooring - clear grade - no finish	88.37 SF		1.38	7.31	0.00	767.93
2,034. Vapor barrier - 15# felt	88.37 SF		0.00	0.20	0.00	17.67
,035. Sand, stain, and finish wood floor	88.37 SF		0.00	3.07	0.00	271.30
/ICTORYCOSUB					12/13/2017	Page: 172



#### **CONTINUED - Hall Extension**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,036. Add for dustless floor sanding	88.37 SF		0.00	0.80	0.00	70.70
2,037. R&R Reducer strip - for wood flooring	6.00 LF		0.22	4.86	0.00	30.48
2,038. Mask or cover per square foot	88.37 SF		0.25	0.00	0.00	22.09
Totals: Hall Extension					0.00	2.540.65



**Coat Room** 

570.41 SF Walls 822.48 SF Walls & Ceiling 28.01 SY Flooring

63.93 LF Ceil. Perimeter

252.07 SF Ceiling252.07 SF Floor63.93 LF Floor Perimeter

Height: 8' 11"

Window Window Door 5' X 3' 5' X 3' 3' X 6' 8" Opens into Exterior Opens into Exterior Opens into FOYER


DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,039. Suspended ceiling tile - 2' x 4'	252.07 SF		0.00	1.22	0.00	307.53
2,040. Batt insulation - 6" - R19 - paper faced	394.67 SF		0.00	0.65	0.00	256.54
2,041. Clean light fixture	4.00 EA		0.00	5.86	0.00	23.44
Note: (2) exterior walls up 4'.						
2,042. $1/2$ " - drywall per LF - up to 4' tall	127.87 LF		0.00	8.30	0.00	1,061.32
Note: 2 layers						
2,043. Texture drywall - heavy hand texture	570.41 SF		0.00	0.58	0.00	330.84
2,044. Paint the walls - two coats	570.41 SF		0.00	0.63	0.00	359.36
2,045. Wood window unit - Detach & reset	1.00 EA		0.00	84.85	0.00	84.85
2,046. Carpenter - General Framer - per hour	4.00 HR		0.00	46.80	0.00	187.20
Note: Wall framing at window must be re	placed.					
2,047. R&R Window stool & apron	5.00 LF		0.45	4.32	0.00	23.85
2,048. Clean window unit (per side) 21 - 40 SF	2.00 EA		0.00	11.10	0.00	22.20
2,049. Seal & paint wood window (per ide) - Large	2.00 EA		0.00	47.96	0.00	95.92
2,050. Casing - oversized - 3 1/4"	71.00 LF		0.00	1.82	0.00	129.22
/ICTORYCOSUB					12/13/2017	Page: 17



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### **CONTINUED - Coat Room**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,051. Seal & paint casing - oversized - two coats	71.00 LF		0.00	1.03	0.00	73.13
2,052. R&R Chair rail - 2 1/2"	26.00 LF		0.24	1.85	0.00	54.34
2,053. Paint chair rail - two coats	26.00 LF		0.00	0.93	0.00	24.18
2,054. Clean mirror	60.00 SF		0.00	0.39	0.00	23.40
2,055. Paint half louvered door slab only - 2 coats (per side)	1.00 EA		0.00	29.95	0.00	29.95
2,056. Paint door or window opening - 2 coats (per side)	1.00 EA		0.00	20.22	0.00	20.22
2,057. Paint door or window opening - Large - 2 coats (per side)	2.00 EA		0.00	23.79	0.00	47.58
2,058. Outlet or switch cover	5.00 EA		0.00	2.23	0.00	11.15
2,059. Baseboard - 3 1/4"	63.93 LF		0.00	1.94	0.00	124.02
2,060. Paint baseboard, oversized - two coats	63.93 LF		0.00	1.01	0.00	64.57
2,061. Glue down carpet	289.88 SF		0.00	1.58	0.00	458.01
15 % waste added for Glue down carpet.						
2,062. Floor prep (scrape rubber back residue)	252.07 SF		0.00	0.34	0.00	85.70
Totals: Coat Room					0.00	3,898.52



Office Height: 8' 4"

460.10 SF Walls 650.69 SF Walls & Ceiling

21.18 SY Flooring 55.25 LF Ceil. Perimeter 190.60 SF Ceiling 190.60 SF Floor 55.25 LF Floor Perimeter

Door Window Door

**VICTORYCOSUB** 

3' X 6' 8" 5' X 3' 3' X 6' 8" Opens into FOYER
Opens into Exterior
Opens into Exterior

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,063. Suspended ceiling tile - 2' x 4'	190.60 SF		0.00	1.22	0.00	232.53
2,064. Batt insulation - 6" - R19 - paper faced	305.62 SF		0.00	0.65	0.00	198.65
2,065. Clean light fixture	4.00 EA		0.00	5.86	0.00	23.44
Note: (2) exterior walls up 4'.						

12/13/2017 Page: 174





#### **CONTINUED - Office**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,066. 1/2" - drywall per LF - up to 4' tall	55.25 LF		0.00	8.30	0.00	458.58
2,067. Texture drywall - heavy hand texture	460.10 SF		0.00	0.58	0.00	266.86
2,068. Paint the walls - two coats	460.10 SF		0.00	0.63	0.00	289.86
2,069. Wood window unit - Detach & reset	1.00 EA		0.00	84.85	0.00	84.85
2,070. Carpenter - General Framer - per hour	4.00 HR		0.00	46.80	0.00	187.20
Note: Wall framing at window must be re	placed.					
2,071. R&R Window stool & apron	5.00 LF		0.45	4.32	0.00	23.85
2,072. Clean window unit (per side) 21 - 40 SF	1.00 EA		0.00	11.10	0.00	11.10
2,073. Seal & paint wood window (per side) - Large	1.00 EA		0.00	47.96	0.00	47.96
2,074. Casing - oversized - 3 1/4"	36.00 LF		0.00	1.82	0.00	65.52
2,075. Seal & paint casing - oversized - two coats	36.00 LF		0.00	1.03	0.00	37.08
,076. Prime & paint door slab only - exterior (per side)	1.00 EA		0.00	29.41	0.00	29.41
2,077. Paint French door slab only - 2 coats (per side)	1.00 EA		0.00	46.22	0.00	46.22
2,078. Paint door or window opening - 2 coats (per side)	2.00 EA		0.00	20.22	0.00	40.44
2,079. Paint door or window opening - Large - 2 coats (per side)	1.00 EA		0.00	23.79	0.00	23.79
2,080. Electrician - per hour	4.00 HR		0.00	84.00	0.00	336.00
Note: Rewire outlets and switch in condu	it.					
2,081. Outlet or switch cover	3.00 EA		0.00	2.23	0.00	6.69
2,082. Baseboard - 3 1/4"	55.25 LF		0.00	1.94	0.00	107.19
2,083. Paint baseboard, oversized - two coats	55.25 LF		0.00	1.01	0.00	55.80
2,084. Glue down carpet	219.19 SF		0.00	1.58	0.00	346.32
15 % waste added for Glue down carpet.						
2,085. Floor prep (scrape rubber back residue)	190.60 SF		0.00	0.34	0.00	64.80
Totals: Office					0.00	2,984.14



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546



Storage Area/Room

Height: 10' 6"

906.61 SF Walls 1,372.39 SF Walls & Ceiling 51.75 SY Flooring 86.34 LF Ceil. Perimeter

465.78 SF Ceiling 465.78 SF Floor 86.34 LF Floor Perimeter

Door Door 3' X 6' 8" 3' X 6' 8" Opens into BAR\_\_DINING **Opens into Exterior** 

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,086. Batt insulation - 4" - R15 - paper faced	465.78 SF		0.00	0.69	0.00	321.39
2,087. 5/8" drywall - hung, taped, ready for texture	1,372.39 SF		0.00	1.37	0.00	1,880.17
2,088. Batt insulation - 6" - R19 - paper faced	906.61 SF		0.00	0.65	0.00	589.30
2,089. Texture drywall - heavy hand texture	1,372.39 SF		0.00	0.58	0.00	795.99
2,090. Paint the walls and ceiling - two toats	1,372.39 SF		0.00	0.63	0.00	864.61
2,091. Fluorescent - four tube - 4' - fixture w/lens	2.00 EA		0.00	97.65	0.00	195.30
2,092. R&R Oullet or switch cover	2.00 EA		0.37	2.23	0.00	5.20
2,093. Exit sign - Detach & reset	1.00 EA		0.00	53.76	0.00	53.76
2,094. Paint door or window opening - 2 coats (per side)	2.00 EA		0.00	20.22	0.00	40.44
2,095. Paint door slab only - 2 coats (per side)	2.00 EA		0.00	24.16	0.00	48.32
2,096. Clean floor	465.78 SF		0.00	0.25	0.00	116.45
Totals: Storage Ares/Room				=======================================	0.00	4.910.93

Totals: Storage Area/Room

Page: 176 **VICTORYCOSUB** 12/13/2017





N 36 Z An B	ar / Dining Area	/ Dining Area			Height: 10' 9"			
	2,658.68	SF Walls		2,993.96 SF Ceiling				
Dining	5,652.65	SF Walls & C	eiling	2,993.96 SF Floor				
	332.66	SY Flooring		245.33 LF Floor Perime				
	250.58	LF Ceil. Perin	neter					
Window	5' X 3	3'		Opens into Exterior				
Window	5' X 3	3'		Opens into Exterior				
Door	3' X (	5' 8"		Opens into Exterior				
Door	3' X (	5' 8"		Opens into Exterior				
Window	5' X 3	3'		Opens into Exterior Opens into Exterior Opens into HALLWAY				
Window	5' X 3	3'						
Missing Wall - Goes to Floor	5' 3"	X 6' 8"						
Window	5' X 3	3'		Opens into Exterior Opens into Exterior				
Window	3' X :	5'						
Window	3' X 3	3' X 5' 3' X 5'		Opens into Exterior Opens into Exterior				
Window	3' X :							
*Door	3' X	5' 8"		Opens into Exterior Opens into Exterior Opens into Exterior				
Door	3' X	5' 8"						
Window	3' X :	5'						
Window	3' X :	5'		Opens into Exterior				
Window	3' X :	5'		Opens into Exterior				
Window	3' X :	5'		Opens into Exterior				
Door	3' X (	6' 8"		Opens into STORA	GE_AREA			
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL		
2,097. Batt insulation - 4" - R15 - paper faced	2,993.96 SF	ſ	0.00	0.69	0.00	2,065.83		
2,098. 5/8" drywall - hung, taped, ready for texture	2,993.96 SF		0.00	1.37	0.00	4,101.73		
2,099. Ceiling fan - Detach & reset	8.00 EA		0.00	147.29	0.00	1,178.32		
2,100. Clean light fixture - fluorescen	nt 15.00 EA		0.00	7.78	0.00	116.70		

2,097. Batt insulation - 4" - R15 - paper faced	2,993.96 SF	0.00	0.69	0.00	2,065.83
2,098. 5/8" drywall - hung, taped, ready for texture	2,993.96 SF	0.00	1.37	0.00	4,101.73
2,099. Ceiling fan - Detach & reset	8.00 EA	0.00	147.29	0.00	1,178.32
2,100. Clean light fixture - fluorescent	15.00 EA	0.00	7.78	0.00	116.70
2,101. Light bulb - Fluorescent tube - 4' soft white - mat. only	5.00 EA	0.00	4.50	0.00	22.50
2,102. Recessed light fixture - Detach & reset trim only	26.00 EA	0.00	1.46	0.00	37.96
2,103. Exit sign - Detach & reset	1.00 EA	0.00	53.76	0.00	53.76
2,104. Exit sign - internal power	1.00 EA	0.00	215.26	0.00	215.26
2,105. 5/8" - drywall per LF - up to 4'	245.33 LF	0.00	8.73	0.00	2,141.73





## **CONTINUED - Bar / Dining Area**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,106. Batt insulation - 6" - R19 - paper faced	957.13 SF		0.00	0.65	0.00	622.13
2,107. Texture drywall - heavy hand texture	5,652.65 SF		0.00	0.58	0.00	3,278.54
2,108. Paint the walls and ceiling - two coats	5,652.65 SF		0.00	0.63	0.00	3,561.17
2,109. Carpenter - General Framer - per hour	4.00 HR		0.00	46.80	0.00	187.20
Note: Repair of wall framing						
2,110. Outlet or switch cover	18.00 EA		0.00	2.23	0.00	40.14
2,111. Paint French door slab only - 2 coats (per side)	2.00 EA		0.00	46.22	0.00	92.44
2,112. Paint door or window opening - Large - 2 coats (per side)	10.00 EA		0.00	23.79	0.00	237.90
2,113. Clean window unit (per side) 10 - 20 SF	7.00 EA		0.00	8.32	0.00	58.24
2,114. Clean window unit (per side) 41 - 60 SF	5.00 EA		0.00	14.16	0.00	70.80
2,115. Seal & paint wood window (per ide) - Large	5.00 EA		0.00	47.96	0.00	239.80
2,116. Seal & paint wood window (per side)	7.00 EA		0.00	36.04	0.00	252.28
2,117. Casing - oversized - 3 1/4"	314.00 LF		0.00	1.82	0.00	571.48
2,118. Paint casing - oversized - two coats	314.00 LF		0.00	1.01	0.00	317.14
2,119. Hand painted mural	189.00 SF		0.00	67.89	0.00	12,831.21
Note: This is to restore or re-paint the 5 as this is only and estimate.	'-3" x 36' archive pri	nt which suffered	damage. The cost	for restorative servi	ces may need to	be adjusted
2,120. R&R Casing - oversized - 3 1/4" hardwood - molded w/detail	82.00 LF		0.30	2.92	0.00	264.04
Note: Mural frame						
2,121. Stain & finish casing	82.00 LF		0.00	1.02	0.00	83.64
2,122. Finish Carpenter - per hour	5.00 HR		0.00	46.01	0.00	230.05
Note: Additional time to custom build m	ural frame.					
2,123. Reglaze 1/4" plexiglass - single pane	186.00 SF		0.00	6.24	0.00	1,160.64
Note: Mural frame						
2,124. Clean bar / back bar	44.00 EA		0.00	19.34	0.00	850.96
2,125. Clean countertop	88.00 SF		0.00	0.41	0.00	36.08
2,126. Clean bar stool	11.00 EA		0.00	7.12	0.00	78.32
2,127. Mirror - 1/4" plate glass	9.00 SF		0.00	9.18	0.00	82.62
Note: Section of bar top						





## CONTINUED - Bar / Dining Area

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,128. Install Bar stool - floor mounted	11.00 EA		0.00	14.12	0.00	155.32
2,129. Remove Bar stool - floor mounted	11.00 EA		5.88	0.00	0.00	64.68
2,130. R&R Oak flooring - clear grade - no finish	2,993.96 SF		1.38	7.31	0.00	26,017.51
2,131. Vapor barrier - 15# felt	2,993.96 SF		0.00	0.20	0.00	598.79
2,132. Sand, stain, and finish wood floor	2,993.96 SF		0.00	3.07	0.00	9,191.46
2,133. Add for dustless floor sanding	2,993.96 SF		0.00	0.80	0.00	2,395.17
2,134. Baseboard - 4 1/4"	245.33 LF		0.00	2.46	0.00	603.51
2,135. Base shoe	245.33 LF		0.00	0.80	0.00	196.26
2,136. Seal & paint baseboard w/cap &/or shoe, oversized- 2 coats	245.33 LF		0.00	1.26	0.00	309.12
Totals: Bar / Dining Area					0.00	74,612.43
Total: Interior					0.00	95,412.63

#### Exterior

#### Front / North Elevation

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,137. R&R Trim board - 1" x 10" - installed (pine)	60.00 LF	1	0.26	4.17	0.00	265.80
Note: Window casings						
2,138. Seal & paint trim - two coats	60.00 LF		0.00	0.92	0.00	55.20
Totals: Front / North Elevation					0.00	321.00

#### **West Elevation**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,139. Reglaze 1/4" annealed/float glass - 40 sf maximum	2.00 SF		0.00	6.25	0.00	12.50
Totals: West Elevation					0.00	12.50

#### Rear / South Elevation





#### **CONTINUED - Rear / South Elevation**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,140. R&R Attic vent - gable end - wood	1.00 EA		4.90	99.01	0.00	103.91
2,141. Seal & paint wood gable vent	1.00 EA		0.00	27.49	0.00	27.49
2,142. Two ladders with jacks and plank (per day)	DA		0.00	78.50	0.00	0.00
Totals: Rear / South Elevation					0.00	131.40

#### **East Elevation**

QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
69.00 SF		0.00	6.24	0.00	430.56
36.00 LF		0.00	1.10	0.00	39.60
4				0.00	470.16
				0.00	935.06
r				0.00	96,347.69
	69.00 SF	69.00 SF 36.00 LF	69.00 SF 0.00  36.00 LF 0.00	69.00 SF 0.00 6.24  36.00 LF 0.00 1.10	69.00 SF 0.00 6.24 0.00  36.00 LF 0.00 1.10 0.00  0.00  0.00

#### **Building 34 - Victoria Well Service**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL	
Note: No damage noted	Note: No damage noted						
Totals: Building 34 - Victoria Well Service				4	0.00	0.00	

#### **Building 35 - COMAT Building**

#### **Building 35 - COMAT Building**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL

Note: Some of the rooms had pre-existing damage not associated with this occurrence. These include the Kitchen, North Breakroom and West Laboratory.


Total: Building 35 - COMAT Building 0.00

Roof

0.00



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546



#### BUR w/ Aggregate

10,618.00 Surface Area 715.80 Total Perimeter Length

106.18 Number of Squares

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,148. Remove Tear off, haul and dispose of 4 ply built-up roofing	106.18 SQ		43.92	0.00	0.00	4,663.43
2,149. Built-up roof with granulated cap sheet - in place	106.18 SQ		0.00	287.69	0.00	30,546.92
2,150. R&R Fiberboard - 1"	10,618. SF 00		0.26	0.65	0.00	9,662.38
2,151. R&R Gravel stop	648.80 LF		0.20	1.18	0.00	895.34
2,152. R&R Flashing - pipe jack	7.00 EA		4.14	23.34	0.00	192.36
2,153. Gutter / downspout - Detach & reset	85.00 LF		0.00	2.40	0.00	204.00
2,154. R&R Furnace vent - rain cap	3.00 EA		6.30	57.82	0.00	192.36
2,155. Central air - condenser unit - Detach & reset	5.00 EA		0.00	435.14	0.00	2,175.70
2,156. R&R Curb flashing	120.00 LF		1.10	12.22	0.00	1,598.40
2,157. R&R Flash parapet wall only - bitumen	85.58 LF		1.18	7.58	0.00	749.68
2,158. R&R Counterflashing - Apron flashing	85.58 LF		0.34	5.14	0.00	468.98
2,159. Insulation - ISO board, 3"	<del>106.18</del> <del>SQ</del>		0.00	<del>218.42</del>	0.00	23.191.84

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

2,160. Insulation - ISO board, 4" 53.09 SQ 0.00 266.88 0.00 14.168

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

Note: Considers tapered insulation to comply with 1/4" per foot drainage requirements.

2,161. 2" x 6" lumber (1 BF per LF) 1,297.59 LF 0.00 1.73 0.00 2,244.83

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

**Note:** Double perimeter band (3") installed to fasten perimeter coping after installation of insulation.

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546


#### **CONTINUED - BUR w/ Aggregate**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,163. Remove Additional charge for high roof (2 stories or greater)	41.71 SQ		3.11	0.00	0.00	129.72
2,164. Additional charge for high roof (2 stories or greater)	41.71 SQ		0.00	9.91	0.00	413.35
Totals: BUR w/ Aggregate					0.00	51,892.62
Total: Roof					0.00	51,892.62
Total: Building 35 - COMAT Building					0.00	51,892.62

# Building #35 - COMAT Building Interior Interior

#### Interior

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Note: Lessee is responsible for me	oving all contents to allow f	or access and rep	pairs.			
Total: Interior					0.00	0.00



#### Southeast Office

840.39 SF Walls 1,183.12 SF Walls & Ceiling 38.08 SY Flooring 81.96 LF Ceil. Perimeter Height: 10' 9"
342.74 SF Ceiling

342.74 SF Floor 81.96 LF Floor Perimeter

Window
Window
Door
Door
Window
DESCRIPTION

10' 2 1/16" X 4'
6' 9 15/16" X 4'
3' X 6' 8"
3' X 6' 8"
6' 9 15/16" X 4'

Opens into Exterior
Opens into Exterior
Opens into BREAK\_ROOM
Opens into COPY\_ROOM

**Opens into Exterior** 

			-				
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL	
2,165. 5/8" drywall - hung, taped, ready for texture	342.74 SF		0.00	1.37	0.00	469.55	
2,166. Acoustic ceiling (popcorn) texture - heavy	342.74 SF		0.00	0.77	0.00	263.91	
2,167. Seal & paint acoustic ceiling (popcorn) texture	342.74 SF		0.00	0.81	0.00	277.62	
3,168. Batt insulation - 6" - R19 - aper faced	342.74 SF		0.00	0.65	0.00	222.78	




## **CONTINUED - Southeast Office**

ESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
169. Task light - directional	3.00 EA		0.00	103.98	0.00	311.94
170. Fluorescent - two tube - 4' - kture w/lens	8.00 EA		0.00	85.33	0.00	682.64
171. Light diffusing panel (i.e., acked ice)	32.00 SF		0.00	1.43	0.00	45.76
172. Trim board - 1" x 6" - installed ine)	32.00 LF		0.00	2.82	0.00	90.24
173. Stain & finish trim	32.00 LF		0.00	1.02	0.00	32.64
174. 5/8" drywall - hung, taped, eavy texture, ready for paint	840.39 SF		0.00	1.80	0.00	1,512.70
175. Seal/prime then paint the walls rice (3 coats)	840.39 SF		0.00	0.84	0.00	705.93
176. Batt insulation - 4" - R13 - aper faced	840.39 SF		0.00	0.50	0.00	420.20
177. Switch	3.00 EA		0.00	11.94	0.00	35.82
178. Outlet	8.00 EA		0.00	11.88	0.00	95.04
179. Clean window unit (per side) 21 40 SF	3.00 EA		0.00	11.10	0.00	33.30
180. Clean window blind - orizontal or vertical	89.36 SF		0.00	0.71	0.00	63.45
181. Paint door or window opening - arge - 2 coats (per side)	3.00 EA		0.00	23.79	0.00	71.37
182. Clean door (per side)	2.00 EA		0.00	4.00	0.00	8.00
183. Paint door or window opening - coats (per side)	2.00 EA		0.00	20.22	0.00	40.44
184. Cove base molding - rubber or nyl, 4" high	81.96 LF		0.00	1.37	0.00	112.29
185. Glue down carpet - heavy	394.15 SF		0.00	3.12	0.00	1,229.75
5 % waste added for Glue down carpet	- heavy traffic.					
186. Mask or cover per square foot	342.74 SF		0.25	0.00	0.00	85.69
otals: Southeast Office	342.74 SF		0.25		0.00	0.00



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546



**Center Office** 

Height: 10'

419.31 SF Walls 551.31 SF Walls & Ceiling 14.67 SY Flooring 46.00 LF Ceil. Perimeter


132.00 SF Ceiling 132.00 SF Floor 46.00 LF Floor Perimeter

Window Door 10' 2 1/16" X 4' 3' X 6' 8" Opens into Exterior
Opens into BREAK\_ROOM

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,187. Suspended ceiling system - 2' x 4'	132.00 SF		0.00	2.24	0.00	295.68
2,188. Batt insulation - 6" - R19 - paper faced	132.00 SF		0.00	0.65	0.00	85.80
2,189. Fluorescent - acoustic grid fixture - four tube, 2'x 4'	1.00 EA		0.00	171.94	0.00	171.94
2,190. 1/2" drywall - hung, taped, heavy texture, ready for paint	419.31 SF		0.00	1.71	0.00	717.02
2,191. Seal/prime then paint the walls wice (3 coats)	419.31 SF		0.00	0.84	0.00	352.22
2,192. Batt insulation - 4" - R13 - paper faced	419.31 SF		0.00	0.50	0.00	209.66
2,193. Switch	1.00 EA		0.00	11.94	0.00	11.94
2,194. Outlet	3.00 EA		0.00	11.88	0.00	35.64
2,195. Clean window unit (per side) 21 - 40 SF	1.00 EA		0.00	11.10	0.00	11.10
2,196. Clean door (per side)	1.00 EA		0.00	4.00	0.00	4.00
2,197. Paint door or window opening - 2 coats (per side)	1.00 EA		0.00	20.22	0.00	20.22
2,198. Paint door or window opening - Large - 2 coats (per side)	1.00 EA		0.00	23.79	0.00	23.79
2,199. Cove base molding - rubber or vinyl, 4" high	46.00 LF		0.00	1.37	0.00	63.02
2,200. Glue down carpet - heavy traffic	151.80 SF		0.00	3.12	0.00	473.62
15 % waste added for Glue down carpet	- heavy traffic.					
2,201. Clean window blind - horizontal or vertical	40.00 SF		0.00	0.71	0.00	28.40
2,202. Mask or cover per square foot	132.00 SF		0.25	0.00	0.00	33.00
Totals: Center Office					0.00	2,537.05



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546



**Rear Entry** 

227.17 SF Walls

59.61 SF Ceiling

286.78 SF Walls & Ceiling

6.62 SY Flooring

30.90 LF Ceil. Perimeter

59.61 SF Floor

27.90 LF Floor Perimeter

Height: 8'

Door Missing Wall - Goes to Floor 3' X 6' 8" 3' X 6' 8"

**Opens into Exterior** 

Opens into LABORATORY\_1

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,203. 5/8" drywall - hung, taped, ready for texture	59.61 SF		0.00	1.37	0.00	81.67
2,204. Batt insulation - 6" - R19 - paper faced	59.61 SF		0.00	0.65	0.00	38.75
2,205. Acoustic ceiling (popcorn) texture - heavy	59.61 SF		0.00	0.77	0.00	45.90
2,206. Seal & paint acoustic ceiling (popcorn) texture	59.61 SF		0.00	0.81	0.00	48.28
2,207. Trim board - 1" x 6" - installed pine)	13.00 LF		0.00	2.82	0.00	36.66
Note: Light alcove						
2,208. Seal & paint trim - two coats	13.00 LF		0.00	0.92	0.00	11.96
2,209. Light diffusing panel (i.e., cracked ice)	8.00 SF		0.00	1.43	0.00	11.44
2,210. 5/8" drywall - hung, taped, heavy texture, ready for paint	227.17 SF		0.00	1.80	0.00	408.91
2,211. Batt insulation - 4" - R13 - paper faced	227.17 SF		0.00	0.50	0.00	113.59
2,212. Seal/prime then paint the walls twice (3 coats)	227.17 SF		0.00	0.84	0.00	190.82
2,213. Switch	1.00 EA		0.00	11.94	0.00	11.94
2,214. Clean exterior door (per side)	1.00 EA		0.00	7.88	0.00	7.88
2,215. Prime & paint door slab only - exterior (per side)	1.00 EA		0.00	29.41	0.00	29.41
2,216. Paint door or window opening - 2 coats (per side)	2.00 EA		0.00	20.22	0.00	40.44
2,217. Cove base molding - rubber or vinyl, 4" high	27.90 LF		0.00	1.37	0.00	38.22
2,218. Clean floor - tile	59.61 SF		0.00	0.36	0.00	21.46
2,219. Mask or cover per square foot	59.61 SF		0.25	0.00	0.00	14.90

Totals: Rear Entry




0.00

1,152.23



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546



**Copy Room** 

Height: 8'

247.17 SF Walls 306.78 SF Walls & Ceiling 6.62 SY Flooring 30.90 LF Ceil. Perimeter

59.61 SF Ceiling 59.61 SF Floor 30.90 LF Floor Perimeter

Door	3' X 6' 8"	Opens into SOUTHEAST_OF

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,220. Remove Tear off painted acoustic ceiling (popcorn) texture	59.61 SF		0.54	0.00	0.00	32.19
2,221. Acoustic ceiling (popcorn) texture - heavy	59.61 SF		0.00	0.77	0.00	45.90
2,222. Seal & paint acoustic ceiling (popcorn) texture	59.61 SF		0.00	0.81	0.00	48.28
2,223. Heat/AC register - Mechanically attached - Detach & reset	1.00 EA		0.00	10.74	0.00	10.74
2,224. Light diffusing panel (i.e., cracked ice)	8.00 SF		0.00	1.43	0.00	11.44
2,225. 5/8" - drywall per LF - up to 4' tall	30.90 LF		0.00	8.73	0.00	269.76
2,226. Batt insulation - 4" - R13 - paper faced	123.58 SF		0.00	0.50	0.00	61.79
2,227. Texture drywall - heavy hand texture	247.17 SF		0.00	0.58	0.00	143.36
2,228. Seal/prime then paint the walls twice (3 coats)	247.17 SF		0.00	0.84	0.00	207.62
2,229. Outlet or switch cover	1.00 EA		0.00	2.23	0.00	2.23
2,230. Closet rod - Detach & reset	8.00 LF		0.00	1.38	0.00	11.04
2,231. Countertop - flat laid plastic laminate - Detach & reset	8.00 LF		0.00	10.60	0.00	84.80
2,232. Clean countertop	16.00 SF		0.00	0.41	0.00	6.56
2,233. Backsplash - plastic laminate	2.64 SF		0.00	4.45	0.00	11.75
2,234. Clean door (per side)	1.00 EA		0.00	4.00	0.00	4.00
2,235. Paint door or window opening - 2 coats (per side)	1.00 EA		0.00	20.22	0.00	20.22
2,236. Cove base molding - rubber or vinyl, 4" high	30.90 LF		0.00	1.37	0.00	42.33
2,237. Glue down carpet - heavy traffic	68.55 SF		0.00	3.12	0.00	213.88
15 % waste added for Glue down carpet	heavy traffic.					
2,238. Mask or cover per square foot	59.61 SF		0.25	0.00	0.00	14.90
Totals: Copy Room					0.00	1,242.79

VICTORYCOSUB

12/13/2017

Page: 186





	\
- 4 %	
8"	Control Rdom
بار الا	
	HVAC

#### **Control Room**

Height: 8'

299.70 SF Walls 384.22 SF Walls & Ceiling 9.39 SY Flooring 39.06 LF Ceil. Perimeter

84.52 SF Ceiling84.52 SF Floor37.43 LF Floor Perimeter

Missing Wall Door Window

Door

1' 7 5/8" X 8' 3' X 6' 8" 7' X 4' 3' X 6' 8" Opens into BREAK\_ROOM
Opens into BREAK\_ROOM
Opens into LABORATORY\_1
Opens into LABORATORY\_1

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,239. Remove Tear off painted acoustic ceiling (popcorn) texture	84.52 SF		0.54	0.00	0.00	45.64
2,240. Acoustic ceiling (popcorn) texture - heavy	84.52 SF		0.00	0.77	0.00	65.08
2,241. Seal & paint acoustic ceiling (popcorn) texture	84.52 SF		0.00	0.81	0.00	68.46
2,242. Heat/AC register - lechanically attached - Detach & reset	1.00 EA		0.00	10.74	0.00	10.74
2,243. Light diffusing panel (i.e., cracked ice)	8.00 SF		0.00	1.43	0.00	11.44
2,244. 5/8" - drywall per LF - up to 4' tall	37.43 LF		0.00	8.73	0.00	326.76
2,245. Batt insulation - 4" - R13 - paper faced	149.71 SF		0.00	0.50	0.00	74.86
2,246. Texture drywall - heavy hand texture	299.70 SF		0.00	0.58	0.00	173.83
2,247. Seal/prime then paint the walls twice (3 coats)	299.70 SF		0.00	0.84	0.00	251.75
2,248. Outlet or switch cover	1.00 EA		0.00	2.23	0.00	2.23
2,249. Closet rod - Detach & reset	8.00 LF		0.00	1.38	0.00	11.04
2,250. Countertop - flat laid plastic laminate - Detach & reset	16.00 LF		0.00	10.60	0.00	169.60
2,251. Clean countertop	32.00 SF		0.00	0.41	0.00	13.12
2,252. Backsplash - plastic laminate	2.64 SF		0.00	4.45	0.00	11.75
2,253. Clean door (per side)	2.00 EA		0.00	4.00	0.00	8.00
2,254. Paint door or window opening - 2 coats (per side)	2.00 EA		0.00	20.22	0.00	40.44
2,255. Clean window unit (per side) 21 - 40 SF	1.00 EA		0.00	11.10	0.00	11.10
2,256. Clean window blind - horizontal or vertical	32.00 SF		0.00	0.71	0.00	22.72





#### **CONTINUED - Control Room**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,257. Paint door or window opening - Large - 2 coats (per side)	1.00 EA		0.00	23.79	0.00	23.79
2,258. Cove base molding - rubber or vinyl, 4" high	37.43 LF		0.00	1.37	0.00	51.28
2,259. Glue down carpet - heavy traffic	97.20 SF	$\times$	0.00	3.12	0.00	303.26
15 % waste added for Glue down carpet	- heavy traffic.	and the same of				
2,260. Mask or cover per square foot	84.52 SF	AND TO SERVE	0.25	0.00	0.00	21.13
Totals: Control Room		Carl Service			0.00	1,718.02

F11 4 - 11 4 -
8-10'2"-10'2"-
- 1
Enty 112 112 P
€ 11 11 T
Room
Room
C 4
ol Richaboratory 1-
4 4
X 0 2
VACT
<del></del>
Om © -12' 5"
9 4
= B 81-9'4"H
16450 way 99'8" -
16Hanway 29'8" -

#### Laboratory 1

1,150.17 SF Walls 2,060.39 SF Walls & Ceiling 101.14 SY Flooring 127.34 LF Ceil. Perimeter

Height: 9' 10"

910.22 SF Floor

910.22 SF Ceiling

124.34 LF Floor Perimeter


Missing Wall - Goes to Floor	3' X 6' 8"	Opens into REAR_ENTRY
Window	10' 2 1/16" X 4'	Opens into Exterior
Window	10' 2 1/16" X 4'	Opens into Exterior
Door	3' X 6' 8"	Opens into HALLWAY_2
Door	3' X 6' 8"	Opens into HALLWAY_2
Window	7' X 4'	Opens into CONTROL_ROOM
Door	3' X 6' 8"	Opens into CONTROL_ROOM

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,261. 5/8" - drywall per LF - up to 4' tall	62.17 LF		0.00	8.73	0.00	542.74
2,262. Batt insulation - 4" - R13 - paper faced	248.69 SF		0.00	0.50	0.00	124.35
2,263. Texture drywall - heavy hand texture	1,150.17 SF		0.00	0.58	0.00	667.10
2,264. Seal/prime then paint the walls twice (3 coats)	1,150.17 SF		0.00	0.84	0.00	966.14
2,265. Heat/AC register - Mechanically attached - Detach & reset	3.00 EA		0.00	10.74	0.00	32.22
2,266. Outlet or switch cover	8.00 EA		0.00	2.23	0.00	17.84
2,267. Clean window unit (per side) 21 40 SF	3.00 EA		0.00	11.10	0.00	33.30



#### **CONTINUED - Laboratory 1**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,268. Clean window blind - horizontal or vertical	72.00 SF		0.00	0.71	0.00	51.12
2,269. Clean door (per side)	3.00 EA		0.00	4.00	0.00	12.00
2,270. Window trim set (casing & stop)	104.00 LF		0.00	2.50	0.00	260.00
2,271. Paint door or window opening - 2 coats (per side)	5.00 EA		0.00	20.22	0.00	101.10
2,272. Cove base molding - rubber or vinyl, 4" high	124.34 LF		0.00	1.37	0.00	170.35
2,273. Glue down carpet - heavy traffic	1,046.75 SF		0.00	3.12	0.00	3,265.86
15 % waste added for Glue down carpet	- heavy traffic.					
2,274. Mask or cover per square foot	910.22 SF		0.25	0.00	0.00	227.56
Totals: Laboratory 1		ALCOHOLD WASHINGTON	TO SHARE WATER		0.00	6,471.68



**HVAC** 

196.15 SF Walls

219.03 SF Walls & Ceiling

2.54 SY Flooring

19.61 LF Ceil. Perimeter

Height: 10'

22.89 SF Ceiling 22.89 SF Floor

19.61 LF Floor Perimeter

3' X 6' 8" Door

Opens into BREAK\_ROOM

DESCRIPTION	QTY RESET	REMOVE	REPLACE	TAX	TOTAL
2,275. Batt insulation - 4" - R13 - unfaced batt	78.46 SF	0.00	0.46	0.00	36.09
2,276. Clean door (per side)	1.00 EA	0.00	4.00	0.00	4.00
2,277. Paint door or window opening - 2 coats (per side)	1.00 EA	0.00	20.22	0.00	20.22
2,278. Outlet	3.00 EA	0.00	11.88	0.00	35.64
2,279. Carpet - metal transition strip	3.00 LF	0.00	1.88	0.00	5.64
2,280. 1/2" - drywall per LF - up to 4' tall	19.61 LF	0.00	8.30	0.00	162.76
Totals: HVAC				0.00	264.35



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

	404.77 SF Wal	ls	168.70	SF Ceiling	
office to the state of the stat	573.48 SF Wal	ls & Ceiling		SF Floor	
Break Room " T	18.74 SY Flo	oring	50.32	LF Floor Perim	eter
1 1 2 4 2 4 1 2 4 1 1 1 1 1 1 1 1 1 1 1	61.29 LF Ceil	. Perimeter			
Door 2'8'	3' X 6' 8"	0	pens into CENTEI	OFFIC	
Door	3' X 6' 8"	/	pens into CENTEI		
Missing Wall	1' 7 5/8" X 7		pens into SOUTH	_	
Door	3' X 6' 8"		pens into CONTR	_	
Door	3' X 6' 8"		pens into CONTR	OL_ROOM	
Missing Wall - Goes to Floor	9' 4" X 6' 8"		pens into HALLW	AV 2	
DESCRIPTION		SET REMOVE	REPLACE	TAX	TOTAL
2,281. Suspended ceiling tile - 2' x 4'	168.70 SF	0.00	1.22	0.00	205.8
2,282. Batt insulation - 6" - R19 - paper faced	168.70 SF	0.00	0.65	0.00	109.6
2,283. Clean light fixture - fluorescent	2.00 JEA	0.00	7.78	0.00	15.5
,284. 1/2" - drywall per LF - up to 4' all	50.3/2 LF	0.00	8.30	0.00	417.6
2,285. Texture drywall - heavy hand exture	404.77 SF	0.00	0.58	0.00	234.7
2,286. Seal/prime then paint the walls/wice (3 coats) - 2 colors	404.77 SF	0.00	1.03	0.00	416.9
2,287. Cold air return cover - Detach & reset	1.00 EA	0.00	14.65	0.00	14.6
2,288. Outlet or switch cover	4.00 EA	0.00	2.23	0.00	8.9
2,289. Clean door (per side)	4.00 EA	0.00	4.00	0.00	16.0
2,290. Paint door or window opening - 2 coats (per side)	5.00 EA	0.00	20.22	0.00	101.1
2,291. Clean countertop	21.00 SF	0.00	0.41	0.00	8.6
2,292. Cove base molding - rubber or vinyl, 4" high	50.32 LF	0.00	1.37	0.00	68.9
2,293. Glue down carpet - heavy traffic	194.01 SF	0.00	3.12	0.00	605.3
15 % waste added for Glue down carpet	- heavy traffic.				
		0.25	0.00	0.00	42.1



-,99	367.3	1 SF Walls		128.33	SF Ceiling	
Office 1	495.6	5 SF Walls & Co	eiling	128.33	SF Floor	
ال الم	14.2	6 SY Flooring		45.33	LF Floor Perim	eter
6.6.10.8.	45.3	3 LF Ceil. Perin	neter			
Window	10'	2 1/16" X 4'	q	pens into Exterior		
Door	3' X	6' 8"	ø	pens into RECEPT	<b>FIONIST</b>	
DESCRIPTION	уто	RESET	REMOVE	REPLACE	TAX	TOTAL
2,295. Suspended ceiling tile - 2' x 4'	128.33 SF		0.00	1.22	0.00	156.56
2,296. Batt insulation - 6" - R19 - paper faced	128.33 SF	\	0.00	0.65	0.00	83.41
2,297. Heat/AC register - Mechanically attached - Detach & reset	1.00 EA		0.00	10.74	0.00	10.74
2,298. 1/2" - drywall per LF - up to 4' tall	45.33 LF	\ /	0.00	8.30	0.00	376.24
2,299. Texture drywall - heavy hand exture	367.31 SF	$\bigvee$	0.00	0.58	0.00	213.04
2,300. Seal/prime then paint the walls twice (3 coats)	367.31 SF	$\wedge$	0.00	0.84	0.00	308.54
2,301. Outlet or switch cover	4.00 EA	/ \	0.00	2.23	0.00	8.9
2,302. Clean window unit (per side) 10 - 20 SF	1.00 EA		0.00	8.32	0.00	8.32
2,303. Clean window blind - horizontal or vertical	28.00 SF	\	0.00	0.71	0.00	19.88
2,304. Clean door (per side)	1.00 EA	\	0.00	4.00	0.00	4.00
2,305. Paint door or window opening - 2 coats (per side)	2.00 EA	\	0.00	20.22	0.00	40.4
2,306. Cove base molding - rubber or vinyl, 4" high	45.33 LF		0.00	1.37	0.00	62.1
2,307. Glue down carpet - heavy traffic	147.58 SF		0.00	3.12	0.00	460.4
15 % waste added for Glue down carpet -	heavy traffic.					
			0.25	0.00	0.00	32.08





Hallway	2			Не	<u>ight:</u> 7' 10"
2'865'3" 3 4" 9'4" 3'8"	705.79 SF Walls		242.96	SF Ceiling	
3'4 2'6" 14'5" 1	948.75 SF Walls &	Ceiling	242.96	SF Floor	
Receptionist Sorage Training 1	27.00 SY Flooring		86.82	LF Floor Perim	eter
9.	109.32 LF Ceil. Peri	imeter			
Missing Wall - Goes to Floor	9' 4" X 6' 8"		Opens into BREAK	_ROOM	
Door	3' X 6' 8"	/	Opens into LABOR	ATORY_1	
Door	3' X 6' 8"		Opens into LABOR		
Missing Wall - Goes to Floor	3' 8" X 6' 8"		Opens into Exterior		
Missing Wall - Goes to Floor	3' 6" X 6' 8"	/	Opens into CENTEI	R_HALLW	
Door	3' X 6' 8"		Opens into TRAINI	NG_1	
Missing Wall - Goes to Floor	6' X 6' 8"		Opens into RECEPT	TIONIST	
DESCRIPTION	QTY RESET	REMOVE	REPLACE	TAX	TOTAL
2,309. Suspended ceiling tile - 2' x 4'	42.96 SF	0.00	1.22	0.00	296.41
2,310. Batt insulation - 6" - R19 - 2 paper faced	42.96 SF	0.00	0.65	0.00	157.92
2,311. 5/8" - drywall per LF - up to 4' tall	86.82 LF	0.00	8.73	0.00	757.94
2,312. Texture drywall - heavy hand texture	05.79 SF	0.00	0.58	0.00	409.36
2,313. Seal/prime then paint the walls twice (3 coats)	05.79 SF	0.00	0.84	0.00	592.86
2,314. Outlet or switch cover	7.00 EA	0.00	2.23	0.00	15.61
2,315. Paint door or window opening - 2 coats (per side)	1.00 EA	0.00	20.22	0.00	20.22
2,316. Paint door or window opening - Large - 2 coats (per side)	3.00 EA	0.00	23.79	0.00	71.3
2,317. Cove base molding - rubber or vinyl, 4" high	86.82 LF	0.00	1.37	0.00	118.94
2,318. Glue down carpet - heavy traffic	19.41 SF	0.00	3.12	0.00	871.76
15 % waste added for Glue down carper- hea	vy traffic.				
2,319. Mask or cover per square foot 2	42.96 SF	0.25	0.00	0.00	60.74
2,320. Clean door (per side)	3.00 EA	0.00	4.00	0.00	12.00
Totals: Hallway 2				0.00	3,385.13

12/13/2017 Page: 192







Foyer	r/Entry					Height: 9
	281.91	SF Walls		90.45	SF Ceiling	
The country of	372.36	SF Walls & Co	eiling	90.45	SF Floor	
	10.05	SY Flooring		31.32 1	LF Floor Perim	eter
67	40.66	LF Ceil. Perim	eter			
Iñ Window - Goes to Floor	3' X	8'	O	pens into Exterior		
Door	3' X	6' 8"	O	pens into Exterior		
Door	3' X	6' 8"	O	pens into Exterior		
Window - Goes to Floor	3' X	8'	O	pens into Exterior		
Missing Wall - Goes to Floor	9' 4"	X 9'	O	pens into RECEPT	TIONIST	
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,321. 1/2" - drywall per LF - up to 4' tall	62.65 LF		0,00	8.30	0.00	520.0
Note: 2 layers	\	\				
2,322. Batt insulation - 4" - R13 - paper faced	52.00 SF		0.00	0.50	0.00	26.0
Note: Exterior wall only						
2,323. Texture drywall - heavy hand texture	281.91 SF	\ /	0.00	0.58	0.00	163.5
2,324. Seal/prime then paint the walls twice (3 coats)	281.91 SF	X	0.00	0.84	0.00	236.8
2,325. Clean window unit (per side) 10 - 20 SF	2.00 EA		0.00	8.32	0.00	16.6
2,326. Clean window blind - horizontal or vertical	34.00 SF	<b>/</b>	0.00	0.71	0.00	24.1
2,327. Clean door - French (per side)	2.00 EA		0.00	12.30	0.00	24.6
2,328. Cove base molding - rubber or vinyl, 4" high	31.32 LF		0.00	1.37	0.00	42.9
2,329. Clean floor - tile	90.45 SF		0.00	0.36	0.00	32.5
2,330. Mask or cover per square foot	90.45 SF		0.25	0.00	0.00	22.6
Totals: Foyer/Entry					0.00	1,109.7



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

11-3'-12' 10" - 6'-12' 8" 4 Rece	ptionist					Height: 9
8 1 2 6	339.2	6 SF Walls		185.39	SF Ceiling	
Receptionist 5	524.6	5 SF Walls & C	eiling	185.39	SF Floor	
Entry 5		0 SY Flooring		34.84	LF Floor Perim	eter
5 - 5	55.1	8 LF Ceil. Perin	neter			
Buhroom Hall  Missing Wall - Goes to Floor	9'4	" X 9'	O	pens into FOYER	FNTDV	
Door		6' 8"		ens into POTER  oens into OFFICE		
Missing Wall - Goes to Floor	6' X		_	ens into HALLW		
Missing Wall - Goes to Floor		68"		oens into BATHR	_	
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,331. 1/2" - drywall per LF - up to 4' tall	69.69 LF		0.00	8.30	0.00	578.43
2,332. Texture drywall - heavy hand texture	339.26 SF		0.00	0.58	0.00	196.77
2,333. Seal/prime then paint the walls twice (3 coats)	339.26 SF		0.00	0.84	0.00	284.98
2,334. Heat/AC register - Mechanically attached - Detach & reset	2.00 EA	$\rangle$	0.00	10.74	0.00	21.48
2,335. Clean recessed light fixture	4.00 EA		0.00	5.86	0.00	23.44
2,336. Clean light fixture	3.00 EA		0.00	5.86	0.00	17.58
2,337. Outlet or switch cover	4.00 EA		0.00	2.23	0.00	8.92
2,338. Clean door (per side)	1.00 EA		0.00	4.00	0.00	4.00
2,339. Clean door / window opening (per side)	1.00 EA		0.00	7.18	0.00	7.18
2,340. Paint door or window opening - 2 coats (per side)	3.00 EA		0.00	20.22	0.00	60.66
2,341. Cove base molding - rubber or vinyl, 4" high	34.84 LF		0.00	1.37	0.00	47.73
2,342. Glue down carpet - heavy traffic	213.20 SF		0.00	3.12	0.00	665.18
15 % waste added for Glue down carpet -	heavy traffic.					
2,343. Mask or cover per square foot	185.39 SF		0.25	0.00	0.00	46.35
Totals: Receptionist	-				0.00	1,962.70



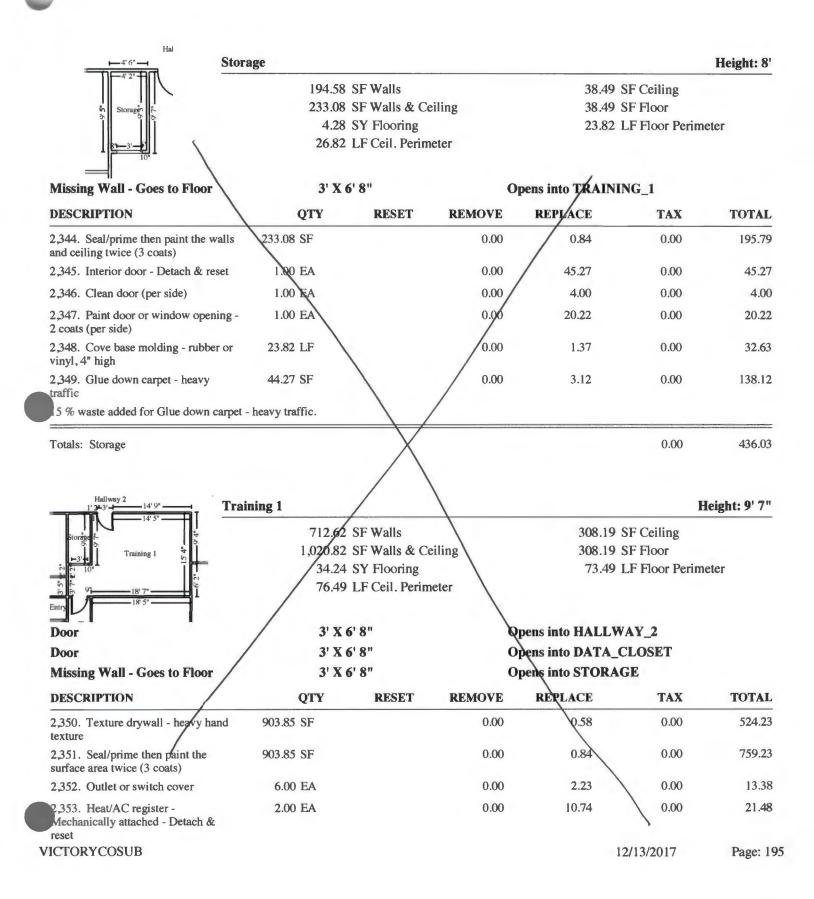



VICTORYCOSUB

8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### **CONTINUED - Training 1**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,354. Cold air return cover - Petach & reset	1.00 EA		0.00	14.65	0.00	14.65
2,355. Remove Task light - directional	2.00 EA		4.90	0.00	0.00	9.80
2,356. Clean countertop	36.00 SF		0.00	0.41	0.00	14.76
2,357. Clean door (per side)	1.00 EA		0.00	4.00	0.00	4.00
2,358. Paint door or window opening - 2 coats (per side)	100 EA		0.00	20.22	0.00	20.22
2,359. Cove base molding - rubber or vinyl, 4" high	73.49 DF		0.00	1.37	0.00	100.68
2,360. Glue down carpet - heavy traffic	354.42 SF		0.00	3.12	0.00	1,105.79
15 % waste added for Glue down carpet - I	neavy traffic.		/			
2,361. Mask or cover per square foot	308.19 SF		0.28	0.00	0.00	77.05
Totals: Training 1					0.00	2,665.27

Height: 8' **Bathroom Hall** 277.33 SF Walks 54.60 SF Ceiling 331.93 SF Walls & Ceiling 54.60 SF Floor 6.07 SY Flooring 33.83 LF Floor Perimeter 38.83 LF Ceil. Perimeter 5' X 6' 8" Opens into RECEPTIONIST Missing Wall - Goes to Floor 3' X 6' 8" Qpens into MENS\_ENTRY Door 3' X 6' 8" Opens into UTILITY\_CLOS Door 3' X 6' 8" Opens into POWDER\_ROOM Door REMOVE REPLACE TAX TOTAL DESCRIPTION **QTY** RESET 0.00 2,362. 1/2" - drywall per LF - up to 4' 67.67 LF 0.00 8.30 561.66 tall 2,363. Texture drywall - heavy hand 277.33 SF 0.00 0.58 0.00 160.85 texture 0.00 0.84 0.00 232.96 2,364. Seal/prime then paint the walls 277.33 SF twice (3 coats) 0.00 2.23 0.00 2.23 2,365. Outlet or switch cover 1.00 EA 0.00 4.00 0.00 12.00 2,366. Clean door (per side) 3.00 EA 21.54 2,367. Clean door / window opening 0.00 7.18 0.00 3.00 EA (per side) 60.66 0.00 20.22 0.00 ,368. Paint door or window opening -3.00 EA 2 coats (per side)

12/13/2017

Page: 196



## **CONTINUED - Bathroom Hall**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,369. Cove base molding - rubber or rinyl, 4" high	33.83 LF		0.00	1.37	0.00	46.3
2,370. Glue down carpet - heavy raffic	62.79 SF		0.00	3.12	0.00	195.9
5 % waste added for Glue down carpet -	heavy traffic.					
2,371. Mask or cover per square foot	54.60 SF		0.25	0.00	0.00	13.6
Totals: Bathroom Hall					0.00	1,307.8
hroom Hall Men	s Entry				Не	eight: 8' 10
5-3'-3'3"	165.39	SF Walls		/ 26.00 S	F Ceiling	
/ Closet Mon's Entry + 5		SF Walls & Ce	eiling	/ 26.00 S		
3'3' - Data Clc		SY Flooring LF Ceil. Perim	eter	18.00 I	F Floor Perim	eter
Aissing Wall - Goes to Floor		6' 8"	/	pens into ROOM1		
Door		6 8"		pens into BATHRO		
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTA
,372. Light diffusing panel (i.e., racked ice)	4.00 SF		0.00	1.43	0.00	5.7
,373. 1/2" - drywall per LF - up to 4'	18.00 LF	X	0.00	8.30	0.00	149.4
,374. Texture drywall - heavy hand exture	165.39 SF	/ `	0.00	0.58	0.00	95.9
2,375. Seal/prime then paint the walls wice (3 coats)	165.39 SF		0.00	0.84	0.00	138.9
376. Outlet or switch cover	1.00 EA		0.00	2.23	0.00	2.2
2,377. Clean door (per side)	1.00 EA		0.00	4.00	0.00	4.0
2,378. Clean door / window opening per side)	2.00 EA		0.00	718	0.00	14.3
,379. Paint door or window opening - coats (per side)	2.00 EA		0.00	20.22	0.00	40.4
,380. Cove base molding - rubber or inyl, 4" high	18.00/LF		0.00	1.37	0.00	24.0
,381. Glue down carpet - heavy raffic	29.90 SF		0.00	3.12	0.00	93.
5 % waste added for Glue down carpet	heavy traffic.					
	3.00 LF		0.00	1.88	0.00	5.0
2,382. Carpet - metal transition strip						
382. Carpet - metal transition strip 383. Mask or cover per square foot	26.00 SF		0.25	0.00	0.00	6.5




## **CONTINUED - Mens Entry**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Totals: Mens Butry		-	***		0.00	581.10
Wility Close Mees Entry  4' 1" 3' - 3' - Mens				/	Н	eight: 8' 10
2 4 3 4 3 2 4 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	366.60	SF Walls		119.86	SF Ceiling	
Mens to to	486.45	SF Walls & C	eiling	/	SF Floor	
5 6	13.32	SY Flooring		40.79	LF Floor Perim	eter
6'9" 3'-3'-3'-3'-3'-3'-3'-3'-3'-3'-3'-3'-3'-3	43.79	LF Ceil. Perin	neter			
Window	3' X :	31	/ 0	pens into Exterior		
Missing Wall - Goes to Floor	3' X			pens into MENS_I		
DESCRIPTION	OX	RESET	REMOVE	REPLACE	TAX	TOTA
2,384. Clean part of the walls	57.64 SF		0.00	0.20	0.00	31.5
Note: From 5' up to ceiling	`	1				
2,385. Clean ceramic tile 2	08.96 SF		0.00	0.30	0.00	62.6
Note: From 5' down to floor	/					
2,386. Clean mirror	24.00 SF		0.00	0.39	0.00	9.3
2,387. Clean sink and faucet	4.00 FA		0.00	9.56	0.00	38.2
2,388. Clean toilet partition - per stall	2.00 EA	`	0.00	14.67	0.00	29.3
2,389. Clean toilet	2.00 EA		0.00	12.05	0.00	24.1
2,390. Clean urinal	3.00 EA		0.00	11.65	0.00	34.9
2,391. Clean window unit (per side) 10	1.00 EA		960	8.32	0.00	8.3
2,392. Clean window blind - horizontal or vertical	12.00 SF		0.00	0.71	0.00	8.5
2,393. Paint door or window opening - 2 coats (per side)	1.00 EA		0.00	20.22	0.00	20.2
2,394. Clean floor - tile	19.86 SF		0.00	0.36	0.00	43.1
Totals: Mens	-		-		0.00	310.4





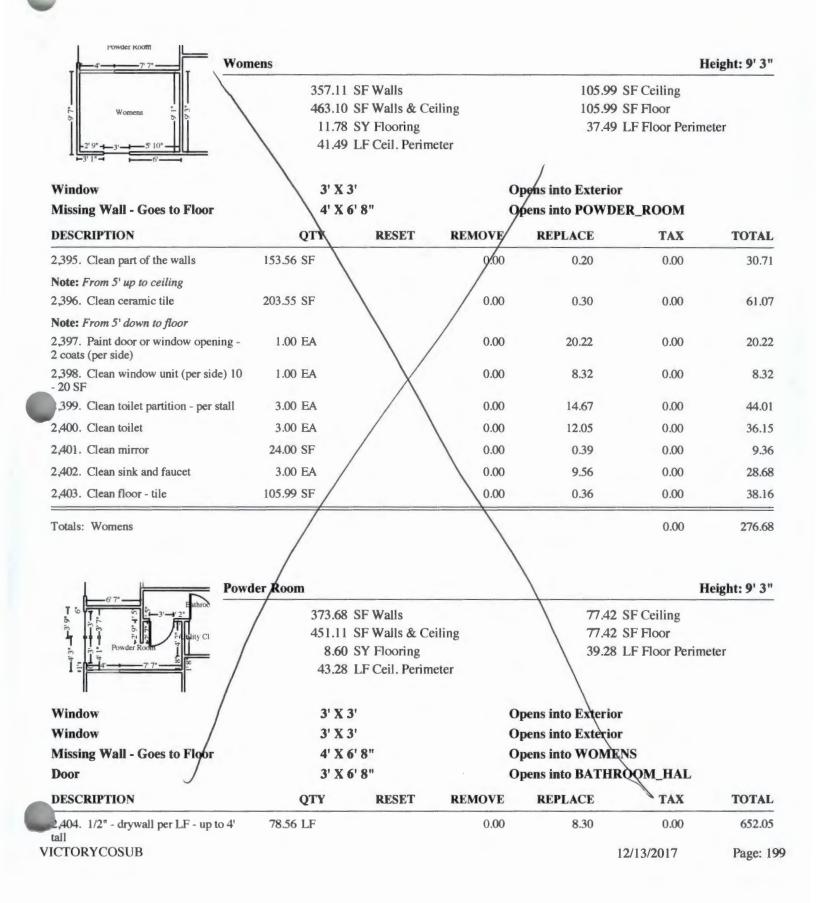



#### **CONTINUED - Powder Room**

DESCRIPTION	\ QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,405. Texture drywall - heavy hand texture	373.68 SF		0.00	0.58	0.00	216.73
2,406. Seal/prime then paint the walls twice (3 coats)	373.68 SF		0.00	0.84	0.00	313.89
2,407. Outlet or switch cover	1.00 EA		0.00	2.23	0.00	2.23
2,408. Clean door (per side)	1.00 EA		0.00	4.00	0.00	4.00
2,409. Clean door / window opening (per side)	2.00 EA		0.00	7/8	0.00	14.36
2,410. Paint door or window opening - 2 coats (per side)	2.00 EA		0.00	20.22	0.00	40.44
2,411. Clean window unit (per side) 10 - 20 SF	1.00 EA		0.00	8.32	0.00	8.32
2,412. Cove base molding - rubber or vinyl, 4" high	39.28 LF		960	1.37	0.00	53.81
2,413. Glue down carpet - heavy traffic	89.04 SF		0.00	3.12	0.00	277.80
15 % waste added for Glue down carpet -	heavy traffic.	/				
2,414. Carpet - metal transition strip	3.00 LF		0.00	1.88	0.00	5.64
,415. Mask or cover per square foot	77.42 SF		0.25	0.00	0.00	19.36
Totals: Powder Room					0.00	1,608.63
10.23	ning 2			\		1,608.63
10.23	596.37 883.77 31.93	SF Walls SF Walls & Co SY Flooring LF Ceil. Perim		287.40		Heig <u>ht:</u> 8' 9"_
Training 2  4' 10"  13' 11"  14' 10"  14' 1"	596.37 883.77 31.93	SF Walls & Co SY Flooring		287.40	) SF Ceiling ) SF Floor	Heig <u>ht:</u> 8' 9"_
Training 2 5 5 5 5 5 5 5 5 5 5 5 5 5 5 5 5 5 5	596.37 883.77 31.93 68.16	SF Walls & Co SY Flooring LF Ceil. Perim	neter	287.44	O SF Ceiling O SF Floor C LF Floor Perin	Height: 8' 9"
Training 2	596.37 883.77 31.93 68.16	SF Walls & Co SY Flooring LF Ceil. Perim	REMOVE	287.44 68.10 REPLACE	O SF Ceiling O SF Floor C LF Floor Perin	Height: 8' 9" neter TOTAL
Training 2  Traini	596.37 883.77 31.93 68.16	SF Walls & Co SY Flooring LF Ceil. Perim	REMOVE	287.44 68.10 REPLACE	O SF Ceiling O SF Floor C LF Floor Perin	Height: 8' 9" neter TOTAL
Training 2  Traini	596.37 883.77 31.93 68.16 QTY	SF Walls & Co SY Flooring LF Ceil. Perim	REMOVE 0.00	287,44 68.16 REPLACE	TAX  0.00  0.00  0.00	Height: 8' 9" meter  TOTAL 19.52
Training 2  Traini	596.37 883.77 31.93 68.16 QTY 16.00 SF 596.37 SF	SF Walls & Co SY Flooring LF Ceil. Perim	<b>REMOVE</b> 0.00 0.00	287.44 68.16 REPLACE 1.22	O SF Ceiling O SF Floor S LF Floor Perin  TAX  0.00	Height: 8' 9"  meter  TOTAL  19.52  500.95
Training 2  Traini	596.37 883.77 31.93 68.16 QTY 16.00 SF 596.37 SF 32.00 SF	SF Walls & Co SY Flooring LF Ceil. Perim	REMOVE  0.00  0.00  0.00	287.44 68.16 REPLACE 1.22 0.84	TAX  0.00  0.00  0.00	Height: 8' 9" meter  TOTAL 19.52 500.95 45.76
Training 2  Traini	596.37 883.77 31.93 68.16 QTY 16.00 SF 596.37 SF 32.00 SF 1.00 EA	SF Walls & Co SY Flooring LF Ceil. Perim	0.00 0.00 0.00 0.00	287.44 68.16 REPLACE 1.22 0.84 1.43 4.00	7 SF Ceiling 0 SF Floor 6 LF Floor Perin  TAX  0.00  0.00  0.00  0.00	Height: 8' 9"  meter  TOTAL  19.52  500.95  45.76  4.00
DESCRIPTION  2,416. Suspended ceiling tile - 2' x 4'  Note: (2) tiles  2,417. Seal/prime then paint the walls twice (3 coats)  2,418. Light diffusing panel (i.e., cracked ice)  2,419. Clean door (per side)  2,420. Paint door or window opening - 2 coats (per side)	596.37 883.77 31.93 68.16 QTY 16.00 SF 596.37 SF 32.00 SF 1.00 EA 1.00 EA	SF Walls & Co SY Flooring LF Ceil. Perim	REMOVE  0.00  0.00  0.00  0.00  0.00	287.44 68.16 REPLACE 1.22 0.84 1.43 4.00 20.22	7AX 0.00 0.00 0.00 0.00 0.00	Height: 8' 9" meter  TOTAL  19.52  500.95  45.76  4.00  20.22





#### **CONTINUED - Training 2**

	CC	ONTINUED - 1	raining 2			
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,422. Cove base molding - runber or vinyl, 4" high	68.16 LF		0.00	1.37	0.00	93.38
2,423. Glue down carpet - heavy traffic	330.51 SF		0.00	3.12	0.00	1,031.19
15 % waste added for Glue down carpet	heavy traffic.					
2,424. Mask or cover per square foot	287.40 SF		0.25	0.00	0.00	71.85
Totals: Training 2					0.00	1,802.45
3'6' 10' Cen	ter Hallway				1	Height: 9' 3'
16-16-1	756.85	SF Walls		319.35 \$	F Ceiling	
Conter Hall Can		SF Walls & Co	eiling	319.35 \$		
11, 2, 4		SY Flooring Li Ceil. Perint	eter	80.84 1	F Floor Perin	neter
Missing Wall - Goes to Floor	3' 6"	X 6' 8'	0	pens into HALLW	AY_2	
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,425. Seal/prime then paint the surface area twice (3 coats)	1,144.20 SF		0.00	0.84	0.00	961.13
2,426. Paint door or window opening - Large - 2 coats (per side)	5.00 EA		0.00	23.79	0.00	118.9
2,427. Cove base molding - rubber or vinyl, 4" high	80.84 LF		0.00	1.37	0.00	110.7
2,428. Glue down carpet - heavy traffic	367/26 SF		8.00	3.12	0.00	1,145.8
15 % waste added for Glue down carpet	- beavy traffic.					
2,429. Carpet - metal transition strip	20.00 LF		0.00	1.88	0.00	37.6
Totals: Center Hallway					0.00	2,374.2
Nor	th Storage					
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,430. Suspended ceiling tile - 2' x 2'	80.00 SF		0.00	1.23	0.00	98.4
Note: (20) Tiles						





Electr	rical					
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,431. Electrician - per hour	24.00 HR		0.00	84.00	0.00	2,016.0
Totals: Electrical	X				0.00	2,016.00
Total: Interior					0.00	44,182.64
Total: Building #35 - COMAT Building I	nterior				0.00	44,182.6
Roof		36 - Animal S	helter / Control	/		
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,452. R&R Pre-Engineered Bldg Skylight panels Note: Opaque panel over the Cat Room	1.00 EA	\	7.35	280.00	0.00	287.3
rotals: Roof		1	1		0.00	287.35
Exter						
Exter DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Exter DESCRIPTION 2,453. R&R Storage shed - Vinyl -		RESET	REMOVE 88.22	REPLACE 730.08		TOTAL
Exter DESCRIPTION  2,453. R&R Storage shed - Vinyl - Gable type - 8' x 8  2,454. R&R Joist - 2x6 floor or ceiling	QTY	RESET		-	TAX	TOTAI 818.30
Exter  DESCRIPTION  2,453. R&R Storage shed - Vinyl - Gable type - 8' x 8  2,454. R&R Joist - 2x6 floor or ceiling system - treated  2,455. R&R Sheathing - plywood -	QTY 1.00 EA	RESET	88.22	730.08	TAX 0.00	TOTAI 818.30 134.6
Exter  DESCRIPTION  2,453. R&R Storage shed - Vinyl - Gable type - 8' x 8  2,454. R&R Joist - 2x6 floor or ceiling system - treated  2,455. R&R Sheathing - plywood - 3/4" - treated  2,456. Additional charge for screwing	QTY 1.00 EA 72.00 BF	RESET	88.22	730.08 1.49	<b>TAX</b> 0.00 0.00	TOTAI 818.3 134.6 133.1
Exter  DESCRIPTION  2,453. R&R Storage shed - Vinyl - Gable type - 8' x 8  2,454. R&R Joist - 2x6 floor or ceiling system - treated  2,455. R&R Sheathing - plywood - 3/4" - treated  2,456. Additional charge for screwing down underlayment/subfloor	QTY 1.00 EA 72.00 BF 64.00 SF	RESET	88.22 0.38 0.40	730.08 1.49 1.68	TAX 0.00 0.00 0.00	TOTAL 818.3 134.6 133.1 30.0
Exter  DESCRIPTION  2,453. R&R Storage shed - Vinyl - Gable type - 8' x 8  2,454. R&R Joist - 2x6 floor or ceiling system - treated  2,455. R&R Sheathing - plywood - 3/4" - treated  2,456. Additional charge for screwing down underlayment/subfloor  Totals: Exterior	QTY 1.00 EA 72.00 BF 64.00 SF	RESET	88.22 0.38 0.40	730.08 1.49 1.68	0.00 0.00 0.00 0.00	TOTAI 818.30 134.64 133.12 30.08
Exter  DESCRIPTION  2,453. R&R Storage shed - Vinyl - Gable type - 8' x 8  2,454. R&R Joist - 2x6 floor or ceiling system - treated  2,455. R&R Sheathing - plywood - 3/4" - treated  2,456. Additional charge for screwing down underlayment/subfloor  Totals: Exterior	QTY 1.00 EA 72.00 BF 64.00 SF	RESET	88.22 0.38 0.40	730.08 1.49 1.68	0.00 0.00 0.00 0.00	287.33  TOTAI  818.30  134.64  133.12  30.00  1,116.14



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

			ront Office			
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,458. R&R Batt insulation - 6" - R19 - paper faced	88.00 SF		0.17	0.65	0.00	72.16
Totals: Front Office					0.00	189.20
Cat	Shelter	X			-0.	1116
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,459. R&R Suspended ceiling tile - 2' x 4'	24.00 8F		0.11	1.22	0.00	31.92
Note: (3) tiles	ALOO SE		0.17	0.65	0.00	10.66
2,460. R&R Batt insulation - 6" - R19 - paper faced	24.00 SF		0.17	0.65	0.00	19.68
Totals: Cat Shelter					0.00	51.60
Total: Building 36 - Animal Shelter / Cor	ntrol		7		0.00	1,644.25
	ling 37 - Highway	y Patrol Weigh RESET	Station REMOVE	REPLACE	0.00 TAX	
Buile / Sca	ling 37 - Highway le	1040		REPLACE		1,644.29
Build / Sca	ding 37 - Highway le QTY	1040		REPLACE		
DESCRIPTION Note: No damage identified.	ding 37 - Highway le QTY eigh Station / Scale	1040	REMOVE	REPLACE	TAX	TOTAL
Build / Scan DESCRIPTION Note: No damage identified.	ding 37 - Highway le QTY eigh Station / Scale	RESET	REMOVE	REPLACE	TAX	TOTAL
DESCRIPTION  Note: No damage identified.  Totals: Building 37 - Highway Patrol Wo	ding 37 - Highway le QTY eigh Station / Scale	RESET	REMOVE	REPLACE	TAX	<b>TOTAL</b>
DESCRIPTION  Note: No damage identified.  Totals: Building 37 - Highway Patrol Wood Roof  Roof	ding 37 - Highway le  QTY  eigh Station / Scale	RESET Building 38 - Ste	REMOVE		<b>TAX</b> 0.00	0.00 TOTAL
DESCRIPTION  Note: No damage identified.  Totals: Building 37 - Highway Patrol We	ding 37 - Highway le  QTY  eigh Station / Scale  B  QTY  2,882.00 8F	RESET Building 38 - Ste	REMOVE	REPLACE	0.00 TAX	TOTAL

VICTORYCOSUB 12/13/2017 Page: 203

**South Elevation** 

Exterior



**VICTORYCOSUB** 

8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### **CONTINUED - South Elevation**

2,468. Gutter - aluminum - up to 5" 70.00 LF 0.00 3.62 0.00  Note: Upper section of gutter only 2,469. Downspout - aluminum - up to 52.00 LR 0.00 3.62 0.00  "2,470. Two ladders with jacks and plank (per day) 2,471. Reglaze window, 1 - 9 sf 2.00 EA 0.00 54.58 0.00  Totals: Front / East Elevation 0.00  Ground Level Interior  South Room  LxWxH 29' 3 15/16" x 19'  878.91 SF Walls 1,450.80 SF Walls & Ceiling 63.54 SY Flooring 263.95 SF Long Wall 97.66 LF Ceil. Perimeter  175.50 SF Short Wall	CRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,465. Vapor barrier 15# felt 30.00 SF 0.00 0.20 0.00 2,465. Seal/prime then paint exterior 735.00 SF 0.00 0.84 0.00  Note: Painting of the siding on the entire South Elevation 2,467. Two ladders with jacks and plank (per day)  Totals: South Elevation  DESCRIPTION  QTY RESET REMOVE REPLACE TAX 2,468. Gutter - aluminum - up to 5" 70.00 LF 0.00 3.62 0.00  Note: Upper section of gutter only 2,469. Downspout - aluminum - up to 5.200 LR 0.00 3.62 0.00  South (per day)  And 0.00 78.50 0.00  Totals: Front / East Elevation  Totals: Front / East Elevation  South Room  LxwxH 29' 3 15/16" x 19'  878.91 SF Walls 1,450.80 SF Walls & Ceiling 571.90 SF Floor 97.66 LF Floor Perimeter 175.50 SF Short Wall 97.66 LF Floor Perimeter 175.50 SF Short Wall	8	5.00 SF	MA	0.00	6.42	0.00	96.30
2,465. Vapor barrier   15# felt   30.00 SF   0.00   0.20   0.00	If more asbestos siding panels are distur	bed during the	repair process, i	t may require abat	ing the entire wall sur	face.	
Note: Painting of the siding on the entire South Elevation   2,467. Two ladders with jacks, and   3.00 DA   0.00   78.50   0.00				/			6.00
2,467. Two ladders with jacks and plank (per day)   0.00   78.50   0.00		5.00 SF		0.00	0.84	0.00	617.40
2.467. Two ladders with jacks and plank (per day)   0.00   78.50   0.00	Painting of the siding on the entire Sou	th Elevation	/				
Pront   East Elevation	7. Two ladders with jacks and			0.00	78.50	0.00	235.50
DESCRIPTION	s: South Elevation					0.00	955.20
2,468. Gutter - aluminum - up to 5"   70.00 LF   0.00   3.62   0.00     Note: Upper section of gutter only   2,469. Downspout - aluminum - up to 52.00 LF   0.00   3.62   0.00     S"   2,470. Two ladders with jacks and plank (per day)   2,471. Reglaze window, 1 - 9 sf   2.00 EA   0.00   54.58   0.00     Totals: Front / East Elevation   0.00     Totals: Exterior   Cround Level Interior	Front	ast Elevation	/				
Note: Upper section of gutter only   2,469. Downspout - aluminum - up to   52.00 LK   5"   0.00   3.62   0.00   5"   2,470. Two ladders with jacks and plank (per day)   2,471. Reglaze window, 1 - 9 sf   2.00 EA   0.00   54.58   0	CRIPTION	QTY /	RESET	REMOVE	REPLACE	TAX	TOTAL
2,469. Downspout - aluminum - up to 52.00 LR 0.00 3.62 0.00 5" 2,470. Two ladders with jacks and plank (per day) 2,471. Reglaze window, 1 - 9 sf 2.00 EA 0.00 54.58 0.00  Totals: Front / East Elevation 0.00  Ground Level Interior  South Room  LxWxH 29' 3 15/16" x 19'  878.91 SF Walls 571.90 SF Ceiling 571.90 SF Floor 97.66 LF Floor Perimeter 175.50 SF Short Wall 97.66 LF Ceil. Perimeter	3. Gutter - aluminum - up to 5" 7	0.00 LF		0.00	3.62	0.00	253.40
South Room   Sou	: Upper section of gutter only	$\vee$					
2,470. Two ladders with jacks and plank (per day) 2,471. Reglaze window, 1 - 9 sf  2.00 EA  0.00  78.50  0.00  78.50  0.00  Totals: Front / East Elevation  0.00  Cround Level Interior  South Room  South Room  ExwxH 29' 3 15/16" x 19'  878.91 SF Walls 1,450.80 SF Walls & Ceiling 63.54 SY Flooring 263.95 SF Long Wall 97.66 LF Ceil. Perimeter	). Downspout - aluminum - up to 5	2.00 LK		0.00	3.62	0.00	188.24
2,471. Reglaze window, 1 - 9 sf 2.00 EA 0.00 54.58 0.00  Totals: Front / East Elevation 0.00  Ground Level Interior  South Room  LxWxH 29' 3 15/16" x 19'  878.91 SF Walls 571.90 SF Ceiling 571.90 SF Floor 97.66 LF Floor Perimeter 263.95 SF Long Wall 97.66 LF Ceil. Perimeter		.00 DA		0.00	78.50	0.00	78.50
South Room   LxWxH 29' 3 15/16" x 19'	. Reglaze window, 1 - 9 sf	2.00 EA	\	0.00	54.58	0.00	109.16
South Room   LxWxH 29' 3 15/16" x 19'	s: Front / East Elevation					0.00	629.30
South Room    LxWxH 29' 3 15/16" x 19'	: Exterior	*		****		0.00	1,584.50
South Room    LxWxH 29' 3 15/16" x 19'			Ground evel	Interior			
878.91 SF Walls  1,450.80 SF Walls & Ceiling  63.54 SY Flooring  263.95 SF Long Wall  97.66 LF Ceil. Perimeter  571.90 SF Ceiling  571.90 SF Floor  97.66 LF Floor Perimeter  175.50 SF Short Wall		,	Ground Rever	interior			
878.91 SF Walls  1,450.80 SF Walls & Ceiling  63.54 SY Flooring  263.95 SF Long Wall  97.66 LF Ceil. Perimeter  571.90 SF Ceiling  571.90 SF Floor  97.66 LF Floor Perimeter  175.50 SF Short Wall							
1,450.80 SF Walls & Ceiling 63.54 SY Flooring 263.95 SF Long Wall 97.66 LF Ceil. Perimeter  571.90 SF Floor 97.66 LF Floor Perimeter 175.50 SF Short Wall	South Ro	oom			LxWxl	H 29' 3 15/16"	x 19' 6" x 9'
1,450.80 SF Walls & Ceiling 63.54 SY Flooring 263.95 SF Long Wall 97.66 LF Ceil. Perimeter  571.90 SF Floor 97.66 LF Floor Perimeter 175.50 SF Short Wall		878.91	SF Walls		571.90	SF Ceiling	
63.54 SY Flooring 97.66 LF Floor Perimeter 263.95 SF Long Wall 97.66 LF Ceil. Perimeter				eiling			
263.95 SF Long Wall 97.66 LF Ceil. Perimeter	X//	-					eter
97.66 LF Ceil. Perimeter					175.50	SF Short Wall	
DESCRIPTION QTY RESET REMOVE REPLACE TAX	· ·		_				
	CRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,472. Drywall Repair - Labor and 1.00 EA 0.00 264.11 0.00 Material		1.00 EA		0.00	264.11	0.00	264.11

Page: 204

12/13/2017



#### **CONTINUED - South Room**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,473. Remove Tear off painted acoustic ceiling (popcorn) texture	571.90 SF		0.54	0.00	0.00	308.83
2,474. Acoustic ceiling (popcorn) texture - heavy	571.90 SF		0.00	0.77	0.00	440.36
2,475. Seal & paint acoustic ceiling (popcorn) texture	571.90 SF		0.00	0.81	0.00	463.24
2,476. Ceiling fan - Detach & reset	1.00 EA		0.00	147.29	0.00	147.29
2,477. Light fixture - Detach & reset	1.00 EA		0.00	41.36	0.00	41.36
2,478. Seal/prime then paint part of the walls twice (3 coats)	395.51 SF		0.00	0.84	0.00	332.23
Note: Walls from 5' up to ceiling.						
2,479. Mask wall - plastic, paper, tape (per LF)	97.66 LF		0.00	0.82	0.00	80.08
2,480. Mask or cover per square foot	571.90 SF		0/25	0.00	0.00	142.98
2,481. Final cleaning - construction - Commercial	571.90 SF	\	0.00	0.11	0.00	62.91
Totals: South Room					0.00	2,283.39

#### **East Center Office**

422.47 SF Walls

557.46 SF Walls & Ceiling

15.00 SY Flooring

109.76 %F Long Wall 46.51 LF Ceil, Perimeter

#### LxWxH 12' 1" x 11' 2 1/16" x 9' 1"

134.99 SF Ceiling

134.99 SF Floor

46.51 LF Floor Perimeter

101.48 SF Short Wall

40.57 LF Cell. Perilleta								
DESCRIPTION	QTY/	RESET	REMOVE	REPLACE	TAX	TOTAL		
2,482. R&R 1/2" drywall - hung, taped, ready for texture	269.99 SF		0.24	1.27	0.00	407.69		
Note: 2 layers								
2,483. Acoustic ceiling (popcorn) texture - heavy	134.99 SF		0.00	0.77	0.00	103.94		
2,484. Seal & paint acoustic ceiling (popcorn) texture	134.99 SF		0.00	0.81	0.00	109.34		
2,485. Fluorescent light fixture - 2' & 4' - Detach & reset	1.00 EA		0.00	60.04	0.00	60.04		
2,486. Seal/prime then paint part of the walls twice (3 coats)	190.11 SF		0.00	0.84	0.00	159.69		
Note: From 5' up to ceiling								
2,487. Mask wall - plastic, paper, tape per LF)	46.51 LF		0.00	0.82	0.00	38.14		
2,488. Mask or cover per square foot	134.99 SF		0.25	0.00	0.00	33.75		
TICTORYCOSUB					12/13/2017	Page: 205		



	CONT	INUED - East	Center Office			
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,489. Final cleaning - construction - Commercial	134.99 SF		0.00	0.11	0.00	14.85
Totals: East Center Office				/	0.00	927.44
Total: Ground Level Interior			/		0.00	3,210.83
		Second Level I	nterior			
Rear	Center Office			LxWxH 17' 6" x	x 10' 3 15/16" x	x 8' 9 15/16"
	491.34	SF Walls		180.74	SF Ceiling	
	672.08	SF Walls & C	filing	180.74	SF Floor	
		SY Flooring			LF Floor Perim	eter
$\checkmark$		SF Long Wall LF Ceil. Perin	neter	91.18	SF Short Wall	
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
,490. Drywall Repair - Labor and Material	1.00 EA		0.00	264.11	0.00	264.11
Note: Ceiling repair. 6' x6' area of double	le layer drywall. /					
2,491. Remove Tear off painted acoustic ceiling (popcorn) texture	180.74 SF	\	0.54	0.00	0.00	97.60
2,492. Acoustic ceiling (popcorn) texture - heavy	180.74 SF		0.00	0.77	0.00	139.17
2,493. Seal & paint acoustic ceiling (popcorn) texture	180.74 SF		0.00	0.81	0.00	146.40
2,494. Cove / ceiling molding - 3/4"	55.66 LF		0.00	0.88	0.00	48.98

4,490. Drywall Repair - Labor and Material	1.00 EA	0.00	264.11	0.00	264.11
Note: Ceiling repair. 6' x6' area of double	layer drywall.				
2,491. Remove Tear off painted acoustic ceiling (popcorn) texture	180.74 SF	0.54	0.00	0.00	97.60
2,492. Acoustic ceiling (popcorn) texture - heavy	180.74 SF	0.00	0.77	0.00	139.17
2,493. Seal & paint acoustic ceiling (popcorn) texture	180. <b>7</b> 4 SF	0.00	0.81	0.00	146.40
2,494. Cove / ceiling molding - 3/4"	55.66 LF	00.9	0.88	0.00	48.98
2,495. Paint cove molding - two coats	55.66 LF	0.00	0.63	0.00	35.07
2,496. Ceiling fan - Detach & reset	1.00 EA	0.00	147.29	0.00	147.29
2,497. Light fixture - Detach & reset	1.00 EA	0.00	41.36	0.00	41.36
2,498. Remove Emergency lighting - battery - Commercial	1.00 EA	7.35	0.00	0.00	7.35
2,499. Seal/prime then paint part of the walls twice (3 coats)	221.10 SF	0.00	0.84	0.00	185.72
Note: Walls from 5' up to ceiling.					
2,500. Mask wall - plastic, paper, tape (per LF)	55.66 LF	0.00	0.82	0.00	45.64
2,501. Mask or cover per square foot	180.74 SF	0.25	0.00	0.00	45.19
2,502. Final cleaning - construction - Commercial	180.74 SF	0.00	0.11	0.00	19.88

Totals: Rear Center Office 0.00 1,223.76



From	nt Center Office				LxWxH 18' 9"	x 10' 3" x 8'
	656.19 21.35	SF Walls SF Walls & Co SY Flooring	eiling	192.1 58.0	9 SF Ceiling 9 SF Floor 0 LF Floor Perim 0 SF Short Wall	eter
		SF Long Wall LF Ceil. Perim	neter	82.0	U Sr Snort Wall	
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,503. Drywall Repair - Labor and Material	1.00 EA		0.00	264/11	0.00	264.11
Note: Ceiling repair. 6' x6' area of doub						
2,504. Heat/AC register - Mechanically attached - Detach & reset	1.00 EA		0.00	10.74	0.00	10.74
2,505. Remove Tear off painted acoustic ceiling (popcorn) texture	192.19 SF		0.54	0.00	0.00	103.78
2,506. Acoustic ceiling (popcorn) texture - heavy	192.19 SF		9.60	0.77	0.00	147.99
2,507. Seal & paint acoustic ceiling (popcorn) texture	192.19 SF		0.00	0.81	0.00	155.67
2,508. Cove / ceiling molding - 3/4"	58.00 LF		0.00	0.88	0.00	51.04
2,509. Paint cove molding - two coats	58.00 LF	X	0.00	0.63	0.00	36.54
2,510. Ceiling fan - Detach & reset	2.00 EA		0.00	147.29	0.00	294.58
2,511. Seal/prime then paint the walls twice (3 coats)	464.00 SF		0.00	0.84	0.00	389.76
2,512. Mask or cover per square foot	192.19 SF		0.25	0.00	0.00	48.05
2,513. Final cleaning - construction - Commercial	192.19 SF		0.00	0.11	0.00	21.14
Totals: Front Center Office					0.00	1,523.40
Kito	hen			LxWxl	H 11' 11 3/8" x 7'	11 3/8" x 8'
		SF Walls	-	010	7 SF Ceiling	
		SF Walls & C	eiling		7 SF Floor	
X////		SY Flooring			9 LF Floor Perim	eter
		SF Long Wall		63.5	Q SF Short Wall	
	39.79	LF Ceil. Perin	neter			
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,514. 1/2" drywall - hung, taped, heavy texture, ready for paint	94.97 SF		0.00	1.71	0.00	162.40
2,515. Seal/prime then paint the ceiling twice (3 coats)	94.97 SF		0.00	0.84	0.00	79.77
ICTORYCOSUB					12/13/2017	Page: 20





#### **CONTINUED - Kitchen**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,516. Light fixture - Detach & reset	1.00 EA		0.00	41.36	0.00	41.36
2,517. Crown molding - 2 1/4"	39.79 LF		0.00	1.98	0.00	78.78
2,518. Paint crown molding - two coats	39.79 LF		0.00	0.97	0.00	38.60
2,519. Mask or cover per square foot	94.97 SF		0.25	0.00	0.00	23.74
2,520. Mask wall - plastic, paper, tape (per LF)	39.79 LF		0.00	0.82	0.00	32.63
2,521. Final cleaning - construction - Commercial	94.97 SF		0.00	0.11	0.00	10.45
Totals: Kitchen					0.00	467.73



Training Room

LxWxH 11' 9 15/16" x 7' 9 15/16" x 8'

92.59 SF Ceiling 92.59 SF Floor

39.31 LF Floor Perimeter

62.62 SF Short Wall



314.50 SF Walls 40√.09 SF Walls & Ceiling 10.29 SY Flooring 94.62 SF Long Wall LF Ceil. Perimeter

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,522. 1/2" drywall - hung, taped, heavy texture, ready for paint	92.59 SF		0.00	1.71	0.00	158.33
2,523. Seal/prime then paint the walls and ceiling twice (3 coats)	407.09 SF	X	0.00	0.84	0.00	341.96
2,524. Cove / ceiling molding - 3/4"	39.31 LF		0.00	0.88	0.00	34.59
2,525. Paint cove molding - two coats	39.31 LF		0.00	0.63	0.00	24.77
2,526. Mask or cover per square foot	92.59 SF	/	0.25	0.00	0.00	23.15
2,527. Final cleaning - construction - Commercial	92.59 SF		0.00	0.11	0.00	10.18
Totals: North Center Room		,			0.00	592.98

LxWxH 40' 9 15/16" x 29' 5 1/16" x 8'

1,124.00 SF Walls

2,325.24 SF Walls & Ceiling 133.47 SY Flooring

326.62 SF Long Wall

140.50 LF Ceil. Perimeter

1,201.24 SF Ceiling 1,201.24 SF Floor 140.50 LF Floor Perimeter

235.38 SF Short Wall





#### **CONTINUED - Training Room**

				,		
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,528. Drywall Repair - Labor and Material	1.00 EA		0.00	264.11	0.00	264.11
Note: Ceiling repair. 4' x 4' area of doub	ole layer drywall.					
2,529. Remove Tear off painted acoustic ceiling (popcorn) texture	1,201.24 SF		0.54	0.00	0.00	648.67
2,530. Acoustic ceiling (popcorn) texture - heavy	1,201.24 SF		0.00	0.77	0.00	924.95
2,531. Seal & paint acoustic ceiling (popcorn) texture	1,201.24 SF		0,00	0.81	0.00	973.00
2,532. Ceiling fan - Detach & reset	3.00 EA		0.00	147.29	0.00	441.87
2,533. Mask and cover light fixture	8.00 KA		0.00	9.25	0.00	74.00
2,534. Mask or cover per square foot	1,201.24 SF		0.25	0.00	0.00	300.31
2,535. Mask wall - plastic, paper, tape (per LF)	140.50 LF	/	0.00	0.82	0.00	115.21
2,536. Final cleaning - construction - Commercial	1,201.24 SF		0.00	0.11	0.00	132.14
Totals: Training Room		$\bigvee$		1 1 2 2 217 277	0.00	3,874.26

**Basement Interior** 

#### **South Storage**

1,3/42.41 SF Walls ,657.00 SF Walls & Ceiling 146.07 SY Flooring

414.00 SF Long Wall

149.16 LF Ceil. Perimeter

#### LxWxH 46' x 28' 6 15/16" x 9'

1,314.59 SF Ceiling 1,314.59 SF Floor

149.16 LF Floor Perimeter

257.20 SF Short Wall

	/					
DESCRIPTION	/ QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,537. Remove Tear off painted acoustic ceiling (popcorn) texture	1,314.59 SF		0.54	0.00	0.00	709.88
2,538. Acoustic ceiling (popcorn) texture - heavy	1,314.59 SF		0.00	0.7	0.00	1,012.23
2,539. Seal & paint acoustic ceiting (popcorn) texture	1,314.59 SF		0.00	0.81	0.00	1,064.82
2,540. Ceiling fan - Detach & reset	2.00 EA		0.00	147.29	0.00	294.58
2,541. Mask and cover light fixture	8.00 EA		0.00	9.25	0.00	74.00
2,542. Mask wall - plastic, paper, tape (per LF)	149.16 LF		0.00	0.82	0.00	122.31
2,543. Mask or cover per square foot	1,314.59 SF		0.25	0.00	0.00	328.65
.544. Contents - move out then reset - Extra large room	1.00 EA		0.00	84.56	0.00	84.56
VICTORYCOSUB					12/13/2017	Page: 20



#### **CONTINUED - South Storage**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,545. Final cleaning - construction - Commercial	1,314.59 SF		0.00	0.11	0.00	144.60
Totals: South Storage					0.00	3,835.63
Nort	h Storage			Lx	WxH 20' 2 1/1	6" x 20' x 9'
	1,126.5: 44.8: 181.5:	9 SF Walls 3 SF Walls & C 3 SY Flooring SF Long Wall 4 LF Ceil. Perin	/	403.44 80.34	SF Ceiling SF Floor LF Floor Perim SF Short Wall	eter
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,546. Drywall Repair - Labor and Material	1.00 EA		0.00	264.11	0.00	264.11
Note: Ceiling repair. 6' x6' area of doubl	le laver drywall.					
.547. Remove Tear off painted acoustic ceiling (popcorn) texture	403.44 SF	X	0.54	0.00	0.00	217.86
2,548. Acoustic ceiling (popcorn) texture - heavy	403.44 SF		0.00	0.77	0.00	310.65
2,549. Seal & paint acoustic ceiling (popcorn) texture	403.44 SF		0.00	0.81	0.00	326.79
2,550. Light fixture - Detach & reset	3.00 EA		0.00	41.36	0.00	124.08
2,551. Mask wall - plastic, paper, tape (per LF)	80.34 LF		0.00	0.82	0.00	65.88
2,552. Mask or cover per square foot	403.44 SF		0.25	0.00	0.00	100.86
2,553. Contents - move out then reset - Large room	1.00 EA		0.00	42.27	0.00	42.27
2,554. Final cleaning - construction - Commercial	403/44 SF		0.00	0.11	0.00	44.38
Totals: North Storage					0.00	1,496.88
					WxH 8' 1" x 6'	11 2/01 - 01
/ Kest	room					11 3/6 X 6
		0 SF Walls			SF Ceiling	
		7 SF Walls & C	eiling		SF Floor LF Floor Perim	atar
		4 SY Flooring 7 SF Long Wall			SF Short Wall	eter
V	04.0	or Long wan		33.39	or short wall	

VICTORYCOSUB

12/13/2017

Page: 210






8380 Warren Parkway / Ste. 700 - Frisco, TX 75034

CONTINUED - I	Restroom
---------------	----------

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,555. R&R 1/2" drywall - hung, taped, ready for texture	56.16 SF		0.24	1.27	0.00	84.80
2,556. Acoustic ceiling (popcorn) texture - heavy	56.16 SF		0.00	0.77	0.00	43.24
2,557. Seal & paint acoustic ceiling (popcorn) texture	56.16 SF		0.00	0.81	0.00	45.49
2,558. Seal/prime then paint part of the walls twice (3 coats)	134.68 SF		0.00	0.84	0.00	113.13
Note: From 4' up to ceiling						
2,559. Mask wall - plastic, paper, tape (per LF)	30.06 LF		0,00	0.82	0.00	24.65
2,560. Mask or cover per square foot	56.16 SF		0.25	0.00	0.00	14.04
2,561. Final cleaning - construction - Commercial	56.16 SF		0.00	0.11	0.00	6.18
Totals: Restroom					0.00	331.53
Total: Basement Interior					0.00	5,664.04
otal: Second Level Interior					0.00	13,346.17
Total: Building 38 - Storehouse	-				0.00	18,717.90

#### Building 39 - AARF Fire Station Roof



#### Roof1

3,306.69 Surface Area 244.84 Total Perimeter Length 33.07 Number of Squares64.00 Total Ridge Length

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,564. R&R Standing seam metal roofing	1,638.14 SF		0.30	4.35	0.00	7,617.35
Note: Nower / North slope only.						
2,565. R&R Aluminum wall coping	70.00 LF		0.34	11.95	0.00	860.30
2,566. Detach & Reset Gutter / downspout - box - aluminum - 6"	64.00 LF	2.40	0.00	0.00	0.00	153.60
2,567. R&R Aluminum idewall/endwall flashing - color finis	57.00 LF		0.34	5.03	0.00	306.09





#### **CONTINUED - Roof1**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,568. R&R Centrifugal exhaust fan - Commercial roof mounted	2.00 EA		0.00	3,026.52	0.00	6,053.04
Note: Based on equipment pricing from (	GREENHECK for a	3/4 HP centrifuga	ıl exhaust fan desi	gned for removal of h	eavy fumes / poll	utants.
2,569. R&R Neoprene pipe jack flashing for metal roofing	3.00 EA		4.65	33.70	0.00	115.05
Totals: Roof1					0.00	15,105.43
Total: Roof					0.00	15,105.43

#### Exterior / General

#### Exterior / General

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,570. Finish Carpenter - per hour	3.00 HR		0.00	46.01	0.00	138.03
Note: Considers time necessary to adjus	t (2) exterior steel do	ors.				
Total: Exterior / General					0.00	138.03

#### **West Elevation**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,571. R&R Wood fence 3'- 4' high - cedar or equal	12.00 LF		3.68	16.79	0.00	245.64
Totals: West Elevation					0.00	245.64
Total: Exterior / General					0.00	383.67
Total: Building 39 - AARF Fire Station					0.00	15,489.10

#### **Building 40 - ERECT-A-TUBE Hangar**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Note: No damage identified						
Totals: Building 40 - ERECT-A-TUI	BE Hangar				0.00	0.00
	Buil	ding #41 - Cor	trol Tower			

Roof

12/13/2017

Page: 212



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

CONTINUED - Roof

DESCRIPTION	QTY	RESE	REMOVE	REPLACE	TAX	TOTAL
Note: No damage to the TPO membrane of 2,577. R&R Exterior outlet or switch cover	roof. 1.00 EA	J.	0.37	6.87	0.00	7.24
Totals: Roof				V	0.00	7.24

#### **Exterior / East Elevation**

DESCRIPTION	QTY	RESET REMOVE	REPLACE	TAX	TOTAL
2,578. R&R Wall/roof panel - ribbed - 24 gauge - 1 1/8" to 1 1/2"	1,215.00 SF	0.30	2.97	0.00	3,973.05
Note: Metal wall panels which extend th	ne full height of the E	'ast elevation.(54" x 22'-6")			
2,579. Rigid foam insulation board - 3/4"	1,215.00 SF	0.00	0.54	0.00	656.10
2,580. Prime & paint metal wall panels	1,215.00 SF	0,00	0.62	0.00	753.30
2,581. R&R Metal outside corner post	108.00 LF	0.74	4.08	0.00	520.56
2582. Metal Structure Installer - per	24.00 HR	0.00	44.55	0.00	1,069.20
Note: Additional cost for lost production	n due to excessive he	ight, working from a lift and comp	liance to safety regulat	ions.	/
Note: Additional cost for lost production (2) men x 1.5 days x 8 HOURS per day		ight, working from a lift and comp	liance to safety regulat	ions.	
		ight, working from a lift and comp 0.00	liance to safety regulat	0.00	3,388.59
(2) men x 1.5 days x 8 HOURS per day	= 24 23.00 EA				3,388.59
(2) men x 1.5 days x 8 HOURS per day 2,583 Letters - cast metal - 7" to 12"	= 24 23.00 EA				3,388.59 4,774.77
(2) men x 1.5 days x 8 HOURS per day 2,583 Letters - cast metal - 7" to 12" Note: Cast metal lettering "Victoria Regu 2,584 Lighted sign - wall mtd	= 24 23.00 EA ional Airport" 1.00 EA	0.00	147.33	0.00	
(2) men x 1.5 days x 8 HOURS per day 2,583 Letters - cast metal - 7" to 12" Note: Cast metal lettering "Victoria Regu 2,584 Lighted sign - wall mtd circular with custom logo - 8' diameter	= 24 23.00 EA ional Airport" 1.00 EA	0.00	147.33	0.00	





Totals: Exterior / East Elevation

5th Floor Recorder Room

510.73 SF Walls 683.39 SF Walls & Ceiling

19.18 SY Flooring53.32 LF Ceil. Perimeter

Height: 9' 7"

0.00

172.66 SF Ceiling 172.66 SF Floor 53.32 LF Floor Perimeter

3' X 6' 8"

**Opens into Exterior** 

VICTORYCOSUB

Door

12/13/2017


Page: 213

17,060.37



#### **CONTINUED - 5th Floor Recorder Room**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,587. 5/8" - drywall per LF - up to 2' tall	15.50 LF		0.00	6.02	0.00	93.31
Note: East wall only						
2,588. Batt insulation - 4" - R13 - paper faced	31.00 SF	1	0.00	0.50	0.00	15.50
2,589. Texture drywall - heavy hand texture	510.73 SF		0.00	0.58	0.00	296.22
2,590. Seal/prime then paint the walls twice (3 coats)	510.73 SF	-	0.00	0.84	0.00	<b>429</b> .01
2,591. Window trim set (casing & stop) - stain grade	24.00 LF		0.00	3.09	0.00	74.16
2,592. Stain & finish door/window trim & jamb - Large (per side)	1.00 EA		0.00	30.93	0.00	30.93
2,593. Clean window unit (per side) 10 - 20 SF	1.00 EA		0.00	8.32	0.00	8.32
2,594. Outlet	2.00 EA		0.00	11.88	0.00	23.76
2,595. Cove base molding - rubber or vinyl, 4" high	53.32 LF		0.00	1.37	0.00	73.05
2,596. Clean floor	172.66 SF		0.00	0.25	0.00	43.17
2,597. Contents - move out then reset	1.00 EA		0.00	28.18	0.00	28.18
2,598. Mask or cover per square foot	172.66 SF		0.25	0.00	0.00	43.17
2,599. Final cleaning - construction - Commercial	172.66 SF		0.00	0.11	0.00	18.99
Totals: 5th Floor Recorder Room					0.00	1,177.77



#### 4th Floor Managers Office

185.06 SF Ceiling

479.88 SF Walls 664.95 SF Walls & Ceiling

20.56 SY Flooring 54.84 LF Ceil. Perimeter 185.06 SF Floor

54.84 LF Floor Perimeter

Height: 8' 9"

Window Door Door

3' X 3' 3' X 6' 8" 3' X 6' 8" **Opens into Exterior Opens into Exterior Opens into Exterior** 

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,600. Suspended ceiling tile - 2' x 2'	16.00 SF	,,	0.00	1.23	0.00	19.68
Note: (4) tiles						
2,601. Batt insulation - 6" - R19 -	16.00 SF		0.00	0.65	0.00	10.40
VICTORYCOSUB					12/13/2017	Page: 214





#### **CONTINUED - 4th Floor Managers Office**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,602. Clean and deodorize carpet	185.06 SF		0.00	0.27	0.00	49.97
Totals: 4th Floor Managers Office					0.00	80.05

**3rd Floor Office** 


Height: 8' 9"

479.88 SF Walls 664.95 SF Walls & Ceiling 20.56 SY Flooring 54.84 LF Ceil. Perimeter 185.06 SF Ceiling 185.06 SF Floor

54.84 LF Floor Perimeter

Window Door Door 3' X 3' 3' X 6' 8" 3' X 6' 8" Opens into Exterior Opens into Exterior Opens into Exterior

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
,603. 5/8" - drywall per LF - up to 2' tall	15.50 LF		0.00	6.02	0.00	93.31
Note: East wall only						
2,604. Batt insulation - 4" - R13 - paper faced	31.00 SF		0.00	0.50	0.00	15.50
2,605. Texture drywall - heavy hand texture	479.88 SF		0.00	0.58	0.00	278.33
2,606. Seal/prime then paint the walls twice (3 coats)	479.88 SF		0.00	0.84	0.00	403.10
2,607. Window trim set (casing & stop) - stain grade	24.00 LF		0.00	3.09	0.00	74.16
2,608. Stain & finish door/window trim & jamb - Large (per side)	1.00 EA		0.00	30.93	0.00	30.93
2,609. Clean window unit (per side) 10 - 20 SF	1.00 EA		0.00	8.32	0.00	8.32
2,610. Outlet	3.00 EA		0.00	11.88	0.00	35.64
2,611. Cove base molding - rubber or vinyl, 4" high	54.84 LF		0.00	1.37	0.00	75.13
2,612. Glue down carpet - heavy traffic	212.82 SF		0.00	3.12	0.00	664.00
15 % waste added for Glue down carpet -	heavy traffic.					
2,613. Floor prep (scrape rubber back residue)	185.06 SF		0.00	0.34	0.00	62.92
2,614. Contents - move out then reset	1.00 EA		0.00	28.18	0.00	28.18
1,615. Mask or cover per square foot	185.06 SF		0.25	0.00	0.00	46.27



#### **CONTINUED - 3rd Floor Office**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,616. Final cleaning - construction - Commercial	185.06 SF		0.00	0.11	0.00	20.36
Totals: 3rd Floor Office					0.00	1,836.15

11	8' 9"
Ţ	2nd Floor Office &
.8.9	12'

Window

Door Door 2nd Floor Office

185.06 SF Ceiling 185.06 SF Floor

664.95 SF Walls & Ceiling 20.56 SY Flooring

479.88 SF Walls

54.84 LF Floor Perimeter

Height: 8' 9"

54.84 LF Ceil. Perimeter

3' X 3'

3' X 6' 8"

3' X 6' 8"

Opens into Exterior Opens into Exterior Opens into Exterior

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,617. Suspended ceiling tile - 2' x 2'	12.00 SF		0.00	1.23	0.00	14.76
Note: (3) tiles						
2,618. Batt insulation - 6" - R19 - paper faced	12.00 SF		0.00	0.65	0.00	7.80
2,619. 5/8" - drywall per LF - up to 2' tall	15.50 LF		0.00	6.02	0.00	93.31
Note: East wall only						
2,620. Batt insulation - 4" - R13 - paper faced	31.00 SF		0.00	0.50	0.00	15.50
2,621. Texture drywall - heavy hand texture	479.88 <b>S</b> F		0.00	0.58	0.00	278.33
2,622. Seal/prime then paint the walls twice (3 coats)	479.88 <b>S</b> F		0.00	0.84	0.00	403.10
2,623. Window trim set (casing & stop) - stain grade	24.00 LF		0.00	3.09	0.00	74.16
2,624. Stain & finish door/window trim & jamb - Large (per side)	1.00 EA		0.00	30.93	0.00	30.93
2,625. Clean window unit (per side) 10 - 20 SF	1.00 EA		0.00	8.32	0.00	8.32
2,626. Outlet	2.00 EA		0.00	11.88	0.00	23.76
2,627. Cove base molding - rubber or vinyl, 4" high	54.84 LF		0.00	1.37	0.00	75.13
2,628. Clean floor	185.06 SF		0.00	0.25	0.00	46.27
2,629. Contents - move out then reset	1.00 EA		0.00	28.18	0.00	28.18
2,630. Mask or cover per square foot	185.06 SF		0.25	0.00	0.00	46.27
VICTORYCOSUB					12/13/2017	Page: 216



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

	CONT	INUED - 2nd	Floor Office			
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,631. Final cleaning - construction - Commercial	185.06 SF		0.00	0.11	0.00	20.36
Totals: 2nd Floor Office					0.00	1,166.18
Total: Interior					0.00	4,260.15
6th	Floor Break Room					
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL

Total: Building #41 - Control Tower	-			0.00	21,402.96
Totals: 6th Floor Break Room				0.00	75.20
2,633. Batt insulation - 6" - R19 - paper faced	40.00 SF	0.00	0.65	0.00	26.00
Note: (10) tiles					
2,632. Suspended ceiling tile - 2' x 2'	40.00 SF	0.00	1.23	0.00	49.20

#### **Building 42 - Precinct #1 Pole Barn Storage**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Note: No damage identified.		· ·				
Totals: Building 42 - Precinct #1 Pole Barn Stora	ige				0.00	0.00

#### Building 43 - Hartman /JP #1 Building (Goldman)

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Note: No damage identified.		1				
Totals: Building 43 - Hartman /JP #1 Building (Gol	ldman)				0.00	0.00

#### Building 44 - Hartman Building (901 E Pecan)

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
				744		

Note: No damage identified.



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### CONTINUED - Building 44 - Hartman Building (901 E Pecan)

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Totals: Building 44 - Hartman Building (9	01 E Pecan)	and the same of th			0.00	0.00

#### Building 45 - JP #4 Building (Mockingbird)

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Note: No damage identified.						
Totals: Building 45 - JP #4 Building (Mocking	bird)	/		4 19.	0.00	0.00

#### Building 46 - JP #2 Building (Lilac)

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Note: No damage identified.						
Totals: Building 46 - JP #2 Building (Lilac)			-		0.00	0.00

## Building 47 - Precinct #4 New Barn (226 Beck Road)

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,639. R&R Roll-up door & hardware - 14' x 14' - 22 gauge	3.00 EA		16.33	1,834.13	0.00	5,551.38
2,640. Dumpster load - Approx. 20 yards, 4 tons of debris	1.00 EA		403.20	0.00	0.00	403.20
Totals: Building 47 - Precinct #4 New Bar	n (226 Beck Road)				0.00	5,954.58

#### **Building 48 - Precinct #4 Storage Building**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Note: No damage identified.						
Totals: Building 48 - Precinct #4 Storage Building					0.00	0.00

#### **Building 50 - Celebration Church (358 Foster Field)**

Roof



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546



#### **Roof Section A**

4,059.53 Surface Area 269.23 Total Perimeter Length 40.60 Number of Squares 89.00 Total Ridge Length

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Note: No visible damage	(					
Totals: Roof Section A				0	0.00	0.00
	Roof Section B				-\-	
44' 9"	738.	14 Surface Area	( )	7.38	Number of Squ	ares
Roof Section B	77.	75 Total Perime	ter Length	/		

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Note: No visible damage						
Totals: Roof Section B					0.00	0.00

# Roof Section C

Roof Section B

#### Roof Section C

379.23 Surface Area 55.17 Total Perimeter Length 3.79 Number of Squares

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,641. Remove Tear off 3 ply built-up roofing (no haul off)	3.79 SQ		22.28	0.00	0.00	84.44
2,642. Built-up 3 ply roofing - in place	3.79 SQ		0.00	195.56	0.00	741.17
2,643. Remove Additional charge for high roof (2 stories or greater)	3.79 SQ		3.11	0.00	0.00	11.79
2,644. Additional charge for high roof 2 stories or greater)	3.79 SQ		0.00	9.91	0.00	37.56
2,645. Aluminum coating - with fiber	379.23 SF		0.00	0.50	0.00	189.62
VICTORYCOSUB					12/13/2017	Page: 219



#### CONTINUED - Roof Section C

CONTINUED - Roof Section C										
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL				
2,646. R&R Gravel stop	55.17 LF		0.20	1.18	0.00	76.13				
2,647. R&R Flash parapet wall only - bitumen	26.00 LF		1.18	7.58	0.00	227.76				
Note: Flashing along wall										
2,648. R&R Counterflashing - Apron flashing	26.00 LF		0.34	5.14	0.00	142.48				
2,649. R&R Curb flashing - bitumen	4.00 LF		1.10	12.22	0.00	53.28				
Note: Base of vent										
2,650. R&R Flashing - pipe jack	1.00 EA		4.14	23.34	0.00	27.48				
2.651. Fiberboard - 1"	379.23 SF		0.00	0.65	0.00	246.50				
This item did not previously exist or expincurred, subject to limits.	ands the scope of rep	pairs, but is requir	ed by current build	ling codes. The code u	pgrade cost is pa	yable when				
2.652. Insulation - ISO board, 311	3.79 SQ		0.00	218.42	0.00	827.81				
This item did not previously exist or expincurred, subject to limits.	oands the scope of rej	pairs, but is requir	ed by current build	ling codes. The code u	pgrade cost is pa	yable when				
2.653. Insulation - ISO board. 3"	+4 50		0.00	218.42	0.00	415.00				
This item did not previously exist or exp neurred, subject to limits.	oands the scope of rep	patrs, but is requir	ed by current build	ling codes. The code u	pgrade cost is pa	yable when				
Note: Considers tapered insulation to co	omply with 1/4" per f	foot drainage requ	urements.							
2,654. 2" x 6" lumber (1 BF per LF)	110.34 LF		0.00	1.73	0.00	190.89				
This item did not previously exist or expincurred, subject to limits.	oands the scope of rej	pairs, but is require	ed by current build	ling codes. The code u	pgrade cost is pa	yable when				
Note: Double perimeter band (3") install	lled to fasten perimet	ter coping after in	dallation of insula	ation.						
2 (55   64 - 1 11	55 17 15		0.00	0.37	0.00	517.01				

2,655. Steel wall coping

55.17 LF

0.00

9.37


0.00

516.9

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

Totals: Roof Section C

0.00 1,591.71



#### **Roof Section D**

541.62 Surface Area 151.92 Total Perimeter Length 5.42 Number of Squares

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,656. Remove Tear off 3 ply built-up oofing (no haul off)	5.42 SQ		22.28	0.00	0.00	120.76
2,657. Built-up 3 ply roofing - in place	5.42 SQ		0.00	195.56	0.00	1,059.94
VICTORYCOSUB					12/13/2017	Page: 220





CONTINUED - Roof Section D

	/						
DESCRIPTION	QTY	RESET	REMOVE /	REPLACE	TAX	TOTAL	
2,658. Aluminum coating - with fiber	541.62 SF		0.00	0.50	0.00	270.81	
2,659. R&R Gravel stop	151.92 LF		0.20	1.18	0.00	209.65	
2,660. R&R Flash parapet wall only - bitumen	53.17 LF		1.18	7.58	0.00	465.77	
Note: Flashing along wall							
2,661. R&R Counterflashing - Apron flashing	53.17 LF		0.34	5.14	0.00	291.37	
2,662. R&R Curb flashing - bitumen	20.00 LF		1.10	12.22	0.00	266.40	
Note: Base of (2) vents measuring 2'-6"	x 2'-6"						
2,663. Detach & Reset Exhaust cap - through flat roof	2.00 EA	41.00	0.00	0.00	0.00	82.00	
2,664. R&R Flashing - pipe jack	2.00 EA		4.14	23.34	0.00	54.96	
2.665. Fiberboard - 1"	541.62 SF		0.00	0.65	0.00	352.05	

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits. 218.42

2,666. Insulation - ISO board, 3"

5.42 SO

0.00

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when

1.183.84

ncurred, subject to limits. 0.00 2,667. Insulation - ISO board, 3" 2.71 SQ 0.00591.92

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when

incurred, subject to limits. Note: Considers tapered insulation to comply with 1/4" per foot drainage requirements.

2,668. 2" x 6" lumber (1 BF per LF)

303.85 LF

0.00

1.73

0.00 525.66

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

Note: Double perimeter band (3") installed to fasten perimeter coping after installation of insulation.

2.669. Steel wall coping

151.92 LF

9.37

0.001,423,49

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

2,670. Gutter / downspout - Detach & reset

36.00 LF

0.00

2.40

0.00

2,908.06 Totals: Roof Section D 0.00

Total: Roof

86.40

0.00 4,499,77

VICTORYCOSUB





8380 Warren Parkway / Ste. 700 - Frisco, TX 75034



#### Interior / Upstairs Lighting / Control Room

LxWxH 21' x 12' x 8'

528.00 SF Walls 780.00 SF Walls & Ceiling 28.00 SY Flooring 168.00 SF Long Wall 66.00 LF Ceil. Perimeter 252.00 SF Ceiling 252.00 SF Floor 66.00 LF Floor Perimeter 96.00 SF Short Wall

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,671. 5/8" drywall - hung, taped, heavy texture, ready for paint	252.00 SF		0.00	1.80	0.00	453.60
2,672. Batt insulation - 6" - R19 - paper faced	252.00 SF	(GL)	0.00	0.65	0.00	163.80
2,673. Seal/prime then paint the walls and ceiling twice (3 coats)	780.00 SF		0.00	0.84	0.00	655.20
2,674. Pluorescent - two tube - 4' - fixture w/lens	2.00 EA	- >	0.00	85.33	0.00	170.66
2,675. Clean and deodorize carpet	252.00 SF	20-	0.00	0.27	0.00	68.04
2,676. Mask or cover per square foot	252.00 SF	20/	0.25	0.00	0.00	63.00
2,677. Final cleaning - construction - commercial	252.00 SF	Kiek	0.00	0.11	0.00	27.72
Totals: Interior / Upstairs Lighting / Con	itrol Room	0	/.		0.00	1,602.02
Total: Building 50 - Celebration Church	(358 Foster Field)	Ero	04		0.00	6,101.79

#### **Building 51 - Sky Restaurant**


#### **Exterior / Front - North Elevation**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,682. R&R Awning - Window/door - Canvas (fixed)	11.00 LF		0.54	93.14	0.00	1,030.48
Totals: Exterior / Front - North Elevation					0.00	1,030.48

#### Roof

#### Rear/South Roof Section

2,702.77 Surface Area 234.86 Total Perimeter Length 27.03 Number of Squares



12/13/2017

Page: 222






8380 Warren Parkway / Ste. 700 - Frisco, TX 75034

#### **CONTINUED - Rear/ South Roof Section**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL	
2,683. R&R Metal roofing	2,702.77 SF		0.30	3.22	0.00	9,513.75	
2,684. R&R Closure strips for metal roofing - inside and/or outside	172.00 LF		0.49	1.16	0.00	283.80	
2,685. R&R Gable trim for metal roofing - 26 gauge	62.00 LF		0.49	3.73	0.00	261.64	
2,686. R&R Aluminum sidewall/endwall flashing - mill finish	86.00 LF		0.34	3.86	0.00	361.20	
2,687. Counter battens - 1x4 - for steel roofing	27.03 SQ		0.00	59.06	0.00	1,596.39	
2,688. R&R Vinyl-faced/laminated insulation - 2"	2,702.77 SF		0.14	0.46	0.00	1,621.66	
2, <mark>6</mark> 89. Gutter / downspout - box - galvanized - 6"	116.00 LF		0.00	6.79	0.00	787.64	
2,690. R&R Drip edge/gutter apron	86.00 LF		0.20	1.41	0.00	138.46	
2,691. Prime & paint gutter / downspout - Oversized	106.00 LF		0.00	1.46	0.00	154.76	
2,692. Tarp - all-purpose poly - per sq ft (lab/mat) - after hrs	891.92 SF		0.00	0.69	0.00	615.42	
otals: Rear/ South Roof Section					0.00	15,334.72	
Total: Roof					0.00	15,334.72	
Total: Building 51 - Sky Restaurant					0.00	16,365.20	

## Building # 51 - Sky Restaurant Interior Main Level



574.75 SF Walls 874.41 SF Walls & Ceiling 33.30 SY Flooring 71.84 LF Ceil. Perimeter 299.66 SF Ceiling 299.66 SF Floor 71.84 LF Floor Perimeter

Height: 8'

W	in	d	OW
Do	00	Г	

3' X 5' 2' 8 1/16" X 6' 8" Opens into Exterior Opens into HALL


DESCRIPTION	OTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,693. R&R Suspended ceiling tile - 2'	299.66 SF		0.13	1.23	0.00	407.54
2,694. R&R Batt insulation - 6" - R19 - aper faced	299.66 SF		0.17	0.65	0.00	245.72





#### **CONTINUED - Banquet #2**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,695. 1/2" - drywall per LF - up to 2' tall	35.92 LF		0.00	5.76	0.00	206.90
2,696. Batt insulation - 4" - R13 - paper faced	46.00 SF		0.00	0.50	0.00	23.00
2,697. Texture drywall - heavy hand texture	574.75 SF		0.00	0.58	0.00	333.36
2,698. Seal/prime then paint the walls twice (3 coats)	574.75 SF		0.00	0.84	0.00	482.79
2,699. Baseboard - 3 1/4"	35.92 LF		0.00	1.94	0.00	69.68
2,700. Seal & paint baseboard - two coats	71.84 LF		0.00	0.98	0.00	70.40
2,701. Mask or cover per square foot	299.66 SF		0.25	0.00	0.00	74.92
2,702. Clean floor - tile	299.66 SF		0.00	0.36	0.00	107.88
2,703. Final cleaning - construction - Commercial	299.66 SF		0.00	0.11	0.00	32.96
Totals: Banquet #2					0.00	2,055.15



Hall Height: 8'

169.42 SF Walls 203.90 SF Walls & Ceiling 3.83 SY Flooring

23.68 LF Ceil. Perimeter

34.48 SF Ceiling 34.48 SF Floor 20.68 LF Floor Perimeter

0.00

60.76

Door Missing Wall - Goes to Floor

Totals: Hall

Door Door 2' 8 1/16" X 6' 8"


3' X 6' 8" 3' X 6' 8" 3' X 6' 8" Opens into BANQUET\_2
Opens into Exterior

Opens into LARGE\_BANQUE Opens into LARGE\_BANQUE

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,704. R&R Suspended ceiling tile - 2' x 2'	34.48 SF		0.13	1.23	0.00	46.89
2,705. Recessed light fixture - Detach & reset trim only	1.00 EA		0.00	1.46	0.00	1.46
2,706. Mask or cover per square foot	34.48 SF		0.25	0.00	0.00	8.62
2,707. Final cleaning - construction - Commercial	34.48 SF		0.00	0.11	0.00	3.79



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546



#### Banquet #1

Height: 9' 2

1,010.40 SF Walls 1,988.64 SF Walls & Ceiling 108.69 SY Flooring 126.70 LF Ceil. Perimeter 978.25 SF Ceiling 978.25 SF Floor 116.70 LF Floor Perimeter

Missing Wall - Goes to Floor Window

10' X 6' 8" 17' X 5' Opens into Exterior Opens into Exterior

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,708. R&R Suspended ceiling tile - 2' x 2'	20.00 SF		0.13	1.23	0.00	27.20
Note: (5) tiles						
2,709. R&R 5/8" drywall - hung, taped, with smooth wall finish	235.04 SF		0.24	2.07	0.00	542.94
2,710. R&R Additional cost for gluing drywall	320.04 SF		0.21	0.17	0.00	121.62
2,711. Clean window unit (per side) 10 - 20 SF	5.00 EA		0.00	8.32	0.00	41.60
,712. Clean window blind - norizontal or vertical	100.00 SF		0.00	0.71	0.00	71.00
2,713. Install Casing - 2 1/4"	44.00 LF		0.00	0.57	0.00	25.08
2,714. Seal/prime then paint the walls twice (3 coats)	1,010.40 SF		0.00	0.84	0.00	848.74
2,715. Install Baseboard - 3 1/4"	27.00 LF		0.00	1.10	0.00	29.70
2,716. Seal & paint baseboard - two coats	116.70 LF		0.00	0.98	0.00	114.37
2,717. Mask or cover per square foot	978.25 SF		0.25	0.00	0.00	244.56
2,718. Contents - move out then reset - Large room	1.00 EA		0.00	42.27	0.00	42.27
2,719. Final cleaning - construction - Commercial	978.25 SF		0.00	0.11	0.00	107.61

Totals: Banquet #1 0.00 2,216,69









#### Large Banquet Hall

Height: 8'

1,566.75	SF Walls
3,594.86	SF Walls & Ceiling
225.35	SY Flooring
195.84	LF Ceil. Perimeter

2,028.11 SF Ceiling 2,028.11 SF Floor 195.84 LF Floor Perimeter

162.1 195.75		
Window	3' X 5'	<b>Opens into Exterior</b>
Window	3' X 5'	<b>Opens into Exterior</b>
Window	3' X 5'	<b>Opens into Exterior</b>
Window	3' X 5'	<b>Opens into Exterior</b>
Window	3' X 5'	<b>Opens into Exterior</b>
Window	3' X 5'	<b>Opens into Exterior</b>
Door	3' X 6' 8"	<b>Opens into Exterior</b>
Door	3' X 6' 8"	<b>Opens into Exterior</b>
Door	3' X 6' 8"	<b>Opens into HALL</b>
Door	3' X 6' 8"	<b>Opens into HALL</b>

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,720. R&R Crown molding - 2 1/4"	195.84 LF		0.39	1.98	0.00	464.14
2,721. Paint crown molding - two coats	195.84 LF		0.00	0.97	0.00	189.96
2,722. R&R Suspended ceiling grid - 2' x 2'	2,028.11 SF		0.12	1.19	0.00	2,656.82
2,723. Suspended ceiling tile - 2' x 2'	2,028.11 SF		0.00	1.23	0.00	2,494.58
2,724. Batt insulation - 6" - R19 - paper faced	2,028.11 SF		0.00	0.65	0.00	1,318.27
2,725. 1/2" drywall - hung, taped, ready for texture	983.38 SF		0.00	1.27	0.00	1,248.89
2,726. Batt insulation - 4" - R13 - paper faced	879.38 SF		0.00	0.50	0.00	439.69
2,727. R&R Additional cost for gluing drywall	200.00 SF		0.21	0.17	0.00	76.00
2,728. $1/2$ " - drywall per LF - up to 4' tall	24.00 LF		0.00	8.30	0.00	199.20
2,729. Texture drywall - heavy hand texture	1,566.75 SF		0.00	0.58	0.00	908.72
2,730. Seal/prime then paint the walls twice (3 coats)	1,566.75 SF		0.00	0.84	0.00	1,316.07
2,731. Casing - 2 1/4"	120.00 LF		0.00	1.24	0.00	148.80
2,732. Paint casing - two coats	120.00 LF		0.00	0.93	0.00	111.60
2,733. Casing - oversized - 3 1/4"	60.00 LF		0.00	1.82	0.00	109.20
2,734. Paint casing - oversized - two coats	60.00 LF		0.00	1.01	0.00	60.60
VICTORYCOSUB					12/13/2017	Page: 22





#### **CONTINUED - Large Banquet Hall**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,735. Baseboard - 3 1/4"	195.84 LF		0.00	1.94	0.00	379.93
2,736. Seal & paint baseboard - two coats	195.84 LF		0.00	0.98	0.00	191.92
2,737. R&R Light diffusing panel (i.e., cracked ice)	16.00 SF		0.11	1.43	0.00	24.64
2,738. Recessed light fixture - trim only	18.00 EA		0.00	15.75	0.00	283.50
2,739. Detach & Reset Fluorescent - acoustic grid fixture, 2' x 2'	8.00 EA	60.04	0.00	0.00	0.00	480.32
2,740. Exit sign - Detach & reset	1.00 EA		0.00	53.76	0.00	53.76
2,741. Clean window unit (per side) 10 - 20 SF	6.00 EA		0.00	8.32	0.00	49.92
2,742. Clean window blind - horizontal or vertical	90.00 SF		0.00	0.71	0.00	63.90
2,743. Paint door slab only - 2 coats (per side)	4.00 EA		0.00	24.16	0.00	96.64
2,744. Paint door or window opening - Large - 2 coats (per side)	2.00 EA		0.00	23.79	0.00	47.58
,745. Door dummy knob - Detach & eset	1.00 EA		0.00	4.61	0.00	4.6
2,746. Clean floor - tile	2,028.11 SF		0.00	0.36	0.00	730.12
2,747. Mask or cover per square foot	2,028.11 SF		0.25	0.00	0.00	507.03
2,748. Contents - move out then reset - Extra large room	1.00 EA		0.00	84.56	0.00	84.56
2,749. Final cleaning - construction - Commercial	2,028.11 SF		0.00	0.11	0.00	223.09
Totals: Large Banquet Hall					0.00	14,964.00
Total: Main Level					0.00	19,296.66
Total: Building # 51 - Sky Restaurant In	terior				0.00	19,296.66

#### **Building 52 - Fisher Stevens (43 Storehouse)**





Roof1

20,821.68 Surface Area 608.22 Total Perimeter Length 208.22 Number of Squares 200.00 Total Ridge Length

VICTORYCOSUB

12/13/2017

Page: 227



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### **CONTINUED - Roof1**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,754. R&R Metal roofing - ribbed - 26 gauge - 1 1/8" to 1 1/2"	20,821. SF 68		0.30	3.30	0.00	74,958.04
Note: 2 panels were damaged at the Sout the aged panels requires complete roof re		ted numerous fas	teners loosened du	se to the metal panels	being rusted. Th	e condition of
2,755. Remove Additional charge for high roof (2 stories or greater)	208.22 SQ	,	3.11	0.00	0.00	647.56
2,756. Additional charge for high roof (2 stories or greater)	208.22 SQ		0.00	9.91	0.00	2,063.46
2,757. R&R Ridge cap - metal roofing	200.00 LF	100	1.62	3.50	0.00	1,024.00
2,758. R&R Gable trim for metal roofing - 26 gauge	202.00 LF		0.49	3.73	0.00	852.44
2,759. Closure strips for metal roofing - inside and/or outside	800.00 LF		0.00	1.16	0.00	928.00
Totals: Roof1	The state of the s				0.00	80,473.50
Total: Roof					0.00	80,473.50

#### Exterior

#### Front / West Elevation

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Note: Several window panes broken from	what appeared to be	e bullets. These a	re not related and	were not included in	our scope of repo	uirs.
2,760. R&R Sectional overhead door, 10' x 12'	1.00 EA		49.01	964.26	0.00	1,013.27
Totals: Front / West Elevation			Aug.		0.00	1,013.27

#### **North Elevation**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,761. Reglaze window, 1 - 9 sf	13.00 EA		0.00	54.58	0.00	709.54
Totals: North Elevation					0.00	709.54

#### Rear / East Elevation

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
762. R&R Fascia - metal - 10"	200.00 LF		0.20	3.78	0.00	796.00
2,763. R&R Fascia - 1" x 8" - #2 pine	200.00 LF		0.20	4.00	0.00	840.00
VICTORYCOSUB					12/13/2017	Page: 228





#### **CONTINUED - Rear / East Elevation**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,764. R&R Downspout - box - galvanized - 6"	84.00 LF		0.30	6.79	0.00	595.56
2,765. R&R Gutter- box - galvanized - 6"	200.00 LF		0.30	6.79	0.00	1,418.00
2,766. R&R Wall/roof panel - ribbed - 29 gauge - up to 1"	4,200.00 SF		0.30	2.18	0.00	10,416.00
2,767. R&R Metal outside corner post	42.00 LF		0.74	4.08	0.00	202.44
2,768. R&R Metal J trim	408.00 LF		0.61	2.02	0.00	1,073.04
2,769. Carpenter - General Framer - per hour	4.00 HR		0.00	46.80	0.00	187.20
Note: Necessary to repair wood plank s.	heathing over which t	he metal panels o	are fastened.			
2,770. Reglaze window, 1 - 9 sf	63.00 EA		0.00	54.58	0.00	3,438.54
Totals: Rear / East Elevation					0.00	18,966.78

#### **South Elevation**

South Devation						
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,771. R&R Sectional overhead door, 12' x 14'	1.00 EA		49.01	1,245.90	0.00	1,294.91
2,772. Reglaze window, 1 - 9 sf	76.00 EA		0.00	54.58	0.00	4,148.08
2,773. R&R Fascia - 1" x 10" - #2 pine	20.00 LF		0.20	4.00	0.00	84.00
2,774. R&R Fascia - metal - 10"	22.00 LF		0.20	3.78	0.00	87.56
Totals: South Elevation					0.00	5,614.55
Total: Exterior					0.00	26,304.14
Total: Building 52 - Fisher Stevens (43 Storehouse)						106,777.64

#### Building 53 - Reliant Field Services Roof



#### Roof1

5,170.35 Surface Area 303.41 Total Perimeter Length 51.70 Number of Squares 100.00 Total Ridge Length





#### **CONTINUED - Roof1**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,780. R&R Metal roofing	77.00 SF		0.30	3.22	0.00	271.04
Note: Considers replacing (3) damaged	roof panels					
2,781. R&R Ridge cap - metal roofing	100.00 LF		1.62	3.50	0.00	512.00
2,782. Metal roofing	5,170.35 SF		0.00	0.20	0.00	1,034.07
Note: Inspect roof   fasteners and tighte	n or replace as neede	d.				
2,783. Closure strips for metal roofing inside and/or outside	36.00 LF		0.00	1.16	0.00	41.76
Totals: Roof1		,			0.00	1,858.87
Total: Roof					0.00	1,858.87

#### Exterior

#### **East Elevation**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
,784. R&R Gutter - box - galvanized - 6"	100.00 LF		0.30	6.79	0.00	709.00
2,785. R&R Downspout - box - galvanized - 6"	45.00 LF		0.30	6.79	0.00	319.05
2,786. Overhead Door Installer - per hour	2.00 HR		0.00	52.10	0.00	104.20
Note: To adjust and service sectional doc	or					
Totals: East Elevation					0.00	1,132.25

#### **North Elevation**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,787. Overhead Door Installer - per hour	2.00 HR		0.00	52.10	0.00	104.20
Note: To adjust and service sectional doc	or					
Totals: North Elevation					0.00	104.20
Total: Exterior					0.00	1,236.45
Total: Building 53 - Reliant Field Service	es				0.00	3,095.32

#### Building 54 - Townsend Remodeling(470 B Foster Field)

Roof





#### Roof1



3,098.04 Surface Area 248.85 Total Perimeter Length

30.98 Number of Squares 90.00 Total Ridge Length

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,792. Remove Tear off, haul and dispose of comp. shingles - 3 tab	30.98 SQ		32.50	0.00	0.00	1,006.85
2,793. Remove Additional layer of comp. shingles, remove (no haul off)	30.98 SQ		13.86	0.00	0.00	429.38
2,794. 3 tab - 25 yr composition shingle roofing - incl. felt	33.33 SQ		0.00	134.65	0.00	4,487.88
2,795. Drip edge	248.85 LF		0.00	1.30	0.00	323.51
2,796. Flashing - pipe jack	1.00 EA		0.00	23.34	0.00	23.34
2,797. Furnace vent - rain cap and storm collar, 5"	1.00 EA		0.00	45.01	0.00	45.01
Totals: Roof1					0.00	6,315.97
Total: Roof					0.00	6.315.97

#### Exterior

#### **North Elevation**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,798. Reglaze window, 1 - 9 sf	4.00 EA		0.00	54.58	0.00	218.32
Totals: North Elevation					0.00	218.32

#### Front / East Elevation

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,799. R&R Fascia - 1" x 8" - #1 pine	32.67 LF		0.20	4.62	0.00	157.47
2,800. Prime & paint exterior fascia - wood, 6"- 8" wide	33.00 LF		0.00	1.37	0.00	45.21
2,801. R&R Trim board - 1" x 2" - installed (pine)	8.00 LF		0.22	1.57	0.00	14.32
2,802. Seal & paint trim - two coats	8.00 LF		0.00	0.92	0.00	7.36





#### **CONTINUED - Front / East Elevation**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Totals: Front / East Elevation					0.00	224.36

#### **South Elevation**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,803. Reglaze window, 1 - 9 sf	1.00 EA		0.00	54.58	0.00	54.58
Note: Several asbestos siding panels as Totals: South Elevation	re broken and/or displ	aced. This appear	rs to be prior dame	age as some previous	0.00	54.58
Total: Exterior		14			0.00	497.26

#### Interior



#### **Rear Materials Room**

814.75 SF Walls 1,445.28 SF Walls & Ceiling 70.06 SY Flooring 237.38 SF Long Wall 101.84 LF Ceil. Perimeter

#### LxWxH 29' 8 1/16" x 21' 3" x 8'

630.53 SF Ceiling 630.53 SF Floor 101.84 LF Floor Perimeter 170.00 SF Short Wall

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,804. R&R 5/8" drywall - hung only (no tape or finish)	630.53 SF		0.24	0.98	0.00	769.25
2,805. R&R Batt insulation - 6" - R19 - paper faced	630.53 SF		0.17	0.65	0.00	517.03
2,806. Fluorescent light fixture - 2' & 4' - Detach & reset	2.00 EA		0.00	60.04	0.00	120.08
2,807. R&R Casing - 2 1/4"	20.00 LF		0.30	1.24	0.00	30.80
Note: Attic access casing						
2,808. Paint casing - two coats	20.00 LF		0.00	0.93	0.00	18.60
2,809. Final cleaning - construction - Commercial	630.53 SF		0.00	0.11	0.00	69.36
Totals: Rear Materials Room					0.00	1,525.12



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546



#### **Shop Paint Area**

#### LxWxH 24' x 19' 8 1/16" x 8'

698.75 SF Walls 1,170.88 SF Walls & Ceiling 52.46 SY Flooring 192.00 SF Long Wall 87.34 LF Ceil. Perimeter

472.13 SF Ceiling 472.13 SF Floor 87.34 LF Floor Perimeter 157.38 SF Short Wall



#### Subroom 1: Offset

#### LxWxH 12' x 10' 3" x 8'

356.00 SF Walls 479.00 SF Walls & Ceiling 13.67 SY Flooring 96.00 SF Long Wall 44.50 LF Ceil. Perimeter 123.00 SF Ceiling 123.00 SF Floor 44.50 LF Floor Perimeter 82.00 SF Short Wall

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,810. Drywall tape joint/repair - per LF	148.00 LF		0.00	4.64	0.00	686.72
2,811. Seal/prime then paint the ceiling twice (3 coats)	595.13 SF		0.00	0.84	0.00	499.91
2,812. Mask or cover per square foot	595.13 SF		0.25	0.00	0.00	148.78
2,813. Mask wall - plastic, paper, tape (per LF)	131.84 LF		0.00	0.82	0.00	108.11
2,814. Final cleaning - construction - Commercial	595.13 SF		0.00	0.11	0.00	65.46
Totals: Shop Paint Area					0.00	1,508.98
Total: Interior					0.00	3,034.10
Total: Building 54 - Townsend Remodeli	ing(470 B Foster Fie	eld)			0.00	9.847.33

Building 55 - Unamed (339 Foster Field)

DESCRIPTION

QTY

RESET REMOVE REPLACE

TAX

TOTAL

Note: Metal Storage building showed no visible damage.

Totals: Building 55 - Unamed (339 Foster Field)


0.00
0.00

Building 56 - LDS Builders (396 Foster Field)
Roof





#### Roof1



1,993.29 Surface Area 187.35 Total Perimeter Length 19.93 Number of Squares61.00 Total Ridge Length

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,817. Remove Tear off, haul and dispose of comp. shingles - Laminated	19.93 SQ		33.61	0.00	0.00	669.85
2,818. Laminated - comp. shingle rfg w/ felt	21.00 SQ		0.00	152.34	0.00	3,199.14
2,819. R&R Drip edge	187.35 LF		0.20	1.30	0.00	281.03
2,820. R&R Flashing - pipe jack	1.00 EA		4.14	23.34	0.00	27.48
2,821. Detach & Reset Roof vent - turbine type	3.00 EA	41.00	0.00	0.00	0.00	123.00
Totals: Roof1					0.00	4,300.50
Total: Roof					0.00	4,300.50

#### Exterior

#### Front / East Elevation

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,822. R&R Fascia - metal - 10"	61.00 LF		0.20	3.78	0.00	242.78
2,823. R&R Soffit - vinyl	72.00 SF		0.18	3.07	0.00	234.00
2,824. R&R Siding - vinyl	467.00 SF		0.26	2.78	0.00	1,419.68
2,825. R&R House wrap (air/moisture barrier)	467.00 SF		0.02	0.22	0.00	112.08
2,826. Exterior light fixture - Detach & reset	1.00 EA		0.00	61.40	0.00	61.40
2,827. Exterior faucet / hose bibb - Detach & reset	1.00 EA		0.00	44.44	0.00	44.44
2,828. Door numbers/letters - Detach & reset	1.00 EA		0.00	7.09	0.00	7.09
2,829. Casing - Detach & reset	17.00 LF		0.00	1.10	0.00	18.70
2,830. Paint casing - oversized - two coats	17.00 LF		0.00	1.01	0.00	17.17
Totals: Front / East Elevation					0.00	2,157.34





8380 Warren Parkway / Ste. 700 - Frisco, TX 75034

#### **North Elevation**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,831. R&R Siding - vinyl	312.00 SF		0.26	2.78	0.00	948.48
2,832. R&R House wrap (air/moisture barrier)	312.00 SF		0.02	0.22	0.00	74.88
2,833. Exterior light fixture - Detach & reset	1.00 EA		0.00	61.40	0.00	61.40
2,834. Exterior faucet / hose bibb - Detach & reset	1.00 EA		0.00	44.44	0.00	44.44
2,835. Door numbers/letters - Detach & reset	1.00 EA		0.00	7.09	0.00	7.09
2,836. Casing - Detach & reset	18.00 LF		0.00	1.10	0.00	19.80
2,837. R&R Casing - oversized - 3 1/4" hardwood	20.00 LF		0.30	2.23	0.00	50.60
2,838. Paint casing - oversized - two coats	38.00 LF	_ )	0.00	1.01	0.00	38.38
Totals: North Elevation					0.00	1,245.07
Total: Exterior					0.00	3,402.41

#### Interior



#### **Work Shop**

1,431.83 SF Walls 2,559.83 SF Walls & Ceiling 125.33 SY Flooring 473.92 SF Long Wall 142.00 LF Ceil. Perimeter

#### LxWxH 47' x 24' x 10' 1"

1,128.00 SF Ceiling 1,128.00 SF Floor 142.00 LF Floor Perimeter 242.00 SF Short Wall

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,839. 5/8" drywall - hung, taped, ready for texture	2,559.83 SF		0.00	1.37	0.00	3,506.97
Note: Considers overlaying 1/4" plywoo	d with drywall. The p	olywood has buck	led.			
2,840. Seal/prime then paint the walls and ceiling twice (3 coats)	2,559.83 SF		0.00	0.84	0.00	2,150.26
2,841. Fluorescent light fixture - 2' & 4' - Detach & reset	5.00 EA		0.00	60.04	0.00	300.20
2,842. Outlet or switch - Detach & reset	9.00 EA		0.00	14.83	0.00	133.47
2,843. Overhead door - Detach & reset	1.00 EA		0.00	203.95	0.00	203.95
2.844. Contents - move out then reset - Extra large room	1.00 EA		0.00	84.56	0.00	84.56





#### **CONTINUED - Work Shop**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,845. Final cleaning - construction - Commercial	1,128.00 SF		0.00	0.11	0.00	124.08
2,846. Mask or cover per square foot	1,128.00 SF		0.25	0.00	0.00	282.00
Totals: Work Shop			1		0.00	6,785.49



#### Storage Area/Room


#### LxWxH 11' 8 1/16" x 10' 2 1/16" x 8'

349.50 SF Walls 468.23 SF Walls & Ceiling 13.19 SY Flooring 93.38 SF Long Wall 43.69 LF Ceil. Perimeter 118.73 SF Ceiling 118.73 SF Floor

43.69 LF Floor Perimeter 81.38 SF Short Wall



#### LxWxH 3' 11 3/8" x 2' 5 1/16" x 8'



9.56 SF Ceiling9.56 SF Floor


12.74 LF Floor Perimeter 19.38 SF Short Wall

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,847. Seal/prime then paint the ceiling twice (3 coats)	128.29 SF		0.00	0.84	0.00	107.76
2,848. Contents - move out then reset - Large room	1.00 EA	\ /	0.00	42.27	0.00	42.27
2,849. Mask wall - plastic, paper, tape (per LF)	56.43 LF		0.00	0.82	0.00	46.27
2,850. Final cleaning - construction - Commercial	128.29 SF	1	0.00	0.11	0.00	14.11
2,851. Mask or cover per square foot	128.29 SF		0.25	0.00	0.00	32.07
Totals: Storage Area/Room	-	3			0.00	242.48
Total: Interior					0.00	7,027.97
Total: Building 56 - LDS Builders (396 F	Foster Field)				0.00	14,730.88

Building 57 - Straight Arrow Archery Roof



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546



#### Roof1

10,360.97 Surface Area 428.01 Total Perimeter Length 103.61 Number of Squares 140.00 Total Ridge Length

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,854. R&R Eave trim for metal roofing - 26 gauge	37.00 LF		0.49	3.43	0.00	145.04
Note: Southeast Corner						
2,855. Metal roofing	10,360. SF 97		0.00	0.20	0.00	2,072.19
Note: Inspect entire roof and replace	fasteners as needed.					
Totals: Roof1					0.00	2.217.23

#### **Porch Roof**



358.61 Surface Area 105.40 Total Perimeter Length 3.59 Number of Squares

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,856. Remove Tear off, haul and dispose of 3 ply built-up roofing	3.59 SQ		33.07	0.00	0.00	118.72
2,857. Built-up 3 ply roofing - in place	3.59 SQ		0.00	195.56	0.00	702.06
2,858. R&R Fiberboard - 1"	358.61 SF		0.26	0.65	0.00	326.34
2,859. R&R Built-up roofing - gravel ballast	3.59 SQ		35.06	23.44	0.00	210.02
2,860. R&R Aluminum sidewall/endwall flashing - color finish	45.00 LF		0.34	5.03	0.00	241.65
Totals: Porch Roof					0.00	1,598.79
Total: Roof					0.00	3,816.02

#### Exterior

#### **South Elevation**





#### **CONTINUED - South Elevation**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,861. R&R Sectional overhead door, 12' x 12'	1.00 EA		49.01	1,073.95	0.00	1,122.96
2,862. 2" x 6" lumber (1 BF per LF)	90.00 LF		0.00	1.73	0.00	155.70
Note: Wall studs & bracing @ overhead of	loor.					
2,863. Header - double 2" x 10"	12.00 LF		0.00	5.40	0.00	64.80
2,864. Carpenter - General Framer - per hour	6.00 HR		0.00	46.80	0.00	280.80
Note: Cost to re-frame the stud wall arou	and the overhead do	or.				
2,865. Jamb and trim for overhead door unit	35.00 LF		0.00	4.43	0.00	155.05
2,866. Door opening (jamb & casing) - 60" or wider - paint grade	1.00 EA		0.00	100.72	0.00	100.72
Totals: South Elevation					0.00	1,880.03
Total: Exterior					0.00	1,880.03
Total: Building 57 - Straight Arrow Arche	егу				0.00	5,696.05

# Building 58 - Celebration Church / UHV Apartments Roof

#### Roof1



9,706.00 Surface Area 514.00 Total Perimeter Length 97.06 Number of Squares

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,869. Remove Built-up roofing - gravel ballast	1,028.00 SF		0.35	0.00	0.00	359.80
Note: Considers sweeping back ballast a	pproximately 2' from	the perimeter to	allow for replacen	nent of the damaged g	ravel stop.	
2,870. Install Built-up roofing - gravel ballast	1,028.00 SF		0.00	0.13	0.00	133.64
2,871. R&R Built-up 3 ply roofing - in place	11.00 SQ		33.07	195.56	0.00	2,514.93
<b>Note:</b> Considers sweeping back the grav to tie in to existing roof.	vel 2' from the perime	ter to allow repa	ir of the gravel sto	p and replace the bui	t-up roofing 2'	from the edge
2,872. R&R Gravel stop	514.00 LF		0.20	1.18	0.00	709.32
2,873. Additional charge for high roof (2 stories or greater)	11.00 SQ		0.00	9.91	0.00	109.01



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### **CONTINUED - Roof1**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Totals: Roof1					0.00	3,826.70
Γotal: Roof						3,826.70
Total: Roof  Total: Building 58 - Celebration Church / UHV Apartments			0.00	3,826.70		

## **Building 59 - Fire Marshall's Storage (354 Hangar)**

#### Roof

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Note: No visible damage to the 3 pl	y Built-Up w/ aluminum s	eal.	\			
Totals: Roof			1		0.00	0.00

#### **Exterior / South Elevation**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,879. Reglaze window, 10 - 16 sf	1.00 EA	- Total	0.00	97.05	0.00	97.05
2,880. Reglaze window, 1 - 9 sf	2.00 EA		0.00	54.58	0.00	109.16
Totals: Exterior / South Elevation					0.00	206.21

#### Interior


DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Note: Substantial pre-existing wo						
Totals: Interior		0.00	0.00			
Total: Building 59 - Fire Marshall	l's Storage (354 Hangar)			<del>-</del>	0.00	206.21

**Building 60 - Vacant (479 Waco Circle)** 

Roof



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546



#### Roof1

6,997.42 Surface Area539.00 Total Perimeter Length

69.97 Number of Squares

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,882. Remove Tear off, haul and dispose of 3 ply built-up roofing	69.97 SQ		33.07	0.00	0.00	2,313.91
2,883. Built-up 3 ply roofing - in place	69.97 SQ		0.00	195.56	0.00	13,683.33
2,884. Aluminum coating - with fiber	6,997.42 SF		0.00	0.50	0.00	3,498.71
2,885. R&R Flashing - pipe jack	5.00 EA		4.14	23.34	0.00	137.40
2,886. R&R Gravel stop	539.00 LF		0.20	1.18	0.00	743.82
2,887. Concrete Roof Deck Repair - Labor and Material	9.00 EA		0.00	140.00	0.00	1,260.00
Note: Repair of (9) holes in the 2" conci	rete deck.					
2.888. Fiberboard - 1"	6.997.42 SF		0.00	0.65	0.00	4548.32

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

2,889. Insulation - ISO board, 3"

69.97 SQ

0.00

218.42

0.00

15,282.85

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

2.890. Insulation - ISO board, 4"

34.99 SQ

0.00

266.88

0.00

9,338.13

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

Note: Considers tapered insulation to comply with 1/4" per foot drainage requirements.

2,891. 2" x 6" lumber (1 BF per LF)

1.078:00 LF

0.00

1.73

0.00

1.864.94

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

Note: Double perimeter band (3") installed to fasten perimeter coping after installation of insulation.

2.892. Steel wall coping

539.00 LF

0.00

9.37

0.00

5.050.43

21,637.17

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

Totals: Roof1 0.00



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546



#### Metal

434.79 Surface Area59.35 Total Perimeter Length

4.35 Number of Squares

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,893. R&R Wall/roof panel - ribbed - 26 gauge - 1 1/8" to 1 1/2"	434.79 SF		0.30	2.48	0.00	1,208.72
2,894. R&R Batt insulation - 6" - R19 - paper faced	434.79 SF		0.17	0.65	0.00	356.52
2,895. R&R Endwall flashing for metal roofing - 26 gauge	16.00 LF		0.55	4.10	0.00	74.40
2,896. R&R Gable trim for metal roofing - 26 gauge	24.00 LF		0.49	3.73	0.00	101.28
2,897. Counter battens - 1x4 - for steel roofing	4.35 SQ		0.00	59.06	0.00	256.91
Totals: Metal					0.00	1,997.83
Total: Roof					0.00	23,635.00

#### Interior

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
<b>Note:</b> No emergency services were intrusion.	performed to the interior of	and we did not in	spect for damages	. We did identify consi	iderable pre-exis	ting water
Totals: Interior					0.00	0.00
Total: Ruilding 60 - Vacant (479 V	Vaco Circle)	1			0.00	23,635,00

# Building 61 - Golden Crescent / GCRP (568 Waco Circle)

#### Roof

# Roof1 F1 F-28,4\*-1 ROUGE LD ROUGE G

#### Roof1

7,881.97 Surface Area 567.04 Total Perimeter Length 78.82 Number of Squares



Totals: Roof1

8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### CONTINUED - Roof1

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Note: The lower extensions showed no a	lamage.					
2,902. Remove Tear off, haul and dispose of 3 ply built-up roofing	78.82 SQ		33.07	0.00	0.00	2,606.58
2,903. Built-up 3 ply roofing - in place	78.82 SQ		0.00	195.56	0.00	15,414.04
2,904. R&R Fiberboard - 1/2"	7,881.97 SF		0.26	0.56	0.00	6,463.21
2,905. Aluminum coating - with fiber	7,881.97 SF		0.00	0.50	0.00	3,940.99
2,906. R&R Gravel stop	567.04 LF		0.20	1.18	0.00	782.52
2,907. R&R Curb flashing -bitumen	12.00 LF		1.10	12.22	0.00	159.84
2,908. Sheathing - spaced 1" x 8"	567.04 SF		0.00	2.59	0.00	1,468.63
Note: Repair of plank decking. 1/3 of pe	rimeter x 3' in from e	dge.				
2,909. R&R Flashing - pipe jack	7.00 EA		4.14	23.34	0.00	192.36
2,910. R&R Furnace vent - rain cap and storm collar, 5"	2.00 EA	-	6.30	45.01	0.00	102.62
2.911. Insulation - ISO board, 3 1/2"	78.82 SQ		0.00	248.82	0.00	19,611.99
2011 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	1 1 6			t dos		

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

912. Insulation - ISO board, 4" 39.41 SQ 0.00 266.88 0.00 10.517.74

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

Note: Considers tapered insulation to comply with 1/4" per foot drainage requirements.

2.913. 2" x 6" lumber (1 BF per LF) 1,134.08 LF 0.00 1.73 0.00 1.961.96

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

Note: Double perimeter band (3") installed to fasten perimeter coping after installation of insulation.

2.914. Steel wall coping 567.04 LF 0.00 9.37 0.00 5.313.16

This item did not previously exist or expands the scope of repairs, but is required by current building codes. The code upgrade cost is payable when incurred, subject to limits.

2,915. Remove Additional charge for 78.82 SQ 3.11 0.00 0.00 245.13

high roof (2 stories or greater)

2,916. Additional charge for high roof (2 stories or greater)

(2 stories or greater)

78.82 SQ

0.00

9.91

0.00

781.11

Total: Roof 0.00 32,157.03

0.00

32,157.03

#### **Exterior / Rear East Elevation**



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### **CONTINUED - Exterior / Rear East Elevation**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,917. Reglaze window, 1 - 9 sf	2.00 EA		0.00	54.58	0.00	109.16
Totals: Exterior / Rear East Elevation					0.00	109.16

#### Interior

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL

Note: No emergency services were performed to the interior and we did not inspect for damages. It is probable that interior water damage has occurred.


Totals: Interior	0.00	0.00
Total: Building 61 - Golden Crescent / GCRP (568 Waco Circle)	0.00	32,266.19

Total: Building 61 - Golden Crescent / GCRP (568 Waco Circle)

## Building 62 - Texas Mile Warehouse (131 Hangar)

#### Roof

#### Roof1



VICTORYCOSUB

10,953.03 Surface Area 450.25 Total Perimeter Length 109.53 Number of Squares 154.00 Total Ridge Length


12/13/2017

Page: 243

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,923. R&R Metal roofing	1,050.00 SF		0.30	3.22	0.00	3,696.00
Note: Damage extends back 15" from th	e South gable along l	both rakes.				
2,924. R&R Furnace vent - rain cap and storm collar, 5"	2.00 EA		6.30	45.01	0.00	102.62
2,925. R&R Gable trim for metal roofing - 26 gauge	70.00 LF		0.49	3.73	0.00	295.40
Note: Both South rakes only.						
2,926. R&R Eave trim for metal roofing - 26 gauge	10.00 LF		0.49	3.43	0.00	39.20
Note: East corner to match existing.						
2,927. R&R Ridge cap - metal roofing	154.00 LF		1.62	3.50	0.00	788.48
2,928. Metal roofing	9,903.03 SF		0.00	0.20	0.00	1,980.61
Note: Inspect remaining roof panels ar	nd replace fasteners a	is needed.				
Totals: Roof1					0.00	6,902.31



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546



## Canopy / South Elevation

183.99 Surface Area38.65 Total Perimeter Length

1.84 Number of Squares

•						
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,929. Remove Tear off, haul and dispose of comp. shingles - 3 tab	1.84 SQ		32.50	0.00	0.00	59.80
2,930. 3 tab - 25 yr composition shingle roofing - incl. felt	2.00 SQ		0.00	134.65	0.00	269.30
2,931. R&R Sheathing - spaced 1" x 8"	183.99 SF		0.36	2.59	0.00	542.77
2,932. R&R Rafters - 2x6 - 24" OC (3-5/12 Gable, per SF of floor)	183.99 SF		0.47	1.49	0.00	360.63
2,933. Step flashing	17.00 LF		0.00	5.59	0.00	95.03
2,934. R&R Coping - color finish	38.00 LF		0.34	2.63	0.00	112.86
2,935. R&R Timber post, 6x6	30.00 LF		2.20	15.59	0.00	533.70
Note: (3) posts 10 l.f. each						
2,936. R&R Header - double 2" x 10"	17.00 LF		4.54	5.40	0.00	168.98
2,937. R&R 2" x 8" ledger(1.33 BF per LF)	17.00 LF		0.48	1.94	0.00	41.14
Totals: Canopy / South Elevation					0.00	2,184.21
Total: Roof					0.00	9,086.52

#### **Exterior / South Elevation**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,938. R&R Exterior door - double - metal - insul flush or panel	1.00 EA	Remove	12.60	407.62	0.00	420.22
2,939. Paint door slab only - 2 coats (per side)	4.00 EA		0.00	24.16	0.00	96.64
2,940. Paint door or window opening - Large - 2 coats (per side)	1.00 EA		0.00	23.79	0.00	23.79
2,941. Door lockset - Detach & reset	2.00 EA		0.00	13.17	0.00	26.34
Totals: Exterior / South Elevation					0.00	566.99

Interior



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546



#### Storage Area/Room

LxWxH 69' x 61' x 14'

3,640.00 SF Walls 7,849.00 SF Walls & Ceiling 467.67 SY Flooring 966.00 SF Long Wall 260.00 LF Ceil. Perimeter

4,209.00 SF Ceiling 4,209.00 SF Floor 260.00 LF Floor Perimeter 854.00 SF Short Wall

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,942. R&R 1/2" water rock (greenboard) hung, taped ready for texture	4,209.00 SF		0.24	1.35	0.00	6,692.31
2,943. Additional cost for high wall or ceiling - Over 14'	4,209.00 SF		0.00	0.04	0.00	168.36
2,944. Seal/prime then paint the ceiling twice (3 coats)	4,209.00 SF		0.00	0.84	0.00	3,535.56
2,945. Contents - move out then reset - Extra large room	1.00 EA		0.00	84.56	0.00	84.56
2,946. Mask or cover per square foot	4,209.00 SF		0.25	0.00	0.00	1,052.25
2,947. Final cleaning - construction - Commercial	4,209.00 SF	- M	0.00	0.11	0.00	462.99
Totals: Storage Area/Room					0.00	11,996.03




#### Office

LxWxH 12' x 11' 6" x 9'

423.00 SF Walls 561.00 SF Walls & Ceiling 15.33 SY Flooring 108.00 SF Long Wall 47.00 LF Ceil. Perimeter 138.00 SF Ceiling 138.00 SF Floor 47.00 LF Floor Perimeter 103.50 SF Short Wall

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,948. R&R 3/4" BC plywood	138.00 SF		0.77	1.55	0.00	320.16
2,949. Stain & finish plywood ceiling	138.00 SF		0.00	1.06	0.00	146.28
2,950. Light fixture - Detach & reset	1.00 EA		0.00	41.36	0.00	41.36
2,951. R&R Crown molding - 2 1/4"	47.00 LF		0.39	1.98	0.00	111.39
2,952. Stain & finish crown molding	47.00 LF		0.00	1.09	0.00	51.23
2,953. Contents - move out then reset	1.00 EA		0.00	28.18	0.00	28.18
2,954. Final cleaning - construction - Commercial	138.00 SF		0.00	0.11	0.00	15.18
2,955. Mask or cover per square foot	138.00 SF		0.25	0.00	0.00	34.50



erminal

8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

		CONTINUED	- Office			
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Totals: Office					0.00	748.28
Total: Interior					0.00	12,744.31
Total: Building 62 - Texas Mile Wareho	use (131 Hangar)				0.00	22,397.8
Building 63 - Condemned (H&H E		Condemned (Ho	&H Door) Ware	ehouse		
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Note: Because this building is condemne	ed, we did not inspect	the roof nor inte	rior. We did note s	ome roof damage wit	h probable interi	or damage.
Total: Building 63 - Condemned (H&H	Door) Warehouse				0.00	0.00
	$\wedge$	Exterior	1	1		_
	Coorei	ty Fencing / So		/	1	
Security Fencing / South Elevation	1	ty rending / So	outh Elevation			
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	тоты
2,961. R&R Post - 27/8" diameter metal - 8' high fence	46.80 EA		8.82	41.42	0.00	2,311.0
Note: Actual posts were 2 7/8" diameter	x 10' height. (8' heig	ht above ground	and 2' in the groun			
2,962. R&R Angle - L 1 1/2" x 1 1/2" x 1/4" thick	138.00 LF		0.83	4.26	0.00	702.4
Note: (3) 1' steel brackets welded to each		4" battens. (46 pd			1	
2,963. R&R Carriage bolt - 3/8" x 2 1/2"	276.00 EA		0.00	0.60	0.00	165.6
Note: Used to secure 2"x4" battens to st	eel brackets. (6 per p	ost x 46 posts)		W T	/	130.7
2,964. R&R 2" x 4" lumber - treated (. 667 BF per LF)	1,428.00 LF		0.31	1.66	0.00	2,813.1
Note: Treated 2"x4" battens placed 2'-6	" apart. (3 x full peri	meter of 476 l.f.)				
2,965. R&R Wall/roof panel - ribbed - 26 gauge - 1 1/8" to 1 1/2"	3,808.00 SF		0.30	2.48	0.00	10,586.2
Note: Solid metal panels 8' height aroun	nd the full perimeter.					
Total: Security Fencing / South Elevation	on				0.00	16,578.4
			11			
Gat	es		4	William Committee of the Committee of th		
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,966. R&R Post - 3" diameter metal -	4.00 EA	1	8.82	57.42	0.00	264.9

12/13/2017 Page: 246 VICTORYCOSUB



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### **CONTINUED - Gates**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,967. R&R Steel pipe fence/ gate - 6' high - rolling- metal panels	100.00 LF		2.45	60.24	0.00	6,269.00
Note: (2) 6' HGT gates x 50' each, cantile cable braces.	evered over (4) rolle	r wheels. The gat	es are constructed	of 2 3/8" steel pipe, r	einforced with a	djustable
Totals: Gates					0.00	6,533.96
Total: Security Fencing / South Elevation					0.00	23,112.42
Total: Exterior		V.			0.00	23,112.42
Total: Building 63 - Condemned (H&H I	Door) Warehouse				0.00	23,112.42

#### **Building 64 - Civil Air Patrol (381 Hangar)**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL

Note: Our inspection found no damage by wind to the Built-Up roof w/ Aggregate. There is need of maintenance as considerable deterioration was noted.

The interior has suffered substantial water damage to the ceiling tiles and drywall walls & ceilings over a long period of time. the damage appeared to be pre-existing to this event.

- We noted some potential asbestos floor tile present.

Totals: Building 64 - Civil Air Patrol (381 Hangar)

0.00

0.00

#### **Building 65 - Old Brig (153 Corpus Christi)**

#### **Building 65 - Old Brig (153 Corpus Christi)**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
<b>Note:</b> This is an all masonry structure reported.	re, which would not have	been affected by	water intrusion. W	Ve did not inspect the i	interior as no dan	nage was
Total: Building 65 - Old Brig (153 (	Corpus Christi)				0.00	0.00

#### Roof

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
Note: The roof consists of built-up w/ as the gravel guard listed below.	ggregate over 50% an	nd exposed built-u	up on the remainde	r. We found no visible	damage to the re	oof except
2,972. Remove Built-up roofing - gravel ballast	30.00 SF		0.35	0.00	0.00	10.50
Note: Considers sweeping back ballast	approximately 2' from	the perimeter to	allow for replacen	nent of the damaged g	ravel stop.	
2,973. Install Built-up roofing - gravel ballast	30.00 SF		0.00	0.13	0.00	3.90



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546


#### **CONTINUED - Roof**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,974. R&R Built-up 3 ply roofing - in place	1.00 SQ		33.07	195.56	0.00	228.63
<b>Note:</b> Considers sweeping back the grave to tie in to existing roof.	l 2' from the perime	ter to allow repa	ir of the gravel sto	p and replace the buil	lt-up roofing 2' fi	rom the edge
2,975. R&R Steel wall coping	10.00 LF		0.34	9.37	0.00	97.10
2,976. R&R Gravel stop	10.00 LF		0.20	1.18	0.00	13.80
Totals: Roof					0.00	353.93

# Exterior / Fencing (South & West Elevations)

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,977. R&R Chain link fence w/posts & top rail - 12' high - 9 gauge	380.00 LF		2.94	33.84	0.00	13,976.40
Note: Heavy gauge security fence with 2' (200 l.f. along the East side and 180 l.)						
,978. R&R Barbed wire - 3 strands mounted on wire arm	760.00 LF		0.41	1.39	0.00	1,368.00
Note: A triple run facing both directions	(2 applications)					
Totals: Exterior / Fencing (South & Wes	st Elevations)				0.00	15,344.40
Total: Building 65 - Old Brig (153 Corpu	s Christi)				0.00	15.698.33

### Building 66 - Old Dorm Building (294 Foster Field)

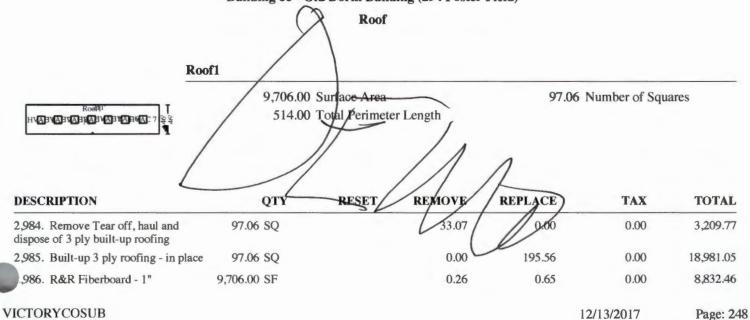






#### **CONTINUED - Roof1**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,987. Aluminum coating - with fiber	9,706.00 SF		0.00	0.50	0.00	4,853.00
2,988. R&R Gravel stop	514.00 LF		0.20	1.18	0.00	709.32
2,989. R&R Curb flashing -bitumen	404.00 LF	X	1.10	12.22	0.00	5,381.28
2,990. Sheathing - spaced 1" x 8"	685.00 SF		0.00	2.59	0.00	1,774.15
Note: Repair of plank decking.	/	// \				
2,991. R&R Flashing - pipe jack	6.00 EA	\ ;	4.14	23.34	0.00	164.88
2,992. Exhaust cap - through flat roof	6.00 EA	\ /	0.00	77.26	0.00	463.56
2,993. Insulation - ISO board, 3 1/2"	97.06	1/	0.00	248.82	0.00	24,150.47
This item did not previously exist or experienced, subject to limits.	ands the scope of rep	airs, but is require	ed by current build	ling codes. The code u	pgrade cost is pa	ayable when
2,994. Insulation - ISO board, 4"	4×53 SQ		100	266.88	0.00	12,951.69
This item did not previously exist or expanding the control of the	ands the scope of rep	airs, but is require	ed by carrent Muile	ling oodes. The code i	ipgrade cost is pa	ayable when
This item did not previously exist or expiniourred, subject to limits.	ands the scope of rep	airs, but is require	by current build	ling codes. The code i	ipgrade cost is po	ayable when
Note: Considers tapered insulation to co	mply with 1/4" per fo	oot drainage requ	irements.	// /		
995. 2" x 6" lumber (1 BF per LF)	1.028.00 LF		0.00	/ /-73	0.00	1.778.44
This item did not previously exist or expincurred, subject to limits.	ands the scope of rep	airs, but is require	ed by current build	ling codes. The code t	ipgrade cost is pa	ayable when
Note: Double perimeter band (3") instal	led to fasten perimete	er coping after ins	stallation of insula	ation.		
2,996. Steel wall coping	514.00 LF		0.00	9.37	0.00	4,816.18
This item did not previously exist or exp incurred, subject to limits.	ands the scope of rep	airs, but is require	ed by current build	ding codes. The code i	apgrade cost is po	ayable when
2,997. Remove Additional charge for	97.06 SQ		3.11	0.00	0.00	301.86
high roof (2 stories or greater)			0.00	9.91	0.00	961.86
high roof (2 stories or greater)  2,998. Additional charge for high roof (2 stories or greater)	97.06 SQ		0.00			



HVAC 1 Height: 7'

317.33 SF Walls 445.78 SF Walls & Ceiling 14.27 SY Flooring 45.33 LF Ceil. Perimeter

128.44 SF Floor45.33 LF Floor Perimeter


128.44 SF Ceiling

DESCRIPTION QTY RESET REMOVE REPLACE TAX TOTAL



#### **CONTINUED - HVAC 1**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
2,999. Remove Exhaust fan - Commercial - rooftop	1.00 EA		172.00	0.00	0.00	172.00
Note: Cost to terminate and remove the e.	xhaust vents from th	ne roof using a cra	ine.			
3,000. R&R Rafters - 2x6 - 24" OC (3-5/12 Gable, per SF of floor)	128.44 SF		0.47	1.49	0.00	251.75
3,001. R&R Sheathing - spaced 1" x 6"	128.44 SF	$\wedge$	0.36	2.06	0.00	310.83
3,002. Metal roofing - ribbed - 26 gauge - 1 1/8" to 1 1/2"	176.44 SF	$\langle \rangle$	0.00	3.30	0.00	582.25
3,003. R&R Fascia - metal - 8"	45.33 LF		0.20	3.35	0.00	160.93
3,004. R&R Stud wall - 2" x 6" x 8' - 24" oc	45.33 LF		1.29	16.25	0.00	795.09
3,005. R&R Sheathing - spaced 1" x 8"	317.33 SF	1>	0.36	2.59	0.00	936.12
3,006. R&R Fiber cement lap siding - 12"	317.33 SF		0.26	2.62	0.00	913.91
3,007. Seal/prime then paint the walls twice (3 coats)	317.33 SF		0.00	0.84	0.00	266.56
3,008. R&R Trim board - 1" x 4" - installed (pine)	56.00 LF		0.23	2.15	0.00	133.28
,009. Seal & paint trim - two coats	56.00 LF		0.00	0.92	0.00	51.52
3,010. R&R Greenhouse door and frame	1.00 EA	4	4.42	500.01	0.00	504.43
3,011. Paint door slab only - 2 coats (per side)	1.00 EA		0.007	24.16	0.00	24.16
Totals: HVAC 1					0.00	5,102.83



**HVAC 2** Height: 7'

> 317.33 SF Walls 445.78 SF Walls & Ceiling

14.27 SY Flooring

45.33 LF Ceil. Perimeter

128.44 SF Ceiling

128.44 SF Floor

45.33 LF Floor Perimeter

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
3,012. Remove Exhaust fan - Commercial - rooftop	1.00 EA		172.00	0.00	0.00	172.00
Note: Cost to terminate and remove the e	xhaust vents from th	ne roof using a cro	ane.			
3,013. R&R Rafters - 2x6 - 24" OC (3-5/12 Gable, per SF of floor)	128.44 SF		0.47	1.49	0.00	251.75
3,014. R&R Sheathing - spaced 1" x 6"	128.44 SF		0.36	2.06	0.00	310.83


12/13/2017 Page: 250 **VICTORYCOSUB** 



#### **CONTINUED - HVAC 2**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
3,015. Metal roofing - ribbed - 26 gauge - 1 1/8" to 1 1/2"	176.44 SF		0.00	3.30	0.00	582.25
3,016. R&R Fascia - metal - 8"	45.33 LF		0.20	3.35	0.00	160.93
3,017. R&R Stud wall - 2" x 6" x 8' - 24" oc	45.33 LF		1.29	16.25	0.00	795.09
3,018. R&R Sheathing - spaced 1" x 8"	317.33 SF		0.36	2.59	0.00	936.12
3,019. R&R Fiber cement lap siding - 12"	317.33 SF		0.26	2.62	0.00	913.91
3,020. Seal/prime then paint the walls twice (3 coats)	317.33 SF		0.00	0.84	0.00	266.56
3,021. R&R Trim board - 1" x 4" - installed (pine)	56.00 LF		0.23	2.15	0.00	133.28
3,022. Seal & paint trim - two coats	56.00 LF	1 1	0.00	0.92	0.00	51.52
3,023. R&R Greenhouse door and frame	1.00 EA	12	4.42	500.01	0.00	504.43
3,024. Paint door slab only - 2 coats (per side)	1.00 EA	1/	0.00	24.16	0.00	24.16
Totals: HVAC 2			11	1	0.00	5,102.83

Height: 7'



317.33 SF Walls

**HVAC 3** 

445.78 SF Walls & Ceiling

14.27 SY Flooring

45.33 LF Ceil. Perimeter

128.44 SF Ceiling 128.44 SF Floor 45.33 LF Floor Perimeter

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
3,025. Remove Exhaust fan - Commercial - rooftop	1.00 EA		172.00	0.00	0.00	172.00
Note: Cost to terminate and remove the e	xhaust vents from th	e roof using a cr	ane.			
3,026. R&R Rafters - 2x6 - 24" OC (3-5/12 Gable, per SF of floor)	128.44 SF		0.47	1.49	0.00	251.75
3,027. R&R Sheathing - spaced 1" x 6"	128.44 SF		0.36	2.06	0.00	310.83
3,028. Metal roofing - ribbed - 26 gauge - 1 1/8" to 1 1/2"	176.44 SF		0.00	3.30	0.00	582.25
3,029. R&R Fascia - metal - 8"	45.33 LF		0.20	3.35	0.00	160.93
3,030. R&R Stud wall - 2" x 6" x 8' - 24" oc	45.33 LF		1.29	16.25	0.00	795.09
3,031. R&R Sheathing - spaced 1" x 8"	317.33 SF		0.36	2.59	0.00	936.12



#### **CONTINUED - HVAC 3**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
3,032. R&R Fiber cement lap siding - 12"	317.33 SF		0.26	2.62	0.00	913.91
3,033. Seal/prime then paint the walls twice (3 coats)	317.33 SF		0.00	0.84	0.00	266.56
3,034. R&R Trim board - 1" x 4" - installed (pine)	56.00 LF		0.23	2.15	0.00	133.28
3,035. Seal & paint trim - two coats	56.00 LF		0.00	0.92	0.00	51.52
3,036. R&R Greenhouse door and frame	1.00 EA	/	4.42	500.01	0.00	504.43
3,037. Paint door slab only - 2 coats (per side)	1.00 EA		0.00	24.16	0.00	24.16
Totals: HVAC 3					0.00	5,102.83

HVAC 4



317.33 SF Walls

445.78 \$F Walls & Ceiling

14.27 SY Flooring

45.33 LF Ceil. Perimeter

Height: 7'

128.44 SF Ceiling 128.44 SF Floor

45.33 LF Floor Perimeter

DESCRIPTION	QTY	RESET	REMOVE	REPLACE)	TAX	TOTAL
3,038. Remove Exhaust fan - Commercial - rooftop	1.00 EA		172.00	0.00	0.00	172.00
Note: Cost to terminate and remove the e.	xhaust vents from th	e roof using a cro	ine.			
3,039. R&R Rafters - 2x6 - 24" OC (3-5/12 Gable, per SF of floor)	128.44 SF		0.47	1.49	0.00	251.75
3,040. R&R Sheathing - spaced 1" x 6"	128.44 SF		0.36	2.06	0.00	310.83
3,041. Metal roofing - ribbed - 26 gauge - 1 1/8" to 1 1/2"	176.44 SF		0.00	3.30	0.00	582.25
3,042. R&R Fascia - metal - 8"	45.33 LF		0.20	3.35	0.00	160.93
3,043. R&R Stud wall - 2" x 6" x 8' - 24" oc	45.33 LF		1.29	16.25	0.00	795.09
3,044. R&R Sheathing - spaced 1" x 8"	317.33 SF		0.36	2.59	0.00	936.12
3,045. R&R Fiber cement lap siding - 12"	317.33 SF		0.26	2.62	0.00	913.91
3,046. Seal/prime then paint the walls twice (3 coats)	317.33 SF		0.00	0.84	0.00	266.56
3,047. R&R Trim board - 1" x 4" - installed (pine)	56.00 LF		0.23	2.15	0.00	133.28
,048. Seal & paint trim - two coats	56.00 LF		0.00	0.92	0.00	51.52

Page: 252 12/13/2017 VICTORYCOSUB






#### **CONTINUED - HVAC 4**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
3,049. R&R Greenhouse door and frame	1.00 EA		4.42	500.01	0.00	504.43
3,050. Paint door slab only - 2 coats (per side)	1.00 EA		0.00	24.16	0.00	24.16
Totals: HVAC 4					0.00	5,102.83

HVA	C5 -		_			Height: 7
	3/7.3	3 SF Walls		128.44 5	SF Ceiling	
HVAC 5 4 64	A45.7	8 SF Walls & Ce	iling	128.44	SF Floor	
	/ 14.2	7 SY Flooring		45.33 I	F Floor Perime	eter
J	45.3	3 LF Geil. Perim	eter			
<u> </u>		1/ _				
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
3,051. Remove Exhaust fan - Commercial - rooftop	1.00 EA		172.00	0.00	0.00	172.00
Note: Cost to terminate and remove the e	xhaust vents from	the roof using a cra				
3,052. R&R Rafters - 2x6 - 24" OC (3- 5/12 Gable, per SF of floor)	128.44 SF		0.47	1.49	0.00	251.75
3,053. R&R Sheathing - spaced 1" x 6"	128.44 SF		0.36	2.06	0.00	310.83
3,054. Metal roofing - ribbed - 26 gauge - 1 1/8" to 1 1/2"	176.44 SF		0.00	350	0.00	582.2
3,055. R&R Fascia - metal - 8"	45.33 LF		0.20	3.35	0.00	160.9
3,056. R&R Stud wall - 2" x 6" x 8' - 24" oc	45.33 LF		1.29	16.25	0.00	795.0
3,057. R&R Sheathing - spaced 1" x 8"	317.33 SF		0.36	2.59	0.00	936.1
3,058. R&R Fiber cement lap siding - 12"	317.33 SF		0.26	2.62	0.00	913.9
3,059. Seal/prime then paint the walls twice (3 coats)	317.33 SF		0.00	0.84	0.00	266.5
3,060. R&R Trim board - 1" x 4" - installed (pine)	56.00 LF		0.23	2.15	0.00	133.2
3,061. Seal & paint trim - two coats	56.00 LF		0.00	0.92	0.00	5 .52
3,062. R&R Greenhouse door and frame	1.00 EA		4.42	500.01	0.00	504.4
3,063. Paint door slab only - 2 coats (per side)	1.00 EA		0.00	24.16	0.00	24.1
Totals: HVAC 5					0.00	5,102.83



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546




**HVAC 6** 

Height: 7'

317.33 SF Walls 445.78 SF Walls & Ceiling 14.27 SY Flooring 45.33 LF Ceil. Perimeter 128.44 SF Ceiling 128.44 SF Floor

45.33 LF Floor Perimeter

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
3,064. Remove Exhaust fan - Commercial - rooftop	1.00 EA		172.00	0.00	0.00	172.00
Note: Cost to terminate and remove the e.	xhaust vents from th	e roof using a cro	ine.			
3,065. R&R Rafters - 2x6 - 24" OC (3- 5/12 Gable, per SF of floor)	128.44 SF		0.47	1.49	0.00	251.75
3,066. R&R Sheathing - spaced 1" x 6"	128.44 SF	)	0.36	2.06	0.00	310.83
3,067. Metal roofing - ribbed - 26 gauge - 1 1/8" to 1 1/2"	176.44 SF		0.00	3.30	0.00	582.25
3,068. R&R Fascia - metal - 8"	45.33 LF		0.20	3.35	0.00	160.93
3,069. R&R Stud wall - 2" x 6" x 8' - 24" oc	45.33 LF	17	1.29	16.25	0.00	795.09
,070. R&R Sheathing - spaced 1" x 8"	317.33 SF	11	0.36	2.59	0.00	936.12
3,071. R&R Fiber cement lap siding - 12"	317.33 SF	1	0.26	2.62	0.00	913.91
3,072. Seal/prime then paint the walls twice (3 coats)	317.33 SF		0.00	7 0.84	0.00	266.56
3,073. R&R Trim board - 1" x 4" - installed (pine)	56.00 LF	/	10.23	2.15	0.00	133.28
3,074. Seal & paint trim - two coats	56.00 LF		\$.00	0.92	0.00	51.52
3,075. R&R Greenhouse door and frame	1.00 EA		4.42	500,01	0.00	504.43
3,076. Paint door slab only - 2 coats (per side)	1.00 EA		0.00	24.16	0.00	24.16
Totals: HVAC 6					0.00	5,102.83



**HVAC7** 

317.33 SF Walls

445.78 SF Walls & Ceiling

14.27 SY Flooring

45.33 LF Ceil. Perimeter

Height: 7'

128.44 SF Ceiling 128.44 SF Floor

45.33 LF Floor Perimeter

ESCRIPTION	OTY	RESET	REMOVE	REPLACE	TAX	TOTAL
ESCRIPTION	QII	RESET	REMOVE	KEI LACE	IAA	IOIAL



#### **CONTINUED - HVAC 7**

DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL
3,077. Remove Exhaust fan - Commercial - rooftop	1.00 EA	, 3	172.00	0.00	0.00	172.00
Note: Cost to terminate and remove the e.	xhaust vents from th	e roof using a cra	ine.			
3,078. R&R Rafters - 2x6 - 24" OC (3- 5/12 Gable, per SF of floor)	128.44 SF		0.47	1.49	0.00	251.75
3,079. R&R Sheathing - spaced 1" x 6"	128.44 SF		0.36	2.06	0.00	310.83
3,080. Metal roofing - ribbed - 26 gauge - 1 1/8" to 1 1/2"	176.44 SF		0.00	3.30	0.00	582.25
3,081. R&R Fascia - metal - 8"	45.33 LF		0.20	3.35	0.00	160.93
3,082. R&R Stud wall - 2" x 6" x 8' - 24" oc	45.33 LF	٨	1.29	16.25	0.00	795.09
3,083. R&R Sheathing - spaced 1" x 8"	317.33 SF	/\	0.36	2.59	0.00	936.12
3,084. R&R Fiber cement lap siding - 12"	317.33 SF	17	0.26	2.62	0.00	913.91
3,085. Seal/prime then paint the walls twice (3 coats)	317.33 SF	X	0.00	0.84	0.00	266.56
3,086. R&R Trim board - 1" x 4" - installed (pine)	56.00 LF	P	1/9/23	2.15	0.00	133.28
,087. Seal & paint trim - two coats	56.00 LF		0.00	7 0.92	0.00	51.52
3,088. R&R Greenhouse door and frame	1.00 EA		4.42	500.01	0.00	504.43
3,089. Paint door slab only - 2 coats (per side)	1.00 EA		6.96	24.16	0.00	24.16
Totals: HVAC 7					0.00	5,102.83
Total: Roof					0.00	81,353.00

#### Interior

Line Item Totals: VICTORYCOSUB

	Interior	Interior							
DESCRIPTION	QTY	RESET	REMOVE	REPLACE	TAX	TOTAL			
	inspected as the building is aband o asbestos floor tile present.	loned and boarde	d up. We did deter	mine that considerabl	e interior water l	has occurred			
Totals: Interior					0.00	0.00			
Total: Building 66 - Old Do	orm Building (294 Foster Field)				0.00	81,353.00			

0.00

2,189,792.41



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

# **Grand Total Areas:**

151,008. 03	SF Walls	96,687.37	SF Ceiling	247,695. 39	SF Walls and Ceiling
96,658.54	SF Floor	10,739.84	SY Flooring	16,570.66	LF Floor Perimeter
9,926.03	SF Long Wall	5,762.51	SF Short Wall	17,013.17	LF Ceil. Perimeter
79,195.07	Floor Area	82,780.58	Total Area	120,553. 07	Interior Wall Area
95,607.35	Exterior Wall Area	7,016.34	Exterior Perimeter of Walls	f	
293,776. 97	Surface Area	2,937,71	Number of Squares	15,801.16	Total Perimeter Length
2,187.92	Total Ridge Length	0.00	Total Hip Length		

12/13/2017 Page: 256





Coverage	Item Total	%	ACV Total	%
Building 1- Old Jail- 206 W. Constitution	32,180.91	1.47%	32,180.91	1.47%
Building 2- Old Courthouse - 101 N. Bridge	2,937.31	0.13%	2,937.31	0.13%
Building 3 - Old Courthouse Tunnel	592.19	0.03%	592.19	0.03%
Building 4 - New Courthouse - 115 N. Bridge	7,043.64	0.32%	7,043.64	0.32%
Building 5 - Old Fire Station - 209 W. Forrest	4,899.80	0.22%	4,899.80	0.22%
Building 6 - PCT #1- Machine Storage- 2000 FM 1686	16,227.18	0.74%	16,227.18	0.74%
Building 7 - PCT #3- Machine Storage - 133 Aloe Field	42,879.82	1.96%	42,879.82	1.96%
Building 8 - PCT #3-Radio Tower-133 Aloe Field	968.14	0.04%	968.14	0.04%
Building 9 - PCT #3-Mechanic Shop - 133 Aloe Field	4,741.44	0.22%	4,741.44	0.22%
Building 10 - PCT #3-Service Center Cover - 133 Aloe Field	3,056.82	0.14%	3,056.82	0.14%
Building 11 - PCT #2-Truck Storage - 3323 Nursery	16,369.52	0.75%	16,369.52	0.75%
Building 12 - Park- Metal Storage - 500 Fordyce Rd.	6,575.61	0.30%	6,575.61	0.30%
Building 13 - Park- Comfort Station - 500 Fordyce Rd.	0.00	0.00%	0.00	0.00%
Building 14 - New Jail - 101 N. Glass	15,570.58	0.71%	15,570.58	0.71%
Building 15 - Airplane Hangar - 133 N. Hangar Dr.	61,776.10	2.82%	61,776.10	2.82%
Building 15 - Airplane Hangar - 133 N. Hangar Dr Code Upgrade	0.00	0.00%	0.00	0.00%
Building 16 - Airplane Hangar(FBO) - 437 S. Hangar Dr.	68,582.64	3.13%	68,582.64	3.13%
Building 16 - Airplane Hangar(FBO) - 437 S. Hangar Dr Code Upgrade	0.00	0.00%	0.00	0.00%
Building 17 - Airplane Hangar B - 305 S. Hangar Dr.	17,829.77	0.81%	17,829.77	0.81%
Building 18 - Airplane Hangar C - 207 Storehouse Dr.	749,024.16	34.21%	749,024.16	34.21%
Building 19 - PCT #4-Truck Storage - 155 Corpus Christi	17,797.56	0.81%	17,797.56	0.81%
Building 20 - PCT #4- Building - 155 Corpus Christi	59,471.59	2.72%	59,471.59	2.72%
Building 20 - PCT #4- Building - 155 Corpus Christi - Code Upgrade	0.00	0.00%	0.00	0.00%
Building 21 - Airplane Hangar(T-Hangar	32,711.61	1.49%	32,711.61	1.49%
VICTORYCOSUB			12/13/2	017

Page: 257





Units)-348 N. Hangar Dr.				
Building 22 - Aircraft Storage(T-Hangar Units)- 388 N. Hangar Dr	100,395.37	4.58%	100,395.37	4.58%
Building 23 - Office Elections & JP #3 - 111 N. Glass	2,559.66	0.12%	2,559.66	0.12%
Building 24 - Airport Terminal /2 Storage Buildings - 609 Foster	33,884.38	1.55%	33,884.38	1.55%
Building 24 - Airport Terminal /2 Storage Buildings - 609 Foster - Code Upgrade	0.00	0.00%	0.00	0.00%
Building 25 - Airport Maintenance w/ Generator - 41 Hangar	32,437.33	1.48%	32,437.33	1.48%
Building 26 - SWB Building / Bridge St. Annex - 204 N. Bridge	104,270.55	4.76%	104,270.55	4.76%
Building 27 - Extension Service - 528 Waco Circle	73,717.46	3.37%	73,717.46	3.37%
Building 27 - Extension Service - 528 Waco Circle - Code Upgrade	0.00	0.00%	0.00	0.00%
Building 28 - Juvenile Detention Center - 97 Foster Field	137.82	0.01%	137.82	0.01%
Building 29 - Modular Building / Highway Patrol	0.00	0.00%	0.00	0.00%
Building 30 - Health Dept - 2805 Navarro	9,373.64	0.43%	9,373.64	0.43%
Building 31 - 4-H Activity Center - 259 Bachelor Dr.	4,034.18	0.18%	4,034.18	0.18%
Building 32 - Fire Marshall Office / TSA - 25 & 27 Hangar Dr.	6,654.66	0.30%	6,654.66	0.30%
Building 33 - Officers Club - 333 Bachelor Dr.	117,400.34	5.36%	117,400.34	5.36%
Building 34 - Victoria Well Service - 169 Aviation Dr.	0.00	0.00%	0.00	0.00%
Building 35 - COMAT Building - 442 Foster Field Dr.	96,075.26	4.39%	96,075.26	4.39%
Building 35 - COMAT Building - 442 Foster Field Dr Code Upgrade	0.00	0.00%	0.00	0.00%
Building 36 - Animal Shelter - 102 Perimeter Rd.	1,644.29	0.08%	1,644.29	0.08%
Building 37 - Weigh Station / Scales - HWY 59 NTH	0.00	0.00%	0.00	0.00%
Building 38 - Storehouse - 103 S Glass	18,717.90	0.85%	18,717.90	0.85%
Building 39 - AARFF Station (Fire Station) - 121 N Hangar	15,489.10	0.71%	15,489.10	0.71%
Building 40 - Erect-A-Tube Hangar - 390 N Hangar Dr	0.00	0.00%	0.00	0.00%
Building 41 - Control Tower / Airport - 348 Bachelor Dr.	21,402.96	0.98%	21,402.96	0.98%
Building 42 - PCT #1-Pole Barn Storage - 16043 FM 1686	0.00	0.00%	0.00	0.00%





_					
	Building 43 - Hartman / JP #1 - 700-704 Goldman	0.00	0.00%	0.00	0.00%
	Building 44 - Hartman Building - 901 E. Pecan	0.00	0.00%	0.00	0.00%
	Building 45 - JP #4 Building - 2604 E Mockingbird	0.00	0.00%	0.00	0.00%
	Building 46 - JP #2-Building - 4407 Lilac	0.00	0.00%	0.00	0.00%
	Building 47 - PCT #4-New Barn - 226 Beck Road	5,954.58	0.27%	5,954.58	0.27%
	Building 48 - PCT #4 - Storage Building - 226 Beck Road	0.00	0.00%	0.00	0.00%
	Building 49 - Old Outreach School - 131 Galveston	0.00	0.00%	0.00	0.00%
	Building 50 - Celebration Church - 358 Foster Field	6,101.79	0.28%	6,101.79	0.28%
	Building 50 - Celebration Church - 358 Foster Field - Code Upgrade	0.00	0.00%	0.00	0.00%
	Building 51 - Sky Restaurant - 236 Foster Field	35,661.86	1.63%	35,661.86	1.63%
	Building 52 - Fisher Stevens - 43 Storehouse	106,777.64	4.88%	106,777.64	4.88%
	Building 53 - Reliant Field Services - 112 Corpus Chrisit	3,095.32	0.14%	3,095.32	0.14%
	Building 54 - Townsend Remodeling Unamed - 470 Foster Field	9,847.33	0.45%	9,847.33	0.45%
	Building 55 - Unamed Building - 339 Foster Field	0.00	0.00%	0.00	0.00%
	Building 56 - LDS Builders - 396 Foster Field	14,730.88	0.67%	14,730.88	0.67%
	Building 57 - Straight Arrow Archery - 60 Storehouse	5,696.05	0.26%	5,696.05	0.26%
	Building 58 - Celebration Church / UHV - 292 Foster Field	3,826.70	0.17%	3,826.70	0.17%
	Building 59 - Fire Marshall Storage - 354 Hangar	206.21	0.01%	206.21	0.01%
	Building 60 - Vacant Building - 479 Waco Circle	23,635.00	1.08%	23,635.00	1.08%
	Building 60 - Vacant Building - 479 Waco Circle - Code Upgrade	0.00	0.00%	0.00	0.00%
	Building 61 - Old Golden Crescent - GCRP - 568 Waco Circle	32,266.19	1.47%	32,266.19	1.47%
	Building 61 - Old Golden Crescent - GCRP - 568 Waco Circle - Code Upgrade	0.00	0.00%	0.00	0.00%
	Building 62 - Texas Mile Warehouse - 131 Hangar	22,397.82	1.02%	22,397.82	1.02%
	Building 63 - Condemned Warehouse (H&H Door) - 158 Hangar	23,112.42	1.06%	23,112.42	1.06%
	Building 64 - Civil Air Patrol - 381 Hangar	0.00	0.00%	0.00	0.00%



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

Total	2,189,792.41	100.00%	2,189,792.41	100.00%
General Conditions	0.00	0.00%	0.00	0.00%
Building 66 - Old Dorm Building - 294 Foster Field - Code Upgrade	0.00	0.00%	0.00	0.00%
Building 66 - Old Dorm Building - 294 Foster Field	81,353.00	3.72%	81,353.00	3.72%
Building 65 - Old Brig - 153 Corpus Christi	15,698.33	0.72%	15,698.33	0.72%



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

# Summary for Building 1- Old Jail- 206 W. Constitution

Line Item Total		32,180.91
Replacement Cost Value Net Claim		\$32,180.91 \$32,180.91
	Andr. Formanionth	
	Andy Farnsworth	
	Project Consultant/ Mgr.	



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

# Summary for Building 2- Old Courthouse - 101 N. Bridge

Line Item Total		2,937.31
Replacement Cost Value Net Claim		\$2,937.31 \$2,937.31
	Andy Farnsworth	
	Project Consultant/ Mgr.	

**VICTORYCOSUB** 

12/13/2017

Page: 262



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

# **Summary for Building 3 - Old Courthouse Tunnel**

Line Item Total		592.19
Replacement Cost Value		\$592.19
Net Claim		\$592.19
	Andy Farnsworth	
	Project Consultant/ Mar	

**VICTORYCOSUB** 

12/13/2017

Page: 263



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

# Summary for Building 4 - New Courthouse - 115 N. Bridge

Line Item Total		7,043.64
Replacement Cost Value		\$7,043.64
Net Claim		\$7,043.64
	Andy Farnsworth	_
	Project Consultant/ Mgr.	



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

# **Summary for Building 5 - Old Fire Station - 209 W. Forrest**

Line Item Total		4,899.80
Replacement Cost Value		\$4,899.80
Net Claim		\$4,899.80
		_
	Andy Farnsworth	
	Project Consultant/ Mgr.	



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

# Summary for Building 6 - PCT #1- Machine Storage- 2000 FM 1686

Line Item Total		16,227.18
Replacement Cost Value Net Claim		\$16,227.18 \$16,227.18
	Andy Farnsworth	
	Project Consultant/ Mgr.	



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

# Summary for Building 7 - PCT #3- Machine Storage - 133 Aloe Field

Line Item Total	42,879.82
Replacement Cost Value	\$42,879.82
Net Claim	\$42,879.82

Andy Farnsworth

Project Consultant/ Mgr.



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

# **Summary for Building 8 - PCT #3-Radio Tower-133 Aloe Field**

Line Item Total		968.14
Replacement Cost Value		\$968.14
Net Claim		\$968.14
	Andy Farnsworth	_
	Project Consultant/ Mgr.	

VICTORYCOSUB



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

# Summary for Building 9 - PCT #3-Mechanic Shop - 133 Aloe Field

Line Item Total		4,741.44
Replacement Cost Value Net Claim		\$4,741.44 \$4,741.44
	Andy Farnsworth	_
	Project Consultant/ Mgr.	



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

# Summary for Building 10 - PCT #3-Service Center Cover - 133 Aloe Field

Line Item Total		3,056.82
Replacement Cost Value		\$3,056.82
Net Claim		\$3,056.82
	Andy Farnsworth	7
	Project Consultant/ Mor	



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

# Summary for Building 11 - PCT #2-Truck Storage - 3323 Nursery

Line Item Total		16,369.52
Replacement Cost Value Net Claim		\$16,369.52 \$16,369.52
	Andy Farnsworth	
	Project Consultant/ Mgr.	



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

# Summary for Building 12 - Park- Metal Storage - 500 Fordyce Rd.

Line Item Total		6,575.61
Replacement Cost Value Net Claim		\$6,575.61 \$6,575.61
	Andy Farnsworth	_
	Project Consultant/ Mar	



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 14 - New Jail - 101 N. Glass

Line Item Total		15,570.58
Replacement Cost Value Net Claim		\$15,570.58 \$15,570.58
	=	
	Andy Farnsworth	
	Project Consultant/ Mgr.	



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 15 - Airplane Hangar - 133 N. Hangar Dr.

Line Item Total		61,776.10
Replacement Cost Value		\$61,776.10
Net Claim		\$61,776.10
	Andy Farnsworth	
	Project Consultant/ Mor	



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 15 - Airplane Hangar - 133 N. Hangar Dr. - Code Upgrade

Line Item Total	0.00
Replacement Cost Value	\$0.00
Net Claim	\$0.00

#### Building 15 - Airplane Hangar - 133 N. Hangar Dr. - Code Upgrade Paid When Incurred

Line Item Total	17,166.01
Replacement Cost Value	\$17,166.01
<b>Total Paid When Incurred</b>	\$17,166.01

Andy Farnsworth
Project Consultant/ Mgr.

**VICTORYCOSUB** 

12/13/2017



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 16 - Airplane Hangar(FBO) - 437 S. Hangar Dr.

Line Item Total		68,582.64
Replacement Cost Value		\$68,582.64
Net Claim		\$68,582.64
•		-
	Andy Farnsworth	
	Project Consultant/ Mgr	



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 16 - Airplane Hangar(FBO) - 437 S. Hangar Dr. - Code Upgrade

0.00
\$0.00
\$0.00
φυ.υυ
red
T

Line Item Total 16,674.89

Replacement Cost Value \$16,674.89

Total Paid When Incurred \$16,674.89

Andy Farnsworth
Project Consultant/ Mgr.



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 17 - Airplane Hangar B - 305 S. Hangar Dr.

17,829.77
17,829.77

Andy Farnsworth

Project Consultant/ Mgr.



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 18 - Airplane Hangar C - 207 Storehouse Dr.

749,024.16
\$749,024.16
\$749,024.16

Andy Farnsworth
Project Consultant/ Mgr.



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 19 - PCT #4-Truck Storage - 155 Corpus Christi

Line Item Total	Jumining 101 Danding 10 1 01 # 1 11 don 500 ago 100 001	17,797.56
Replacement Cost Value		\$17,797.56
Net Claim		\$17,797.56
	Andy Farnsworth	
	Project Consultant/ Mgr.	



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034

### Summary for Building 20 - PCT #4- Building - 155 Corpus Christi

Line Item Total		59,471.59
Replacement Cost Value		\$59,471.59
Net Claim		\$59,471.59
	Andy Farnsworth	

Project Consultant/ Mgr.

**VICTORYCOSUB** 

12/13/2017





8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 20 - PCT #4- Building - 155 Corpus Christi - Code Upgrade

Line Item Total	0.00
Replacement Cost Value	\$0.00
Net Claim	\$0.00

#### Building 20 - PCT #4- Building - 155 Corpus Christi - Code Upgrade Paid When Incurred

Line Item Total	10,538.19
Replacement Cost Value	\$10,538.19
Total Paid When Incurred	\$10,538.19

Andy Farnsworth
Project Consultant/ Mgr.



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 21 - Airplane Hangar (T-Hangar Units)-348 N. Hangar Dr.

Line Item Total	32,711.61
Replacement Cost Value	\$32,711.61
Net Claim	\$32,711.61
Net Claim	\$32,/11.0

Andy Farnsworth
Project Consultant/ Mgr.

12/13/2017



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 22 - Aircraft Storage(T-Hangar Units)- 388 N. Hangar Dr

Replacement Cost Value \$10	
	00,395.37
Net Claim \$10	00,395.37

Andy Farnsworth

Project Consultant/ Mgr.



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 23 - Office Elections & JP #3 - 111 N. Glass

Line Item Total	2,559.66
Replacement Cost Value	\$2,559.66
Net Claim	\$2,559.66

Andy Farnsworth

Project Consultant/ Mgr.



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 24 - Airport Terminal /2 Storage Buildings - 609 Foster

Line Item Total		33,884.38
Replacement Cost Value Net Claim		\$33,884.38 \$33,884.38
Net Claim		\$33,884.38
	Andy Farnsworth	
	Project Consultant/ Mgr.	



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 24 - Airport Terminal /2 Storage Buildings - 609 Foster - Code Upgrade

Line Item Total		0.00
Replacement C	Cost Value	\$0.00
<b>Net Claim</b>		\$0.00
Bu	uilding 24 - Airport Terminal /2 Storage Buildings - 609 Foster - Code U	Upgrade Paid When
	Incurred	

| Curred | 7,608.47 | Replacement Cost Value | \$7,608.47 |

Total Paid When Incurred \$7,608.47

Andy Farnsworth
Project Consultant/ Mgr.



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 25 - Airport Maintenance w/ Generator - 41 Hangar

Line Item Total		32,437.33
Replacement Cost Value Net Claim		\$32,437.33 \$32,437.33
	Andy Farnsworth	
	Project Consultant/ Mgr.	



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 26 - SWB Building / Bridge St. Annex - 204 N. Bridge

Line Item Total		104,270.55
Replacement Cost Value Net Claim		\$104,270.55 \$104,270.55
	Andy Farnsworth	
	· ·	
	Project Consultant/ Mgr.	



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### **Summary for Building 27 - Extension Service - 528 Waco Circle**

Line Item Total		73,717.46
Replacement Cost Value		\$73,717.46
Net Claim		\$73,717.46
	Andy Farnsworth	_
	Project Consultant/ Mgr.	



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546


#### Summary for Building 27 - Extension Service - 528 Waco Circle - Code Upgrade

Line Item Total	0.00
Replacement Cost Value	\$0.00
Net Claim	\$0.00

#### Building 27 - Extension Service - 528 Waco Circle - Code Upgrade Paid When Incurred

Line Item Total	21,004.15
Replacement Cost Value	\$21,004.15
Total Paid When Incurred	\$21,004.15

Andy Farnsworth
Project Consultant/ Mgr.



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 28 - Juvenile Detention Center - 97 Foster Field

Line Item Total	137.82
Replacement Cost Value	\$137.82
Net Claim	\$137.82

Andy Farnsworth

Project Consultant/ Mgr.

**VICTORYCOSUB** 

12/13/2017

## Virtus Group 8380 Warren Park

8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 30 - Health Dept - 2805 Navarro

Line Item Total	9,373.64
Replacement Cost Value Net Claim	\$9,373.64 \$9,373.64
Net Ciaini	φ2,973.04

Andy Farnsworth
Project Consultant/ Mgr.

VICTORYCOSUB

12/13/2017



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 31 - 4-H Activity Center - 259 Bachelor Dr.

Line Item Total		4,034.18
Replacement Cost Value		\$4,034.18
Net Claim		\$4,034.18
	Andy Farnsworth	_
	Project Consultant/ Mgr.	



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 32 - Fire Marshall Office / TSA - 25 & 27 Hangar Dr.

Line Item Total		6,654.66
Replacement Cost Value Net Claim		\$6,654.66 \$6,654.66
	Andy Farnsworth	
	Project Consultant/ Mgr.	

Virtus

8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 33 - Officers Club - 333 Bachelor Dr.

Line Item Total		117,400.34
Replacement Cost Value Net Claim		\$117,400.34 \$117,400.34
	Andy Farnsworth	
	Project Consultant/ Mgr.	


## Virtus

#### **Virtus Group**

8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 35 - COMAT Building - 442 Foster Field Dr.

Line Item Total		96,075.26
Replacement Cost Value		\$96,075.26
Net Claim		\$96,075.26
	Andy Farnsworth	
	Project Consultant/ Mgr.	





8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 35 - COMAT Building - 442 Foster Field Dr. - Code Upgrade

Line Item Total	0.00
Replacement Cost Value	\$0.00
Net Claim	\$0.00
•	

#### Building 35 - COMAT Building - 442 Foster Field Dr. - Code Upgrade Paid When Incurred

Line Item Total	45,684.59
Replacement Cost Value	\$45,684.59
Total Paid When Incurred	\$45,684.59

Andy Farnsworth
Project Consultant/ Mgr.

**VICTORYCOSUB** 

12/13/2017



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 36 - Animal Shelter - 102 Perimeter Rd.

Line Item Total		1,644.29
Replacement Cost Value		\$1,644.29
Net Claim		\$1,644.29
	Andy Farnsworth	
	Project Consultant/ Mgr.	



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 38 - Storehouse - 103 S Glass

Line Item Total		18,717.90
Replacement Cost Value Net Claim		\$18,717.90 \$18,717.90
	Andy Farnsworth	_
	Project Consultant/ Mgr.	



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 39 - AARFF Station (Fire Station) - 121 N Hangar

Line Item Total		15,489.10
Replacement Cost Value		\$15,489.10
Net Claim		\$15,489.10
	Andy Farnsworth	

Project Consultant/ Mgr.





8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 41 - Control Tower / Airport - 348 Bachelor Dr.

Line Item Total	21,402.96
Replacement Cost Value	\$21,402.96
Net Claim	\$21,402.96
	=======================================

Andy Farnsworth

Project Consultant/ Mgr.





8380 Warren Parkway / Ste. 700 - Frisco, TX 75034

#### Summary for Building 47 - PCT #4-New Barn - 226 Beck Road

Line Item Total	5,954.58
Replacement Cost Value	\$5,954.58
Net Claim	\$5,954.58

Andy Farnsworth

Project Consultant/ Mgr.

## Virtus

#### **Virtus Group**

8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 50 - Celebration Church - 358 Foster Field

Line Item Total	6,101.79
Replacement Cost Value	\$6,101.79
Net Claim	\$6,101.79
	=

Andy Farnsworth

Project Consultant/ Mgr.

**VICTORYCOSUB** 

12/13/2017



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 50 - Celebration Church - 358 Foster Field - Code Upgrade

Line Item Total	0.00
Replacement Cost Value	\$0.00
Net Claim	\$0.00

#### Building 50 - Celebration Church - 358 Foster Field - Code Upgrade Paid When Incurred

Line Item Total	6,274.10
Replacement Cost Value	\$6,274.10
Total Paid When Incurred	\$6,274.10

Andy Farnsworth
Project Consultant/ Mgr.

**VICTORYCOSUB** 

12/13/2017

## Virtus

#### **Virtus Group**

8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 51 - Sky Restaurant - 236 Foster Field

Line Item Total		35,661.86
Replacement Cost Value Net Claim		\$35,661.86 \$35,661.86
	Andy Farnsworth	_
	Project Consultant/ Mar	

# Virtus

#### **Virtus Group**

8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### **Summary for Building 52 - Fisher Stevens - 43 Storehouse**

Line Item Total		106,777.64
Replacement Cost Value Net Claim		\$106,777.64 \$106,777.64
	Andy Farnsworth	
	Project Consultant/ Mgr.	

## Virtus 8380 W

#### **Virtus Group**

8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### **Summary for Building 53 - Reliant Field Services - 112 Corpus Chrisit**

Line Item Total		3,095.32
Replacement Cost Value		\$3,095.32
Net Claim		\$3,095.32
	Andy Farnsworth	
	Project Consultant/ Mgr.	



Virtus 8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 54 - Townsend Remodeling Unamed - 470 Foster Field

Line Item Total		9,847.33
Replacement Cost Value		\$9,847.33
Net Claim		\$9,847.33
		=
	Andy Farnsworth	

Project Consultant/ Mgr.

# Virtus

#### **Virtus Group**

8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 56 - LDS Builders - 396 Foster Field

Line Item Total		14,730.88
Replacement Cost Value Net Claim		\$14,730.88 \$14,730.88
	Andy Farnsworth	
	Project Consultant/ Mgr	



# Virtus 8380 913-

#### **Virtus Group**

8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### **Summary for Building 57 - Straight Arrow Archery - 60 Storehouse**

Line Item Total		5,696.05
Replacement Cost Value Net Claim		\$5,696.05 \$5,696.05
	Andy Farnsworth	_
	Project Consultant/ Mor	



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 58 - Celebration Church / UHV - 292 Foster Field

Line Item Total		3,826.70
Replacement Cost Value		\$3,826.70
Net Claim		\$3,826.70
	Andr Franciscoth	_
	Andy Farnsworth	
	Project Consultant/ Mgr.	



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 59 - Fire Marshall Storage - 354 Hangar

Line Item Total		206.21
Replacement Cost Value Net Claim		\$206.21 \$206.21
	Andy Farnsworth	
	Project Consultant/ Mgr.	



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 60 - Vacant Building - 479 Waco Circle

Line Item Total		23,635.00
Replacement Cost Value Net Claim		\$23,635.00 \$23,635.00
	Andy Farnsworth	_
	Project Consultant/ Mgr.	



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 60 - Vacant Building - 479 Waco Circle - Code Upgrade

Line Item Total	0.00
Replacement Cost Value	\$0.00
Net Claim	\$0.00
<b>Building 60 - Vacant Building - 479 Waco Circl</b>	e - Code Upgrade Paid When Incurred
	e - Code Upgrade Paid When Incurred 36,084.67
Building 60 - Vacant Building - 479 Waco Circl Line Item Total Replacement Cost Value	

Andy Farnsworth

Project Consultant/ Mgr.



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 61 - Old Golden Crescent - GCRP - 568 Waco Circle

Line Item Total	32,266.19
Replacement Cost Value	\$32,266.19
Net Claim	\$32,266.19

Andy Farnsworth

Project Consultant/ Mgr.



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

Summary for Building 61 - Old Golden Crescent - GCRP - :	668 Waco Circle - Code Upgrade
Line Item Total	0.00
Replacement Cost Value Net Claim	\$0.00 \$0.00
Building 61 - Old Golden Crescent - GCRP - 568 Waco Circle -	Code Upgrade Paid When Incurred
Building 61 - Old Golden Crescent - GCRP - 568 Waco Circle - Line Item Total	Code Upgrade Paid When Incurred

Andy Farnsworth

Project Consultant/ Mgr.



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 62 - Texas Mile Warehouse - 131 Hangar

Line Item Total		22,397.82
Replacement Cost Value Net Claim		\$22,397.82 \$22,397.82
	Andy Farnsworth	
	Project Consultant/ Mgr.	



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 63 - Condemned Warehouse (H&H Door) - 158 Hangar

Line Item Total		23,112.42
Replacement Cost Value Net Claim		\$23,112.42 \$23,112.42
	Andy Farnsworth	_
	Project Consultant/ Mgr.	



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 65 - Old Brig - 153 Corpus Christi


Line Item Total		15,698.33
Replacement Cost Value		\$15,698.33
Net Claim		\$15,698.33
	Andy Farnsworth	_
	Project Consultant/ Mgr.	



Virtus 8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 66 - Old Dorm Building - 294 Foster Field

Line Item Total		81,353.00
Replacement Cost Value Net Claim		\$81,353.00 \$81,353.00
	Andy Farnsworth	_
	Project Consultant/ Mgr.	



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

#### Summary for Building 66 - Old Dorm Building - 294 Foster Field - Code Upgrade

Line Item Total	0.00
Replacement Cost Value Net Claim	\$0.00 \$0.00

#### Building 66 - Old Dorm Building - 294 Foster Field - Code Upgrade Paid When Incurred

Line Item Total	43,696.78
Replacement Cost Value	\$43,696.78
Total Paid When Incurred	\$43,696.78

Andy Farnsworth Project Consultant/ Mgr.

**VICTORYCOSUB** 

12/13/2017

Page: 322



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

**Recap of Taxes** 



#### Recap by Room

**Estimate: VICTORYCOSUB** 

Area: Building 1- Old Jail

: Ground level		2	
Homeland Security		789.05	0.04%
Coverage: Building 1- Old Jail- 206 W. Constitution	100.00% =	789.05	0.000
Copy Room	100.000	1,996.95	0.09%
Coverage: Building 1- Old Jail- 206 W. Constitution <b>Joe's Office</b>	100.00% =	1,996.95 <b>899.70</b>	0.04%
Coverage: Building 1- Old Jail- 206 W. Constitution  Closet 1	100.00% =	899.70 <b>45.10</b>	
Coverage: Building 1- Old Jail- 206 W. Constitution  Toilet 1	100.00% =	45.10 <b>4.98</b>	
Coverage: Building 1- Old Jail- 206 W. Constitution	100.00% =	4.98 <b>952.32</b>	0.04%
Office 1  Coverage: Building 1- Old Jail- 206 W. Constitution	100.00% =	952.32	0.04%
Closet 2		45.10	
Coverage: Building 1- Old Jail- 206 W. Constitution Hallway 2	100.00% =	45.10 <b>45.05</b>	
Coverage: Building 1- Old Jail- 206 W. Constitution  Toilet	100.00% =	45.05 <b>3.26</b>	
Coverage: Building 1- Old Jail- 206 W. Constitution Leon's Office	100.00% =	3.26 <b>782.19</b>	0.04%
Coverage: Building 1- Old Jail- 206 W. Constitution North Hall	100.00% =	782.19 <b>105.97</b>	0.0176
Coverage: Building 1- Old Jail- 206 W. Constitution Computer Room	100.00% =	105.97 13.24	
Coverage: Building 1- Old Jail- 206 W. Constitution	100.00% =	13.24	
Interdiction Sgt Office		899.46	0.04%
Coverage: Building 1- Old Jail- 206 W. Constitution Stairwell	100.00% =	899.46 <b>9.55</b>	
Coverage: Building 1- Old Jail- 206 W. Constitution South Hall	100.00% =	9.55 <b>19.52</b>	
Coverage: Building 1- Old Jail- 206 W. Constitution Entry	100.00% =	19.52 <b>29.28</b>	
Coverage: Building 1- Old Jail- 206 W. Constitution Kitchen Hall	100.00% =	29.28 <b>2.98</b>	
Coverage: Building 1- Old Jail- 206 W. Constitution Conference Room	100.00% =	2.98 1,011.20	0.05%
Coverage: Building 1- Old Jail- 206 W. Constitution  Kitchen	100.00% =	1,011.20 17.75	0.00
Coverage: Building 1- Old Jail- 206 W. Constitution	100.00% =	17.75	
ORYCOSUB		12/13/2017	Page: 324



8380 Warren	Parkway /	Ste.	700 -	Frisco,	TX	75034
913-601-4546	5					

	Jack Justice's Office		743.28	0.03%
	Coverage: Building 1- Old Jail- 206 W. Constitution	100.00% =	743.28	
	Interdiction		1,418.59	0.06%
	Coverage: Building 1- Old Jail- 206 W. Constitution	100.00% =	1,418.59	
	Kennel		5.70	
	Coverage: Building 1- Old Jail- 206 W. Constitution	100.00% =	5.70 <b>3.85</b>	
	Toilet 2	100.00%		
	Coverage: Building 1- Old Jail- 206 W. Constitution	100.00% =	3.85	
	Area Subtotal: Ground level		9,844.07	0.45%
	Coverage: Building 1- Old Jail- 206 W. Constitution	100.00% =	9,844.07	
	Area Subtotal: Building 1- Old Jail		9,844.07	0.45%
	Coverage: Building 1- Old Jail- 206 W. Constitution	100.00% =	9,844.07	
Area:	Bldg 1- Old Jail Basement			
Area:	Basement		2.255.01	0.110
	Team Room		2,355.81	0.11%
	Coverage: Building 1- Old Jail- 206 W. Constitution	100.00% =	2,355.81	0.110
En.	Storage 1		2,420.23	0.11%
	Coverage: Building 1- Old Jail- 206 W. Constitution	100.00% =	2,420.23	
_	Supply Room		1,152.90	0.05%
	Coverage: Building 1- Old Jail- 206 W. Constitution	100.00% =	1,152.90	
	Storage 2		1,617.70	0.07%
	Coverage: Building 1- Old Jail- 206 W. Constitution	100.00% =	1,617.70	
	Mens		6.01	
	Coverage: Building 1- Old Jail- 206 W. Constitution	100.00% =	6.01	
	East Foyer		3.57	
	Coverage: Building 1- Old Jail- 206 W. Constitution	100.00% =	3.57	
	Womens		4.19	
	Coverage: Building 1- Old Jail- 206 W. Constitution	100.00% =	4.19	
	Resident Agent		1,816.82	0.08%
	Coverage: Building 1- Old Jail- 206 W. Constitution	100.00% =	1,816.82	
	Kitchen		2,442.87	0.11%
	Coverage: Building 1- Old Jail- 206 W. Constitution	100.00% =	2,442.87	
	Stairwell		10.00	
	Coverage: Building 1- Old Jail- 206 W. Constitution	100.00% =	10.00	
	Hallway	100.00%	1,928.68	0.09%
	Coverage: Building 1- Old Jail- 206 W. Constitution	100.00% =	1,928.68	
	Hall 1	100.00% =	210.50	0.01%
	Coverage: Building 1- Old Jail- 206 W. Constitution	100.00% =	210.50	0.02
	Closet	100.00% =	3.26	
		100 00% -	3.26	
	Coverage: Building 1- Old Jail- 206 W. Constitution  Public Safety	100.00% =	2,218.71	0.10%
VICTO	RYCOSUB		12/13/2017	Page: 3

Virtus Group

8380 Warren Parkway / Ste. 700 - Frisco, TX 75034
913-601-4546

Coverage: Building 1- Old Jail- 206 W. Constitution	100.00% =	2,218.71	
Joint Intelligence		6,145.59	0.28%
Coverage: Building 1- Old Jail- 206 W. Constitution	100.00% =	6,145.59	
Area Subtotal: Basement		22,336.84	1.02%
Coverage: Building 1- Old Jail- 206 W. Constitution	100.00% =	22,336.84	
Area Subtotal: Bldg 1- Old Jail Basement		22,336.84	1.02%
Coverage: Building 1- Old Jail- 206 W. Constitution	100.00% =	22,336.84	
a: Building 2- Old Courthouse			
Women's Restroom / Third Floor		150.05	0.01%
Coverage: Building 2- Old Courthouse - 101 N. Bridge	100.00% =	150.05	
Hearing Room 303		1,502.50	0.07%
Coverage: Building 2- Old Courthouse - 101 N. Bridge	100.00% =	1,502.50	
Room 202 (Second Floor)		1,284.76	0.06%
Coverage: Building 2- Old Courthouse - 101 N. Bridge	100.00% =	1,284.76	
Area Subtotal: Building 2- Old Courthouse		2,937.31	0.13%
Coverage: Building 2- Old Courthouse - 101 N. Bridge	100.00% =	2,937.31	
<b>Building 3 - Old Courthouse Tunnel</b>		592.19	0.03%
Coverage: Building 3 - Old Courthouse Tunnel	100.00% =	592.19	
: Building 4- New Courthouse			
Roof		578.40	0.03%
Coverage: Building 4 - New Courthouse - 115 N. Bridge	100.00% =	578.40	
Employee Breakroom (Basement)		775.18	0.04%
Coverage: Building 4 - New Courthouse - 115 N. Bridge	100.00% =	775.18	
Stairwell (Second & Third Floors)		1,577.35	0.07%
Coverage: Building 4 - New Courthouse - 115 N. Bridge	100.00% =	1,577.35	
Women's Restroom / Second Floor		600.04	0.03%
Coverage: Building 4 - New Courthouse - 115 N. Bridge	100.00% =	600.04	
Third Floor Hallway		1,671.44	0.08%
Coverage: Building 4 - New Courthouse - 115 N. Bridge	100.00% =	1,671.44	
Second Floor Hallway		1,841.23	0.08%
Coverage: Building 4 - New Courthouse - 115 N. Bridge	100.00% =	1,841.23	
Area Subtotal: Building 4- New Courthouse		7,043.64	0.32%
Coverage: Building 4 - New Courthouse - 115 N. Bridge	100.00% =	7,043.64	
a: Building 5- Old Fire Station			
a: Main Level			
Main Truck Bay		4,061.77	0.19%
Coverage: Building 5 - Old Fire Station - 209 W. Forrest	100.00% =	4,061.77	
TORYCOSUB		12/13/2017	Page: 3



Virtus 8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

	838.03	0.04%
100.00% =	838.03	
	4,899.80	0.22%
100.00% =	4,899.80	
	4,899.80	0.22%
100.00% =	4,899.80	
	160.72	0.01%
100.00% =	160.72	
	•	0.23%
100.00% =		
		0.32%
100.00% =	7,068.88	
	12,198.24	0.56%
100.00% =	12,198.24	
	547.04	0.020
100.0007	567.06	0.03%
100.00% =	<b>567.06</b> 567.06	0.03%
100.00% =		0.03%
100.00% = 100.00% =	567.06	
	567.06 567.06	
	<b>567.06 567.06</b> 567.06	0.03%
100.00% =	567.06 567.06 567.06	0.03%
100.00% =	567.06 567.06 567.06 567.06	0.03%
100.00% = 100.00% =	567.06 567.06 567.06 567.06	0.03%
100.00% =	567.06 567.06 567.06 567.06	0.03%
100.00% = 100.00% =	567.06 567.06 567.06 567.06	0.03%
	100.00% =  100.00% =  100.00% =	100.00% = 838.03 4,899.80 100.00% = 4,899.80 100.00% = 160.72 100.00% = 160.72 100.00% = 4,968.64 100.00% = 4,968.64 7,068.88 100.00% = 7,068.88

# Virtus Group 8380 Warren Park 913-601-4546

8380 Warren Parkway /	Ste. 700	- Frisco,	TX 75034
913-601-4546			



,			
Sign Storage Structure		15,291.69	0.70%
Coverage: Building 7 - PCT #3- Machine Storage - 133 Aloe Field	100.00% =	15,291.69	
Area Subtotal: Roof		29,326.64	1.34%
Coverage: Building 7 - PCT #3- Machine Storage - 133 Aloe Field	100.00% =	29,326.64	
Area Subtotal: Bldg 7- PCT 3 Machine / Sign Storage		29,326.64	1.34%
Coverage: Building 7 - PCT #3- Machine Storage - 133 Aloe Field	100.00% =	29,326.64	
rea: Building 8- PCT 3 Radio Tower Storage Building		968.14	0.04%
Coverage: Building 8 - PCT #3-Radio Tower-133 Aloe Field	100.00% =	968.14	0.04 //
Area Subtotal: Building 8- PCT 3 Radio Tower		968.14	0.04%
Coverage: Building 8 - PCT #3-Radio Tower-133 Aloe Field	100.00% =	968.14	
rea: Building 9- PCT 3 Mechanic Shop			
rea: Roof			
Storage Cage		1,592.90	0.07%
Coverage: Building 9 - PCT #3-Mechanic Shop - 133 Aloe Field	100.00% =	1,592.90	
Lean Too Shed		2,919.74	0.13%
Coverage: Building 9 - PCT #3-Mechanic Shop - 133 Aloe Field	100.00% =	2,919.74	0.04.04
Mechanic Shop Roof		228.80	0.01%
Coverage: Building 9 - PCT #3-Mechanic Shop - 133 Aloe Field	100.00% =	228.80	
Area Subtotal: Roof		4,741.44	0.22%
Coverage: Building 9 - PCT #3-Mechanic Shop - 133 Aloe Field	100.00% =	4,741.44	
Area Subtotal: Building 9- PCT 3 Mechanic Shop		4,741.44	0.22%
Coverage: Building 9 - PCT #3-Mechanic Shop - 133 Aloe Field	100.00% =	4,741.44	
rea: Building 10- PCT 3 Service Center Cover			
rea: Roof		0.33	
Service / Fuel Center Roof		3,056.82	0.14%
Coverage: Building 10 - PCT #3-Service Center Cover - 133 Aloe Field	100.00% =	3,056.82	
CTORYCOSUB		12/13/2017	Page: 3

Area Subtotal: Roof		3,056.82	0.14%
Coverage: Building 10 - PCT #3-Service Center Cover - 133 Aloe Field	100.00% =	3,056.82	
Area Subtotal: Building 10- PCT 3 Service Center Cover		3,056.82	0.14%
Coverage: Building 10 - PCT #3-Service Center Cover - 133 Aloe Field	100.00% =	3,056.82	
rea: Building 11- PCT 2 Truck Storage (Nursery Road) Exterior / East Elevation		1,122.96	0.05%
Coverage: Building 11 - PCT #2-Truck Storage - 3323 Nursery	100.00% =	1,122.96	
rea: Roof			
South Truck Shed Roof		6,458.88	0.29%
Coverage: Building 11 - PCT #2-Truck Storage - 3323 Nursery	100.00% =	6,458.88	
Sign Storage Roof		2,488.34	0.11%
Coverage: Building 11 - PCT #2-Truck Storage - 3323 Nursery	100.00% =	2,488.34	
Sign Storage Lean-Too Shed		2,440.86	0.11%
Coverage: Building 11 - PCT #2-Truck Storage - 3323 Nursery	100.00% =	2,440.86	
Area Subtotal: Roof		11,388.08	0.52%
Coverage: Building 11 - PCT #2-Truck Storage - 3323 Nursery	100.00% =	11,388.08	
East Truck Shed		3,858.48	0.18%
Coverage: Building 11 - PCT #2-Truck Storage - 3323 Nursery	100.00% =	3,858.48	
Area Subtotal: Building 11- PCT 2 Truck Storage (Nurser	y Road)	16,369.52	0.75%
Coverage: Building 11 - PCT #2-Truck Storage - 3323 Nursery	100.00% =	16,369.52	
rea: Bldg #12- Patriot Park Metal Storage Structures			
ea: Roof		4.00 / 80	0.049
Vehicle Storage Roof	100.00%	1,296.57	0.06%
Coverage: Building 12 - Park- Metal Storage - 500 Fordyce Rd.  Open Canopy	100.00% =	1,296.57 2,335.79	0.11%
Coverage: Building 12 - Park- Metal Storage - 500	100.00% =	2,335.79	U.11 /0
Fordyce Rd.	100.0070 =	2,333.19	
Area Subtotal: Roof		3,632.36	0.17%
Coverage: Building 12 - Park- Metal Storage - 500 Fordyce Rd.	100.00% =	3,632.36	
CTORYCOSUB		12/13/2017	Page: 3

Exterior / Front South Elevation		472.92	0.02%
Coverage: Building 12 - Park- Metal Storage - 500 Fordyce Rd.	100.00% =	472.92	
Area Subtotal: Bldg #12- Patriot Park Metal Storage Stru	ctures	4,105.28	0.19%
Coverage: Building 12 - Park- Metal Storage - 500 Fordyce Rd.	100.00% =	4,105.28	
a: Building #12- Patriot Park Office			
a: Interior Office Office		1 447 05	0.07%
Coverage: Building 12 - Park- Metal Storage - 500	100.00% =	<b>1,447.05</b> 1,447.05	0.07%
Fordyce Rd.	100.00% =	1,447.03	
Closet		1,023.28	0.05%
Coverage: Building 12 - Park- Metal Storage - 500 Fordyce Rd.	100.00% =	1,023.28	
Area Subtotal: Interior Office		2,470.33	0.11%
Coverage: Building 12 - Park- Metal Storage - 500 Fordyce Rd.	100.00% =	2,470.33	
Area Subtotal: Building #12- Patriot Park Office		2,470.33	0.11%
Coverage: Building 12 - Park- Metal Storage - 500 Fordyce Rd.	100.00% =	2,470.33	
a: Building 14- New Jail			
a: Main Level Patrol Office		4,248.33	0.19%
Coverage: Building 14 - New Jail - 101 N. Glass	100.00% =	4,248.33	0.17 /0
Conference Room		2,147.40	0.10%
Coverage: Building 14 - New Jail - 101 N. Glass	100.00% =	2,147.40	
Valdez Office		860.57	0.04%
Coverage: Building 14 - New Jail - 101 N. Glass	100.00% =	860.57	0.000
Classroom	100 000	1,783.31	0.08%
Coverage: Building 14 - New Jail - 101 N. Glass Captain Canfield's Office	100.00% =	1,783.31 <b>1,243.42</b>	0.06%
Coverage: Building 14 - New Jail - 101 N. Glass	100.00% =	1,243.42	0,00
Jones Office		773.26	0.04%
Coverage: Building 14 - New Jail - 101 N. Glass	100.00% =	773.26	
Restroom		716.92	0.03%
Coverage: Building 14 - New Jail - 101 N. Glass	100.00% =	716.92	0.00
Chief Deputy Boyd	100 000	1,330.55	0.06%
Coverage: Building 14 - New Jail - 101 N. Glass Sheriff O'Connor's Office	100.00% =	1,330.55 <b>1,222.46</b>	0.06%
Coverage: Building 14 - New Jail - 101 N. Glass	100.00% =	1,222.46	J.00 /0
TORYCOSUB		12/13/2017	Page:
		12/13/2017	* abo.



Courts		201,79	0.01%
Coverage: Building 14 - New Jail - 101 N. Glass	100.00% =	201.79	
Area Subtotal: Main Level		14,528.01	0.66%
Coverage: Building 14 - New Jail - 101 N. Glass	100.00% =	14,528.01	
Records Restroom		452.40	0.02%
Coverage: Building 14 - New Jail - 101 N. Glass	100.00% =	452.40	
Dispatch Server Room		590.17	0.03%
Coverage: Building 14 - New Jail - 101 N. Glass	100.00% =	590.17	
Area Subtotal: Building 14- New Jail		15,570.58	0.71%
Coverage: Building 14 - New Jail - 101 N. Glass	100.00% =	15,570.58	
rea: Building 15- Hewitt Hangar Roof			
rea: Exterior			
South Elevation		12,898.39	0.59%
Coverage: Building 15 - Airplane Hangar - 133 N. Hangar Dr.	100.00% =	12,898.39	
North Elevation		2,020.72	0.09%
Coverage: Building 15 - Airplane Hangar - 133 N. Hangar Dr.	100.00% =	2,020.72	
Area Subtotal: Exterior		14,919.11	0.68%
Coverage: Building 15 - Airplane Hangar - 133 N. Hangar Dr.	100.00% =	14,919.11	
rea: Roof			
North Flat Roof		14,896.91	0.68%
Coverage: Building 15 - Airplane Hangar - 133 N. Hangar Dr.	100.00% =	14,896.91	
Area Subtotal: Roof		14,896.91	0.68%
Coverage: Building 15 - Airplane Hangar - 133 N. Hangar Dr.	100.00% =	14,896.91	
Area Subtotal: Building 15- Hewitt Hangar Roof		29,816.02	1.36%
Coverage: Building 15 - Airplane Hangar - 133 N. Hangar Dr.	100.00% =	29,816.02	
rea: Building 15 - Hewitt Hangar Interior			
rea: Main Level			
Larry's Office		2,431.41	0.11%
Coverage: Building 15 - Airplane Hangar - 133 N. Hangar Dr.	100.00% =	2,431.41	
Waiting Area		4,126.67	0.19%
CTORYCOSUB		12/13/2017	Page:


**VICTORYCOSUB** 

8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

Coverage: Building 15 - Airplane Hangar - 133 N. Hangar Dr.	100.00% =	4,126.67	
Break Area		4,474.87	0.20%
Coverage: Building 15 - Airplane Hangar - 133 N. Hangar Dr.	100.00% =	4,474.87	
Toilet 1		590.95	0.03%
Coverage: Building 15 - Airplane Hangar - 133 N. Hangar Dr.	100,00% =	590.95	
Washing Area		551.96	0.03%
Coverage: Building 15 - Airplane Hangar - 133 N. Hangar Dr.	100.00% =	551.96	
Toilet 2		244.86	0.01%
Coverage: Building 15 - Airplane Hangar - 133 N. Hangar Dr.	100.00% =	244.86	0.22%
Workshop	100.00%	7,322.86	0.33%
Coverage: Building 15 - Airplane Hangar - 133 N. Hangar Dr.  Roy's Office	100.00% =	7,322.86 1,711.08	0.08%
Coverage: Building 15 - Airplane Hangar - 133 N. Hangar	100.00% =		0.00%
Dr.	100.00% =	1,711.08	
Storage Area/Room		4,290.94	0.20%
Coverage: Building 15 - Airplane Hangar - 133 N. Hangar Dr.	100.00% =	4,290.94	
Office		6,214.48	0.28%
Coverage: Building 15 - Airplane Hangar - 133 N. Hangar Dr.	100.00% =	6,214.48	
Area Subtotal: Main Level		31,960.08	1.46%
Coverage: Building 15 - Airplane Hangar - 133 N. Hangar Dr.	100.00% =	31,960.08	
Area Subtotal: Building 15 - Hewitt Hangar Interior		31,960.08	1.46%
Coverage: Building 15 - Airplane Hangar - 133 N. Hangar Dr.	100.00% =	31,960.08	
Building 16 - FBO Hangar Roof			
Exterior		2 200 52	0.110
South Elevation	100.000	2,308.72	0.11%
Coverage: Building 16 - Airplane Hangar(FBO) - 437 S. Hangar Dr. West Elevation	100.00% =	2,308.72 <b>20,266.38</b>	0.93%
Coverage: Building 16 - Airplane Hangar(FBO) - 437 S.	100.00% =	20,266.38	055 /0
Hangar Dr.			
Area Subtotal: Exterior		22,575.10	1.03%
Coverage: Building 16 - Airplane Hangar(FBO) - 437 S. Hangar Dr.	100.00% =	22,575.10	

Page: 333

12/13/2017



Dock			
Area: Roof South Flat Roof		19,234.51	0.88%
Coverage: Building 16 - Airplane Hangar(FBO) - 437 S. Hangar Dr.	100.00% =	19,234.51	
Pitched Metal Roof		1,453.28	0.07%
Coverage: Building 16 - Airplane Hangar(FBO) - 437 S. Hangar Dr.	100.00% =	1,453.28	
Roof4		4,148.10	0.19%
Coverage: Building 16 - Airplane Hangar(FBO) - 437 S. Hangar Dr.	100.00% =	4,148.10	
Area Subtotal: Roof		24,835.89	1.13%
Coverage: Building 16 - Airplane Hangar(FBO) - 437 S. Hangar Dr.	100.00% =	24,835.89	
Area Subtotal: Building 16 - FBO Hangar Roof		47,410.99	2.17%
Coverage: Building 16 - Airplane Hangar(FBO) - 437 S. Hangar Dr.	100.00% =	47,410.99	
area: Building #16 - FBO Hangar Interior			
rea: Main Level		4 = 4 < 00	0.000
Break Room	Table 1	1,746.90	0.08%
Coverage: Building 16 - Airplane Hangar(FBO) - 437 S. Hangar Dr.	100.00% =	1,746.90 <b>783.02</b>	0.04%
Quite Room 2	100.00% =	783.02	0.04 70
Coverage: Building 16 - Airplane Hangar(FBO) - 437 S. Hangar Dr.  Quite Room 1	100.00% =	969.20	0.04%
Coverage: Building 16 - Airplane Hangar(FBO) - 437 S.	100.00% =	969.20	
Hangar Dr. Hallway		2,364.40	0.11%
Coverage: Building 16 - Airplane Hangar(FBO) - 437 S. Hangar Dr.	100.00% =	2,364.40	
Office		1,002.80	0.05%
Coverage: Building 16 - Airplane Hangar(FBO) - 437 S. Hangar Dr.	100.00% =	1,002.80	
<b>Business Center</b>		1,176.42	0.05%
Coverage: Building 16 - Airplane Hangar(FBO) - 437 S. Hangar Dr.	100.00% =	1,176.42	0.100
Lounge		4,117.97	0.19%
Coverage: Building 16 - Airplane Hangar(FBO) - 437 S. Hangar Dr.	100.00% =	4,117.97 <b>1,194.32</b>	0.05%
Mens  Covernos: Puilding 16 Airplane Hangar(FRO) - 437 S	100.00% =	1,194.32	0.00 /0
Coverage: Building 16 - Airplane Hangar(FBO) - 437 S. Hangar Dr. Restroom Hall	100.00% =	952.07	0.04%
Coverage: Building 16 - Airplane Hangar(FBO) - 437 S. Hangar Dr.	100.00% =	952.07	
CTORYCOSUB		12/13/2017	Page: 33



	969.95	0.04%
100.00% =	969.95	
	698.91	0.03%
100.00% =	698.91	
	1,077.28	0.05%
100.00% =	1,077.28	
	451.07	0.02%
100.00% =	451.07	0.450
	ŕ	0.17%
100.00% =	3,667.34	
	21,171.65	0.97%
100.00% =	21,171.65	
	21,171.65	0.97%
100.00% =	21,171.65	
100.000	15,995.64	0.73%
100.00% =	15,995.64	
	15,995.64	0.73%
100.00% =	15,995.64	0.000
	,	0.08%
100.00% =	1,834.13	
	17,829.77	0.81%
100.00% =	17,829.77	
	167,056.80	7.63%
100.00% =	1/7 05/ 00	
100.00% =	167,056.80	
100.00% =		20.420
100.00% =	447,185.42	20.42%
	100.00% =  100.00% =  100.00% =  100.00% =  100.00% =  100.00% =  100.00% =	100.00% = 969.95 698.91 100.00% = 698.91 1,077.28 100.00% = 1,077.28 451.07 100.00% = 451.07 3,667.34 100.00% = 21,171.65 100.00% = 21,171.65 100.00% = 15,995.64 100.00% = 15,995.64 100.00% = 15,995.64 100.00% = 15,995.64 1,834.13 100.00% = 17,829.77 100.00% = 17,829.77



Coverage: Building 18 - Airplane Hangar C - 207 Storehouse Dr.	100.00% =	447,185.42	
Shed Ext		22,243.54	1.02%
Coverage: Building 18 - Airplane Hangar C - 207 Storehouse Dr.	100.00% =	22,243.54	
Area Subtotal: Roof		469,428.96	21.44%
Coverage: Building 18 - Airplane Hangar C - 207 Storehouse Dr.	100.00% =	469,428.96	
Area Subtotal: Building 18 - Hangar C		636,485.76	29.07%
Coverage: Building 18 - Airplane Hangar C - 207 Storehouse Dr.	100.00% =	636,485.76	5 1 A 07
General Conditions	100.000	112,538.40	5.14%
Coverage: Building 18 - Airplane Hangar C - 207 Storehouse Dr.	100.00% =	112,538.40	
a: Building #19 - Precinct 4 -Truck Storage			
a: Roof		17,797.56	0.81%
Truck Shed / Storage	100 000		0.01 /0
Coverage: Building 19 - PCT #4-Truck Storage - 155 Corpus Christi	100.00% =	17,797.56	
Area Subtotal: Roof		17,797.56	0.81%
Coverage: Building 19 - PCT #4-Truck Storage - 155 Corpus Christi	100.00% =	17,797.56	
Area Subtotal: Building #19 - Precinct 4 - Truck Storage		17,797.56	0.81%
Coverage: Building 19 - PCT #4-Truck Storage - 155 Corpus Christi	100.00% =	17,797.56	
a: Building 20 - Precinct 4 - Building Roof			
a: Roof		19,346.23	0.88%
Metal	100 000	19,346.23	0.00 70
Coverage: Building 20 - PCT #4- Building - 155 Corpus Christi	100.00% =	19,340.23	
		7,850.20	0.36%
2 Story / BUR			
Coverage: Building 20 - PCT #4- Building - 155 Corpus Christi	100.00% =	7,850.20	
Coverage: Building 20 - PCT #4- Building - 155 Corpus		27,196.43	1.24%
Coverage: Building 20 - PCT #4- Building - 155 Corpus Christi	100.00% =		1.24%
Coverage: Building 20 - PCT #4- Building - 155 Corpus Christi  Area Subtotal: Roof Coverage: Building 20 - PCT #4- Building - 155 Corpus		27,196.43	1.24%
Coverage: Building 20 - PCT #4- Building - 155 Corpus Christi  Area Subtotal: Roof Coverage: Building 20 - PCT #4- Building - 155 Corpus Christi		<b>27,196.43</b> 27,196.43	





Christi

#### Area: Building #20 - Precinct 4 - Building Interior

Office 2		2 60ñ KE	0.14
	100.00% =	<b>3,089.65</b> 3,089.65	0.1
Coverage: Building 20 - PCT #4- Building - 155 Corpus Christi Hall 2	100.00% =	1,902.10	0.0
	100 000	,	0.0
Coverage: Building 20 - PCT #4- Building - 155 Corpus Christi	100.00% =	1,902.10	
Break Room		1,997.81	0.0
Coverage: Building 20 - PCT #4- Building - 155 Corpus Christi	100.00% =	1,997.81	
Office 1		4,497.82	0.2
Coverage: Building 20 - PCT #4- Building - 155 Corpus Christi	100.00% =	4,497.82	
Hallway		3,071.43	0.1
Coverage: Building 20 - PCT #4- Building - 155 Corpus Christi	100.00% =	3,071.43	
Storage		3,181.55	0.1
Coverage: Building 20 - PCT #4- Building - 155 Corpus Christi	100.00% =	3,181.55	0.0
Shower 1		1,483.05	0.0
Coverage: Building 20 - PCT #4- Building - 155 Corpus Christi	100.00% =	1,483.05	
Shower 2		1,493.39	0.0
Coverage: Building 20 - PCT #4- Building - 155 Corpus Christi	100.00% =	1,493.39	
Women		2,152.35	0.1
Coverage: Building 20 - PCT #4- Building - 155 Corpus Christi	100.00% =	2,152.35	
Mens		4,785.88	0.2
Coverage: Building 20 - PCT #4- Building - 155 Corpus Christi	100.00% =	4,785.88	
Dressing Room		1,603.09	0.0
Coverage: Building 20 - PCT #4- Building - 155 Corpus	100.00% =	1,603.09	
Christi Truck Bay 1		1,001.04	0.0
Coverage: Building 20 - PCT #4- Building - 155 Corpus Christi	100.00% =	1,001.04	
Electrical		2,016.00	0.0
Coverage: Building 20 - PCT #4- Building - 155 Corpus Christi	100.00% =	2,016.00	
Area Subtotal: Main Level		32,275.16	1.4
Coverage: Building 20 - PCT #4- Building - 155 Corpus Christi	100.00% =	32,275.16	



8380 Warren Parkway	/	Ste.	700 -	Frisco,	TX	75034
913-601-4546						

Area Subtotal: Building #20 - Precinct 4 - Building Interior		32,275.16	1.47%
Coverage: Building 20 - PCT #4- Building - 155 Corpus Christi	100.00% =	32,275.16	
rea: Building 21 - North T Hangar Roof			
area: Roof			
Roof1		25,925.22	1.18%
Coverage: Building 21 - Airplane Hangar(T-Hangar Units) -348 N. Hangar Dr.	100.00% =	25,925.22	
Area Subtotal: Roof		25,925.22	1.189
Coverage: Building 21 - Airplane Hangar(T-Hangar Units) -348 N. Hangar Dr.	100.00% =	25,925.22	
Area Subtotal: Building 21 - North T Hangar Roof		25,925.22	1.189
Coverage: Building 21 - Airplane Hangar(T-Hangar Units) -348 N. Hangar Dr.	100.00% =	25,925.22	
area: Building # 21 - North T Hangar Interior / Exterior			
rea: Main Level		6 796 20	0.210
Airfield Storage / Southeast Corner  Coverage: Building 21 - Airplane Hangar(T-Hangar Units) -348 N. Hangar Dr.	100.00% =	<b>6,786.39</b> 6,786.39	0.319
Area Subtotal: Main Level		6,786.39	0.319
Coverage: Building 21 - Airplane Hangar(T-Hangar Units) -348 N. Hangar Dr.	100.00% =	6,786.39	
Area Subtotal: Building # 21 - North T Hangar Interior / Ext	erior	6,786.39	0.319
Coverage: Building 21 - Airplane Hangar(T-Hangar Units) -348 N. Hangar Dr.	100.00% =	6,786.39	
Area: Building 22 - South T Hangar Roof			
area: Roof		7.5	
Roof1		51,151.37	2.349
Coverage: Building 22 - Aircraft Storage(T-Hangar Units)- 388 N. Hangar Dr	100.00% =	51,151.37	
Area Subtotal: Roof		51,151.37	2.349
Coverage: Building 22 - Aircraft Storage(T-Hangar Units)- 388 N. Hangar Dr Exterior / South Elevation	100.00% =	51,151.37 <b>49,244.00</b>	2.25%
Coverage: Building 22 - Aircraft Storage(T-Hangar Units)- 388 N. Hangar Dr	100.00% =	49,244.00	220
/			



	V	Vi	rtu	Ş
-	_			

Area Subtotal: Building 22 - South T Hangar Roof		100,395.37	4.58%
Coverage: Building 22 - Aircraft Storage(T-Hangar Units)-388 N. Hangar Dr	100.00% =	100,395.37	
Area: Building 23 - Office- Elections & JP 3			
Area: Main Level			
Admin Office		1,074.54	0.05%
Coverage: Building 23 - Office Elections & JP #3 - 111 N. Glass	100.00% =	1,074.54 <b>832.24</b>	0.04%
Sally's Office	100 0007 -		0.04 70
Coverage: Building 23 - Office Elections & JP #3 - 111 N. Glass Copy Room	100.00% =	832.24 <b>652.88</b>	0.03%
Coverage: Building 23 - Office Elections & JP #3 - 111 N.	100.00% =	652.88	0.00
Glass	100.00% =	032.00	
Area Subtotal: Main Level		2,559.66	0.12%
Coverage: Building 23 - Office Elections & JP #3 - 111 N. Glass	100.00% =	2,559.66	
Area Subtotal: Building 23 - Office- Elections & JP 3		2,559.66	0.12%
Coverage: Building 23 - Office Elections & JP #3 - 111 N. Glass	100.00% =	2,559.66	
Area: Building # 24- Airport Terminal with Storage Vaults General Exterior / Airstrip Fencing		22,358.40	1.02%
Coverage: Building 24 - Airport Terminal /2 Storage	100.00% =	22,358.40	1.02 /0
Buildings - 609 Foster Terminal Roof	100.00 % =	178.20	0.01%
Coverage: Building 24 - Airport Terminal /2 Storage	100.00% =	178.20	000270
Buildings - 609 Foster  Airport Terminal Exterior- Porte Cochere	100.00 % =	3,723.37	0.17%
Coverage: Building 24 - Airport Terminal /2 Storage	100.00% =	3,723.37	
Buildings - 609 Foster		20.00	
South Baggage Area		801.40	0.04%
Coverage: Building 24 - Airport Terminal /2 Storage Buildings - 609 Foster	100.00% =	801.40	
Check-In Area		34.88	
Coverage: Building 24 - Airport Terminal /2 Storage Buildings - 609 Foster	100.00% =	34.88	
Airline Operations Room		656.16	0.03%
Coverage: Building 24 - Airport Terminal /2 Storage Buildings - 609 Foster	100.00% =	656.16	
Area: South Storage Vault		# 200 O.1	0.050
South Storage Vault Roof	400.5	5,392.94	0.25%
Coverage: Building 24 - Airport Terminal /2 Storage Buildings - 609 Foster	100.00% =	5,392.94	
VICTORYCOSUB		12/13/2017	Page: 33

Virtus

8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

	97.05	
100.00% =	97.05	
	641.98	0.03%
100.00% =	641.98	
	6,131.97	0.28%
100.00% =	6,131.97	
age Vaults	33,884.38	1.55%
100.00% =	33,884.38	
	2.643.44	0.12%
100.00% =	2,643.44	0.12 /
	1,369.28	0.06%
100.00% =	1,369.28	
	998.59	0.05%
100.00% =	998.59	0.160
100.000	,	0.16%
100.00% =		0.27%
100.00% =	5,887.90	J = 1 /
	9,590.86	0.449
100.00% =	9,590.86	
	,	0.099
100.00% =	1,898.72	
	25,978.16	1.19%
100.00% =	25,978.16	
station	25,978.16	1.19%
100.00% =	25,978.16	
	100.00% =  100.00% =  100.00% =  100.00% =  100.00% =  100.00% =  100.00% =  100.00% =  100.00% =	100.00% = 97.05 641.98 100.00% = 641.98  6,131.97 100.00% = 6,131.97  age Vaults 100.00% = 33,884.38  100.00% = 1,369.28 100.00% = 998.59 100.00% = 998.59 100.00% = 3,589.37 100.00% = 3,589.37 100.00% = 5,887.90 100.00% = 9,590.86 100.00% = 9,590.86 100.00% = 1,898.72 100.00% = 1,898.72 100.00% = 25,978.16 25,978.16 25,978.16




#### Area: Building # 25 - Electrical Vault with Generator

Flat / Built-Up with Aggregate			4,273.39	0.20%
Coverage: Building 25 - Airport Maintenance w/ Generator - 41 Hangar	100.00%	=	4,273.39	
Metal			2,185.78	0.10%
Coverage: Building 25 - Airport Maintenance w/ Generator - 41 Hangar	100.00%	=	2,185.78	
Area Subtotal: Roof			6,459.17	0.29%
Coverage: Building 25 - Airport Maintenance w/ Generator - 41 Hangar	100.00%	=	6,459.17	
Area Subtotal: Building # 25 - Electrical Vault with Generator	•		6,459.17	0.29%
Coverage: Building 25 - Airport Maintenance w/ Generator - 41 Hangar	100.00%	=	6,459.17	
Building 26 - Bridge Street Annex			1 400 00	0.07%
Roof  Coverage: Building 26 - SWB Building / Bridge St.	100.00%	_	<b>1,498.98</b> 1,498.98	U.U/ %
Annex - 204 N. Bridge	100.00%	_	1,470.70	
Emergency Operation Center / Elevator Mechanical			88,481.58	4.04%
Coverage: Building 26 - SWB Building / Bridge St. Annex - 204 N. Bridge	100.00%	=	88,481.58	
EOC RegionalTraining Center			2,259.08	0.10%
Coverage: Building 26 - SWB Building / Bridge St. Annex - 204 N. Bridge	100.00%	=	2,259.08	
EOC Library			781.66	0.04%
Coverage: Building 26 - SWB Building / Bridge St. Annex - 204 N. Bridge	100.00%	=	781.66	0.04%
Historical Commission Office (1st Floor)			1,384.22	0.06%
Coverage: Building 26 - SWB Building / Bridge St. Annex - 204 N. Bridge	100.00%	=	1,384.22 <b>22.56</b>	
Storage(1st Floor)	100 000			
Coverage: Building 26 - SWB Building / Bridge St. Annex - 204 N. Bridge	100.00%	-	22.56	0.220
East Foyer & Hallway (1st Floor)	100 000		6,933.62	0.32%
Coverage: Building 26 - SWB Building / Bridge St. Annex - 204 N. Bridge Historic Archives Document Storage	100.00%	=	6,933.62 <b>590.29</b>	0.03%
Coverage: Building 26 - SWB Building / Bridge St.	100.00%	_	590.29	0.03 70
Annex - 204 N. Bridge  Stairwell Atrium (2nd Floor)	100.00%	_	1,039.98	0.05%
Coverage: Building 26 - SWB Building / Bridge St. Annex - 204 N. Bridge	100.00%	=	1,039.98	0.00 /0
County Clerk Cage (2nd Floor)			1,278.58	0.06%
Coverage: Building 26 - SWB Building / Bridge St. Annex - 204 N. Bridge	100.00%	=	1,278.58	
				Page:



8380 Warren	Parkway /	Ste. 7	700 -	Frisco,	TX	75034
913-601-4540	5					

Area Subtotal: Building 26 - Bridge Street Annex		104,270.55	4.76%
Coverage: Building 26 - SWB Building / Bridge St. Annex - 204 N. Bridge	100.00% =	104,270.55	
Area: Building 27 - Extension Service			
Area: Roof			
Flat Built- Up with Aggregate		22,295.97	1.02%
Coverage: Building 27 - Extension Service - 528 Waco Circle	100.00% =	22,295.97	
Area Subtotal: Roof		22,295.97	1.02%
Coverage: Building 27 - Extension Service - 528 Waco Circle	100.00% =	22,295.97	
Area Subtotal: Building 27 - Extension Service		22,295.97	1.02%
Coverage: Building 27 - Extension Service - 528 Waco Circle	100.00% =	22,295.97	
Area: Building #27 - Extension Service Interior			
rea: Main Level			
Office 1		500.70	0.02%
Coverage: Building 27 - Extension Service - 528 Waco Circle	100.00% =	500.70	
Managers Office		294.32	0.01%
Coverage: Building 27 - Extension Service - 528 Waco Circle	100.00% =	294.32	
Foyer/Entry		316.81	0.01%
Coverage: Building 27 - Extension Service - 528 Waco Circle	100.00% =	316.81	0.04.00
Secretary		296.12	0.01%
Coverage: Building 27 - Extension Service - 528 Waco Circle	100.00% =	296.12	
Yellow Office		669.06	0.03%
Coverage: Building 27 - Extension Service - 528 Waco Circle	100.00% =	669.06	
Orange Office		1,504.75	0.07%
Coverage: Building 27 - Extension Service - 528 Waco Circle	100.00% =	1,504.75	
Hallway		11,064.90	0.51%
Coverage: Building 27 - Extension Service - 528 Waco Circle	100.00% =	11,064.90	
Double Office #3	100.005	3,556.95	0.16%
Coverage: Building 27 - Extension Service - 528 Waco Circle	100.00% =	3,556.95	
Break Room		6,227.83	0.28%
Coverage: Building 27 - Extension Service - 528 Waco	100.00% =	6,227.83	
VICTORYCOSUB		12/13/2017	Page: 34





Circle Office 2		2,407.86	0.11%
Coverage: Building 27 - Extension Service - 528 Waco Circle	100.00% =	2,407.86	
Meeting Room		8,409.09	0.38%
Coverage: Building 27 - Extension Service - 528 Waco Circle	100.00% =	8,409.09	
Women		1,800.23	0.08%
Coverage: Building 27 - Extension Service - 528 Waco Circle	100.00% =	1,800.23	
Men	100 000	716.98	0.03%
Coverage: Building 27 - Extension Service - 528 Waco Circle Data Closet	100.00% =	716.98 <b>783.83</b>	0.04%
Coverage: Building 27 - Extension Service - 528 Waco Circle	100.00% =	783.83	0.0170
Double Office #2		1,904.53	0.09%
Coverage: Building 27 - Extension Service - 528 Waco Circle	100.00% =	1,904.53	
Double Office #1		1,827.87	0.08%
Coverage: Building 27 - Extension Service - 528 Waco Circle	100.00% =	1,827.87	0.050
Conference Room	100.000	1,097.31	0.05%
Coverage: Building 27 - Extension Service - 528 Waco Circle Anderson Office	100.00% =	1,097.31 <b>500.70</b>	0.02%
Coverage: Building 27 - Extension Service - 528 Waco Circle	100.00% =	500.70	0.02 /0
Wilhelm Office		279.26	0.01%
Coverage: Building 27 - Extension Service - 528 Waco Circle	100.00% =	279.26	
Area Subtotal: Main Level		44,159.10	2.02%
Coverage: Building 27 - Extension Service - 528 Waco Circle	100.00% =	44,159.10	
Electrical		2,520.00	0.12%
Coverage: Building 27 - Extension Service - 528 Waco Circle	100.00% =	2,520.00	
HVAC		4,742.39	0.22%
Coverage: Building 27 - Extension Service - 528 Waco Circle	100.00% =	4,742.39	
Area Subtotal: Building #27 - Extension Service Interior		51,421.49	2.35%
Coverage: Building 27 - Extension Service - 528 Waco Circle	100.00% =	51,421.49	
Building 28 - Juvenile Detention Center			
Male Unit Office	100.00%	137.82	0.01%
Coverage: Building 28 - Juvenile Detention Center - 97	100.00% =	137.82 12/13/2017	Page: 343
RYCOSUB		12/13/2017	rage: 343



-		-		
Fos	ter	HI	10	n

Foster Field			
Area Subtotal: Building 28 - Juvenile Detention Center		137.82	0.01%
Coverage: Building 28 - Juvenile Detention Center - 97 Foster Field	100.00% =	137.82	
rea: Building 30 - Health Department			
rea: Exterior		2,279.66	0.10%
Coverage: Building 30 - Health Dept - 2805 Navarro	100.00% =	2,279.66	
Storage Building		1,328.14	0.06%
Coverage: Building 30 - Health Dept - 2805 Navarro	100.00% =	1,328.14	
Area Subtotal: Exterior		3,607.80	0.16%
Coverage: Building 30 - Health Dept - 2805 Navarro	100.00% =	3,607.80	
rea: Interior		4.475.00	0.050
Foyer/Entry		1,165.32	0.05%
Coverage: Building 30 - Health Dept - 2805 Navarro	100.00% =	1,165.32	
Receptionist		1,093.98	0.05%
Coverage: Building 30 - Health Dept - 2805 Navarro	100.00% =	1,093.98	0.068
Admin Office		1,318.68	0.06%
Coverage: Building 30 - Health Dept - 2805 Navarro Manager's Office	100.00% =	1,318.68 <b>830.96</b>	0.04%
Coverage: Building 30 - Health Dept - 2805 Navarro	100.00% =	830.96	0.04 /0
Breastfeeding Counsellor	100.00 % =	<b>627.45</b>	0.03%
Coverage: Building 30 - Health Dept - 2805 Navarro	100.00% =	627.45	
Dietician	100.00%	729.45	0.03%
Coverage: Building 30 - Health Dept - 2805 Navarro	100.00% =	729.45	
Area Subtotal: Interior		5,765.84	0.26%
Coverage: Building 30 - Health Dept - 2805 Navarro	100.00% =	5,765.84	
Area Subtotal: Building 30 - Health Department		9,373.64	0.43%
Coverage: Building 30 - Health Dept - 2805 Navarro	100.00% =	9,373.64	
rea: Building 31 - 4-H Activity Center		06.00	
Exterior / South Elevation	100.000	96.00	
Coverage: Building 31 - 4-H Activity Center - 259 Bachelor Dr.	100.00% =	96.00	
rea: Interior		V 250 No.	
Womens		2,780.50	0.13%
Coverage: Building 31 - 4-H Activity Center - 259 Bachelor Dr.	100.00% =	2,780.50	
Hallway		1,157.68	0.05%
CTORYCOSUB		12/13/2017	Page: 3

8380 Warren Parkway	/	Ste.	700 -	Frisco,	TX	75034
913-601-4546						

100.00% =	1,157.68	
	3,938.18	0.18%
100.00% =	3,938.18	
	4,034.18	0.18%
100.00% =	4,034.18	
100 00% -		
100.00% =	7.32	
	201 22	0.01%
100 00% =		0.01 70
100.00 // =		
	1	0.06%
100.00% =	,	
		0.05%
100.00% =		0.09%
100 00% =	•	0.05 /0
100.00 %		0.09%
100.00% =	1,970.59	
	6,647.14	0.30%
100.00% =	6,647.14	
	6,654.66	0.30%
100.00% =	6,654.66	
		0.96%
100.00% =	21,052.65	
	21,052.65	0.96%
	12/13/2017	Page: 3
	100.00% =  100.00% =  100.00% =  100.00% =  100.00% =  100.00% =  100.00% =	3,938.18 3,938.18 100.00% = 3,938.18 100.00% = 4,034.18 100.00% = 7.52 100.00% = 301.33 100.00% = 1,301.08 100.00% = 1,081.97 100.00% = 1,992.17 100.00% = 1,970.59 100.00% = 1,970.59 100.00% = 6,647.14 100.00% = 6,654.66 100.00% = 21,052.65 100.00% = 21,052.65 21,052.65

Coverage: Building 33 - Officers Club - 333 Bachelor Dr.	100.00% =	21,052.65	
Area Subtotal: Building #33 - Officers Club		21,052.65	0.96%
Coverage: Building 33 - Officers Club - 333 Bachelor Dr.	100.00% =	21,052.65	
ea: Building 33 - Officers Club Interior			
ea: Interior			
Washroom		360.62	0.02%
Coverage: Building 33 - Officers Club - 333 Bachelor Dr.	100.00% =	360.62	0.100
Foyer	100 000	2,200.86	0.10%
Coverage: Building 33 - Officers Club - 333 Bachelor Dr. <b>Hallway</b>	100.00% =	2,200.86 <b>2,624.09</b>	0.12%
Coverage: Building 33 - Officers Club - 333 Bachelor Dr.	100.00% =	2,624.09	0.12 /0
Mens	100.00% =	513.88	0.02%
Coverage: Building 33 - Officers Club - 333 Bachelor Dr.	100.00% =	513.88	0.02,0
Womens		766.51	0.04%
Coverage: Building 33 - Officers Club - 333 Bachelor Dr.	100.00% =	766.51	
Hall Extension		2,540.65	0.12%
Coverage: Building 33 - Officers Club - 333 Bachelor Dr.	100.00% =	2,540.65	
Coat Room		3,898.52	0.18%
Coverage: Building 33 - Officers Club - 333 Bachelor Dr.	100.00% =	3,898.52	0.4.400
Office	100 000	2,984.14	0.14%
Coverage: Building 33 - Officers Club - 333 Bachelor Dr.	100.00% =	2,984.14 <b>4,910.93</b>	0.22%
Storage Area/Room  Coverage: Building 33 - Officers Club - 333 Bachelor Dr.	100.00% =	4,910.93	0.2270
Bar / Dining Area	100.00% =	74,612.43	3.41%
Coverage: Building 33 - Officers Club - 333 Bachelor Dr.	100.00% =	74,612.43	011170
Area Subtotal: Interior		95,412.63	4.36%
Coverage: Building 33 - Officers Club - 333 Bachelor Dr.	100.00% =	95,412.63	12070
ea: Exterior			
Front / North Elevation		321.00	0.01%
Coverage: Building 33 - Officers Club - 333 Bachelor Dr.	100.00% =	321.00	
West Elevation		12.50	
Coverage: Building 33 - Officers Club - 333 Bachelor Dr.	100.00% =	12.50	0.040
Rear / South Elevation	100 000	131.40	0.01%
Coverage: Building 33 - Officers Club - 333 Bachelor Dr. East Elevation	100.00% =	131.40 <b>470.16</b>	0.02%
Coverage: Building 33 - Officers Club - 333 Bachelor Dr.	100.00% =	470.16	0.02 /0
Area Subtotal: Exterior		025.06	0.04%
	100 000	935.06	0.04%
Coverage: Building 33 - Officers Club - 333 Bachelor Dr.	100.00% =	935.06	
Area Subtotal: Building 33 - Officers Club Interior		96,347.69	4.40%
TORYCOSUB		12/13/2017	Page:



Coverage: Building 33 - Officers Club - 333 Bachelor Dr.	100.00% =	96,347.69	
Area: Building 35 - COMAT Building			
Area: Roof			
BUR w/ Aggregate		51,892.62	2.37%
Coverage: Building 35 - COMAT Building - 442 Foster Field Dr.	100.00% =	51,892.62	
Area Subtotal: Roof		51,892.62	2.37%
Coverage: Building 35 - COMAT Building - 442 Foster Field Dr.	100.00% =	51,892.62	
Area Subtotal: Building 35 - COMAT Building		51,892.62	2.37%
Coverage: Building 35 - COMAT Building - 442 Foster Field Dr.	100.00% =	51,892.62	
Area: Building #35 - COMAT Building Interior			
Area: Interior			
Southeast Office		6,811.06	0.31%
Coverage: Building 35 - COMAT Building - 442 Foster Field Dr.  Center Office	100.00% =	6,811.06 <b>2,537.05</b>	0.12%
	100 0007 -	,	0.12 %
Coverage: Building 35 - COMAT Building - 442 Foster Field Dr.  Rear Entry	100.00% =	2,537.05 1,152.23	0.05%
Coverage: Building 35 - COMAT Building - 442 Foster	100.00% =	1,152.23	
Field Dr. Copy Room		1,242.79	0.06%
Coverage: Building 35 - COMAT Building - 442 Foster	100.00% =	1,242.79	0.00 /0
Field Dr. Control Room		1,718.02	0.08%
Coverage: Building 35 - COMAT Building - 442 Foster	100.00% =	1,718.02	0.00 //
Field Dr.	100,00% =		
Laboratory 1		6,471.68	0.30%
Coverage: Building 35 - COMAT Building - 442 Foster Field Dr.	100.00% =	6,471.68	
HVAC		264.35	0.01%
Coverage: Building 35 - COMAT Building - 442 Foster Field Dr.	100.00% =	264.35	
Break Room		2,266.08	0.10%
Coverage: Building 35 - COMAT Building - 442 Foster Field Dr.	100.00% =	2,266.08	0.000
Office 1	100 000/	1,784.72	0.08%
Coverage: Building 35 - COMAT Building - 442 Foster Field Dr.	100.00% =	1,784.72	
Hallway 2		3,385.13	0.15%
Coverage: Building 35 - COMAT Building - 442 Foster	100.00% =	3,385.13	
VICTORYCOSUB		12/13/2017	Page: 347



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

Field Dr. Foyer/Entry		1,109.77	0.05%
Coverage: Building 35 - COMAT Building - 442 Foster Field Dr.	100.00% =	1,109.77	
Receptionist		1,962.70	0.09%
Coverage: Building 35 - COMAT Building - 442 Foster Field Dr.	100.00% =	1,962.70	
Storage		436.03	0.02%
Coverage: Building 35 - COMAT Building - 442 Foster Field Dr.	100.00% =	436.03	
Training 1	400.000	2,665.27	0.12%
Coverage: Building 35 - COMAT Building - 442 Foster Field Dr.  Bathroom Hall	100.00% =	2,665.27	0.06
	100.000	1,307.80	0.06%
Coverage: Building 35 - COMAT Building - 442 Foster Field Dr.  Mens Entry	100.00% =	1,307.80 <b>581.10</b>	0.03%
Coverage: Building 35 - COMAT Building - 442 Foster	100 000/		0.05%
Field Dr.  Mens	100.00% =	581.10	0.010
	100 000	310.42	0.01%
Coverage: Building 35 - COMAT Building - 442 Foster Field Dr.  Womens	100.00% =	310.42 <b>276.68</b>	0.01%
	100 000/		0.01%
Coverage: Building 35 - COMAT Building - 442 Foster Field Dr.  Powder Room	100.00% =	276.68 1 <b>,608.63</b>	0.07%
Coverage: Building 35 - COMAT Building - 442 Foster	100.00% =	1,608.63	0.07 /0
Field Dr.  Training 2	100.50%	1,802.45	0.08%
Coverage: Building 35 - COMAT Building - 442 Foster	100.00% =	1,802.45	
Field Dr. Center Hallway		2,374.28	0.11%
Coverage: Building 35 - COMAT Building - 442 Foster Field Dr.	100.00% =	2,374.28	
North Storage		98.40	
Coverage: Building 35 - COMAT Building - 442 Foster Field Dr.	100.00% =	98.40	
Electrical		2,016.00	0.09%
Coverage: Building 35 - COMAT Building - 442 Foster Field Dr.	100.00% =	2,016.00	
Area Subtotal: Interior		44,182.64	2.02%
Coverage: Building 35 - COMAT Building - 442 Foster Field Dr.	100.00% =	44,182.64	
Area Subtotal: Building #35 - COMAT Building Interior		44,182.64	2.02%
Coverage: Building 35 - COMAT Building - 442 Foster Field Dr.	100.00% =	44,182.64	



Area: Building 36 - Animal Shelter / Control			
Roof		287.35	0.01%
Coverage: Building 36 - Animal Shelter - 102 Perimeter Rd.	100.00% =	287.35	
Exterior		1,116.14	0.05%
Coverage: Building 36 - Animal Shelter - 102 Perimeter Rd.	100.00% =	1,116.14	
Front Office		189.20	0.01%
Coverage: Building 36 - Animal Shelter - 102 Perimeter Rd.	100.00% =	189.20	
Cat Shelter		51.60	
Coverage: Building 36 - Animal Shelter - 102 Perimeter Rd.	100.00% =	51.60	
Area Subtotal: Building 36 - Animal Shelter / Control		1,644.29	0.08%
Coverage: Building 36 - Animal Shelter - 102 Perimeter Rd.	100.00% =	1,644.29	
area: Building 38 - Storehouse		FFC 10	0.02%
Roof		576.40	0.03%
Coverage: Building 38 - Storehouse - 103 S Glass	100.00% =	576.40	
rea: Exterior South Elevation		955.20	0.04%
Coverage: Building 38 - Storehouse - 103 S Glass	100.00% =	955.20	0.0470
Front / East Elevation	100.00% =	<b>629.30</b>	0.03%
Coverage: Building 38 - Storehouse - 103 S Glass	100.00% =	629.30	0.00 /0
Area Subtotal: Exterior		1,584.50	0.07%
Coverage: Building 38 - Storehouse - 103 S Glass	100.00% =	1,584.50	
Area: Ground Level Interior		2 202 20	0.100
South Room	100.000	2,283.39	0.10%
Coverage: Building 38 - Storehouse - 103 S Glass	100.00% =	2,283.39	0.0407
East Center Office		927.44	0.04%
Coverage: Building 38 - Storehouse - 103 S Glass	100.00% =	927.44	
Area Subtotal: Ground Level Interior		3,210.83	0.15%
Coverage: Building 38 - Storehouse - 103 S Glass	100.00% =	3,210.83	
Area: Second Level Interior Rear Center Office		1,223.76	0.06%
	100.00% =	1,223.76	0.00 /0
Coverage: Building 38 - Storehouse - 103 S Glass Front Center Office	100.00% =	1,523.40	0.07%
	100 000/	1,523.40	0.01 /0
Coverage: Building 38 - Storehouse - 103 S Glass Kitchen	100.00% =	<b>467.73</b>	0.02%
ICTORYCOSUB		12/13/2017	Page: 3

# Virtus Group 8380 Warren Park 913-601-4546

8380 Warren Parkway	/	Ste.	700 -	Frisco, T	'X	75034
913-601-4546						

Coverage: Building 38 - Storehouse - 103 S Glass North Center Room	100.00% =	467.73 <b>592.98</b>	0.03%
Coverage: Building 38 - Storehouse - 103 S Glass	100.00% =	592.98	0.100
Training Room  Coverage: Building 38 - Storehouse - 103 S Glass	100.00% =	<b>3,874.26</b> 3,874.26	0.18%
Area: Basement Interior South Storage		3,835.63	0.18%
Coverage: Building 38 - Storehouse - 103 S Glass	100.00% =	3,835.63	
North Storage		1,496.88	0.07%
Coverage: Building 38 - Storehouse - 103 S Glass	100.00% =	1,496.88	
Restroom		331.53	0.02%
Coverage: Building 38 - Storehouse - 103 S Glass	100.00% =	331.53	
Area Subtotal: Basement Interior		5,664.04	0.26%
Coverage: Building 38 - Storehouse - 103 S Glass	100.00% =	5,664.04	
Area Subtotal: Second Level Interior		13,346.17	0.61%
Coverage: Building 38 - Storehouse - 103 S Glass	100.00% =	13,346.17	
Area Subtotal: Building 38 - Storehouse		18,717.90	0.85%
Coverage: Building 38 - Storehouse - 103 S Glass	100.00% =	18,717.90	
Area: Roof Roof1		15,105.43	0.69%
Coverage: Building 39 - AARFF Station (Fire Station) - 121 N Hangar	100.00% =	15,105.43	
Area Subtotal: Roof		15,105.43	0.69%
Coverage: Building 39 - AARFF Station (Fire Station) - 121 N Hangar	100.00% =	15,105.43	
Area: Exterior / General		138.03	0.01%
Coverage: Building 39 - AARFF Station (Fire Station) - 121 N Hangar	100.00% =	138.03	
West Elevation	000 800	245.64	0.01%
Coverage: Building 39 - AARFF Station (Fire Station) - 121 N Hangar	100.00% =	245.64	
Area Subtotal: Exterior / General		383.67	0.02%
Coverage: Building 39 - AARFF Station (Fire Station) - 121 N Hangar	100.00% =	383.67	
Area Subtotal: Building 39 - AARF Fire Station		15,489.10	0.71%
Coverage: Building 39 - AARFF Station (Fire Station) -	100.00% =	15,489.10	
VICTORYCOSUB		12/13/2017	Page: 350





121 N Hangar

: Building #41 - Control Tower Roof		7.24	
Coverage: Building 41 - Control Tower / Airport - 348 Bachelor Dr.	100.00% =	7.24	
Exterior / East Elevation		17,060.37	0.78%
Coverage: Building 41 - Control Tower / Airport - 348 Bachelor Dr.	100.00% =	17,060.37	
: Interior		1 177 77	0.05%
5th Floor Recorder Room	100 000/	1,177.77	0.05%
Coverage: Building 41 - Control Tower / Airport - 348 Bachelor Dr. 4th Floor Managers Office	100.00% =	1,177.77 <b>80.05</b>	
Coverage: Building 41 - Control Tower / Airport - 348	100.00% =	80.05	
Bachelor Dr.  3rd Floor Office	100.00%	1,836.15	0.08%
Coverage: Building 41 - Control Tower / Airport - 348	100.00% =	1,836.15	
Bachelor Dr.			0.050
2nd Floor Office	.00.000	1,166.18	0.05%
Coverage: Building 41 - Control Tower / Airport - 348 Bachelor Dr.	100.00% =	1,166.18	
Area Subtotal: Interior		4,260.15	0.19%
Coverage: Building 41 - Control Tower / Airport - 348 Bachelor Dr.  6th Floor Break Room	100.00% =	4,260.15 <b>75.20</b>	
Coverage: Building 41 - Control Tower / Airport - 348	100.00% =	75.20	
Bachelor Dr.	100.00%	75.20	
Area Subtotal: Building #41 - Control Tower		21,402.96	0.98%
Coverage: Building 41 - Control Tower / Airport - 348 Bachelor Dr.	100.00% =	21,402.96	0.080
Building 47 - Precinct #4 New Barn (226 Beck Road)	100.000	5,954.58	0.27%
Coverage: Building 47 - PCT #4-New Barn - 226 Beck Road	100.00% =	5,954.58	
a: Building 50 - Celebration Church (358 Foster Field)			
a: Roof		4 = 24 = 4	
Roof Section C	100.000	1,591.71	0.07%
Coverage: Building 50 - Celebration Church - 358 Foster Field Roof Section D	100.00% =	1,591.71 <b>2,908.06</b>	0.13%
Coverage: Building 50 - Celebration Church - 358 Foster Field	100.00% =	2,908.06	0.13 /0
Area Subtotal: Roof			0.21%
CORYCOSUB		12/13/2017	Page:

V	Virtus

		4,499.77	
100.00%	=	4,499.77	
		1,602.02	0.07%
100.00%	=	1,602.02	0.07 /6
er Field)		6,101.79	0.28%
100.00%	=	6,101.79	
		,	0.05%
100.00%	=	1,030.48	
		,	0.70%
100.00%	=	15,334.72	
		15,334.72	0.70%
100.00%	=	15,334.72	
		16,365.20	0.75%
100.00%	=	16,365.20	
100.000		· ·	0.09%
100.00%	=		
100 000			
100.00%	=	60.76	
		2,216.69	0.10%
100.00%	=	2,216.69	
		14,964.06	0.68%
100.00%	=	14,964.06	
		19,296.66	0.88%
100.00%	=	19,296.66	
		12/13/2017	Page: 35
	100.00% er Field) 100.00%  100.00%  100.00%  100.00%  100.00%  100.00%  100.00%	100.00% =  100.00% =  100.00% =  100.00% =  100.00% =  100.00% =  100.00% =  100.00% =  100.00% =	1,602.02 1,602.02 1,602.02  er Field) 100.00% = 6,101.79  100.00% = 1,030.48 1,030.4

# Virtus Group 8380 Warren Park 913-601-4546

8380 Warren	Parkway /	Ste.	700 -	Frisco,	TX 75034
913-601-454	6				

Area Subtotal: Building # 51 - Sky Restaurant Interior			19,296.66	0.88%
Coverage: Building 51 - Sky Restaurant - 236 Foster Field	100.00%	=	19,296.66	
rea: Building 52 - Fisher Stevens (43 Storehouse)				
rea: Roof				
Roof1			80,473.50	3.67%
Coverage: Building 52 - Fisher Stevens - 43 Storehouse	100.00%	=	80,473.50	
Area Subtotal: Roof			80,473.50	3.67%
Coverage: Building 52 - Fisher Stevens - 43 Storehouse	100.00%	=	80,473.50	
rea: Exterior				
Front / West Elevation			1,013.27	0.05%
Coverage: Building 52 - Fisher Stevens - 43 Storehouse	100.00%	=	1,013.27	
North Elevation			709.54	0.03%
Coverage: Building 52 - Fisher Stevens - 43 Storehouse	100.00%	=	709.54	
Rear / East Elevation			18,966.78	0.87%
Coverage: Building 52 - Fisher Stevens - 43 Storehouse	100.00%	=	18,966.78	
South Elevation			5,614.55	0.26%
Coverage: Building 52 - Fisher Stevens - 43 Storehouse	100.00%	=	5,614.55	
Area Subtotal: Exterior			26,304.14	1.20%
Coverage: Building 52 - Fisher Stevens - 43 Storehouse	100.00%	=	26,304.14	
Area Subtotal: Building 52 - Fisher Stevens (43 Storehouse)			106,777.64	4.88%
Coverage: Building 52 - Fisher Stevens - 43 Storehouse	100.00%	=	106,777.64	
rea: Building 53 - Reliant Field Services				
rea: Roof			1.050.05	0.000
Roof1			1,858.87	0.08%
Coverage: Building 53 - Reliant Field Services - 112 Corpus Chrisit	100.00%	=	1,858.87	
Area Subtotal: Roof			1,858.87	0.08%
Coverage: Building 53 - Reliant Field Services - 112 Corpus Chrisit	100.00%	=	1,858.87	
rea: Exterior				
East Elevation			1,132.25	0.05%
Coverage: Building 53 - Reliant Field Services - 112 Corpus Chrisit	100.00%	=	1,132.25	
North Elevation	400		104.20	
Coverage: Building 53 - Reliant Field Services - 112 Corpus Chrisit	100.00%	=	104.20	
CTORYCOSUB			12/13/2017	Page: 3





Virtus 8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

Area Subtotal: Exterior		1,236.45	0.06%
Coverage: Building 53 - Reliant Field Services - 112 Corpus Chrisit	100.00% =	1,236.45	
Area Subtotal: Building 53 - Reliant Field Services		3,095.32	0.14%
Coverage: Building 53 - Reliant Field Services - 112 Corpus Chrisit	100.00% =	3,095.32	
Area: Building 54 - Townsend Remodeling(470 B Foster Field)			
Area: Roof			
Roof1		6,315.97	0.29%
Coverage: Building 54 - Townsend Remodeling Unamed - 470 Foster Field	100.00% =	6,315.97	
Area Subtotal: Roof		6,315.97	0.29%
Coverage: Building 54 - Townsend Remodeling Unamed - 470 Foster Field	100.00% =	6,315.97	
Area: Exterior		218.32	0.01%
North Elevation	100.000		0.01%
Coverage: Building 54 - Townsend Remodeling Unamed - 470 Foster Field  Front / East Elevation	100.00% =	218.32 <b>224.36</b>	0.01%
Coverage: Building 54 - Townsend Remodeling Unamed - 470 Foster Field	100.00% =	224.36	
South Elevation		54.58	
Coverage: Building 54 - Townsend Remodeling Unamed - 470 Foster Field	100.00% =	54.58	
Area Subtotal: Exterior		497.26	0.02%
Coverage: Building 54 - Townsend Remodeling Unamed - 470 Foster Field	100.00% =	497.26	
Area: Interior		1,525.12	0.07%
Rear Materials Room  Coverage: Building 54 - Townsend Remodeling Unamed - 470 Foster Field	100.00% =	1,525.12	0.07 70
Shop Paint Area		1,508.98	0.07%
Coverage: Building 54 - Townsend Remodeling Unamed - 470 Foster Field	100.00% =	1,508.98	
Area Subtotal: Interior		3,034.10	0.14%
Coverage: Building 54 - Townsend Remodeling Unamed - 470 Foster Field	100.00% =	3,034.10	
Area Subtotal: Building 54 - Townsend Remodeling(470 B Fe	oster Field)	9,847.33	0.45%
VICTORYCOSUB		12/13/2017	Page: 3



Wirtus 8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

Coverage: Building 54 - Townsend Remodeling Unamed - 470 Foster Field	100.00%	=	9,847.33	
rea: Building 56 - LDS Builders (396 Foster Field)				
rea: Roof				
Roof1			4,300.50	0.20%
Coverage: Building 56 - LDS Builders - 396 Foster Field	100.00%	=	4,300.50	
Area Subtotal: Roof			4,300.50	0.20%
Coverage: Building 56 - LDS Builders - 396 Foster Field	100.00%	-	4,300.50	
rea: Exterior				
Front / East Elevation			2,157.34	0.10%
Coverage: Building 56 - LDS Builders - 396 Foster Field	100.00%	=	2,157.34	
North Elevation			1,245.07	0.06%
Coverage: Building 56 - LDS Builders - 396 Foster Field	100.00%	=	1,245.07	
Area Subtotal: Exterior			3,402.41	0.16%
Coverage: Building 56 - LDS Builders - 396 Foster Field	100.00%	=	3,402.41	
rea: Interior				
Work Shop			6,785.49	0.31%
Coverage: Building 56 - LDS Builders - 396 Foster Field	100.00%	=	6,785.49	
Storage Area/Room			242.48	0.01%
Coverage: Building 56 - LDS Builders - 396 Foster Field	100.00%	=	242.48	
Area Subtotal: Interior			7,027.97	0.32%
Coverage: Building 56 - LDS Builders - 396 Foster Field	100.00%	=	7,027.97	
Area Subtotal: Building 56 - LDS Builders (396 Foster Field)			14,730.88	0.67%
Coverage: Building 56 - LDS Builders - 396 Foster Field	100.00%	=	14,730.88	
area: Building 57 - Straight Arrow Archery				
rea: Roof				
Roof1			2,217.23	0.10%
Coverage: Building 57 - Straight Arrow Archery - 60 Storehouse	100.00%	=	2,217.23	
Porch Roof			1,598.79	0.07%
Coverage: Building 57 - Straight Arrow Archery - 60 Storehouse	100.00%	=	1,598.79	
Area Subtotal: Roof			3,816.02	0.17%
Coverage: Building 57 - Straight Arrow Archery - 60 Storehouse	100.00%	=	3,816.02	
ICTORYCOSUB			12/13/2017	Page: 3



		1.880.03	0.09%
100.00%	=	1,880.03	000770
		1,880.03	0.09%
100.00%	=	1,880.03	
		5,696.05	0.26%
100.00%	=	5,696.05	
		3 826 70	0.17%
100.00%	=	3,826.70	0.17 /0
		3,826.70	0.17%
100.00%	=	3,826.70	
rtments		3,826.70	0.17%
100.00%	=	3,826.70	
			0.01%
100.00%	=	206.21	
ngar)		206.21	0.01%
nngar) 100.00%	=	<b>206.21</b> 206.21	0.01%
	=		0.01%
	=	206.21	
100.00%		206.21 21,637.17	0.01%
		206.21 21,637.17 21,637.17	0.99%
100.00%	=	21,637.17 21,637.17 1,997.83	
100.00%	=	206.21 21,637.17 21,637.17	0.99%
100.00%	=	21,637.17 21,637.17 1,997.83	0.99%
	100.00% 100.00% 100.00% rtments 100.00%	100.00% =  100.00% =  100.00% =  100.00% =  rtments  100.00% =	1,880.03 100.00% = 1,880.03  5,696.05 100.00% = 5,696.05  3,826.70 3,826.70 3,826.70 3,826.70 100.00% = 3,826.70  rtments 100.00% = 3,826.70 206.21

Coverage:	Building 60 - Vacant Building - 479 Waco	100.00% =	23,635.00	
Circle	building 60 - Vacant Building - 479 Waco	100.00%		
Area Subtotal:	Building 60 - Vacant (479 Waco Circle)		23,635.00	1.08%
Coverage: Circle	Building 60 - Vacant Building - 479 Waco	100.00% =	23,635.00	
rea: Building 61 - Go	olden Crescent / GCRP (568 Waco Circle)			
rea: Roof				
Roof1			32,157.03	1.47%
Coverage: 568 Waco	Building 61 - Old Golden Crescent - GCRP - Circle	100.00% =	32,157.03	
Area Subtotal:	Roof		32,157.03	1.47%
568 Waco		100.00% =	32,157.03 109.16	
	r East Elevation	100.000		
Coverage: 568 Waco	Building 61 - Old Golden Crescent - GCRP - Circle	100.00% =	109.16	
Area Subtotal	Building 61 - Golden Crescent / GCRP (568	8 Waco Circle)	32,266.19	1.47%
		100000		
Coverage: 568 Waco	Building 61 - Old Golden Crescent - GCRP - Circle	100.00% =	32,266.19	
568 Waco		100.00% =	32,266.19	
568 Waco rea: Building 62 - To rea: Roof	Circle	100.00% =		0.22//
568 Waco rea: Building 62 - To rea: Roof Roof1	Circle exas Mile Warehouse (131 Hangar)		6,902.31	0.32%
568 Waco rea: Building 62 - To rea: Roof Roof1 Coverage: Hangar	Circle  exas Mile Warehouse (131 Hangar)  Building 62 - Texas Mile Warehouse - 131	100.00% =	<b>6,902.31</b> 6,902.31	
568 Waco rea: Building 62 - To rea: Roof Roof1 Coverage: Hangar Canopy / Sout	Circle  exas Mile Warehouse (131 Hangar)  Building 62 - Texas Mile Warehouse - 131  h Elevation	100.00% =	6,902.31 6,902.31 2,184.21	0.32% 0.10%
568 Waco rea: Building 62 - To rea: Roof Roof1 Coverage: Hangar Canopy / Sout	Circle  exas Mile Warehouse (131 Hangar)  Building 62 - Texas Mile Warehouse - 131		<b>6,902.31</b> 6,902.31	
568 Waco rea: Building 62 - To rea: Roof Roof1 Coverage: Hangar Canopy / Sout Coverage:	exas Mile Warehouse (131 Hangar)  Building 62 - Texas Mile Warehouse - 131  h Elevation  Building 62 - Texas Mile Warehouse - 131	100.00% =	6,902.31 6,902.31 2,184.21	
rea: Building 62 - To rea: Roof Roof1 Coverage: Hangar Canopy / Sout Coverage: Hangar	exas Mile Warehouse (131 Hangar)  Building 62 - Texas Mile Warehouse - 131  h Elevation  Building 62 - Texas Mile Warehouse - 131	100.00% =	6,902.31 6,902.31 2,184.21 2,184.21 9,086.52 9,086.52	0.10%
rea: Building 62 - To rea: Roof Roof1 Coverage: Hangar Canopy / Sout Coverage: Hangar Area Subtotal Coverage:	Circle  Exas Mile Warehouse (131 Hangar)  Building 62 - Texas Mile Warehouse - 131  h Elevation  Building 62 - Texas Mile Warehouse - 131  : Roof  Building 62 - Texas Mile Warehouse - 131	100.00% = 100.00% =	6,902.31 6,902.31 2,184.21 2,184.21 9,086.52 9,086.52 566.99	0.10%
rea: Building 62 - To rea: Roof Roof1 Coverage: Hangar Canopy / Sout Coverage: Hangar Area Subtotal Coverage: Hangar Exterior / Sou	Circle  Exas Mile Warehouse (131 Hangar)  Building 62 - Texas Mile Warehouse - 131  h Elevation  Building 62 - Texas Mile Warehouse - 131  : Roof  Building 62 - Texas Mile Warehouse - 131	100.00% = 100.00% =	6,902.31 6,902.31 2,184.21 2,184.21 9,086.52 9,086.52	0.10%
rea: Building 62 - To rea: Roof Roof1 Coverage: Hangar Canopy / Sout Coverage: Hangar Area Subtotal Coverage: Hangar Exterior / Sou Coverage: Hangar	Circle  exas Mile Warehouse (131 Hangar)  Building 62 - Texas Mile Warehouse - 131  h Elevation  Building 62 - Texas Mile Warehouse - 131  : Roof  Building 62 - Texas Mile Warehouse - 131  th Elevation  Building 62 - Texas Mile Warehouse - 131	100.00% = 100.00% =	6,902.31 6,902.31 2,184.21 2,184.21 9,086.52 9,086.52 566.99 566.99	0.10%
rea: Building 62 - To rea: Roof Roof1 Coverage: Hangar Canopy / Sout Coverage: Hangar Area Subtotal Coverage: Hangar Exterior / Sou Coverage: Hangar Exterior / Sou Coverage: Hangar Storage Area/	Circle  exas Mile Warehouse (131 Hangar)  Building 62 - Texas Mile Warehouse - 131  h Elevation  Building 62 - Texas Mile Warehouse - 131  : Roof  Building 62 - Texas Mile Warehouse - 131  th Elevation  Building 62 - Texas Mile Warehouse - 131	100.00% =  100.00% =  100.00% =	6,902.31 6,902.31 2,184.21 2,184.21 9,086.52 9,086.52 566.99 566.99	0.10%
rea: Building 62 - To rea: Roof Roof1 Coverage: Hangar Canopy / Sout Coverage: Hangar Area Subtotal Coverage: Hangar Exterior / Sou Coverage: Hangar Coverage: Hangar Coverage: Hangar Coverage: Hangar Coverage: Hangar	Circle  exas Mile Warehouse (131 Hangar)  Building 62 - Texas Mile Warehouse - 131  h Elevation  Building 62 - Texas Mile Warehouse - 131  : Roof  Building 62 - Texas Mile Warehouse - 131  th Elevation  Building 62 - Texas Mile Warehouse - 131	100.00% = 100.00% =	6,902.31 6,902.31 2,184.21 2,184.21 9,086.52 9,086.52 566.99 566.99	0.10% 0.41% 0.03%
rea: Building 62 - To rea: Roof Roof1 Coverage: Hangar Canopy / Sout Coverage: Hangar Area Subtotal Coverage: Hangar Exterior / Sou Coverage: Hangar Area: Interior Storage Area/ Coverage: Hangar Office	Circle  exas Mile Warehouse (131 Hangar)  Building 62 - Texas Mile Warehouse - 131  h Elevation  Building 62 - Texas Mile Warehouse - 131  : Roof  Building 62 - Texas Mile Warehouse - 131  th Elevation  Building 62 - Texas Mile Warehouse - 131  Room  Building 62 - Texas Mile Warehouse - 131	100.00% =  100.00% =  100.00% =  100.00% =	6,902.31 6,902.31 2,184.21 2,184.21 9,086.52 9,086.52 566.99 566.99	0.10%
rea: Building 62 - To rea: Roof Roof1 Coverage: Hangar Canopy / Sout Coverage: Hangar Area Subtotal Coverage: Hangar Exterior / Sou Coverage: Hangar Area: Interior Storage Area/ Coverage: Hangar Office	Circle  exas Mile Warehouse (131 Hangar)  Building 62 - Texas Mile Warehouse - 131  h Elevation  Building 62 - Texas Mile Warehouse - 131  : Roof  Building 62 - Texas Mile Warehouse - 131  th Elevation  Building 62 - Texas Mile Warehouse - 131	100.00% =  100.00% =  100.00% =	6,902.31 6,902.31 2,184.21 2,184.21 9,086.52 9,086.52 566.99 566.99	0.10% 0.41% 0.03%





Hangar				
Area Subtotal: Interior			12,744.31	0.58%
Coverage: Building 62 - Texas Mile Warehouse - 131 Hangar	100.00%	=	12,744.31	
Area Subtotal: Building 62 - Texas Mile Warehouse (131 Ha	ngar)		22,397.82	1.02%
Coverage: Building 62 - Texas Mile Warehouse - 131 Hangar	100.00%	=	22,397.82	
Area: Building 63 - Condemned (H&H Door) Warehouse				
Area: Exterior				
Area: Security Fencing / South Elevation			16,578.46	0.76%
Coverage: Building 63 - Condemned Warehouse (H&H Door) - 158 Hangar	100.00%	=	16,578.46	
Gates			6,533.96	0.30%
Coverage: Building 63 - Condemned Warehouse (H&H Door) - 158 Hangar	100.00%	=	6,533.96	
Area Subtotal: Security Fencing / South Elevation			23,112.42	1.06%
Coverage: Building 63 - Condemned Warehouse (H&H Door) - 158 Hangar	100.00%	=	23,112.42	
Area Subtotal: Exterior			23,112.42	1.06%
Coverage: Building 63 - Condemned Warehouse (H&H Door) - 158 Hangar	100.00%	=	23,112.42	
Area Subtotal: Building 63 - Condemned (H&H Door) Ware	ehouse		23,112.42	1.06%
Coverage: Building 63 - Condemned Warehouse (H&H Door) - 158 Hangar	100.00%	=	23,112.42	
Area: Building 65 - Old Brig (153 Corpus Christi)			353.93	0.02%
Roof  Coverage: Building 65 - Old Brig - 153 Corpus Christi	100.00%	_	353.93	0.02 /0
Exterior / Fencing (South & West Elevations)	100.00 %	_	15,344.40	0.70%
Coverage: Building 65 - Old Brig - 153 Corpus Christi	100.00%	=	15,344.40	
Area Subtotal: Building 65 - Old Brig (153 Corpus Christi)			15,698.33	0.72%
Coverage: Building 65 - Old Brig - 153 Corpus Christi	100.00%	=	15,698.33	
Area: Building 66 - Old Dorm Building (294 Foster Field)				
Area: Roof				
Roof1			45,633.19	2.08%
Coverage: Building 66 - Old Dorm Building - 294 Foster Field	100.00%	=	45,633.19	
VICTORYCOSUB			12/13/2017	Page: 3



HVAC 1				
			5,102.83	0.23%
Coverage: Building 66 - Old Dorm Building - 294 Foster	100.00%	=	5,102.83	
Field				- 2.000
HVAC 2			5,102.83	0.23%
Coverage: Building 66 - Old Dorm Building - 294 Foster Field	100.00%	=	5,102.83	
HVAC 3			5,102.83	0.23%
Coverage: Building 66 - Old Dorm Building - 294 Foster	100.00%	=	5,102.83	
Field HVAC 4			5,102.83	0.23%
Coverage: Building 66 - Old Dorm Building - 294 Foster	100.00%	_	5,102.83	02370
Field  HVAC 5	100.00%	-	5,102.83	0.23%
	100.00%	_	,	025/0
Coverage: Building 66 - Old Dorm Building - 294 Foster Field  HVAC 6	100.00%	=	5,102.83 5,102.83	0.23%
	100.000		,	0.23%
Coverage: Building 66 - Old Dorm Building - 294 Foster Field	100.00%	=	5,102.83	0.224
HVAC 7	100		5,102.83	0.23%
Coverage: Building 66 - Old Dorm Building - 294 Foster Field	100.00%	=	5,102.83	
Area Subtotal: Roof		_	81,353.00	3.72%
Coverage: Building 66 - Old Dorm Building - 294 Foster	100.00%	=	81,353.00	
Field				
Area Subtotal: Building 66 - Old Dorm Building (294 Foster	Field)	_	81,353.00	3.72%
Coverage: Building 66 - Old Dorm Building - 294 Foster Field	100.00%	=	81,353.00	
tal of Areas		-	2,189,792.41	100.00%
coverage: Building 1- Old Jail- 206 W. Constitution	1.47%	=	<b>2,189,792.41</b> 32,180.91	100.00%
Coverage: Building 1- Old Jail- 206 W. Constitution Coverage: Building 2- Old Courthouse - 101 N. Bridge	0.13%	=	32,180.91 2,937.31	100.00%
Coverage: Building 1- Old Jail- 206 W. Constitution Coverage: Building 2- Old Courthouse - 101 N. Bridge Coverage: Building 3 - Old Courthouse Tunnel	0.13% 0.03%	=	32,180.91 2,937.31 592.19	100.00%
Coverage: Building 1- Old Jail- 206 W. Constitution Coverage: Building 2- Old Courthouse - 101 N. Bridge Coverage: Building 3 - Old Courthouse Tunnel Coverage: Building 4 - New Courthouse - 115 N. Bridge	0.13% 0.03% 0.32%	= = =	32,180.91 2,937.31 592.19 7,043.64	100.00%
Coverage: Building 1- Old Jail- 206 W. Constitution Coverage: Building 2- Old Courthouse - 101 N. Bridge Coverage: Building 3 - Old Courthouse Tunnel Coverage: Building 4 - New Courthouse - 115 N. Bridge Coverage: Building 5 - Old Fire Station - 209 W. Forrest	0.13% 0.03% 0.32% 0.22%	= = = =	32,180.91 2,937.31 592.19 7,043.64 4,899.80	100.00%
Coverage: Building 1- Old Jail- 206 W. Constitution Coverage: Building 2- Old Courthouse - 101 N. Bridge Coverage: Building 3 - Old Courthouse Tunnel Coverage: Building 4 - New Courthouse - 115 N. Bridge	0.13% 0.03% 0.32%	= = = =	32,180.91 2,937.31 592.19 7,043.64	100.00%
Coverage: Building 1- Old Jail- 206 W. Constitution Coverage: Building 2- Old Courthouse - 101 N. Bridge Coverage: Building 3 - Old Courthouse Tunnel Coverage: Building 4 - New Courthouse - 115 N. Bridge Coverage: Building 5 - Old Fire Station - 209 W. Forrest Coverage: Building 6 - PCT #1- Machine Storage- 2000	0.13% 0.03% 0.32% 0.22%	= = = =	32,180.91 2,937.31 592.19 7,043.64 4,899.80	100.00%
Coverage: Building 1- Old Jail- 206 W. Constitution Coverage: Building 2- Old Courthouse - 101 N. Bridge Coverage: Building 3 - Old Courthouse Tunnel Coverage: Building 4 - New Courthouse - 115 N. Bridge Coverage: Building 5 - Old Fire Station - 209 W. Forrest Coverage: Building 6 - PCT #1- Machine Storage- 2000 FM 1686 Coverage: Building 7 - PCT #3- Machine Storage - 133	0.13% 0.03% 0.32% 0.22% 0.74% 1.96% 0.04%	= = = = = = = = = = = = = = = = = = = =	32,180.91 2,937.31 592.19 7,043.64 4,899.80 16,227.18 42,879.82 968.14	100.00%
Coverage: Building 1- Old Jail- 206 W. Constitution Coverage: Building 2- Old Courthouse - 101 N. Bridge Coverage: Building 3 - Old Courthouse Tunnel Coverage: Building 4 - New Courthouse - 115 N. Bridge Coverage: Building 5 - Old Fire Station - 209 W. Forrest Coverage: Building 6 - PCT #1- Machine Storage- 2000 FM 1686 Coverage: Building 7 - PCT #3- Machine Storage - 133 Aloe Field Coverage: Building 8 - PCT #3-Radio Tower-133 Aloe	0.13% 0.03% 0.32% 0.22% 0.74% 1.96% 0.04%	= = = = =	32,180.91 2,937.31 592.19 7,043.64 4,899.80 16,227.18 42,879.82 968.14 4,741.44	100.00%
Coverage: Building 1- Old Jail- 206 W. Constitution Coverage: Building 2- Old Courthouse - 101 N. Bridge Coverage: Building 3 - Old Courthouse Tunnel Coverage: Building 4 - New Courthouse - 115 N. Bridge Coverage: Building 5 - Old Fire Station - 209 W. Forrest Coverage: Building 6 - PCT #1- Machine Storage- 2000 FM 1686 Coverage: Building 7 - PCT #3- Machine Storage - 133 Aloe Field Coverage: Building 8 - PCT #3-Radio Tower-133 Aloe Field Coverage: Building 9 - PCT #3-Mechanic Shop - 133 Aloe Field Coverage: Building 10 - PCT #3-Service Center Cover- 133 Aloe Field	0.13% 0.03% 0.32% 0.22% 0.74% 1.96% 0.04% 0.22%	= = = = = = = = = = = = = = = = = = = =	32,180.91 2,937.31 592.19 7,043.64 4,899.80 16,227.18 42,879.82 968.14 4,741.44 3,056.82	100.00%
Coverage: Building 2- Old Courthouse - 101 N. Bridge Coverage: Building 3 - Old Courthouse Tunnel Coverage: Building 4 - New Courthouse - 115 N. Bridge Coverage: Building 5 - Old Fire Station - 209 W. Forrest Coverage: Building 6 - PCT #1- Machine Storage- 2000 FM 1686 Coverage: Building 7 - PCT #3- Machine Storage - 133 Aloe Field Coverage: Building 8 - PCT #3-Radio Tower-133 Aloe Field Coverage: Building 9 - PCT #3-Mechanic Shop - 133 Aloe Field Coverage: Building 10 - PCT #3-Service Center Cover- 133 Aloe Field Coverage: Building 11 - PCT #2-Truck Storage - 3323 Nursery	0.13% 0.03% 0.32% 0.22% 0.74% 1.96% 0.04% 0.22% 0.14% 0.75%		32,180.91 2,937.31 592.19 7,043.64 4,899.80 16,227.18 42,879.82 968.14 4,741.44 3,056.82 16,369.52	100.00%
Coverage: Building 1- Old Jail- 206 W. Constitution Coverage: Building 2- Old Courthouse - 101 N. Bridge Coverage: Building 3 - Old Courthouse Tunnel Coverage: Building 4 - New Courthouse - 115 N. Bridge Coverage: Building 5 - Old Fire Station - 209 W. Forrest Coverage: Building 6 - PCT #1- Machine Storage- 2000 FM 1686 Coverage: Building 7 - PCT #3- Machine Storage - 133 Aloe Field Coverage: Building 8 - PCT #3-Radio Tower-133 Aloe Field Coverage: Building 9 - PCT #3-Mechanic Shop - 133 Aloe Field Coverage: Building 10 - PCT #3-Service Center Cover- 133 Aloe Field Coverage: Building 11 - PCT #2-Truck Storage - 3323	0.13% 0.03% 0.32% 0.22% 0.74% 1.96% 0.04% 0.22%		32,180.91 2,937.31 592.19 7,043.64 4,899.80 16,227.18 42,879.82 968.14 4,741.44 3,056.82	100.00%
Coverage: Building 1- Old Jail- 206 W. Constitution Coverage: Building 2- Old Courthouse - 101 N. Bridge Coverage: Building 3 - Old Courthouse Tunnel Coverage: Building 4 - New Courthouse - 115 N. Bridge Coverage: Building 5 - Old Fire Station - 209 W. Forrest Coverage: Building 6 - PCT #1- Machine Storage- 2000 FM 1686 Coverage: Building 7 - PCT #3- Machine Storage - 133 Aloe Field Coverage: Building 8 - PCT #3-Radio Tower-133 Aloe Field Coverage: Building 9 - PCT #3-Mechanic Shop - 133 Aloe Field Coverage: Building 10 - PCT #3-Service Center Cover- 133 Aloe Field Coverage: Building 11 - PCT #2-Truck Storage - 3323 Nursery Coverage: Building 12 - Park- Metal Storage - 500	0.13% 0.03% 0.32% 0.22% 0.74% 1.96% 0.04% 0.22% 0.14% 0.75%		32,180.91 2,937.31 592.19 7,043.64 4,899.80 16,227.18 42,879.82 968.14 4,741.44 3,056.82 16,369.52	100.00%





	Coverage: Building 14 - New Jail - 101 N. Glass	0.71% =	15,570.58
	Coverage: Building 15 - Airplane Hangar - 133 N. Hangar Dr.	2.82% =	61,776.10
	Coverage: Building 16 - Airplane Hangar(FBO) - 437 S. Hangar Dr.	3.13% =	68,582.64
	Coverage: Building 17 - Airplane Hangar B - 305 S. Hangar Dr.	0.81% =	17,829.77
	Coverage: Building 18 - Airplane Hangar C - 207 Storehouse Dr.	34.21% =	749,024.16
	Coverage: Building 19 - PCT #4-Truck Storage - 155 Corpus Christi	0.81% =	17,797.56
	Coverage: Building 20 - PCT #4- Building - 155 Corpus Christi	2.72% =	59,471.59
	Coverage: Building 21 - Airplane Hangar(T-Hangar Units) -348 N. Hangar Dr.	1.49% =	32,711.61
	Coverage: Building 22 - Aircraft Storage(T-Hangar Units)- 388 N. Hangar Dr	4.58% =	100,395.37
	Coverage: Building 23 - Office Elections & JP #3 - 111 N. Glass	0.12% =	2,559.66
	Coverage: Building 24 - Airport Terminal /2 Storage Buildings - 609 Foster	1.55% =	33,884.38
	Coverage: Building 25 - Airport Maintenance w/ Generator - 41 Hangar	1.48% =	32,437.33
	Coverage: Building 26 - SWB Building / Bridge St. Annex - 204 N. Bridge	4.76% =	104,270.55
	Coverage: Building 27 - Extension Service - 528 Waco Circle	3.37% =	73,717.46
	Coverage: Building 28 - Juvenile Detention Center - 97 Foster Field	0.01% =	137.82
	Coverage: Building 30 - Health Dept - 2805 Navarro	0.43% =	9,373.64
	Coverage: Building 31 - 4-H Activity Center - 259 Bachelor Dr.	0.18% =	4,034.18
	Coverage: Building 32 - Fire Marshall Office / TSA - 25 & 27 Hangar Dr.	0.30% =	6,654.66
	Coverage: Building 33 - Officers Club - 333 Bachelor Dr.	5.36% =	117,400.34
	Coverage: Building 35 - COMAT Building - 442 Foster Field Dr.	4.39% =	96,075.26
	Coverage: Building 36 - Animal Shelter - 102 Perimeter Rd.	0.08% =	1,644.29
	Coverage: Building 38 - Storehouse - 103 S Glass	0.85% =	18,717.90
	Coverage: Building 39 - AARFF Station (Fire Station) - 121 N Hangar	0.71% =	15,489.10
	Coverage: Building 41 - Control Tower / Airport - 348 Bachelor Dr.	0.98% =	21,402.96
	Coverage: Building 47 - PCT #4-New Barn - 226 Beck Road	0.27% =	5,954.58
	Coverage: Building 50 - Celebration Church - 358 Foster Field	0.28% =	6,101.79
	Coverage: Building 51 - Sky Restaurant - 236 Foster Field	1.63% =	35,661.86
	Coverage: Building 52 - Fisher Stevens - 43 Storehouse	4.88% =	106,777.64
0	Coverage: Building 53 - Reliant Field Services - 112 Corpus Chrisit	0.14% =	3,095.32
	Coverage: Building 54 - Townsend Remodeling Unamed -	0.45% =	9,847.33
VICTOR	YCOSUB		12/13/2017

Page: 360



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

470 Foster Field			
Coverage: Building 56 - LDS Builders - 396 Foster Field	0.67% =	14,730.88	
Coverage: Building 57 - Straight Arrow Archery - 60 Storehouse	0.26% =	5,696.05	
Coverage: Building 58 - Celebration Church / UHV - 292 Foster Field	0.17% =	3,826.70	
Coverage: Building 59 - Fire Marshall Storage - 354 Hangar	0.01% =	206.21	
Coverage: Building 60 - Vacant Building - 479 Waco Circle	1.08% =	23,635.00	
Coverage: Building 61 - Old Golden Crescent - GCRP - 568 Waco Circle	1.47% =	32,266.19	
Coverage: Building 62 - Texas Mile Warehouse - 131 Hangar	1.02% =	22,397.82	
Coverage: Building 63 - Condemned Warehouse (H&H Door) - 158 Hangar	1.06% =	23,112.42	
Coverage: Building 65 - Old Brig - 153 Corpus Christi	0.72% =	15,698.33	
Coverage: Building 66 - Old Dorm Building - 294 Foster Field	3.72% =	81,353.00	

Total 2,189,792.41 100.00%





#### **Recap by Category**

Items			Total	%
ACOUSTICAL TREATMENTS			28,844.04	1.32%
Coverage: Building 1- Old Jail- 206 W. Constitution	@	20.65% =	5,955.01	
Coverage: Building 4 - New Courthouse - 115 N. Bridge	@	2.42% =	697.84	
Coverage: Building 14 - New Jail - 101 N. Glass	@	3.60% =	1,037.77	
Coverage: Building 15 - Airplane Hangar - 133 N. Hangar Dr.	@	16.61% =	4,790.82	
Coverage: Building 16 - Airplane Hangar(FBO) - 437 S. Hangar Dr.	@	3.64% =	1,048.54	
Coverage: Building 24 - Airport Terminal /2 Storage Buildings - 609 Foster	@	1.34% =	386.63	
Coverage: Building 26 - SWB Building / Bridge St. Annex - 204 N. Bridge	@	3.68% =	1,061.70	
Coverage: Building 27 - Extension Service - 528 Waco Circle	@	22.38% =	6,454.63	
Coverage: Building 28 - Juvenile Detention Center - 97 Foster Field	@	0.26% =	75.40	
Coverage: Building 32 - Fire Marshall Office / TSA - 25 & 27 Hangar Dr.	@	0.02% =	4.92	
Coverage: Building 33 - Officers Club - 333 Bachelor Dr.	@	1.87% =	540.06	
Coverage: Building 35 - COMAT Building - 442 Foster Field Dr.	@	4.17% =	1,203.94	
Coverage: Building 36 - Animal Shelter - 102 Perimeter Rd.	@	0.47% =	136.64	
Coverage: Building 41 - Control Tower / Airport - 348 Bachelor Dr.	@	0.29% =	83.64	
Coverage: Building 51 - Sky Restaurant - 236 Foster Field	@	18.61% =	5,366.50	
APPLIANCES			122.16	0.019
Coverage: Building 16 - Airplane Hangar(FBO) - 437 S. Hangar Dr.	@	100.00% =	122.16	
AWNINGS & PATIO COVERS			1,024.54	0.059
Coverage: Building 51 - Sky Restaurant - 236 Foster Field	@	100.00% =	1,024.54	



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

Items			Total	%
CABINETRY			7,585.24	0.35%
Coverage: Building 15 - Airplane Hangar - 133 N. Hangar Dr.	@	3.69% =	279.84	
Coverage: Building 16 - Airplane Hangar(FBO) - 437 S. Hangar Dr.	@	1.70% =	129.00	
Coverage: Building 25 - Airport Maintenance w/ Generator - 41 Hangar	@	61.38% =	4,655.95	
Coverage: Building 27 - Extension Service - 528 Waco Circle	@	26.59% =	2,016.80	
Coverage: Building 31 - 4-H Activity Center - 259 Bachelor Dr.	@	2.98% =	225.75	
Coverage: Building 35 - COMAT Building - 442 Foster Field Dr.	@	3.66% =	277.90	
CONT: CLEAN - HARD FURNITURE			1,052.28	0.05%
Coverage: Building 16 - Airplane Hangar(FBO) - 437 S. Hangar Dr.	@	11.69% =	123.00	
Coverage: Building 33 - Officers Club - 333 Bachelor Dr.	@	88.31% =	929.28	



Wirtus 8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

tems			Total	%
LEANING			22,778.98	1.04%
Coverage: Building 1- Old Jail- 206 W. Constitution	@	6.48% =	1,475.69	
Coverage: Building 2- Old Courthouse - 101 N. Bridge	@	0.29% =	65.69	
Coverage: Building 3 - Old Courthouse Tunnel	@	0.07% =	16.36	
Coverage: Building 4 - New Courthouse - 115 N. Bridge	@	3.35% =	763.12	
Coverage: Building 5 - Old Fire Station - 209 W. Forrest	@	1.06% =	241.84	
Coverage: Building 6 - PCT #1- Machine Storage- 2000 FM 1686	@	0.99% =	225.61	
Coverage: Building 12 - Park- Metal Storage - 500 Fordyce Rd.	@	0.11% =	24.67	
Coverage: Building 14 - New Jail - 101 N. Glass	@	10.05% =	2,289.16	
Coverage: Building 15 - Airplane Hangar - 133 N. Hangar Dr.	@	6.07% =	1,381.58	
Coverage: Building 16 - Airplane Hangar(FBO) - 437 S. Hangar Dr.	@	5.84% =	1,329.29	
Coverage: Building 20 - PCT #4- Building - 155 Corpus Christi	@	2.80% =	637.46	
Coverage: Building 23 - Office Elections & JP #3 - 111 N. Glass	@	0.27% =	61.18	
Coverage: Building 24 - Airport Terminal /2 Storage Buildings - 609 Foster	@	3.07% =	700.24	
Coverage: Building 25 - Airport Maintenance w/ Generator - 41 Hangar	@	5.35% =	1,218.21	
Coverage: Building 26 - SWB Building / Bridge St. Annex - 204 N. Bridge	@	5.17% =	1,176.92	
Coverage: Building 27 - Extension Service - 528 Waco Circle	@	19.79% =	4,507.56	
Coverage: Building 28 - Juvenile Detention Center - 97 Foster Field	@	0.03% =	6.80	
Coverage: Building 30 - Health Dept - 2805 Navarro	@	1.32% =	301.38	
Coverage: Building 31 - 4-H Activity Center - 259 Bachelor Dr.	@	2.50% =	570.43	
Coverage: Building 32 - Fire Marshall Office / TSA - 25 & 27 Hangar Dr.	@	1.54% =	350.81	
Coverage: Building 33 - Officers Club - 333 Bachelor Dr.	@	4.62% =	1,051.42	
Coverage: Building 35 - COMAT Building - 442 Foster Field Dr.	@	5.47% =	1,245.60	
Coverage: Building 38 - Storehouse - 103 S Glass	@	2.05% =	466.71	
Coverage: Building 41 - Control Tower / Airport - 348 Bachelor Dr.	@	0.98% =	224.08	
Coverage: Building 50 - Celebration Church - 358 Foster Field	@	0.42% =	95.76	
Coverage: Building 51 - Sky Restaurant -	@	6.29% =	1,431.87	Dogg
CTORYCOSUB			12/13/2017	Page:





Items			Total	%
236 Foster Field				
Coverage: Building 54 - Townsend Remodeling Unamed - 470 Foster Field	@	0.59% =	134.82	
Coverage: Building 56 - LDS Builders - 396 Foster Field	@	0.61% =	138.19	
Coverage: Building 62 - Texas Mile Warehouse - 131 Hangar	@	2.84% =	646.53	
CONCRETE & ASPHALT			2,430.84	0.11%
Coverage: Building 15 - Airplane Hangar - 133 N. Hangar Dr.	@	100.00% =	2,430.84	*****
CONTENT MANIPULATION			3,269.36	0.15%
Coverage: Building 1- Old Jail- 206 W. Constitution	@	30.60% =	1,000.55	
Coverage: Building 4 - New Courthouse - 115 N. Bridge	@	0.86% =	28.18	
Coverage: Building 6 - PCT #1- Machine Storage- 2000 FM 1686	@	1.72% =	56.36	
Coverage: Building 14 - New Jail - 101 N. Glass	@	16.38% =	535.48	
Coverage: Building 15 - Airplane Hangar - 133 N. Hangar Dr.	@	2.59% =	84.56	
Coverage: Building 16 - Airplane Hangar(FBO) - 437 S. Hangar Dr.	@	1.29% =	42.27	
Coverage: Building 20 - PCT #4- Building - 155 Corpus Christi	@	1.29% =	42.27	
Coverage: Building 23 - Office Elections & JP #3 - 111 N. Glass	@	3.02% =	98.63	
Coverage: Building 24 - Airport Terminal /2 Storage Buildings - 609 Foster	@	2.59% =	84.56	
Coverage: Building 25 - Airport Maintenance w/ Generator - 41 Hangar	@	2.59% =	84.54	
Coverage: Building 26 - SWB Building / Bridge St. Annex - 204 N. Bridge	@	6.47% =	211.39	
Coverage: Building 30 - Health Dept - 2805 Navarro	@	12.93% =	422.80	
Coverage: Building 38 - Storehouse - 103 S Glass		3.88% =	126.83	
Coverage: Building 41 - Control Tower / Airport - 348 Bachelor Dr.		2.59% =	84.54	
Coverage: Building 51 - Sky Restaurant - 236 Foster Field	@	3.88% =	126.83	
Coverage: Building 56 - LDS Builders - 396 Foster Field		3.88% =	126.83	
Coverage: Building 62 - Texas Mile Warehouse - 131 Hangar	@	3.45% =	112.74	



tems			Total	%
GENERAL DEMOLITION			137,149.00	6.26%
Coverage: Building 1- Old Jail- 206 W.	@	0.23% =	312.55	
Constitution				
Coverage: Building 2- Old Courthouse - 101 N. Bridge	@	0.11% =	149.29	
Coverage: Building 3 - Old Courthouse Tunnel	@	0.03% =	37.19	
Coverage: Building 4 - New Courthouse - 115 N. Bridge	@	0.19% =	258.25	
Coverage: Building 5 - Old Fire Station - 209 W. Forrest	@	0.40% =	549.65	
Coverage: Building 6 - PCT #1- Machine Storage- 2000 FM 1686	@	0.97% =	1,331.31	
Coverage: Building 7 - PCT #3- Machine Storage - 133 Aloe Field	@	2.84% =	3,899.19	
Coverage: Building 9 - PCT #3-Mechanic Shop - 133 Aloe Field	@	0.28% =	380.63	
Coverage: Building 10 - PCT #3-Service Center Cover - 133 Aloe Field	@	0.07% =	99.21	
Coverage: Building 11 - PCT #2-Truck Storage - 3323 Nursery	@	1.24% =	1,696.32	
Coverage: Building 12 - Park- Metal Storage - 500 Fordyce Rd.	@	0.27% =	366,22	
Coverage: Building 14 - New Jail - 101 N. Glass	@	0.72% =	991.70	
Coverage: Building 15 - Airplane Hangar - 133 N. Hangar Dr.	@	2.07% =	2,841.31	
Coverage: Building 16 - Airplane Hangar(FBO) - 437 S. Hangar Dr.	@	3.02% =	4,140.65	
Coverage: Building 17 - Airplane Hangar B - 305 S. Hangar Dr.	@	0.18% =	246.68	
Coverage: Building 18 - Airplane Hangar C - 207 Storehouse Dr.	@	25.98% =	35,626.98	
Coverage: Building 19 - PCT #4-Truck Storage - 155 Corpus Christi	@	1.26% =	1,724.55	
Coverage: Building 20 - PCT #4- Building - 155 Corpus Christi	@	1.97% =	2,698.46	
Coverage: Building 22 - Aircraft Storage(T-Hangar Units)- 388 N. Hangar Dr	@	3.26% =	4,474.54	
Coverage: Building 24 - Airport Terminal /2 Storage Buildings - 609 Foster	@	0.90% =	1,228.57	
Coverage: Building 25 - Airport Maintenance w/ Generator - 41 Hangar	@	1.29% =	1,763.96	
Coverage: Building 26 - SWB Building / Bridge St. Annex - 204 N. Bridge	@	0.12% =	160.26	
Coverage: Building 27 - Extension Service - 528 Waco Circle	@	4.56% =	6,257.42	
Coverage: Building 28 - Juvenile Detention Center - 97 Foster Field	@	0.01% =	15.45	
Coverage: Building 31 - 4-H Activity Center - 259 Bachelor Dr.	@	0.15% =	207.43	
Coverage: Building 32 - Fire Marshall	@	0.02% =	23.59	
CTORYCOSUB			12/13/2017	Page:





ms			Total	9/
Office / TSA - 25 & 27 Hangar Dr.				
Coverage: Building 33 - Officers Club - 333 Bachelor Dr.	@	6.86% =	9,410.30	
Coverage: Building 35 - COMAT Building - 442 Foster Field Dr.	@	6.47% =	8,870.73	
Coverage: Building 36 - Animal Shelter - 102 Perimeter Rd.	@	0.13% =	179.89	
Coverage: Building 38 - Storehouse - 103 S Glass	@	2.36% =	3,232.97	
Coverage: Building 39 - AARFF Station (Fire Station) - 121 N Hangar	@	0.43% =	592.73	
Coverage: Building 41 - Control Tower / Airport - 348 Bachelor Dr.	@	0.42% =	580.50	
Coverage: Building 47 - PCT #4-New Barn - 226 Beck Road	@	0.33% =	452.19	
Coverage: Building 50 - Celebration Church - 358 Foster Field	@	0.35% =	480.56	
Coverage: Building 51 - Sky Restaurant - 236 Foster Field	@	2.02% =	2,775.50	
Coverage: Building 52 - Fisher Stevens - 43 Storehouse	@	6.66% =	9,128.62	
Coverage: Building 53 - Reliant Field Services - 112 Corpus Chrisit	@	0.17% =	228.60	
Coverage: Building 54 - Townsend Remodeling Unamed - 470 Foster Field	@	1.35% =	1,857.82	
Coverage: Building 56 - LDS Builders - 396 Foster Field	@	0.93% =	1,274.81	
Coverage: Building 57 - Straight Arrow Archery - 60 Storehouse	@	0.31% =	420.27	
Coverage: Building 58 - Celebration Church / UHV - 292 Foster Field	@	0.60% =	826.37	
Coverage: Building 60 - Vacant Building - 479 Waco Circle	@	1.94% =	2,667.32	
Coverage: Building 61 - Old Golden Crescent - GCRP - 568 Waco Circle	@	3.70% =	5,069.21	
Coverage: Building 62 - Texas Mile Warehouse - 131 Hangar	@	2.35% =	3,227.16	
Coverage: Building 63 - Condemned Warehouse (H&H Door) - 158 Hangar	@	1.74% =	2,385.62	
Coverage: Building 65 - Old Brig - 153 Corpus Christi	@	1.08% =	1,477.77	
Coverage: Building 66 - Old Dorm Building - 294 Foste: Field	@	7.68% =	10,528.70	





Items			Total	%
DOORS			234,265.79	10.70%
Coverage: Building 6 - PCT #1- Machine Storage- 2000 FM 1686	@	1.75% =	4,089.57	
Coverage: Building 7 - PCT #3- Machine Storage - 133 Aloe Field	@	0.73% =	1,711.26	
Coverage: Building 11 - PCT #2-Truck Storage - 3323 Nursery	@	0.46% =	1,073.95	
Coverage: Building 15 - Airplane Hangar - 133 N. Hangar Dr.	@	0.10% =	232.10	
Coverage: Building 17 - Airplane Hangar B - 305 S. Hangar Dr.	@	0.78% =	1,834.13	
Coverage: Building 18 - Airplane Hangar C - 207 Storehouse Dr.	@	67.62% =	158,400.00	
Coverage: Building 20 - PCT #4- Building - 155 Corpus Christi	@	0.24% =	559.38	
Coverage: Building 21 - Airplane Hangar(T-Hangar Units)-348 N. Hangar Dr.	@	0.09% =	211.23	
Coverage: Building 22 - Aircraft Storage(T-Hangar Units)- 388 N. Hangar Dr	@	21.02% =	49,244.00	
Coverage: Building 25 - Airport Maintenance w/ Generator - 41 Hangar	@	1.56% =	3,655.55	
Coverage: Building 27 - Extension Service - 528 Waco Circle	@	0.04% =	90.54	
Coverage: Building 32 - Fire Marshall Office / TSA - 25 & 27 Hangar Dr.	@	0.01% =	12.27	
	@	0.02% =	45.27	
Coverage: Building 47 - PCT #4-New Barn - 226 Beck Road	@	2.35% =	5,502.39	
Coverage: Building 52 - Fisher Stevens - 43 Storehouse	@	0.94% =	2,210.16	
Coverage: Building 53 - Reliant Field Services - 112 Corpus Chrisit	@	0.09% =	208.40	
Coverage: Building 56 - LDS Builders - 396 Foster Field	@	0.09% =	203.95	
Coverage: Building 57 - Straight Arrow Archery - 60 Storehouse	@	0.46% =	1,073.95	
Coverage: Building 62 - Texas Mile Warehouse - 131 Hangar	@	0.17% =	407.62	
Coverage: Building 66 - Old Dorm Building - 294 Foster Field	@	1.49% =	3,500.07	





Items			Total	%
DRYWALL			107,473.76	4.91%
Coverage: Building 3 - Old Courthouse Tunnel	@	0.34% =	362.19	
	@	0.03% =	36.28	
	@	0.21% =	223.26	
	@	0.29% =	309.05	
	@	1.82% =	1,959.60	
	@	5.29% =	5,680.25	
	@	5.50% =	5,911.22	
Coverage: Building 18 - Airplane Hangar C - 207 Storehouse Dr.	@	15.72% =	16,890.91	
Coverage: Building 20 - PCT #4- Building - 155 Corpus Christi	@	10.33% =	11,102.05	
	@	4.34% =	4,663.86	
	@	0.49% =	528.22	
Coverage: Building 27 - Extension Service - 528 Waco Circle	@	6.29% =	6,765.17	
Coverage: Building 31 - 4-H Activity Center - 259 Bachelor Dr.	@	0.87% =	936.25	
	@	1.74% =	1,873.39	
Coverage: Building 33 - Officers Club - 333 Bachelor Dr.	@	15.54% =	16,697.42	
Coverage: Building 35 - COMAT Building - 442 Foster Field Dr.	@	11.28% =	12,125.52	
	@	5.31% =	5,702.56	
Coverage: Building 41 - Control Tower / Airport - 348 Bachelor Dr.	@	1.05% =	1,132.81	
Coverage: Building 50 - Celebration Church - 358 Foster Field	@	0.42% =	453.60	
Coverage: Building 51 - Sky Restaurant - 236 Foster Field	@	3.23% =	3,472.01	
Coverage: Building 54 - Townsend Remodeling Unamed - 470 Foster Field	@	1.31% =	1,412.75	
Coverage: Building 56 - LDS Builders - 396 Foster Field	@	3.31% =	3,553.24	
Coverage: Building 62 - Texas Mile Warehouse - 131 Hangar	@	5.29% =	5,682.15	





Items			Total	%
ELECTRICAL			25,383.05	1.16%
Coverage: Building 1- Old Jail- 206 W. Constitution	@	0.05% =	11.94	
Coverage: Building 2- Old Courthouse - 101 N. Bridge	@	0.05% =	13.38	
Coverage: Building 14 - New Jail - 101 N. Glass	@	1.21% =	306.16	
Coverage: Building 15 - Airplane Hangar - 133 N. Hangar Dr.	@	8.43% =	2,140.98	
Coverage: Building 16 - Airplane Hangar(FBO) - 437 S. Hangar Dr.	@	8.29% =	2,105.10	
Coverage: Building 17 - Airplane Hangar B -	@	6.88% =	1,747.62	
305 S. Hangar Dr. Coverage: Building 20 - PCT #4- Building -	@	12.23% =	3,105.03	
155 Corpus Christi Coverage: Building 21 - Airplane Hangar(T-	@	1.42% =	359.82	
Hangar Units)-348 N. Hangar Dr. Coverage: Building 25 - Airport	@	1.57% =	399.24	
Maintenance w/ Generator - 41 Hangar Coverage: Building 26 - SWB Building /	@	5.91% =	1,498.98	
Bridge St. Annex - 204 N. Bridge Coverage: Building 27 - Extension Service -	@	12.71% =	3,226.10	
528 Waco Circle Coverage: Building 31 - 4-H Activity Center	@	0.09% =	23.41	
- 259 Bachelor Dr. Coverage: Building 32 - Fire Marshall	@	0.25% =	62.44	
Office / TSA - 25 & 27 Hangar Dr. Coverage: Building 33 - Officers Club - 333	@	1.60% =	405.13	
Bachelor Dr. Coverage: Building 35 - COMAT Building -	@	9.17% =	2,326.76	
442 Foster Field Dr. Coverage: Building 39 - AARFF Station	@	23.85% =	6,053.04	
(Fire Station) - 121 N Hangar Coverage: Building 41 - Control Tower /	@	5.77% =	1,464.45	
Airport - 348 Bachelor Dr. Coverage: Building 56 - LDS Builders - 396	@	0.53% =	133.47	
Foster Field ELECTRICAL - SPECIAL SYSTEMS			2,872.70	0.13%
Coverage: Building 27 - Extension Service -	@	20.64% =	593.04	0.13%
528 Waco Circle Coverage: Building 30 - Health Dept - 2805	@	79.36% =	2,279.66	
Navarro				
MISC. EQUIPMENT - AGRICULTURAL			3,698.56	0.17%
Coverage: Building 17 - Airplane Hangar B - 305 S. Hangar Dr.	@	100.00% =	3,698.56	





Items			Total	%
MISC, EQUIPMENT - COMMERCIAL			97,824.39	4.47%
Coverage: Building 16 - Airplane Hangar(FBO) - 437 S. Hangar Dr.	@	1.59% =	1,558.80	
Coverage: Building 26 - SWB Building / Bridge St. Annex - 204 N. Bridge	@	89.66% =	87,711.20	
Coverage: Building 32 - Fire Marshall Office / TSA - 25 & 27 Hangar Dr.	@	0.23% =	221.53	
Coverage: Building 33 - Officers Club - 333 Bachelor Dr.	@	0.16% =	155.32	
Coverage: Building 41 - Control Tower / Airport - 348 Bachelor Dr.	@	8.34% =	8,163.36	
Coverage: Building 56 - LDS Builders - 396 Foster Field	@	0.01% =	14.18	
HEAVY EQUIPMENT			45,430.40	2.07%
Coverage: Building 18 - Airplane Hangar C - 207 Storehouse Dr.	@	100.00% =	45,430.40	
EXCAVATION			360.00	0.02%
Coverage: Building 30 - Health Dept - 2805 Navarro	@	100.00% =	360.00	
FLOOR COVERING - CARPET			41,562.86	1.90%
Coverage: Building 1- Old Jail- 206 W. Constitution	@	24.20% =	10,059.88	
Coverage: Building 14 - New Jail - 101 N. Glass	@	2.29% =	953.30	
Coverage: Building 15 - Airplane Hangar - 133 N. Hangar Dr.	@	13.25% =	5,506.41	
Coverage: Building 23 - Office Elections & JP #3 - 111 N. Glass	@	5.26% =	2,184.86	
Coverage: Building 26 - SWB Building / Bridge St. Annex - 204 N. Bridge	@	9.02% =	3,747.14	
Coverage: Building 30 - Health Dept - 2805 Navarro	@	8.91% =	3,704.53	
Coverage: Building 32 - Fire Marshall Office / TSA - 25 & 27 Hangar Dr.	@	3.83% =	1,593.46	
Coverage: Building 33 - Officers Club - 333 Bachelor Dr.		2.30% =	954.83	
Coverage: Building 35 - COMAT Building - 442 Foster Field Dr.		29.19% =	12,131.53	
Coverage: Building 41 - Control Tower / Airport - 348 Bachelor Dr.	@	1.75% =	726.92	
FLOOR COVERING - CERAMIC TILE			942.51	0.049
Coverage: Building 14 - New Jail - 101 N. Glass	@	23.87% =	224.97	
Coverage: Building 20 - PCT #4- Building - 155 Corpus Christi	@	76.13% =	717.54	





Wirtus 8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

Items			Total	9/6
FLOOR COVERING - VINYL			14,436.94	0.66%
Coverage: Building 1- Old Jail- 206 W. Constitution	@	27.34% =	3,947.02	
Coverage: Building 4 - New Courthouse - 115 N. Bridge	@	17.47% =	2,522.64	
Coverage: Building 6 - PCT #1- Machine Storage- 2000 FM 1686	@	6.85% =	989.21	
Coverage: Building 14 - New Jail - 101 N. Glass	@	5.20% =	750.18	
Coverage: Building 15 - Airplane Hangar - 133 N. Hangar Dr.	@	3.46% =	499.48	
Coverage: Building 23 - Office Elections & JP #3 - 111 N. Glass	@	1.49% =	214.99	
Coverage: Building 25 - Airport Maintenance w/ Generator - 41 Hangar	@	4.91% =	709.16	
Coverage: Building 26 - SWB Building / Bridge St. Annex - 204 N. Bridge	@	3.17% =	457.13	
Coverage: Building 27 - Extension Service - 528 Waco Circle	@	5.32% =	767.81	
Coverage: Building 30 - Health Dept - 2805 Navarro	@	9.26% =	1,337.13	
Coverage: Building 31 - 4-H Activity Center - 259 Bachelor Dr.	@	1.94% =	280.17	
Coverage: Building 32 - Fire Marshall Office / TSA - 25 & 27 Hangar Dr.	@	1.69% =	244.44	
Coverage: Building 35 - COMAT Building - 442 Foster Field Dr.	@	8.87% =	1,280.37	
Coverage: Building 41 - Control Tower / Airport - 348 Bachelor Dr.	@	1.55% =	223.31	
Coverage: Building 62 - Texas Mile Warehouse - 131 Hangar	@	1.48% =	213.90	
FLOOR COVERING - WOOD			36,033.74	1.65
Coverage: Building 32 - Fire Marshall Office / TSA - 25 & 27 Hangar Dr.	@	0.07% =	26.19	
Coverage: Building 33 - Officers Club - 333 Bachelor Dr.	@	99.91% =	36,001.55	
Coverage: Building 38 - Storehouse - 103 S Glass	@	0.02% =	6.00	
PERMITS AND FEES			62,400.00	2.85
Coverage: Building 18 - Airplane Hangar C - 207 Storehouse Dr.	@	100.00% =	62,400.00	200



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

Items			Total	%
FENCING			44,871.52	2.05%
Coverage: Building 11 - PCT #2-Truck	@	0.34% =	154.20	
Storage - 3323 Nursery				
Coverage: Building 19 - PCT #4-Truck	@	0.18% =	82.84	
Storage - 155 Corpus Christi				
Coverage: Building 24 - Airport Terminal /2	@	49.83% =	22,358.40	
Storage Buildings - 609 Foster				
Coverage: Building 39 - AARFF Station	@	0.45% =	201.48	
(Fire Station) - 121 N Hangar				
Coverage: Building 63 - Condemned	@	18.18% =	8,159.00	
Warehouse (H&H Door) - 158 Hangar				
Coverage: Building 65 - Old Brig - 153	@	31.01% =	13,915.60	
Corpus Christi				





Virtus 8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

tems			Total	9
INISH CARPENTRY / TRIMWORK			11,904.30	0.549
Coverage: Building 1- Old Jail- 206 W.	@	6.34% =	754.32	
Constitution			00.00	
Coverage: Building 6 - PCT #1- Machine Storage- 2000 FM 1686	@	0.83% =	99.38	
Coverage: Building 12 - Park- Metal Storage - 500 Fordyce Rd.	@	1.66% =	197.78	
Coverage: Building 15 - Airplane Hangar - 133 N. Hangar Dr.	@	1.10% =	130.73	
Coverage: Building 16 - Airplane Hangar(FBO) - 437 S. Hangar Dr.	@	21.41% =	2,549.17	
Coverage: Building 20 - PCT #4- Building - 155 Corpus Christi	@	6.29% =	749.23	
Coverage: Building 25 - Airport Maintenance w/ Generator - 41 Hangar	@	4.83% =	574.94	
Coverage: Building 27 - Extension Service - 528 Waco Circle	@	0.37% =	44.64	
Coverage: Building 32 - Fire Marshall Office / TSA - 25 & 27 Hangar Dr.	@	2.06% =	244.86	
Coverage: Building 33 - Officers Club - 333 Bachelor Dr.	@	26.16% =	3,114.13	
Coverage: Building 35 - COMAT Building - 442 Foster Field Dr.	@	3.44% =	408.98	
Coverage: Building 38 - Storehouse - 103 S Glass	@	1.79% =	213.39	
Coverage: Building 39 - AARFF Station (Fire Station) - 121 N Hangar	@	1.16% =	138.03	
Coverage: Building 41 - Control Tower / Airport - 348 Bachelor Dr.	@	1.87% =	222.48	
Coverage: Building 51 - Sky Restaurant - 236 Foster Field	@	9.66% =	1,150.15	
Coverage: Building 54 - Townsend Remodeling Unamed - 470 Foster Field	@	0.31% =	37.36	
Coverage: Building 56 - LDS Builders - 396 Foster Field	@	0.70% =	83.10	
Coverage: Building 57 - Straight Arrow Archery - 60 Storehouse	@	2.15% =	255.77	
Coverage: Building 62 - Texas Mile Warehouse - 131 Hangar	@	0.78% =	93.06	
Coverage: Building 66 - Old Dorm Building - 294 Foster Field	@	7.08% =	842.80	



8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

Items			Total	%
FINISH HARDWARE		,	366.87	0.02%
Coverage: Building 15 - Airplane Hangar - 133 N. Hangar Dr.	@	15.62% =	57.30	
Coverage: Building 20 - PCT #4- Building - 155 Corpus Christi	@	40.69% =	149.28	
Coverage: Building 21 - Airplane Hangar(T-Hangar Units)-348 N. Hangar Dr.	@	15.31% =	56.16	
Coverage: Building 25 - Airport Maintenance w/ Generator - 41 Hangar	@	2.39% =	8.78	
Coverage: Building 27 - Extension Service - 528 Waco Circle	@	2.39% =	8.78	
Coverage: Building 31 - 4-H Activity Center - 259 Bachelor Dr.	@	10.37% =	38.06	
Coverage: Building 33 - Officers Club - 333 Bachelor Dr.	@	4.79% =	17.56	
Coverage: Building 51 - Sky Restaurant - 236 Foster Field	@	1.26% =	4.61	
Coverage: Building 62 - Texas Mile Warehouse - 131 Hangar	@	7.18% =	26.34	
FIRE PROTECTION SYSTEMS			10.89	0.00%
Coverage: Building 26 - SWB Building / Bridge St. Annex - 204 N. Bridge	@	100.00% =	10.89	

12/13/2017 Page: 375





Items			Total	%
FRAMING & ROUGH CARPENTRY			202,358.12	9.24%
Coverage: Building 7 - PCT #3- Machine	@	2.15% =	4,346.68	
Storage - 133 Aloe Field				
Coverage: Building 8 - PCT #3-Radio Tower-133 Aloe Field	@	0.15% =	309.08	
Coverage: Building 10 - PCT #3-Service Center Cover - 133 Aloe Field	@	0.10% =	193.92	
Coverage: Building 11 - PCT #2-Truck Storage - 3323 Nursery	@	0.26% =	517.76	
Coverage: Building 12 - Park- Metal Storage - 500 Fordyce Rd.	@	0.12% =	237.74	
Coverage: Building 15 - Airplane Hangar - 133 N. Hangar Dr.	@	0.09% =	184.35	
Coverage: Building 18 - Airplane Hangar C - 207 Storehouse Dr.	@	90.44% =	183,020.22	
Coverage: Building 21 - Airplane Hangar(T-Hangar Units)-348 N. Hangar Dr.	@	0.05% =	103.96	
Coverage: Building 27 - Extension Service - 528 Waco Circle	@	0.18% =	357.28	
Coverage: Building 30 - Health Dept - 2805 Navarro	@	0.15% =	309.08	
Coverage: Building 33 - Officers Club - 333 Bachelor Dr.	@	0.28% =	561.60	
Coverage: Building 36 - Animal Shelter - 102 Perimeter Rd.	@	0.12% =	244.88	
Coverage: Building 52 - Fisher Stevens - 43 Storehouse	@	0.09% =	187.20	
Coverage: Building 57 - Straight Arrow Archery - 60 Storehouse	@	0.25% =	501.30	
Coverage: Building 62 - Texas Mile Warehouse - 131 Hangar	@	0.20% =	398.93	
Coverage: Building 63 - Condemned Warehouse (H&H Door) - 158 Hangar	@	1.25% =	2,536.08	
Coverage: Building 66 - Old Dorm Building - 294 Foster Field	@	4.13% =	8,348.06	
LASS, GLAZING, & STOREFRONTS			8,911.20	0.41
Coverage: Building 18 - Airplane Hangar C 207 Storehouse Dr.	@	82.14% =	7,320.00	
Coverage: Building 33 - Officers Club - 333 Bachelor Dr.	@	17.86% =	1,591.20	

12/13/2017 Page: 376



VICTORYCOSUB

8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

Items			Total	%
HEAT, VENT & AIR CONDITIONING			8,505.37	0.39%
Coverage: Building 1- Old Jail- 206 W. Constitution	@	1.39% =	118.14	
Coverage: Building 4 - New Courthouse - 115 N. Bridge	@	0.13% =	10.74	
Coverage: Building 15 - Airplane Hangar - 133 N. Hangar Dr.	@	1.84% =	156.46	
Coverage: Building 16 - Airplane Hangar(FBO) - 437 S. Hangar Dr.	@	2.08% =	177.16	
Coverage: Building 20 - PCT #4- Building - 155 Corpus Christi	@	1.74% =	147.86	
Coverage: Building 25 - Airport Maintenance w/ Generator - 41 Hangar	@	0.76% =	64.44	
Coverage: Building 27 - Extension Service - 528 Waco Circle	@	56.25% =	4,784.66	
Coverage: Building 32 - Fire Marshall Office / TSA - 25 & 27 Hangar Dr.	@	0.84% =	71.76	
Coverage: Building 33 - Officers Club - 333 Bachelor Dr.	@	2.97% =	252.50	
Coverage: Building 35 - COMAT Building - 442 Foster Field Dr.	@	29.23% =	2,485.86	
Coverage: Building 38 - Storehouse - 103 S Glass	@	0.13% =	10.74	
Coverage: Building 54 - Townsend Remodeling Unamed - 470 Foster Field	@	0.53% =	45.01	
Coverage: Building 61 - Old Golden Crescent - GCRP - 568 Waco Circle	@	1.06% =	90.02	
Coverage: Building 62 - Texas Mile Warehouse - 131 Hangar	@	1.06% =	90.02	

Page: 377 12/13/2017





ems				Total	%
ISULATION				25,319.24	1.16%
Coverage: Building 4 - New Courthouse -	@	0.45%	=	114.40	
115 N. Bridge					
Coverage: Building 6 - PCT #1- Machine	@	0.40%		101.83	
Storage- 2000 FM 1686					
Coverage: Building 11 - PCT #2-Truck	@	3.23%	=	818.66	
Storage - 3323 Nursery					
Coverage: Building 12 - Park- Metal	@	1.95%	=	493.66	
Storage - 500 Fordyce Rd.					
Coverage: Building 14 - New Jail - 101 N.	@	4.49%	=	1,137.98	
Glass					
Coverage: Building 15 - Airplane Hangar -	@	11.76%	=	2,977.41	
133 N. Hangar Dr.					
Coverage: Building 16 - Airplane	@	4.11%	<u></u>	1,040.07	
Hangar(FBO) - 437 S. Hangar Dr.					
Coverage: Building 20 - PCT #4- Building -	@	13.46%	<del></del>	3,407.30	
155 Corpus Christi					
Coverage: Building 24 - Airport Terminal /2	@	0.81%	=	204.31	
Storage Buildings - 609 Foster				==	
Coverage: Building 25 - Airport	@	2.98%	=	754.14	
Maintenance w/ Generator - 41 Hangar				721.00	
Coverage: Building 26 - SWB Building /	@	2.10%	=	531.80	
Bridge St. Annex - 204 N. Bridge	-			2.564.50	
Coverage: Building 27 - Extension Service -	@	10.13%	= 1	2,564.58	
528 Waco Circle				40.17	
Coverage: Building 28 - Juvenile Detention	<b>@</b>	0.16%	=	40.17	
Center - 97 Foster Field		0.650		170.50	
Coverage: Building 31 - 4-H Activity Center	(a)	0.67%	=	170.50	
- 259 Bachelor Dr.		0.560		141.28	
Coverage: Building 32 - Fire Marshall	@	0.56%	=	141.20	
Office / TSA - 25 & 27 Hangar Dr.		16 1107		4,161.43	
Coverage: Building 33 - Officers Club - 333	@	16.44%	=	4,101.43	
Bachelor Dr.	(1)	6.97%	_	1,764.86	
Coverage: Building 35 - COMAT Building -	w	0.97%	_	1,704.80	
442 Foster Field Dr. Coverage: Building 36 - Animal Shelter -	@	0.29%	_	72.80	
102 Perimeter Rd.	a	0.29 10	_	72.00	
Coverage: Building 41 - Control Tower /	@	2.95%	_	746.80	
Airport - 348 Bachelor Dr.	0	2.75 %	_	7 10.00	
Coverage: Building 50 - Celebration Church	<b>@</b>	0.65%	=	163.80	
- 358 Foster Field		0.05 %			
Coverage: Building 51 - Sky Restaurant -	@	12.71%	=	3,219.01	
236 Foster Field					
Coverage: Building 54 - Townsend	@	1.62%	=	409.84	
Remodeling Unamed - 470 Foster Field					
Coverage: Building 60 - Vacant Building -	@	1.12%	=	282.61	
479 Waco Circle					
ABOR ONLY				34,502.08	1.589
Coverage: Building 18 - Airplane Hangar C	· @	99.52%	=	34,336.80	
207 Storehouse Dr.		772210			
Coverage: Building 33 - Officers Club - 333	@	0.48%	=	165.28	
Bachelor Dr.		3			
CTORYCOSUB				12/13/2017	Page: 3





tems				Total	%
IGHT FIXTURES				23,507.87	1.07%
Coverage: Building 1- Old Jail- 206 W. Constitution	@	7.92%	=	1,861.24	
Coverage: Building 2- Old Courthouse - 101 N. Bridge	@	0.83%	=	195.95	
Coverage: Building 3 - Old Courthouse Tunnel	@	0.35%	=	82.72	
Coverage: Building 4 - New Courthouse - 115 N. Bridge	@	0.77%	=	180.12	
Coverage: Building 12 - Park- Metal Storage - 500 Fordyce Rd.	@	0.95%	=	223.12	
Coverage: Building 14 - New Jail - 101 N. Glass	@	0.35%	=	82.72	
Coverage: Building 15 - Airplane Hangar - 133 N. Hangar Dr.	@	5.18%	=	1,218.80	
Coverage: Building 16 - Airplane Hangar(FBO) - 437 S. Hangar Dr.	@	2.92%	=	686.87	
Coverage: Building 20 - PCT #4- Building - 155 Corpus Christi	@	6.69%	=	1,572.97	
Coverage: Building 21 - Airplane Hangar(T-Hangar Units)-348 N. Hangar Dr.	@	0.57%	=	133.01	
Coverage: Building 24 - Airport Terminal /2 Storage Buildings - 609 Foster	@	2.70%	=	635.84	
Coverage: Building 25 - Airport Maintenance w/ Generator - 41 Hangar	@	3.26%	=	765.36	
Coverage: Building 26 - SWB Building / Bridge St. Annex - 204 N. Bridge	@	1.33%	=	311.65	
Coverage: Building 27 - Extension Service - 528 Waco Circle	@	36.14%	=	8,495.31	
Coverage: Building 31 - 4-H Activity Center - 259 Bachelor Dr.	@	0.23%	=	53.76	
Coverage: Building 33 - Officers Club - 333 Bachelor Dr.	@	8.86%	=	2,083.58	
Coverage: Building 35 - COMAT Building - 442 Foster Field Dr.	@	4.96%	=	1,166.52	
Coverage: Building 38 - Storehouse - 103 S Glass	@	6.95%	=	1,633.81	
Coverage: Building 41 - Control Tower / Airport - 348 Bachelor Dr.	@	2.34%	=	550.38	
Coverage: Building 50 - Celebration Church - 358 Foster Field	@	0.73%	=	170.66	
Coverage: Building 51 - Sky Restaurant - 236 Foster Field	@	3.48%	=	819.04	
Coverage: Building 54 - Townsend Remodeling Unamed - 470 Foster Field	@	0.51%	=	120.08	
Coverage: Building 56 - LDS Builders - 396 Foster Field	@	1.80%	=	423.00	
Coverage: Building 62 - Texas Mile Warehouse - 131 Hangar	@	0.18%	=	41.36	
IARBLE - CULTURED OR NATURAL				124.81	0.01%
Coverage: Building 31 - 4-H Activity Center - 259 Bachelor Dr.	@	100.00%	=	124.81	
TORYCOSUB				12/13/2017	Page: 3





Items			Total	%
MIRRORS & SHOWER DOORS			82.62	0.00%
Coverage: Building 33 - Officers Club - 333 Bachelor Dr.	@	100.00% =	82.62	
METAL STRUCTURES & COMPONENTS			59,836.20	2.73%
Coverage: Building 6 - PCT #1- Machine Storage- 2000 FM 1686	@	10.57% =	6,326.40	
Coverage: Building 12 - Park- Metal Storage - 500 Fordyce Rd.	@	0.50% =	297.60	
Coverage: Building 16 - Airplane Hangar(FBO) - 437 S. Hangar Dr.	@	20.68% =	12,375.58	
Coverage: Building 18 - Airplane Hangar C - 207 Storehouse Dr.	. @	6.39% =	3,825.60	
Coverage: Building 19 - PCT #4-Truck Storage - 155 Corpus Christi	@	2.38% =	1,425.60	
Coverage: Building 21 - Airplane Hangar(T-Hangar Units)-348 N. Hangar Dr.	@	6.56% =	3,925.44	
Coverage: Building 24 - Airport Terminal /2 Storage Buildings - 609 Foster	@	0.30% =	178.20	
Coverage: Building 39 - AARFF Station (Fire Station) - 121 N Hangar	@	11.91% =	7,125.91	
Coverage: Building 41 - Control Tower / Airport - 348 Bachelor Dr.	@	7.82% =	4,677.75	
Coverage: Building 52 - Fisher Stevens - 43 Storehouse	@	15.30% =	9,156.00	
Coverage: Building 60 - Vacant Building - 479 Waco Circle	@	1.80% =	1,078.28	
Coverage: Building 63 - Condemned Warehouse (H&H Door) - 158 Hangar	@	15.78% =	9,443.84	
INTERIOR LATH & PLASTER			2,703.85	0.12%
Coverage: Building 2- Old Courthouse - 101 N. Bridge	@	12.34% =	333.66	
Coverage: Building 4 - New Courthouse - 115 N. Bridge	@	12.21% =	330.15	
Coverage: Building 5 - Old Fire Station - 209 W. Forrest	@	69.45% =	1,877.84	
Coverage: Building 26 - SWB Building / Bridge St. Annex - 204 N. Bridge	@	6.00% =	162.20	
0				





Virtus 8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

Items			Total	%
PLUMBING			4,312.33	0.20%
Coverage: Building 15 - Airplane Hangar - 133 N. Hangar Dr.	@	2.31% =	99.82	
Coverage: Building 16 - Airplane Hangar(FBO) - 437 S. Hangar Dr.	@	5.65% =	243.47	
Coverage: Building 20 - PCT #4- Building - 155 Corpus Christi	@	61.12% =	2,635.67	
Coverage: Building 25 - Airport Maintenance w/ Generator - 41 Hangar	@	9.00% =	387.94	
Coverage: Building 27 - Extension Service - 528 Waco Circle	@	10.15% =	437.62	
Coverage: Building 31 - 4-H Activity Center - 259 Bachelor Dr.	@	9.71% =	418.93	
Coverage: Building 56 - LDS Builders - 396 Foster Field	@	2.06% =	88.88	
PANELING & WOOD WALL FINISHES			8,728.62	0.40%
Coverage: Building 1- Old Jail- 206 W. Constitution	@	69.58% =	6,073.69	
Coverage: Building 12 - Park- Metal Storage - 500 Fordyce Rd.	@	12.43% =	1,085.37	
Coverage: Building 20 - PCT #4- Building - 155 Corpus Christi	@	17.98% =	1,569.56	





tems			Total	%
AINTING			102,541.70	4.689
Coverage: Building 1- Old Jail- 206 W. Constitution	@	0.60% =	610.88	
Coverage: Building 2- Old Courthouse - 101 N. Bridge	@	2.03% =	2,082.29	
Coverage: Building 3 - Old Courthouse Tunnel	@	0.09% =	93.73	
Coverage: Building 4 - New Courthouse - 115 N. Bridge	@	1.26% =	1,290.20	
Coverage: Building 5 - Old Fire Station - 209 W. Forrest	@	1.80% =	1,846.81	
Coverage: Building 6 - PCT #1- Machine Storage- 2000 FM 1686	@	0.18% =	186.30	
Coverage: Building 7 - PCT #3- Machine Storage - 133 Aloe Field	@	0.28% =	284.87	
Coverage: Building 12 - Park- Metal Storage - 500 Fordyce Rd.	@	0.27% =	272.83	
Coverage: Building 14 - New Jail - 101 N. Glass	@	4.95% =	5,074.55	
Coverage: Building 15 - Airplane Hangar - 133 N. Hangar Dr.	@	5.03% =	5,162.47	
Coverage: Building 16 - Airplane Hangar(FBO) - 437 S. Hangar Dr.	@	7.24% =	7,425.27	
Coverage: Building 20 - PCT #4- Building - 155 Corpus Christi	@	5.78% =	5,929.18	
Coverage: Building 21 - Airplane Hangar(T-Hangar Units)-348 N. Hangar Dr.	@	0.09% =	88.76	
Coverage: Building 24 - Airport Terminal /2 Storage Buildings - 609 Foster	@	0.63% =	640.96	
Coverage: Building 25 - Airport Maintenance w/ Generator - 41 Hangar	@	3.88% =	3,978.38	
Coverage: Building 26 - SWB Building / Bridge St. Annex - 204 N. Bridge	@	2.92% =	2,997.38	
Coverage: Building 27 - Extension Service - 528 Waco Circle	@	8.27% =	8,478.79	
Coverage: Building 31 - 4-H Activity Center - 259 Bachelor Dr.	@	0.54% =	558.81	
Coverage: Building 32 - Fire Marshall Office / TSA - 25 & 27 Hangar Dr.	@	1.74% =	1,783.72	
Coverage: Building 33 - Officers Club - 333 Bachelor Dr.	@	22.65% =	23,220.86	
Coverage: Building 35 - COMAT Building - 442 Foster Field Dr.	@	8.96% =	9,191.51	
Coverage: Building 38 - Storehouse - 103 S Glass	@	5.64% =	5,787.39	
Coverage: Building 41 - Control Tower / Airport - 348 Bachelor Dr.	@	2.03% =	2,081.30	
Coverage: Building 50 - Celebration Church - 358 Foster Field	@	0.64% =	655.20	
Coverage: Building 51 - Sky Restaurant - 236 Foster Field	@	3.59% =	3,685.43	
Coverage: Building 54 - Townsend	@	0.56% =	571.08	-
CTORYCOSUB			12/13/2017	Page:



Wirtus 8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

Items			Total	%
Remodeling Unamed - 470 Foster Field				
Coverage: Building 56 - LDS Builders - 396	@	2.26% =	2,313.57	
Foster Field				
Coverage: Building 62 - Texas Mile	@	3.76% =	3,853.50	
Warehouse - 131 Hangar				
Coverage: Building 66 - Old Dorm Building	@	2.34% =	2,395.68	
- 294 Foster Field				





ems			Total	%
OOFING			683,954.47	31.23%
Coverage: Building 4 - New Courthouse -	@	0.08% =	578.40	
115 N. Bridge				
Coverage: Building 6 - PCT #1- Machine	@	0.29% =	2,016.32	
Storage- 2000 FM 1686				
Coverage: Building 7 - PCT #3- Machine	@	4.53% =	30,959.10	
Storage - 133 Aloe Field				
Coverage: Building 9 - PCT #3-Mechanic	@	0.64% =	4,360.81	
Shop - 133 Aloe Field				
Coverage: Building 10 - PCT #3-Service	@	0.40% =	2,763.69	
Center Cover - 133 Aloe Field				
Coverage: Building 11 - PCT #2-Truck	@	1.77% =	12,108.63	
Storage - 3323 Nursery				
Coverage: Building 12 - Park- Metal	@	0.49% =	3,325.94	
Storage - 500 Fordyce Rd.	_			
Coverage: Building 15 - Airplane Hangar -	@	1.60% =	10,972.17	
133 N. Hangar Dr.	0	1.00%	10,7 / 20.1 /	
Coverage: Building 16 - Airplane	@	3.73% =	25,504.46	
Hangar(FBO) - 437 S. Hangar Dr.	C.	3.7370 =	25,504.40	
Coverage: Building 18 - Airplane Hangar C -	@	28.71% =	196,349.65	
	· W	28.71% =	190,349.03	
207 Storehouse Dr.		1 720 -	11 900 41	
Coverage: Building 19 - PCT #4-Truck	@	1.73% =	11,800.41	
Storage - 155 Corpus Christi		2.249	22 192 42	
Coverage: Building 20 - PCT #4- Building -	@	3.24% =	22,182.43	
155 Corpus Christi		. =0.7	05.005.00	
Coverage: Building 21 - Airplane Hangar(T-	(a)	3.79% =	25,925.22	
Hangar Units)-348 N. Hangar Dr.	-		44.474.00	
Coverage: Building 22 - Aircraft Storage(T-	@	6.82% =	46,676.83	
Hangar Units)- 388 N. Hangar Dr				
Coverage: Building 24 - Airport Terminal /2	@	0.65% =	4,440.16	
Storage Buildings - 609 Foster				
Coverage: Building 25 - Airport	@	0.70% =	4,812.16	
Maintenance w/ Generator - 41 Hangar				
Coverage: Building 27 - Extension Service -	@	2.51% =	17,194.80	
528 Waco Circle				
Coverage: Building 33 - Officers Club - 333	@	1.75% =	11,987.43	
Bachelor Dr.				
Coverage: Building 35 - COMAT Building -	@	6.05% =	41,345.91	
442 Foster Field Dr.			ŕ	
Coverage: Building 38 - Storehouse - 103 S	@	0.08% =	576.40	
Glass				
Coverage: Building 39 - AARFF Station	@	0.06% =	387.81	
(Fire Station) - 121 N Hangar	-		22.132	
Coverage: Building 50 - Celebration Church	@	0.58% =	3,995.81	
- 358 Foster Field			2,72102	
Coverage: Building 51 - Sky Restaurant -	@	1.64% =	11,183.31	
236 Foster Field		1.01/0	11,10001	
Coverage: Building 52 - Fisher Stevens - 43	@	10.70% =	73,156.46	
	G.	10.7070 -	73,130.40	
Storehouse Covernge: Puilding 53 Paliant Field	(0)	0.24% =	1,673.77	
Coverage: Building 53 - Reliant Field	@	U.2470 =	1,0/3.//	
Services - 112 Corpus Chrisit	(6)	0.71% -	4,834.73	
Coverage: Building 54 - Townsend	@	0.71% =		
TORYCOSUB			12/13/2017	Page:



Wirtus 8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

Items			Total	%
Remodeling Unamed - 470 Foster Field				
Coverage: Building 56 - LDS Builders - 396 Foster Field	@	0.52% =	3,589.04	
Coverage: Building 57 - Straight Arrow Archery - 60 Storehouse	@	0.50% =	3,444.76	
Coverage: Building 58 - Celebration Church / UHV - 292 Foster Field	@	0.44% =	3,000.33	
Coverage: Building 60 - Vacant Building - 479 Waco Circle	@	2.87% =	19,606.79	
Coverage: Building 61 - Old Golden Crescent - GCRP - 568 Waco Circle	@	3.95% =	26,997.80	
Coverage: Building 62 - Texas Mile Warehouse - 131 Hangar	@	1.04% =	7,136.81	
Coverage: Building 65 - Old Brig - 153 Corpus Christi	@	0.03% =	211.26	
Coverage: Building 66 - Old Dorm Building - 294 Foster Field	@	7.14% =	48,854.87	
SCAFFOLDING			2,373.32	0.11%
Coverage: Building 4 - New Courthouse - 115 N. Bridge	@	9.83% =	233.32	
Coverage: Building 5 - Old Fire Station - 209 W. Forrest	@	6.76% =	160.40	
Coverage: Building 18 - Airplane Hangar C - 207 Storehouse Dr.	@	64.72% =	1,536.00	
Coverage: Building 20 - PCT #4- Building - 155 Corpus Christi	@	1.09% =	25.92	
Coverage: Building 21 - Airplane Hangar(T-Hangar Units)-348 N. Hangar Dr.	@	4.37% =	103.68	
Coverage: Building 38 - Storehouse - 103 S Glass	@	13.23% =	314.00	





Virtus 8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

Items			Total	%
SIDING			13,582.79	0.62%
Coverage: Building 6 - PCT #1- Machine Storage- 2000 FM 1686	@	0.96% =	131.04	
Coverage: Building 7 - PCT #3- Machine Storage - 133 Aloe Field	@	1.20% =	163.20	
Coverage: Building 16 - Airplane Hangar(FBO) - 437 S. Hangar Dr.	@	12.73% =	1,728.90	
Coverage: Building 21 - Airplane Hangar(T-Hangar Units)-348 N. Hangar Dr.	@	0.96% =	130.56	
Coverage: Building 25 - Airport Maintenance w/ Generator - 41 Hangar	@	5.23% =	710.62	
Coverage: Building 33 - Officers Club - 333 Bachelor Dr.	@	0.73% =	99.01	
Coverage: Building 38 - Storehouse - 103 S Glass	@	0.71% =	96.30	
Coverage: Building 39 - AARFF Station (Fire Station) - 121 N Hangar	@	6.16% =	836.50	
Coverage: Building 41 - Control Tower / Airport - 348 Bachelor Dr.	@	3.24% =	440.64	
Coverage: Building 52 - Fisher Stevens - 43 Storehouse	@	7.33% =	995.52	
Coverage: Building 56 - LDS Builders - 396 Foster Field	@	17.21% =	2,337.00	
Coverage: Building 65 - Old Brig - 153 Corpus Christi	@	0.69% =	93.70	
Coverage: Building 66 - Old Dorm Building - 294 Foster Field	@	42.85% =	5,819.80	





Items			Total	%
SOFFIT, FASCIA, & GUTTER			14,886.72	0.68%
Coverage: Building 6 - PCT #1- Machine Storage- 2000 FM 1686	@	2.45% =	364.80	
Coverage: Building 7 - PCT #3- Machine Storage - 133 Aloe Field	@	10.18% =	1,515.52	
Coverage: Building 12 - Park- Metal Storage - 500 Fordyce Rd.	@	0.34% =	50.68	
Coverage: Building 14 - New Jail - 101 N. Glass	@	1.18% =	175.00	
Coverage: Building 16 - Airplane Hangar(FBO) - 437 S. Hangar Dr.	@	1.93% =	288.00	
Coverage: Building 17 - Airplane Hangar B - 305 S. Hangar Dr.	@	7.62% =	1,133.93	
Coverage: Building 18 - Airplane Hangar C - 207 Storehouse Dr.	@	2.43% =	362.40	
Coverage: Building 24 - Airport Terminal /2 Storage Buildings - 609 Foster	@	19.68% =	2,929.46	
Coverage: Building 31 - 4-H Activity Center - 259 Bachelor Dr.	@	0.64% =	96.00	
Coverage: Building 35 - COMAT Building - 442 Foster Field Dr.	@	1.37% =	204.00	
Coverage: Building 38 - Storehouse - 103 S Glass	@	2.97% =	441.64	
Coverage: Building 39 - AARFF Station (Fire Station) - 121 N Hangar	@	1.03% =	153.60	
Coverage: Building 50 - Celebration Church - 358 Foster Field	@	0.58% =	86.40	
Coverage: Building 51 - Sky Restaurant - 236 Foster Field	@	5.29% =	787.64	
Coverage: Building 52 - Fisher Stevens - 43 Storehouse	@	24.50% =	3,647.52	
Coverage: Building 53 - Reliant Field Services - 112 Corpus Chrisit	@	6.61% =	984.55	
Coverage: Building 54 - Townsend Remodeling Unamed - 470 Foster Field	@	1.01% =	150.94	
Coverage: Building 56 - LDS Builders - 396 Foster Field	@	3.03% =	451.62	
Coverage: Building 66 - Old Dorm Building - 294 Foster Field	@	7.14% =	1,063.02	
STEEL COMPONENTS			4,957.10	0.23%
Coverage: Building 19 - PCT #4-Truck Storage - 155 Corpus Christi	@	55.76% =	2,764.16	, <u>-</u>
Coverage: Building 21 - Airplane Hangar(T-Hangar Units)-348 N. Hangar Dr.	@	32.38% =	1,605.06	
Coverage: Building 63 - Condemned Warehouse (H&H Door) - 158 Hangar	@	11.86% =	587.88	





Virtus 8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

Items			Total	%
TOILET & BATH ACCESSORIES			462.86	0.02%
Coverage: Building 14 - New Jail - 101 N. Glass	@	11.24% =	52.01	
Coverage: Building 15 - Airplane Hangar - 133 N. Hangar Dr.	@	2.31% =	10.68	
Coverage: Building 16 - Airplane Hangar(FBO) - 437 S. Hangar Dr.	@	5.30% =	24.55	
Coverage: Building 25 - Airport Maintenance w/ Generator - 41 Hangar	@	4.61% =	21.36	
Coverage: Building 27 - Extension Service - 528 Waco Circle	@	1.15% =	5.34	
Coverage: Building 31 - 4-H Activity Center - 259 Bachelor Dr.	@	70.77% =	327.56	
Coverage: Building 33 - Officers Club - 333 Bachelor Dr.	@	4.61% =	21.36	
TIMBER FRAMING			2,984.90	0.149
Coverage: Building 18 - Airplane Hangar C - 207 Storehouse Dr.	@	84.33% =	2,517.20	
Coverage: Building 62 - Texas Mile Warehouse - 131 Hangar	@	15.67% =	467.70	
TEMPORARY REPAIRS			8,057.89	0.379
Coverage: Building 15 - Airplane Hangar - 133 N. Hangar Dr.	@	25.31% =	2,039.35	
Coverage: Building 17 - Airplane Hangar B - 305 S. Hangar Dr.	@	8.45% =	680.85	
Coverage: Building 18 - Airplane Hangar C - 207 Storehouse Dr.	@	12.51% =	1,008.00	
Coverage: Building 33 - Officers Club - 333 Bachelor Dr.	@	46.09% =	3,714.27	
Coverage: Building 51 - Sky Restaurant - 236 Foster Field	@	7.64% =	615.42	
WINDOWS - ALUMINUM			1,388.22	0.069
Coverage: Building 15 - Airplane Hangar - 133 N. Hangar Dr.	@	54.79% =	760.55	
Coverage: Building 21 - Airplane Hangar(T-Hangar Units)-348 N. Hangar Dr.	@	4.95% =	68.71	
Coverage: Building 25 - Airport Maintenance w/ Generator - 41 Hangar	@	40.26% =	558.96	





Items			Total	9/
WINDOW REGLAZING & REPAIR			30,016.59	1.379
Coverage: Building 2- Old Courthouse - 101 N. Bridge	@	0.32% =	97.05	
Coverage: Building 15 - Airplane Hangar - 133 N. Hangar Dr.	@	40.44% =	12,137.84	
Coverage: Building 17 - Airplane Hangar B - 305 S. Hangar Dr.	@	28.28% =	8,488.00	
Coverage: Building 24 - Airport Terminal /2 Storage Buildings - 609 Foster	@	0.32% =	97.05	
Coverage: Building 25 - Airport	@	0.09% =	26.82	
Maintenance w/ Generator - 41 Hangar Coverage: Building 26 - SWB Building / Bridge St. Annex - 204 N. Bridge	@	0.36% =	109.16	
Coverage: Building 27 - Extension Service - 528 Waco Circle	@	0.18% =	54.58	
Coverage: Building 33 - Officers Club - 333 Bachelor Dr.	@	0.04% =	12.50	
Coverage: Building 38 - Storehouse - 103 S Glass	@	0.36% =	109.16	
Coverage: Building 52 - Fisher Stevens - 43 Storehouse	@	27.64% =	8,296.16	
Coverage: Building 54 - Townsend Remodeling Unamed - 470 Foster Field	@	0.91% =	272.90	
Coverage: Building 59 - Fire Marshall Storage - 354 Hangar	@	0.69% =	206.21	
Coverage: Building 61 - Old Golden Crescent - GCRP - 568 Waco Circle	@	0.36% =	109.16	
WINDOW TREATMENT			449.77	0.02
Coverage: Building 25 - Airport Maintenance w/ Generator - 41 Hangar	@	63.33% =	284.84	
Coverage: Building 26 - SWB Building / Bridge St. Annex - 204 N. Bridge	@	36.67% =	164.93	
WINDOWS - WOOD			5,937.42	0.27
Coverage: Building 25 - Airport	@	39.38% =	2,338.12	02
Maintenance w/ Generator - 41 Hangar	(6)	37.30 % =	2,000.12	
Coverage: Building 26 - SWB Building / Bridge St. Annex - 204 N. Bridge	@	57.76% =	3,429.60	
Coverage: Building 33 - Officers Club - 333 Bachelor Dr.	@	2.86% =	169.70	
WALLPAPER			612.01	0.039
Coverage: Building 27 - Extension Service - 528 Waco Circle	@	100.00% =	612.01	0.00
WATER EXTRACTION & REMEDIATION			31.42	0.00
Coverage: Building 16 - Airplane Hangar(FBO) - 437 S. Hangar Dr.	@	92.65% =	29.11	0.00
Coverage: Building 31 - 4-H Activity Center - 259 Bachelor Dr.	@	7.35% =	2.31	



Wirtus 8380 Warren Parkway / Ste. 700 - Frisco, TX 75034 913-601-4546

Items			Total	%
EXTERIOR STRUCTURES			4,568.20	0.21%
Coverage: Building 8 - PCT #3-Radio Tower-133 Aloe Field	@	14.43% =	659.06	
Coverage: Building 20 - PCT #4- Building - 155 Corpus Christi	@	49.03% =	2,240.00	
Coverage: Building 30 - Health Dept - 2805 Navarro	@	14.43% =	659.06	
Coverage: Building 36 - Animal Shelter - 102 Perimeter Rd.	@	22.11% =	1,010.08	
Subtotal			2,189,792.41	100.00%
